



AECOM
1625 Summit Lake Drive
Suite 200
Tallahassee, FL 32317
www.aecom.com

850 574 3197 tel
850 402 6490 fax

February 3, 2015

Mr. Scott Miller
Remedial Project Manager
Superfund Remedial and Technical Services Branch
U.S. Environmental Protection Agency, Region 4
Atlanta Federal Center
61 Forsyth Street
Atlanta, Georgia 30303-8960

**Subject: 2014 Annual Report
OU-1 and OU-2 Agrico Site
Pensacola, Florida
EPA ID: FLD 98022 1857**

Dear Mr. Miller:

AECOM through URS Corporation (URS), a wholly-owned subsidiary, on behalf of Phillips 66 (Phillips), successor to ConocoPhillips and Williams representing Agrico Chemical Company is submitting this 2014 Annual Report for the Agrico site in Pensacola, Florida. This report presents the results of O&M activities conducted during 2014 for the site. The sampling event and reporting as well as other activities are conducted in accordance with the U.S. Environmental Protection Agency (EPA) approved OU-1 and OU-2 Operation and Maintenance Plans (September 1996, November 1998, respectively). These plans have been modified and approved by EPA based on report recommendations or other correspondences as follows: Recommendations presented in the November 30, 2006 Evaluation of Long-Term Groundwater Monitoring Network Technical Memorandum Report and the subsequent January 22, 2007 EPA comment letter concurring with the listed recommendations. Additionally, as per your letter dated September 2, 2008, the semi-annual groundwater sampling was discontinued as of the May 2008 event. All OU-1 wells are now a part of the site-wide groundwater monitoring program. Also, EPA approved O&M recommendations (January 25, 2010) were implemented in 2010. URS also implemented in 2010 approved recommendations (February 2, 2010) related to Monitored Natural Attenuation and approved recommendations (September 20, 2010) as stated in the June 2010 Five-Year Review Report (2005-2010) Third Five-Year Review Report for Agrico Chemical Company site, regarding the Bayou Texar surface water sampling.

The following recommendations are part of the 2014 Annual Report.

- The former Agrico source area remains controlled. MNA evaluations indicate modifications to the monitoring program are appropriate. It is recommended that the groundwater monitoring frequency be changed to every 5 years.



Mr. Scott Miller
Remedial Project Manager
USEPA, Region IV
February 3, 2015
Page 2

- It is recommended that the surface water component of the monitoring program be discontinued. It has been demonstrated through evaluation and sampling that there is no significant risk caused by the groundwater plume discharge to the surface water.
- It is recommended that the notifications –Agency Coordination Memo and the FDOT inquiry for intrusive activity be change to every 5 years to correspond with the sampling activity.
- Recommended schedule - The next scheduled sampling event for the Agrico Site is proposed for November 2019, with a report to follow in March 2020. It is anticipated that the EPA Five-Year Review Report will be issued in July 2020.

It should be noted that the maintenance schedule for the site will be unchanged and regular maintenance will occur on at least a monthly basis. Also the advisory notice to contractors and the checking for new well construction will continue on an annual basis.

As requested, a copy of the report will be sent directly to the site document repository, the West Florida Regional Library, Genealogy Branch in Pensacola.

AECOM will be uploading the electronic data for 2014 to the EPA DART system as per the guidance memorandum from EPA Region 4's Superfund Division Director requiring that environmental sampling data be submitted to EPA in a Region 4 electronic format.

Should you have any questions or require additional information regarding this report, please contact Ms. Terry D. Vandell (Phillips) at (580) 767-6561 or Mr. John Carey (Agrico Chemical Company Representative) at (918) 573-8215.

Sincerely,

A handwritten signature in blue ink, reading "Jeffry R. Wagner". The signature is fluid and cursive, with a long horizontal stroke extending to the right.

Jeffry R. Wagner, P.G., V.P.
Principal Hydrogeologist

JRW:lc

Enclosure: 1 CD

cc: Walsta Jean-Baptiste – FDEP, Hazardous Waste Cleanup Section, Tallahassee
Alex Webster– FDEP, Northwest District, Pensacola
John Carey– Agrico Chemical Company Representative
Terry Vandell-Bell – Phillips 66
Bill Nelson – West Florida Public Library, Genealogy Branch, Pensacola

R E P O R T

2014 ANNUAL REPORT

AGRICO SITE PENSACOLA, FLORIDA OPERABLE UNITS ONE (OU-1) AND TWO (OU-2)

EPA ID: FLD 980221857

Submitted to

US Environmental Protection Agency, Region 4
Atlanta, Georgia

Prepared for

Phillips 66
Ponca City, Oklahoma
and
Williams, Inc. on behalf of
Agrico Chemical Company
Tulsa, Oklahoma

February 3, 2015



AECOM through URS Corporation, a wholly-owned subsidiary
1625 Summit Lake Drive
Tallahassee, Florida 32317
850.574.3197
12806620.00000

Certification By Florida Registered Professional Geologist

In accordance with Chapter 492, Florida Statutes, the geologic aspects of this *2014 Annual Report for the Agrico Chemical Site, Operable Unit One (OU-1) and Operable Unit Two (OU-2)* located in Pensacola, Florida has been prepared by or supervised by the undersigned registered Florida Professional Geologist. AECOM through URS Corporation (URS), a wholly-owned subsidiary has prepared the geologic information presented in this Annual Report in a manner consistent with sound geologic practices and the customary level of care and skill exercised by members of the profession currently practicing in the same locality under similar circumstances.

Information developed and presented by others was used by URS in good faith as representative of the site conditions. The work performed by URS is in conformance with the current standards of practice.




Jeffrey R. Wagner, P.G. V.P.
Registered Professional Geologist
Florida License No. 156
2/2/15
(Date)

Table of Contents

Executive Summary.....	ES-1
Section 1 Introduction.....	1-1
1.1 Five-Year Reviews.....	1-3
Section 2 Site Location and Background	2-1
2.1 Site Description.....	2-1
2.2 Site Access and Deed Restrictions.....	2-1
2.3 Document Repository	2-1
2.4 Site History	2-2
2.5 Operable Unit One Remedy.....	2-4
2.5.1 Operation and Maintenance	2-5
2.6 Operable Unit Two Remedy	2-6
2.7 Annual O&M Tasks for Operable Units One and Two	2-6
2.8 Other Contamination Sources In the Vicinity of the Agrico Site	2-7
Section 3 Hydrogeology	3-1
3.1 Hydrogeologic Framework of the Sand-And-Gravel Aquifer	3-1
3.1.1 Surficial Zone.....	3-1
3.1.2 Low-Permeability Zone	3-1
3.1.3 Main Producing Zone	3-1
3.2 Hydraulic Head Differences and Groundwater Flow Boundaries	3-2
3.3 Rainfall Conditions	3-2
Section 4 Notification Tasks.....	4-1
Section 5 Sampling Results	5-1
5.1 Groundwater Sampling	5-1
5.1.1 Monitoring Well Network.....	5-1
5.1.2 Well Purging	5-2
5.1.3 Investigation Derived Waste.....	5-2
5.1.4 Water Level Measurements	5-2
5.2 Bayou Texar Sampling	5-2
5.3 Chemical Analyses.....	5-3
5.4 Sampling Results	5-4
5.5 Groundwater Field Parameters	5-4
5.5.1 Specific Conductance.....	5-4
5.5.2 pH.....	5-6
5.5.3 Dissolved Oxygen.....	5-10
5.5.4 Oxidation-Reduction Potential.....	5-12
5.6 Bayou Texar Sampling Results.....	5-14
5.7 QA/QC Review	5-15

Table of Contents

	5.8	Groundwater Sampling Results	5-16
Section 6		Conclusions/Recommendations	6-1
	6.1	OU-1 Remedy	6-1
	6.2	OU-2 Remedy	6-1
	6.2.1	Notifications.....	6-1
	6.2.2	Sampling Results – Groundwater and Surface Water.....	6-2
	6.2.3	Bayou Texar.....	6-3
	6.3	Recommendations.....	6-5
Section 7		References and Additional Bibliography.....	7-1

Tables

Table 1	Groundwater Monitoring Well Network – Long-Term and Periodic Monitoring Wells
Table 2	Monitoring Well Construction Details
Table 3	Groundwater Field Parameter Results
Table 4	Groundwater Elevations
Table 5	Surface Water Field Parameter Results
Table 6	Advisory Notice Distribution List
Table 7	Irrigation Well Information
Table 8	Comparison of COC Results at Groundwater Monitoring Locations for Surficial Zone and Main Producing Zone
Table 9	Comparison of COC Results at Long-Term Monitoring Locations for Surface Water

Figures

Figure 1	Site Location and Site-wide Monitoring Well Locations - OU-1 and OU-2
Figure 2	View of OU-1 (Former Facility Area) with Current Features
Figure 3	Irrigation Well Locations
Figure 4	Hydrogeologic Conceptual Model (from Agrico Site to Bayou Texar)
Figure 5	Potentiometric Surface, Surficial Zone, November 2014
Figure 6	Potentiometric Surface, Main Producing Zone, November 2014
Figure 7	Annual Rainfall and Cumulative Departure from Normal, NOAA Rainfall Station, Pensacola, Florida
Figure 8	Fluoride Concentration Delineation (Main Producing Zone), November 2014
Figure 9	Combined Radium 226 + 228 Delineation (Main Producing Zone), November 2014

Appendices

Appendix A	Analytical Laboratory Reports
Appendix B	Groundwater Level Trends for Surficial Zone and Main Producing Zone Monitoring Wells
Appendix C	Pertinent OU-1 and OU-2 Correspondences and Documentation
Appendix D	Inspection Reports for 2014

The activities being conducted for the Agrico Site in Pensacola, Florida are under the oversight of the U.S. Environmental Protection Agency (EPA), as outlined by the Consent Decrees (1994 and 1997) and the EPA Records of Decision (ROD) (1992 and 1994). The Site has been divided into two operable units (OU). The first operable unit (OU-1) addressed the cleanup of on-site source material. The second operable unit (OU-2) addresses groundwater under the Site and downgradient of the Site. In 1995, remedial actions began for OU-1. Impacted soils and all sludge materials were collected and treated by solidification/stabilization. Additional fluoride-impacted soils were excavated. These soils, as well as the treated soils and sludges, were stabilized by placing them into an engineered excavated unlined area above the water-table and covering them with a multi-layered cap designed to prevent rainfall infiltration from contacting the materials. By keeping the underlying soil dry, the soils remain stabilized. The OU-1 remedial actions were certified complete by EPA in April 1997. With the source area controlled, EPA addressed OU-2, the groundwater, by selecting a monitored natural attenuation (MNA) remedy. The selected remedy involves actions aimed at limiting exposure while natural attenuation processes remediate the groundwater.

After extensive sampling of many constituents during the assessment phase (1990-1993), a risk evaluation was performed. The EPA selected seven constituents of concern (COC) for initial long-term groundwater and surface water monitoring. For OU-1, these COCs included lead, arsenic, and fluoride. These were soil COCs and since the soils were stabilized on-site, monitoring of these constituents in the groundwater provided for assessing the integrity of the OU-1 remedy over time. For OU-2, these constituents include arsenic, fluoride, combined radium 226 plus radium 228, chloride, sulfate, and nitrate plus nitrite. The groundwater performance standards established by each of the RODs for OU-1 and OU-2 are as follows:

- Total Lead 0.015 milligrams per liter (mg/L)
- Total Arsenic 0.050 mg/L
- Fluoride 4.0 mg/L
- Radium 226 +228 5.0 pico Curies per liter (pCi/L)
- Chloride 250 mg/L
- Sulfate 250 mg/L
- Nitrate + nitrite 10 mg/L (analysis of nitrite indicates results at all groundwater monitoring locations are less than detection limit and a higher performance standard is appropriate; nitrite analysis discontinued as per EPA approval, January 22, 2007).

Beginning in November 2005, changes were approved for the long-term monitoring network. In 2005, an upgradient groundwater monitoring well (PIP-D) was added to the network. In 2007, the OU-1 monitoring well network was merged with the OU-2 monitoring network to form the long-term site-wide network. Initially all constituents were monitored in the OU-1 wells. In 2007, nitrite was eliminated as a constituent since it was determined that the nitrogen detected was only nitrate. Also in 2007, surficial zone monitoring wells AC-5S, AC-24S, AC-26S, NWD-2S, and NWD-4S were changed from long-term monitoring to periodic monitoring. In 2009, periodic monitoring wells, AC-9D2, AC-24D, and AC-28D were changed to annual sampling locations. In 2010, arsenic and lead were discontinued from the list of analytes for the long-term network including monitoring wells located in OU-1. As per the EPA approved

(February 5, 2010) recommendation from the *Evaluation of Monitored Natural Attenuation in Groundwater Report* (August 19, 2009), arsenic has been deleted from the list of analytes for the long-term monitoring well network except at AC-2S and AC-3S. In 2010, the surface water long-term monitoring network changes included the deletion of the upstream monitoring of Carpenter's Creek (ACSW-BL). Other changes for 2010 included three additional monitoring stations in Bayou Texar. These stations included near-bottom surface water sampling for fluoride only.

The Site is currently in the long-term Operations and Maintenance (O&M) phase, with monitored natural attenuation as the selected groundwater remedy.

This 2014 Annual Report presents the results of groundwater activities conducted for both OU-1 and OU-2. The 2014 results will be the basis of the EPA 2015 Five-Year Review. The 2014 O&M tasks are as follows:

- Annual groundwater sampling for the defined COCs (fluoride, radium 226, radium 228, chloride, sulfate, and nitrate) for all the surficial and main producing zones long-term and periodic monitoring wells within OU-1 and OU-2. Data collected during the annual sampling events are used to evaluate the effectiveness of the monitored natural attenuation remedy for groundwater.
- Annual surface water sampling in Bayou Texar for the same COCs identified for groundwater. This sampling is to assess the surface water quality for potential effects from the groundwater discharge.
- Annual advisory notices are distributed to water well contractors, irrigation system installers, and pool contractors to inform these contractors of the area where groundwater impacts related to the Agrico plume are located. The annual advisory also informs them of the well construction moratorium in effect by the Northwest Florida Water Management District (NFWFMD).
- Review the Northwest Florida Water Management District well construction permit records to confirm that no wells have been inadvertently installed within the OU-2 area. Because of the existing well construction moratorium, the expectation is that no new wells will be permitted in this area.
- Activities related to coordination and dissemination of site information to local, regional, and state agencies.
- Site inspection reporting and site maintenance activity.

OPERABLE UNIT ONE REMEDY

The Operable Unit One (OU-1) addressed the cleanup of the source on-site. EPA approved the source remedy in the 1992 OU-1 ROD and it included excavation, solidification and stabilization for on-site soils and sludges. Following the ROD issuance, actions by Conoco were initiated to re-acquire ownership of the property so that the OU-1 remedy could be implemented.

In 1995, remedial construction activities began. Lead and arsenic-impacted soils and all sludge materials were collected and treated by solidification/stabilization using cement. Other fluoride-impacted soils were collected for consolidation. These consolidated soils and treated soils and

sludges were installed in lifts and compacted in the excavation based on engineering designs and standards. The material was placed approximately 20 ft above the saturated groundwater level within the unsaturated, dry portion of the sediments underlying the Site. The source control was certified by EPA to be complete in April 1997.

OPERABLE UNIT TWO REMEDY

The remedy chosen by EPA for the impacted groundwater associated with the Agrico Site is monitored natural attenuation. The 2014 results indicate that the Agrico plume continues to be adequately defined. The 2014 sampling results compare favorably to past sampling results, which indicate that the source area remains controlled. The limited extent of the surficial zone plume is caused by the significant downward vertical component to the contaminant transport downgradient of OU-1. The decreasing trends in the surficial zone are a result of the OU-1 source control measures which allows for natural attenuation processes to be effective downgradient. The source area remedy remains an effective measure in eliminating migration of COCs from the OU-1 area to the groundwater.

Monitored Natural Attenuation Results

Dr. Huber concluded in his 2009 report that the data show that mechanisms for attenuation are in place throughout the OU-2 area. These mechanisms and the OU-1 source remedy are resulting in decreasing concentrations that are propagating downgradient toward Bayou Texar, as expected. For the plume area, the highest concentrations for each constituent are declining and downgradient peaks are less than historical highs. Increases are still happening for individual wells, but the overall concentrations are still less than the historical highs. It is estimated from Huber's statistical evaluation that much of the groundwater will reach the target concentrations within two to three decades. However, the discharge area near Bayou Texar may take longer. The processes at this discharge boundary are more complex and do not follow the upgradient time line. Additionally, radium declines may lag behind the other constituents and is more dependent on increases in pH as the overall chemical conditions improve upgradient. Initial fate and transport modeling performed for the Site in the early 1990s suggested targets would not be reached for at least 70 years. About 20 years has passed since the source controls were implemented. The 50 years remaining is still reasonable and well within the targets estimated with the statistical evaluation. The statistical evaluation performed by URS including the 2014 data continues to support Huber's 2009 evaluation.

The statistical uncertainty for the Agrico data set is low. Data is consistent within each well and shows relatively little random variability. For this reason and the fact that decades are still needed to reach targets, recommendations for changes in monitoring frequency have been proposed for the Site. Attenuation will eventually occur everywhere within the OU-2 area but time is required for attenuation progress.

Groundwater Sampling Results

Groundwater results for November 2014 continue to compare favorably to past results.

Overall concentration trends within the surficial zone are downward and the impact extent is shrinking. Impacts are very limited for this zone. This is a direct result of effective source control and the local hydrogeologic conditions.

For the main producing zone, the overall flattening of trends is what has been predicted. This flattening should be expected to continue for some time and eventually evolve into a slowly decreasing trend that accelerates with time.

Slight upward or downward ticks in the trends for the COCs are to be expected over time. It is the long-term trend for each of the COC that is important.

Groundwater Levels

Results of water level measurements collected in November 2014 indicate that groundwater flow remains toward Bayou Texar for both the surficial zone and main producing zone. In 2014, groundwater flow patterns closely followed historical patterns.

Bayou Texar Sampling Results

The long-term surface water results indicate that Bayou Texar is not adversely affected by impacted groundwater from the Agrico Site discharge to the bayou. All near-bottom surface water samples collected during the sampling event of November 2014 indicated that fluoride concentrations were 1.3 milligrams per Liter (mg/L) or less which is below the surface water standard of 5 mg/L.

The evaluation (URS, September 4, 2009) of the primary discharge area for the Agrico plume in Bayou Texar indicates there is no significant risk to populations of demersal fish or to benthic macroinvertebrate communities that inhabit the reach due to fluoride concentrations.

Furthermore, results indicate the fluoride solubility in the majority of surface sediments and in all pore waters within the primary discharge area for the Agrico plume is controlled by mineral precipitation reactions. This reaction causes dissolved fluoride concentrations to be buffered in near surface sediment pore water and in surface water in this primary discharge reach of Bayou Texar.

NWFWMD Well Construction Moratorium

During 2014, no additional irrigation wells were identified from the Northwest Florida Water Management District (NWFWMD) well construction permit records. The well construction moratorium initiated in February 2001 is still in effect and has no termination date. Well prohibition for the defined area which includes the Agrico area is part of NWFWMD's Rule 40A-3.

Advisory Notice

The annual advisory notice was distributed by URS to water well contractors, irrigation system installers, and pool contractors to inform them of the groundwater conditions and the existence of a well construction moratorium within the OU-2 area.

Institutional Controls Coordination

A memorandum was distributed to the local, regional, and state agencies listed below, soliciting information for any changes or proposed new regulatory rules or policies that may affect the institutional controls currently in place for the area. The agencies include:

Florida Department of Environmental Protection (FDEP), Tallahassee and Pensacola
Emerald Coast Utilities Authority (ECUA) (formerly Escambia County Utilities
Authority)
Northwest Florida Water Management District (NFWFMD)
City of Pensacola
Escambia County Health Department (ECHD)
Escambia County Neighborhood and Environmental Services Department
Florida Department of Transportation (FDOT), District Three (Chipley)

FIVE-YEAR REVIEWS

Three Five-Year Reviews have been conducted by EPA for the Agrico Site. The First Five-Year Review occurred in 2000, the Second Five-Year Review occurred in 2004-2005, and the Third Five-Year Review occurred in 2010. Each review concluded that the remedy at the Site is functioning as intended by the RODs for OU-1 and OU-2, and remains protective of human health and the environment. The O&M activities were to be continued and conducted as approved. The 2014 data results will be used as the basis for the fourth Five-Year Review which will be issued by EPA about July 2015.

RECOMMENDATIONS

- The former Agrico source area remains controlled. MNA evaluations indicate source zone depletions and modifications to the monitoring program are appropriate. It is recommended that the groundwater monitoring frequency be changed to every 5 years. It is recommended that November remain as the month for sampling.
- Furthermore, it is recommended that the surface water component of the monitoring program be discontinued. It has been demonstrated through evaluation and sampling that there is no significant risk to the surface water from the groundwater plume discharge to the surface water.
- Recommended schedule - The next scheduled sampling event for the Agrico Site is proposed for November 2019, with a report to follow in March 2020. It is anticipated that the EPA Five-Year Review Report will be issued in July 2020.
- It is recommended that the notifications –Agency Coordination Memo and the FDOT inquiry for intrusive activity be change to every 5 years to correspond with the sampling activity.

AECOM through URS Corporation (URS), a wholly owned subsidiary, has prepared this 2014 Annual Report on behalf of Phillips 66 Company and Agrico Chemical Company represented by Williams Companies, Inc. (Williams). This annual report was prepared in accordance with the following:

- United States Environmental Protection Agency (EPA) Consent Decree (CD) dated May 4, 1994 and the March 10, 1997 amended Consent Decree for the Agrico Site (Agrico);
- The Record of Decision (ROD) for Operable Unit One (OU-1) issued on September 29, 1992;
- The Operation and Maintenance (O&M) Plan for OU-1 dated September 1996 including Appendix I – Groundwater Monitoring Plan by Woodward-Clyde Consultants (currently, URS);
- The ROD for Operable Unit Two (OU-2) issued August 25, 1994;
- The SOW which outlines the work to be performed as the remedy for OU-2;
- The EPA-approved (April 26, 1999) Remedial Action Work Plan and related plans;
- The O&M Plan dated November 1998.
- The Evaluation of Long-Term Groundwater Monitoring Network – Section 12 - Recommendations, Technical Memorandum Report dated November 30, 2006 and subsequent EPA approval of recommendations in EPA comment letter dated January 22, 2007.
- The EPA approval dated September 2, 2008 to discontinue OU-1 semi-annual sampling and to perform annual sampling. The last OU-1 semi-annual sampling event was conducted in May 2008.
- Minor O&M recommendations dated November 18, 2009 were approved by EPA on January 25, 2010.
- Recommendations in the report, *Evaluation of Monitored Natural Attenuation in Groundwater (August 19, 2009- William Huber)* and approved by EPA on February 5, 2010.
- EPA's Third Five-Year Review (June 2010) recommendations related to surface water sampling locations for Bayou Texar.
- Recommendations in the second report, *Evaluation of Monitored Natural Attenuation in Groundwater (October 23, 2013-William Huber)*.

This is the sixteenth comprehensive annual report since the initial one in 1999. The report documents both OU-1 and OU-2 activities performed at the Site for 2014. The annual report was preceded by OU-1 semi-annual sampling results reported annually from 1997-1999. These OU-1 annual reports continued through 2005. The annual report for OU-2 was submitted separately from the OU-1 report from 1999 through 2005. One of the recommendations of the evaluation of the long-term monitoring network (URS, November 30, 2006) was to combine these networks. Beginning with the 2007 Annual Report, the groundwater requirements were integrated so that OU-1 (on-site) and OU-2 (off-site) groundwater impacts could be readily evaluated. Since November 2007, groundwater from the OU-1 monitoring wells has been

analyzed for the same constituents of concern as the OU-2 monitoring wells, as per EPA's request.

EPA approved (September 2, 2008) the integration of the groundwater monitoring requirements for OU-1 and OU-2 so that the monitoring satisfies the original OU-2 monitoring objective - monitoring of the surficial zone and main producing zone, on-site and off-site - downgradient of the Site for the purpose of evaluating the monitored natural attenuation remedy. The original monitoring objective for OU-1 was to only evaluate the effectiveness of the RCRA cap remedy. The effectiveness was demonstrated by a statistical evaluation that confirmed the integrity of the containment system with data collected from 1997 to 2001. Additionally, it has been further confirmed by data collected since 2001, a total of 15 years.

Summary of Sampling Modifications Initiated in November 2007

- Semi-annual sampling of OU-1 groundwater monitoring wells was discontinued and changed to annual sampling as part of the November sampling event. The OU-1 surficial zone monitoring wells, ACB-31S, ACB-32S, AC-33S, AC-34S, and AC-7SR, were integrated into a site-wide groundwater monitoring network. The analyte list for these wells was changed to include the OU-2 analyte list. In addition to total lead, total arsenic and fluoride (COCs in the OU-1 ROD), the groundwater samples from these wells were analyzed for chloride, sulfate, nitrate, radium 226, and radium 228 (COCs in the OU-2 ROD).
- Nitrite has been deleted from the Site's analyte list as modified by implementation of EPA-approved long-term monitoring evaluation recommendations (URS, 2006d).
- Surficial zone monitoring wells AC-5S, AC-24S, AC-26S, NWD-2S, and NWD-4S were changed from long-term to periodic monitoring wells. Additionally, monitoring well NWD-3S was removed from the monitoring network because it was destroyed as a result of off-site construction.
- The groundwater sampling purging procedure was changed from extracting a minimum of three well volumes to a low-flow purge procedure that allows for collecting water quality field parameters after one well volume is purged, and then one-quarter well volume thereafter until three stable water quality parameter readings are collected. This procedure is in accordance with the FDEP SOP for sampling monitoring wells.
- Prior to November 2006, annual reports were prepared for OU-1 and OU-2. Annual reporting for these areas has been combined into one annual report.

Summary of Sampling Modifications Initiated in November 2009

- Additional groundwater sampling was requested by EPA in their comment letter dated October 15, 2009 regarding the Evaluation of Monitored Natural Attenuation in Groundwater Report. The additional wells included periodic monitoring wells AC-9D2, AC-24D, and AC-28D. Constituents to be analyzed from the groundwater from these monitoring wells are the same as the long-term network constituents. The status of these wells was changed from periodic to long-term until sufficient sampling results have been collected on an annual basis.

Summary of Sampling Modifications Initiated in November 2010

- Analysis of lead and arsenic were discontinued from the long-term network groundwater analyses for monitoring wells based on the EPA approval (February 5, 2010) of recommendations in the August 19, 2009, “*Evaluation of Monitored Natural Attenuation in Groundwater*”. In that report, the absence of arsenic and lead in groundwater samples collected from the monitoring well network was reported. The exception is for AC-2S and AC-3S. Total arsenic will continue to be analyzed for these two wells to verify the continued effectiveness of the OU-1 cap.
- Sampling of Carpenter’s Creek at the Ninth Avenue Bridge (ACSW-BL) was discontinued as per January 25, 2010 approval of the November 18, 2009 Recommendations to Operations and Maintenance Plans for OU-1 and OU-2.
- Three surface water sampling locations were added to the sampling program and include BT-02, BT-107 and BT-127. These near-bottom surface water samples are analyzed for fluoride only (EPA recommendation in June 2010, Third Five-Year Review Report).

1.1 FIVE-YEAR REVIEWS

The EPA has conducted three Five-Year Reviews for the Agrico Site. The results of these reviews were presented in the February 2000, July 2005, and June 2010 EPA reports. Each of the three reviews concluded that (1) all areas were in compliance and (2) the remedy at the Site is functioning as intended by the RODs for OU-1 and OU-2, and remains protective of human health and the environment. The fourth Five-Year Review will be issued by EPA about July 2015. The data collected as part of the 2014 Annual Report will serve as the basis for the 2015 Five-Year Review. Following the 2015 five-year review, the next EPA Five-Year Review will be in 2020.

2.1 SITE DESCRIPTION

The Agrico Site is located at 118 East Fairfield Drive, which is at the northwest corner of Fairfield Drive and Interstate I-110 in Pensacola, Escambia County, Florida. The Site consists of 29.84 acres in Township 2 South, Range 30 West of Section 5 and the latitude and longitude at the center of this area is 302709.8914 degrees west and 871318.9648 degrees north, respectively. The Site is bordered by I-110 to the east, Fairfield Drive to the south, CSX railroad to the west, and a construction aggregate business (Vulcan Materials/Conrad Yelvington Distribution) to the north. An approximately 100-foot wide Gulf Power Company easement and overhead electrical lines are near the eastern boundary of the Site. Site access is from the north side of Fairfield Drive, approximately 600 feet (ft) west of the I-110 overpass. Uncle Bob's Self Storage operates storage warehouses on an Agrico Site out-parcel in the south-central area. The Site location is illustrated on **Figure 1**.

2.2 SITE ACCESS AND DEED RESTRICTIONS

Access to the Agrico Site is restricted. The property is secured by a perimeter chain link security fence with locked gates, and the Site is regularly inspected. Restrictive and Site informational signs are posted advising the public of the on-site conditions, and a URS contact phone number is also posted for inquiries. Posted signs are present at the entry gates of the fenced OU-1 property. The wording on the signs is as follows:

Authorized Personnel Only

Please Do Not Disturb Soil Cover

Impacted Waste Material May Be Present Below the Ground Surface

For Information Call 850-251-7208

A Restrictive Covenant (**Appendix C**) for the Site was filed against the property deed with the Escambia County Clerk of the Circuit Court and is dated July 11, 1997. The Restrictive Covenant states in summary that construction or related activities that would interfere with maintaining the Site remedial measures are prohibited by the legal deed restrictions. Any use of the property contrary to the Record of Decision is prohibited, as per the covenant filed for the property.

2.3 DOCUMENT REPOSITORY

The EPA maintains Site information at the West Florida Regional Library, Genealogy Branch. This repository contains project documents, fact sheets, and reference material. EPA encourages the public to review these documents to gain a more thorough understanding of the Site. The address of the library is as follows:

West Florida Regional Library, Genealogy Branch
5740 N. 9th Ave
Pensacola, Florida 32505
850-494-7373

Through 2011, the West Florida Regional Library on West Gregory Street was the repository for the Agrico documents. Since 2011 and currently, these documents are found at the Genealogy Branch on North 9th Avenue.

EPA also has Site information located at the following web site:

<http://www.epa.gov/region04/superfund/sites/npl/florida/agricchemfl.html>

A specific web site was developed for the Agrico Pensacola Site and is located at:

www.agricopensacola.com

This web site contains general information about the Agrico Site, contains the Site fact sheets, and provides contact information for EPA. The web site has been modified and a documents page has been added. Electronic files for four reports were uploaded to this page. The reports that are now accessible via this web site include (1) Evaluation of Monitored Natural Attenuation in Groundwater (URS, 2009), (2) The Third Five-Year Review Report (E2 Inc., 2010), (3) 2011 Annual Report (URS, 2012), (4) 2012 Annual Report (URS 2013), Evaluation of Monitored Natural Attenuation in Groundwater (Report #2), (URS, October 2013), and 2013 Annual Report (URS 2014).

2.4 SITE HISTORY

The former facility at the Agrico Site was a superphosphate process facility as opposed to a continuous wet-process phosphoric acid facility that became dominant with phosphoric fertilizer industry starting in the 1960s and 1970s and continued during the modern era. According to the U.S. Department of Agriculture and Tennessee Valley Authority document titled *Superphosphate: Its History, Chemistry, and Manufacturing* (December 1964), the Irish firm known as W. & H. M. Goulding, Ltd. of Dublin, Ireland opened the Goulding Fertilizer Company, Pensacola, Florida factory in 1891 at the current Agrico Site location. The Goulding Fertilizer Company plant had an annual fertilizer production capacity of 45,000 tons. A sulfuric acid manufacturing plant co-existed on the Site. The source of sulfur was pyrite ore. The source of the phosphate for manufacturing the fertilizer was Central Florida mines and was transported to the facility via rail. The Pensacola plant started operations by manufacturing normal superphosphate, and then operated as a concentrated superphosphate plant (the second of its kind in the United States at the time) from 1898 to 1901. Operations by the Goulding Fertilizer Company continued until 1911, when the factory was sold to an American interest, The American Agricultural Chemical Company (TAACC).

TAACC manufactured normal superphosphate and also continued the manufacturing of sulfuric acid using pyrite ore until 1920, when the source of sulfur dioxide was changed to elemental sulfur. TAACC operated the plant through 1963, when Continental Oil Company (Continental) purchased the assets of TAACC (U.S. Department of Agriculture, 1964).

After the acquisition of TAACC, Continental operated the agrichemical business as the Agrico Chemical Company, a wholly owned subsidiary of Continental. During the time period from 1963 to 1972, the same manufacturing process was used as during the TAACC period (U.S. Department of Agriculture, 1964). From 1967 to 1968, in addition to producing virgin acid from sulfur, the plant purchased and utilized an unknown volume of spent sulfuric acid (Geraghty & Miller, 1993a and 1993b). Continental Oil Company operated the plant until 1972.

In April 1972, The Williams Companies, Inc. (Williams) (Tulsa, Oklahoma) purchased the assets associated with Agrico Chemical Company from Continental Oil's Agrico Chemical Division. Under Williams, Agrico Chemical Company operated as a newly formed Delaware corporation and subsidiary of Williams. At this time, Agrico Chemical Company was one of the country's largest chemical fertilizer companies. In 1972, the Pensacola plant began manufacturing monoammonium phosphate in addition to superphosphate, and continued this manufacturing from 1972 to 1975. Normal superphosphate was combined with ammonia to produce monoammonium phosphate. The ammonification process produced nitrate. The macronutrient potassium was blended into the ammoniated phosphate product in various blends. The potassium source was potash, mostly potassium chloride, stored on-site, inside the plant, on concrete floors. In later years, two micronutrients, zinc and magnesium, were added to the ammoniated phosphate product blends at the plant. According to the plant manager and Agrico corporate purchasing agent, the macronutrient and micronutrient sources were purchased as pure products and not as by-products. The peak season for production at the Pensacola plant was March through June. Agrico Chemical Company operated the plant continuously until June 1975, when the plant was shut down (Geraghty & Miller 1993a and 1993b). Subsequently, the Agrico Chemical Company assets were sold to Freeport-McMoRan Resources Partners (Freeport McMoRan) in 1987.

The former plant property was sold to Margod, a Florida partnership, and F.A. Baird, Jr. in August 1977. The former plant buildings and process equipment were demolished in late 1979. After demolition, only the concrete foundations remained in place. A storage warehouse was constructed on the southern portion of the property adjacent to Fairfield Drive between 1979 and 1981, with additional warehouse construction taking place between 1981 and 1986. The Site property (except for the storage warehouse outparcel) was sold to Conoco, Inc. in 1995. The warehouse area is considered an out parcel of the original property. The majority of the remaining Site debris and concrete foundations was later consolidated and placed with the waste material under the RCRA cap during the OU-1 Remedial Action (RA) activities beginning in 1995. There are no permanent buildings from the original operations remaining on the Site. One foundation from an original Site building remains in the southwest portion of the property.

EPA conducted a hazardous waste site investigation at the facility in October 1983. The results of the study indicated that the on-site soils and on-site surface water impoundment were impacted with elevated levels of fluoride and lead. Groundwater was not sampled during that investigation. However, an effort was made to locate private shallow wells in the vicinity of the Site, and none were located.

The Florida Department of Environmental Regulation (FDER) (now Florida Department of Environmental Protection) (FDEP) conducted a groundwater assessment at the Site in January 1987 (Watts, et.al., July 1988) followed by a supplementary assessment in January and February 1989 (Watts, et.al., August 1989). The study concluded that the Site contaminants, primarily fluoride and sulfate, had impacted the area groundwater. While conducting the assessment for the former Agrico Site, FDER discovered contamination from the former Escambia Treating Company Site that had comingled with a portion of the Agrico plume.

EPA listed the Site on the National Priorities List (NPL) on October 4, 1989. Conoco, Inc. and Freeport McMoRan (parents of the Agrico Chemical Company) entered into an Administrative Order on Consent (AOC) on September 29, 1989. According to the terms of the AOC, the companies agreed to conduct source (soils) and groundwater investigations at the Site. The Site

was remediated starting in 1995, and remediation of impacted soils and sludges was certified complete by EPA in April 1997. Currently, Williams (on behalf of Agrico Chemical Company) and Phillips 66 are responsible for implementing the activities associated with the O&M Plans for OU-1 and OU-2.

In mid-2012, ConocoPhillips separated into two standalone companies. The environmental remediation activities conducted at the Agrico Site in the past by ConocoPhillips is now managed by Phillips 66.

2.5 OPERABLE UNIT ONE REMEDY

The first operable unit (OU-1) addressed the cleanup of the source on-site. **Figure 2** shows a 2013 aerial photograph of the Site and the current features associated with OU-1. A Record of Decision (ROD) for OU-1 issued by EPA Region 4 on September 29, 1992 selected the remedy to be implemented for on-site soils and sludges. The selected remedy was based on a Site remedial investigation and feasibility study, including a human health and environmental risk assessment, and soil and groundwater characteristics for the Site. Following the ROD issuance, actions by Conoco were initiated to re-acquire ownership of the property so that the remedy could be implemented.

In 1995, remedial construction activities began. Lead and arsenic-impacted soils and all sludge materials were collected and treated by solidification/stabilization using cement. Other fluoride-impacted soils were collected for consolidation. These consolidated soils and treated soils and sludges were installed in lifts and compacted in the excavation based on engineering designs and standards. The material was placed approximately 20 ft above the saturated groundwater level within the unsaturated, dry portion of the sediments underlying the Site. The source control was certified by EPA to be complete in April 1997.

On the surface, the material was covered with a 4-ft thick multi-layered engineered cap designed to prevent rainfall from contacting the underlying stabilized soils. The cap covers an area of 12 acres. The impervious nature of the cap causes storm water runoff volumes to be significantly greater than the volume generated before the construction of the remedy. For this reason, an elaborate system of piping and runoff collection devices was installed at the Site. The storm water collection system significantly minimizes runoff from flowing off the Site. Runoff generated on-site is collected and contained on-site by returning runoff to one of two storm water management impoundments constructed as part of the OU-1 remedial action. Because the north storm water impoundment is located upgradient from the stabilized soils, EPA required that a slurry wall be constructed between the north storm water impoundment and the stabilized containment area. The purpose of the slurry wall is to prevent infiltrating storm water from contacting the stabilized materials that are contained within the unsaturated subsurface containment area. A continuous limonite lense (a thin iron precipitation concretion) underlies the north storm water pond. This dense lense causes standing water for extended periods of time within this pond. Whereas, the south drainage pond is not underlain by the limonite layer and stormwater readily infiltrates into the subsurface beneath this pond so that the south pond is dry most of the time.

The following actions were performed as part of the OU-1 remedial action completed in April 1997:

- Excavated and solidified approximately 45,000 cubic yards of arsenic- and lead-impacted soil and contaminated sludge and soils from Site sludge ponds.
- Consolidated approximately 110,000 cubic yards of fluoride-impacted soils.
- Within excavation areas, rubble from building foundations and consolidated soils were placed in a layered fashion, with the uppermost portion of the excavation filled with solidified/stabilized soils and sludges.
- An engineered 4-ft thick, seven-layer cap, consisting in part of impervious fabric, High Density Polyethylene (HDPE) liner, and geotextile materials, was constructed over the stabilized soils within the containment area.
- Constructed a 700-ft long, 2-ft thick slurry wall upgradient of the containment area to prevent infiltrating storm water from contacting consolidated/stabilized soils.
- Installed a drainage collection system so that storm water generated on-site is contained on-Site in one of two storm water impoundments, preventing off-site runoff.
- Deed restrictions were attached to the property controlling future uses of the property, assuring protection of the containment structure.
- Security fencing with locked gates was installed to restrict unauthorized access to the property.
- Five monitoring wells were constructed to serve as long-term groundwater sampling locations to evaluate the effectiveness of the implemented OU-1 remedial action. These five monitoring wells were monitored to demonstrate the effectiveness through 2007. After 2007, the wells were integrated and combined with the OU-2 wells to form a site-wide groundwater monitoring network. The purpose of this site-wide network is to demonstrate the effectiveness of the monitored natural attenuation remedy for groundwater.

2.5.1 Operation and Maintenance

Regular activities are conducted for the Site in accordance with the EPA-approved Operations & Maintenance (O&M) Plan for OU-1 (September 20, 1996).

Elements of the O&M for OU-1 are as follows:

- General facility inspection and regular lawn care service for the Site. The grass is cut on at least a monthly basis between October and April and on at least a biweekly basis between May and September.
- Visual inspections of the drain inlet and outlet system are conducted after storm events with maintenance initiated, as required.
- Inspections of the Site are conducted following major storm events.

The inspection reports for 2014 are presented in **Appendix D**.

2.6 OPERABLE UNIT TWO REMEDY

The ROD for OU-2 was issued by EPA Region 4 on August 25, 1994. The OU-2 ROD presents EPA's selected remedial action for treatment of groundwater. The following discussion is based on the August 1994 ROD and includes the rationale for the selected OU-2 remedy. The OU-2 area is shown on **Figure 3** and was delineated to correspond to the previously completed irrigation well survey area. This area encompasses a larger area than the defined groundwater impact area. The OU-2 area is roughly bound by Palafox Street to the west, E. Cross Street to the south, Fairfield Drive to the north and Bayou Texar to the east.

The EPA selected remedy of monitored natural attenuation meets all EPA and Comprehensive Environmental Response, Compensation, and Liability Act (CERCLA) criteria. The remedy is protective of human health and the environment and complies with federal and state requirements that are legally applicable or relevant and appropriate to the remedial action. This remedy utilizes permanent solutions and alternative treatment (or resource recovery) technologies to the maximum extent practicable. The reduction of toxicity, mobility, and volume of the Site groundwater contamination has been controlled through source control (OU-1) and monitored natural attenuation (OU-2).

EPA views the monitored natural attenuation remedy as being at least more protective of human health and the environment than the pump-and-treat technology alternatives that were previously considered for this Site. This remedy avoids potentially adverse impacts associated with the groundwater extraction and treatment alternatives.

2.7 ANNUAL O&M TASKS FOR OPERABLE UNITS ONE AND TWO

The field activities associated with this 2014 Annual Report included the following O&M tasks:

- Annual groundwater sampling (November 2014) of 23 long-term groundwater monitoring wells (for both OU-1 and OU-2)
- Annual groundwater sampling of 17 periodic groundwater monitoring wells.
- Annual surface water sampling at two long-term locations in Bayou Texar.
- Annual surface water sampling at three surface water sampling locations within the primary groundwater discharge reach of Bayou Texar
- Annual advisory notices distributed to water well contractors, irrigation system installers, and pool contractors. This list of contractors was compiled from the NFWFMD list of licensed water well contractors, from Escambia County construction permit records, and from the telephone directory.
- Coordination and dissemination of site information to local, regional, and state agencies.
- Annual Florida Department of Transportation inquiry of construction activities scheduled for Fairfield Drive between the CSX overpass and the I-110 interchange.
- Annual review of NFWFMD well construction permits records to identify any potential new well construction downgradient of the Agrico Site. Also annual inquiry on status of NFWFMD well construction moratorium in the vicinity of the ETC and Agrico sites.
- Regular maintenance of property associated with the former Agrico Chemical Company (OU-1).

2.8 OTHER CONTAMINATION SOURCES IN THE VICINITY OF THE AGRICO SITE

Past sampling results conducted by ECUA for supply wells south of the Agrico area have indicated impacts to ECUA supply wells, which initiated an assessment by FDEP in the late 1990s. This assessment identified two areas, collectively referred to as Site 348. Both areas are located less than 0.5 miles south of the Agrico Site. One is the former fertilizer manufacturing operations known as Kaiser Fertilizer plant. The second is known as the former Southern Cotton Oil Company. This site was a fertilizer mixing and storage facility.

Reportedly, the sources which may have contributed to impacted groundwater affecting the F & Scott Streets Well, the East Plant Well, Well No. 6, Well No. 8, and Well No. 9 are still under investigation by FDEP. Three of these ECUA wells have been shut down and pumping discontinued (East Plant, Well No. 8, and Well No. 9) due to groundwater impacts. The COCs identified by FDEP at Site 348 are similar to the Agrico COCs, including radium 228 and ammonia. The Agrico plume was not implicated as a source or a factor in the impacts to these wells (Mactec, 2010). Additionally, the former Agrico plant was not associated with the either operations identified by FDEP that are related to Site 348.

No pumping effects are occurring within the current Agrico plume boundary that will cause the plume to move outside the natural groundwater flow path. This is verified by the past 16 years of water level measurements and potentiometric surfaces that show the natural groundwater flow direction remains consistently to the east, toward Bayou Texar. Consistency of groundwater flow patterns is also demonstrated by the individual water level trend data). The discontinued municipal pumping in the downtown area due to impacts from non-Agrico sources, also significantly decreases the potential of the Agrico plume to migrate from its current plume boundary. These conditions and other groundwater flow conditions negate the potential for future Agrico plume migration that could affect any public water supply well.

Water level measurements collected during the past 16 years indicate that the remaining irrigation pumpage occurring within the OU-2 area is not significantly affecting the direction of groundwater flow. The primary groundwater flow controls are natural, including Bayou Texar, which functions as the eastern discharge boundary for the Agrico plume.

3.1 HYDROGEOLOGIC FRAMEWORK OF THE SAND-AND-GRAVEL AQUIFER

The vertical profile of the Sand-and-Gravel aquifer consists of beds of sand and gravel interbedded with beds of silt, clay, and fine sand sediments (**Figure 4**). The permeability of these beds is variable, both laterally and vertically. However, the subsurface sequence can be divided into three distinct zones. These zones vary greatly in thickness and lithology throughout Escambia County. In addition, individual beds of sand or clay within these zones are highly discontinuous, resulting in considerable heterogeneity within the zones. The major zones are the surficial zone, the low-permeability zone, and the main producing zone (Roaza, et al., 1991).

3.1.1 Surficial Zone

The surficial zone consists of the uppermost layer of sediments. It contains the unsaturated zone and the shallow surficial water table. The surficial zone varies in thickness, but is generally less than 100 ft thick beneath the OU-2 monitoring area. The surficial zone consists primarily of quartz sand ranging in size from fine sand to gravel. Thin beds of limonite-cemented sandstone also occur. The zone contains thin beds of clay and silt that are highly discontinuous. These low-permeability beds occur both in the unsaturated and the saturated portions of the zone. Groundwater within the surficial zone primarily moves downward through the underlying lower-permeability zone to the main producing zone of the aquifer.

3.1.2 Low-Permeability Zone

The low-permeability zone underlies the surficial zone and is composed of sediments with overall lower permeability characteristics than sediments above or below the zone. This zone forms a semi-confining layer and acts to restrict the vertical flow of groundwater between the overlying surficial zone and the underlying main producing zone. The actual lithology of this zone is variable, ranging from poorly sorted sand and silt to sandy clay to clay beds. Locally, well-sorted, water-bearing sands can also occur within this zone. Poor sorting and a higher percentage of clays and silts distinguish this zone from the other zones. The thickness of this zone in the subsurface underlying the facility ranges from about 20 to 50 ft (Roaza, et al., 1993).

The thickness and lithology of this zone is important because of its effect on vertical permeability. The low vertical permeability of this zone maintains the hydraulic head difference between the surficial and main producing zones in certain areas. This head difference imparts the vertical gradient responsible for the transport of dissolved constituents downward from the surficial zone to the main producing zone beneath the OU-1 Site (see **Figures 5 and 6**).

3.1.3 Main Producing Zone

The main producing zone is the most productive portion of the Sand-and-Gravel aquifer and is the zone tapped by most water supply wells. The main producing zone is the deepest portion of the aquifer. The groundwater within this zone exists under semi-confined conditions. The main producing zone consists of moderate to well-sorted sand and gravel, along with minor interbedded layers of sandy clay and clay. Locally and regionally, variations occur in the lithology of the main producing zone. Changes with depth tend to be gradual and include varying grain size distribution and changes in the degree of sorting.

The clay beds interbedded within this zone generally constitute 10 to 40 percent of the thickness. In some areas, the productive intervals can be correlated and appear to be continuous over a distance of many miles. The saturated thickness of the main producing zone near the Site is approximately 100 ft.

The main producing zone is recharged by leakage through the low-permeability zone. The actual amount of recharge is determined by the hydraulic head difference between the surficial zone and the main producing zone, the vertical permeability of the low-permeability zone, and the presence of any pumping wells. Groundwater from this zone discharges into Bayou Texar from east and west directions, which represents a discharge boundary for groundwater in OU-2.

3.2 HYDRAULIC HEAD DIFFERENCES AND GROUNDWATER FLOW BOUNDARIES

Within the former Site boundary (OU-1), the hydraulic head for the surficial zone is slightly higher than the hydraulic head in the main producing zone, which causes the surficial zone to infiltrate and recharge the main producing zone. This causes the plume emanating from the Site to be transported and diverted to the main producing zone within about 0.4 mile of the Site. For this reason, the surficial zone plume has limited areal extent; and with source control and ongoing source depletion, significant trends toward decreasing concentrations within the plume have occurred in the surficial zone. Near the bayou, the main producing zone hydraulic head is slightly higher than the surficial zone, causing the main producing zone to discharge into the bayou (see **Figures 4, 5, and 6**). The bayou is a discharge boundary; therefore, groundwater from the west and east directions of Bayou Texar discharge into the bayou. This creates a boundary condition for the groundwater flow and plume transport. The Agrico plume discharges from the west into Bayou Texar along with the westerly groundwater flow component. Groundwater from the east (at least as far away as the Pensacola Airport) also discharges to the bayou. **Figure 4** shows the hydrogeologic conceptual model from the Agrico Site to Bayou Texar.

Within OU-2, groundwater generally flows laterally and vertically (both upward near the discharge boundary and downward in recharge areas) within the Sand-and-Gravel aquifer. The overall direction of groundwater flow is easterly toward Bayou Texar. Head variations between zones are important in controlling the vertical direction of groundwater flow. **Figures 5 and 6** show the potentiometric surfaces on November 10, 2014 for the surficial zone and main producing zone, respectively. These surfaces are similar to those measured historically.

The flow direction downgradient of the Agrico Site is primarily controlled by the Bayou Texar discharge boundary conditions. Near the bayou, vertical head differences between aquifer zones cause groundwater to flow vertically from the main producing zone upwards, and groundwater discharges to the bayou. There is evidence that the bayou is a discharge boundary for both the surficial and main producing zones of the aquifer, and that groundwater does not pass under the bayou as underflow. Water levels within both zones to the north, east, and west of Bayou Texar indicate a groundwater flow direction toward the bayou boundary.

3.3 RAINFALL CONDITIONS

Rainfall records collected at the Pensacola Airport indicate that 2014 was characterized by about +18 inches above average normal rainfall (average about 61.87 inches based on 1900-2014

period of rainfall record), with a total accumulation of 80.17 inches during 2014. For the past 10 years, extremes in rainfall were observed. There was abundant rainfall in 2005 followed by a drought in 2006. During 2006, the total rainfall was 45.26 inches, or 16.27 inches below normal. The hurricanes during 2005 produced a very wet year, with an annual total of 87.32 inches, or 25.79 inches above normal.

A significant storm event occurred in April 2014. Between April 29 and April 30, 2014, the Pensacola area received rainfall totals ranging from 16 to 24 inches. Widespread flooding occurred in many parts of the county and within the vicinity of the Site. The rain ended about 6:30 am on April 30, 2014. The Site was inspected at 14:15 pm on April 30, 2014. The south drainage pond had topped the pond banks. Flood water was contained north of the Fairfield Drive railroad overpass and the railroad right-of-way. Flooding extended along the southern annex road to just east of the storage warehouse property where the stormwater pond on this out parcel also topped the pond's banks. The north pond was full and topping banks but flooding contained on Site. An inspection of the cap area indicated that the cap was intact and no damage occurred.

Figure 7 presents the annual rainfall data for the period of record from the NOAA Pensacola station. Also included on **Figure 7** is a graph showing the cumulative departure from normal rainfall. This graph, in general, mimics groundwater level trends. For 2003-2005, the cumulative departure from normal data indicates that groundwater levels were on the rise, reaching a high in 2005. Since 2005, the annual accumulation has been less so the departure from normal has declined but the overall rainfall for the past 5 years has been above normal. The pattern is reflective more of a wet cycle than a dry trend.

An annual advisory notice (**Appendix C**) is sent to contractors conducting work in southern Escambia County. The advisory notice is sent to water well contractors, irrigation system installers, and pool contractors, informing them of groundwater conditions in the vicinity of the Agrico Site. The contractor listing is updated annually from yellow pages listing, well contractor licenses listing, and returned “not deliverable – no forwarding address” notices. For the purposes of the advisory notice, the area identified is approximately bounded on the north by Fairfield Drive, on the west side by Palafox Street, on the south side by Bobe Street, and on the east side by Bayou Texar. The notice states that the construction of wells in this area, including lawn irrigation wells, may be restricted due to the occurrence of impacted groundwater. The contractors were advised to contact the NFWFMD, the Northwest District of FDEP, or the Escambia County Health Department for further information. The annual advisory notice was distributed on October 16, 2014 to the contractors listed in **Table 6**. **Table 6** was revised to reflect new contractors and changes in information since last year.

Currently, institutional controls are in place that provide protection to the public drinking water supply. As part of the OU-2 remedy, periodic checking is performed to determine the status of institutional controls established by local, regional, and state agencies. In order to verify that controls remain in place, annual letters are sent to the various agencies requesting information on any changes or proposed changes. Since these agencies also receive reports regarding groundwater conditions, the purpose of the communications are: 1) to address any questions the agencies have concerning groundwater conditions and 2) to receive a status report from the agencies concerning the existing regulations, planned rule changes, or new regulations which control groundwater use in the Agrico OU-2 area.

Institutional controls include the following:

1. Well construction and consumptive use approval (NFWFMD)

On February 22, 2001, the NFWFMD Board passed a moratorium on drilling new wells, including irrigation wells, in the Agrico and Escambia Treating Company areas. The moratorium remained in effect during 2014 and is expected to continue into the future since there is no expiration date for the moratorium.

The moratorium affects the west side of the bayou only because the Agrico plume does not extend across the bayou due to hydrogeologic boundary flow conditions (the bayou receives groundwater recharge from groundwater flows from both the east and west). Thus, the bayou serves as a flow boundary to the Agrico plume and prevents any flow farther east.

This moratorium is governed by the NFWFMD Rule 40A-3 which is incorporated into the rule as 40A-3.055 Prohibitions:

- (1) The construction of certain, specified types of water wells shall be prohibited in the following areas:
 - (a) Escambia Treating and Agrico Superfund Sites, South Escambia County – permitting of all water wells other than monitor wells or aquifer restoration wells shall be prohibited with the area inside and bounded on the west by CSX railroad corridor, on the east by Bayou Texar, on the south by East Cross Street projected in a straight line until it intersects Bayou Texar, and on the north by Hyatt Street, North

Davis Highway, Wynnehurst Street, Kenneth Street, Boxwood Drive, Ash Drive, Ninth Avenue, and Hillbrook Way projected in a straight line until it intersects Bayou Texar.

2. Irrigation systems approval (ECHD):

A letter dated February 2, 2005 was received from the Director of the Environmental Health Services, Escambia County Health Department, indicating that the ECHD no longer approves or disapproves irrigation systems. The coordination with the City of Pensacola Building Inspection office for installation of irrigation systems is no longer a function performed by ECHD.

Based on this information, the only regulatory control as it relates to groundwater within the OU-2 area is managed by the Northwest Florida Water Management District in their well construction permit program.

3. The location of the Agrico plume is well defined, and ECUA is on the distribution list for reports related to the Agrico plume. Because of this information, a future well location in the vicinity of the Site is highly improbable.
4. Existing wells are regularly sampled by ECUA, which reports these data as part of their permits to FDEP. Therefore, any potential impacts to the supply wells caused by existing plumes can be assessed. For example, existing impacts from Site 348 are currently under assessment by FDEP as a result of analytical results from ECUA wells (F & Scott Well, East Plant Well, Well No. 8, and Well No. 9).
5. The Northwest District for the Florida Department of Environmental Protection has designated the area that encompasses both the Agrico plume area and the ETC plume area as a contaminated area under Chapter 62-524, Florida Administrative Code (FAC). The area is the same as the OU-2 area defined on **Figure 3**. The FDEP designated area also includes a portion to the north of the Agrico OU-2 area that is associated with the ETC plume. Chapter 62-524 FAC is closely tied to the NFWFMD well construction permit program since the designated area requires more stringent processes by the permit applicant before a well construction permit can be issued by the NFWFMD. Since there is a moratorium on the issuance of a well construction permits within the designated area, the moratorium provides more stringent restrictions than Chapter 62-254.
6. On December 10, 2014, the NFWFMD well construction database was queried and no new wells were found confirming no new well construction for the moratorium area.
7. Deed restrictions on Agrico Property provide for certain future land use and subsurface limitations.

On December 3, 2014, a memorandum was distributed to:

- Alex Webster– FDEP, Northwest District, Pensacola; as of February 2014,
- Walsta Jean-Baptiste - FDEP, Tallahassee
- Tim Haag - Emerald Coast Utilities Authority
- Tom Brown– NFWFMD
- Thaddeus Cohen - City of Pensacola

- Mark Spitznagel and Robert Merritt - Escambia County Health Department
- Keith Wilkens – Escambia County, Neighborhood and Environmental Services
- Alan Hagans – Florida Department of Transportation, District Three (Chipley)

A copy of the memorandum was also distributed to Scott Miller, Project Manager, EPA, Region 4.

On December 3, 2014, FDOT was sent an annual inquiry regarding construction activities. On December 3, 2014, Alan Hagans (FDOT-Chipley), District 3 Contamination Impacts Coordinator, responded to the inquiry by indicating that all the planned 2015 projects and those in the 2015- 2020 Five Year Plan were non-intrusive activities (**Appendix C**).

5.1 GROUNDWATER SAMPLING

Annual groundwater samples were collected from the long-term monitoring network in November 2014. The total number of monitoring wells sampled in November 2014 includes 14 surficial zone wells and 25 main producing zone wells. Monitoring well, AC-28D was not sampled. The URS sampling team misidentified another unknown well as AC-28D that was subsequently sampled but since the results were not for AC-28D, the results were not included in this report. The unknown well is a shallow well that lies between AC-28D and AC-9D2 and is not associated with the Agrico well network (either currently or historically).

Groundwater samples were collected in accordance with the FDEP's SOPs for Field Sampling (Revised March 1, 2014, effective July 30, 2014). Sample collection techniques, sample documentation, preservation requirements, sampling equipment decontamination procedures, the types and number of quality assurance/quality control (QA/QC) samples collected, and specifications that allow for the verification of the precision, accuracy, and completeness of data collected are all detailed in the SAP (O&M Plan, November 1998).

5.1.1 Monitoring Well Network

Monitoring Locations

Monitoring locations for wells installed either in the surficial or main producing zones of the Sand-and-Gravel aquifer are shown on **Figure 1**. Since this sampling event occurred during the Five Year Review period, both long-term and periodic monitoring wells were sampled. **Table 1** lists the wells in the Agrico monitoring network, including long-term monitoring wells which are sampled annually (includes measuring groundwater levels) and periodic monitoring wells where groundwater levels are measured annually and wells are sampled during the Five-Year Review. **Table 2** presents the well construction details for all monitoring wells associated with the groundwater monitoring program for the Agrico Site.

Sampling Constituents

Groundwater was sampled in 2014 for the following constituents of concern in both the surficial and deep zones:

- Fluoride
- Arsenic, Total (only in monitoring wells, AC-2S and AC-3S)
- Chloride
- Sulfate
- Nitrate
- Radium 226 and Radium 228 (naturally occurring); also reported as the sum of combined radium 226 + 228 results

Lead and arsenic are no longer included as analytical parameters for all groundwater samples. Arsenic is only analyzed in AC-2S and AC-3S wells.

5.1.2 Well Purging

Each monitoring well associated with the monitoring network was purged and sampled with an electric, 2-inch, stainless steel, low-flow submersible pump and polyethylene tubing. All wells were purged a minimum of one and a half well volumes before sampling. When a well was purged dry, it was allowed to recover before sampling. Field parameters, including pH, specific conductivity, turbidity, temperature, dissolved oxygen, and oxidation reduction potential were collected from all wells during purging. A summary of groundwater field parameters is presented in **Table 3**.

5.1.3 Investigation Derived Waste

Development and purge water pumped from each well was collected in a temporary storage tank installed on a field trailer. When the mobile storage tank was filled to capacity, the recovered water was transferred to a larger temporary storage tank located on the Agrico OU-1 Site. In accordance with the FDEP guidelines, the wastewater is managed as industrial waste.

The IDW (non-hazardous groundwater purge water) is transported by Liquid Environmental Solutions (LES) to their Mobile, Alabama facility (EPA ID Number ALO 000 859 421). There it is treated and disposed of in accordance with state and federal regulations. The purge water, 5,500 gallons, was picked up and transported for disposal on November 19 and 25, 2014.

5.1.4 Water Level Measurements

On November 10, 2014, groundwater levels were measured in all Agrico monitoring wells for OU-1 and OU-2 (25 main producing zone wells and 14 surficial zone wells). Water levels were collected prior to purging in wells scheduled for sampling. These water level measurements were used to evaluate water level fluctuations and groundwater flow direction. All measurements were used to prepare potentiometric surface maps for the surficial and main producing zones of the Sand-and-Gravel aquifer.

Static groundwater levels from all identified monitoring wells associated with the Agrico Site (**Figure 1**) were measured to within ± 0.01 ft. Measurements were collected with an electronic water level tape using the top of casing (TOC) as the measuring point. The measurements were subsequently referenced to the TOC elevations and used to calculate groundwater elevations. This information was used to confirm that groundwater flow directions remain similar to previous years. Groundwater elevations are presented in **Table 4**.

5.2 BAYOU TEXAR SAMPLING

Five surface water sampling locations were selected in specific areas of Bayou Texar based on the following information: (1) concentration pattern of the Agrico groundwater constituents moving downgradient toward Bayou Texar; (2) previous results of work performed in the bayou (Entrix, 1993a, 1993b, and 1993c); and (3), results of sampling during August 2008 and May 2009. Four of the sampling locations were within the primary groundwater discharge reach of Bayou Texar. One sampling location was downstream of the Agrico plume discharge area (**Figure 1**).

Surface Water Sampling

Two near-bottom surface water samples (ACSW-1 and ACSW-2 (**Figure 1**)) have been collected annually as part of the long-term monitoring O&M network to assess the quality of surface water in Bayou Texar. Surface water sample ACSW-1 is collected within the segment of the brackish bayou known to receive groundwater discharge from the plume and surface water sample ACSW-2 is also collected in the brackish bayou downstream of the identified impacted discharge segment.

Three near-bottom surface water samples (BT-02, BT-107, and BT-127) are located within the vicinity of ACSW-1 (**Figure 1**). These locations became part of the surface water network in November 2010.

All sampling points are in brackish water locations that are tidally influenced. Saline water from Pensacola Bay is drawn into the bayou during high tide. The locations of the surface water sampling are shown on **Figure 1**. All surface water samples are collected at low tide.

Surface water sampling is conducted in accordance with the November 1998 Sampling and Analysis Plan (SAP). The samples are collected from a boat. A discrete sample is collected at the deepest section of each transect. Samples are collected using a peristaltic pump and disposable polyethylene tubing attached to PVC pipe, which is lowered to the appropriate depth. The depth of each sample collected is approximately 6 inches above the floor of the bayou. Field parameters, including pH, specific conductivity, turbidity, and temperature, are collected in conjunction with the surface water samples.

A summary of the 2014 surface water field parameters is presented in **Table 5**.

Sampling Constituents

The following constituents were analyzed for in surface water samples ACSW-1 and ACSW-2 in November 2014:

- Fluoride
- Chloride
- Sulfate
- Nitrate
- Radium 226 and Radium 228 (naturally occurring); reported also as the sum of combined radium 226 + 228 results.

For sampling locations BT-02, BT-107, and BT-127, fluoride was the only constituent analyzed.

5.3 CHEMICAL ANALYSES

Groundwater and surface water samples collected for the 2014 (November) event were submitted to TestAmerica Laboratories, Inc. (TA), Tallahassee, Florida. All analyses were performed by the Tallahassee and Pensacola laboratories (Certification No. E81005 and E81010, respectively), except radium 226 and radium 228 which was analyzed by TA Richland (Certification No. E87829). All analyses were performed pursuant to NELAP requirements. TA is a certified analytical laboratory by EPA, and the State of Florida. All analytical reports were prepared in

accordance with TA's Level III report format. The following analytical methods were used to analyze the specific media in accordance with SW-846.

CONSTITUENT	ANALYTICAL METHOD
Fluoride	340.2
Chloride	300.0 (Ion Chromatography)
Sulfate	300.0 (Ion Chromatography)
Nitrate	353.2 Nitrate by calculation
Arsenic	6010B
Radium 226	903.1 Mod (RL-RA—001)(Alpha Scintillation)
Radium 228	904 Mod (RL-RA—001)(Gas Proportional Counters)

5.4 SAMPLING RESULTS

The November 2014 sampling activities completed the annual sampling requirement for the Agrico Site. A total of 39 monitoring wells were sampled. Figure 1 shows the sampling locations for the Agrico Site.

Field parameter details from the November 2014 sampling event are shown in **Table 3** and historical trends are shown on graphs within this section.

Details of Bayou Texar sampling results are presented in **Table 5** and **Table 9**.

The groundwater sampling results for the identified COCs detected in the surficial and main producing zones for the site-wide monitoring wells are discussed in this section. Details of results are provided in **Table 8**, **Figures 8**, and **Figure 9**.

Appendix A contains all laboratory analytical reports from the November 2014 sampling event.

5.5 GROUNDWATER FIELD PARAMETERS

In addition to the Agrico COCs, several field parameters are collected as part of the groundwater sampling program (**Table 3**). These parameters include water temperature, pH, dissolved oxygen, turbidity, specific conductance, and the oxidation-reduction potential. An understanding of these parameters can be important in understanding the relationships between COC concentrations and field parameter ranges in values, in defining and understanding ranges of background concentrations, and in evaluating overall COC concentration trends. A more detailed discussion of selected field parameters, including specific conductance, pH, dissolved oxygen and the oxidation-reduction potential follows.


5.5.1 Specific Conductance

Specific conductance is a measure of how well a water sample conducts an electrical current. It is a straightforward measurement that can be made with reasonable accuracy in the field. It is, therefore, often used as a proxy for the total dissolved solids (TDS) analysis. The conductance values are collected in micro Siemens per centimeter units (uS/cm).

Within the main producing zone plume, the specific conductance values were generally greater than 250 uS/cm and currently range as high as 1,381 uS/cm. Outside of the plume, conductance ranged from a low of 70 to less than 250 uS/cm, which are within in the range of background values. As groundwater recharges the Sand-and-Gravel aquifer in Escambia County, it encounters relatively little soluble material, and the water has characteristically low hardness (soft) and is relatively unmineralized. The aquifer is composed of mostly quartz sand, which is not very soluble. The abundant rainfall and the aquifer's high permeability keep the groundwater moving, and the residence time is such that the water does not tend to contain a significant quantity of dissolved mineral matter. Specific conductivity within the surficial zone of the sand-and-gravel aquifer appears to be within the range of background for all shallow well samples.


Surficial Zone Groundwater:

The shallow groundwater conductivity vs. time chart is shown below.

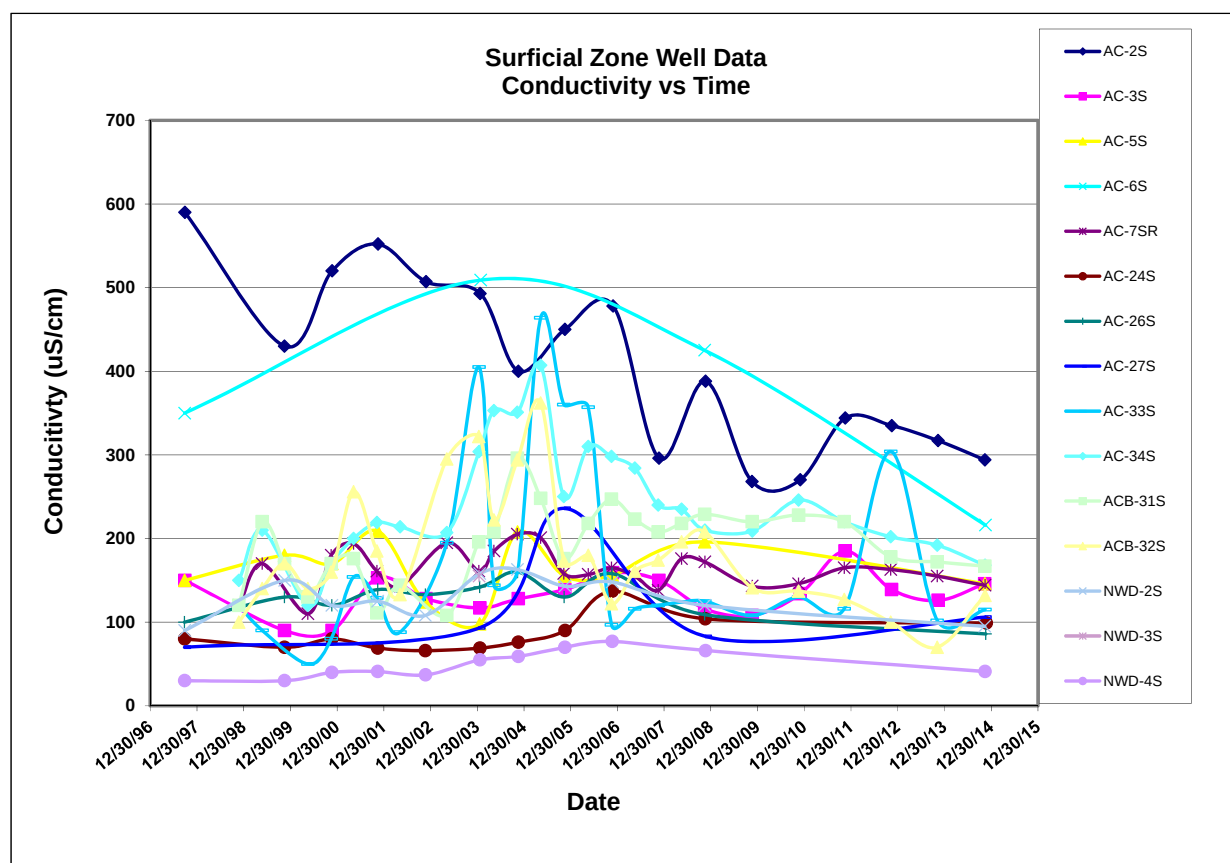

Main Producing Zone Groundwater:

The deep groundwater conductivity vs. time chart is shown below.

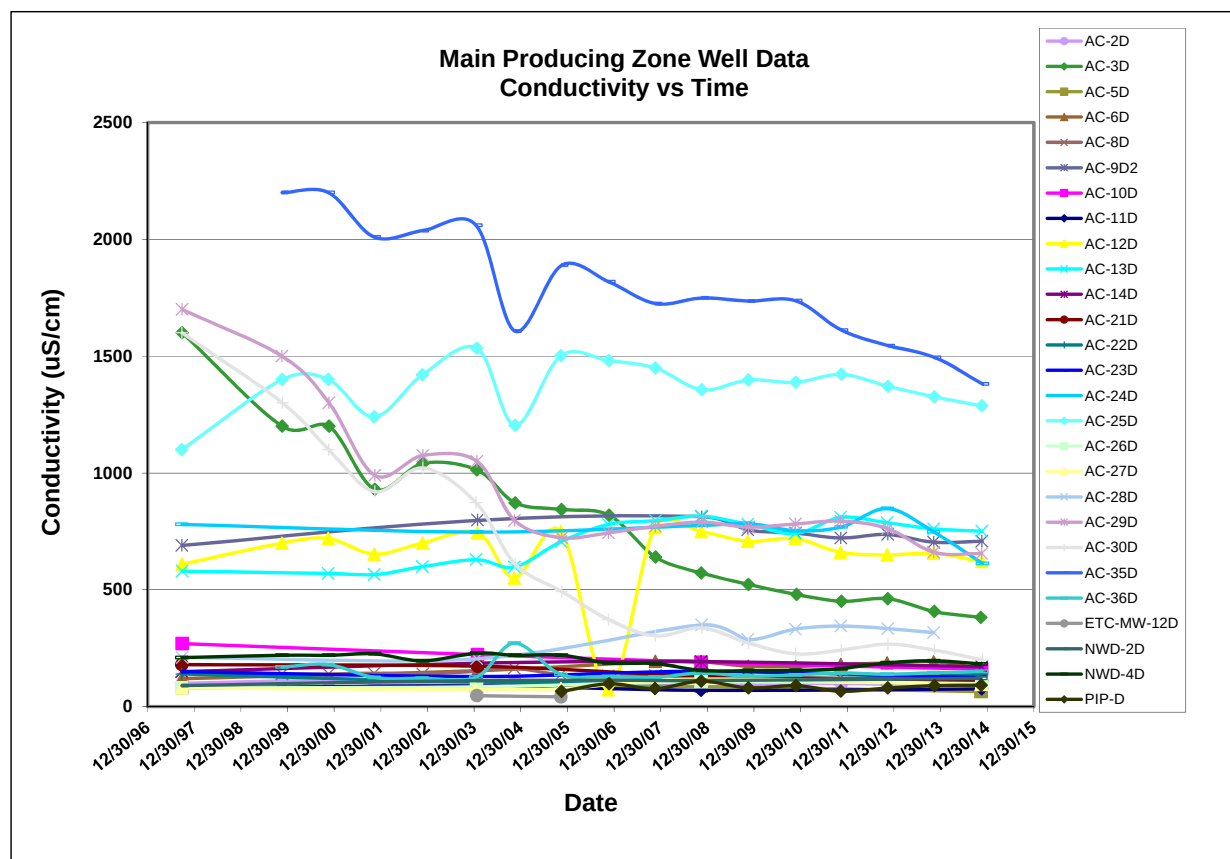

5.5.2 pH

Groundwater pH within the Sand-and-Gravel aquifer underlying Escambia County reflects generally acidic conditions (less than 7.0 standard units, su). The reason for the acidic conditions is that rainwater has a pH generally less than 5.5 su in the Escambia County area (Trapp, 1973). This low rainfall pH, coupled with the high recharge from rainfall to the aquifer and the relatively inert nature of the sandy sediments that comprise the aquifer, yields a groundwater pH that is acidic.

Information from the U. S. Geological Survey (USGS) collected in Escambia County was reviewed for groundwater pH data. The period 1968 to 1980 was an extensive data collection time in Escambia County by the USGS. A total of 222 observations of pH (Coffin, 1982) were collected from 69 sites distributed throughout southern Escambia County. The sites were located to characterize general groundwater conditions and were not associated with any assessment of known contamination sites. The range of pH for the 222 observations was 3.4 to 8.9 su. The average pH for the 12 year period was 5.28 su. Background pH conditions are variable and are controlled by local recharge conditions, seasonal rainfall patterns, and whether the groundwater is from a shallow or deep source. Generally, the groundwater occurring at shallow depths (less than 100 ft below land surface) is more acidic than deeper occurring groundwater that tends to approach neutral conditions.

In addition to the above pH data for groundwater, a review was conducted of long-term pH data for a surface water gaging station on the Perdido River at Barrineau Park. The Perdido River is the westernmost boundary for Escambia County. The station is located about the middle portion of the county and shows that base flow streamflow conditions have pH values generally less than 5 su. Since the base flow of this stream, as well as, other streams in the county is derived from groundwater, this is another line of evidence that groundwater pH conditions are acidic.

Geochemically, pH is an important factor in understanding the occurrence of radium in the groundwater beneath Escambia County. Historically, the impacts from radium are well documented within the county and many of these exceedances are not associated with known contaminated sites. As the USGS data indicates, the groundwater can have a naturally occurring background value as low as 3.4 su. Likewise, the data showed that 101 of the 222 observations of pH were less than 5 su. This indicates acidic background conditions existing for the groundwater in southern Escambia County.


Exceedances of radium in Escambia County are believed to be associated with naturally occurring thorium minerals in the subsurface. USGS research (Zapecza and Szabo, 1988) at sites throughout the eastern United States indicate that when groundwater pH is approaching 4.5 to 5 su or lower and thorium is present, a process known as recoil mobilization is possible. This recoil process allows radium 228 to be released to the groundwater from the minerals containing thorium. For Escambia County as a whole, it is possible to activate this release with what is considered background groundwater conditions.

The acidity reflected by low pH in groundwater within the Agrico plume is most likely the result of former operational processes whereby wastewater was disposed in the former on-site impoundments at the former Agrico facility (Watts, et al, 1988). Since the completion of the OU-1 Remedial Action, the pH of shallow groundwater conditions within the plume has improved and currently is between 4.60 and 6.47 su. The current range of pH values within the main producing zone plume is 3.99 to 4.57 su. Upgradient of the former Site, the designated off-site upgradient monitoring well, PIP-D shows a current groundwater pH of 4.79 su.

The trends in groundwater pH from the Agrico network monitoring wells are reflected in the following graphs for the surficial and main producing zones of the aquifer.


Surficial Zone Groundwater:

The surficial zone groundwater pH vs. time chart is shown below.

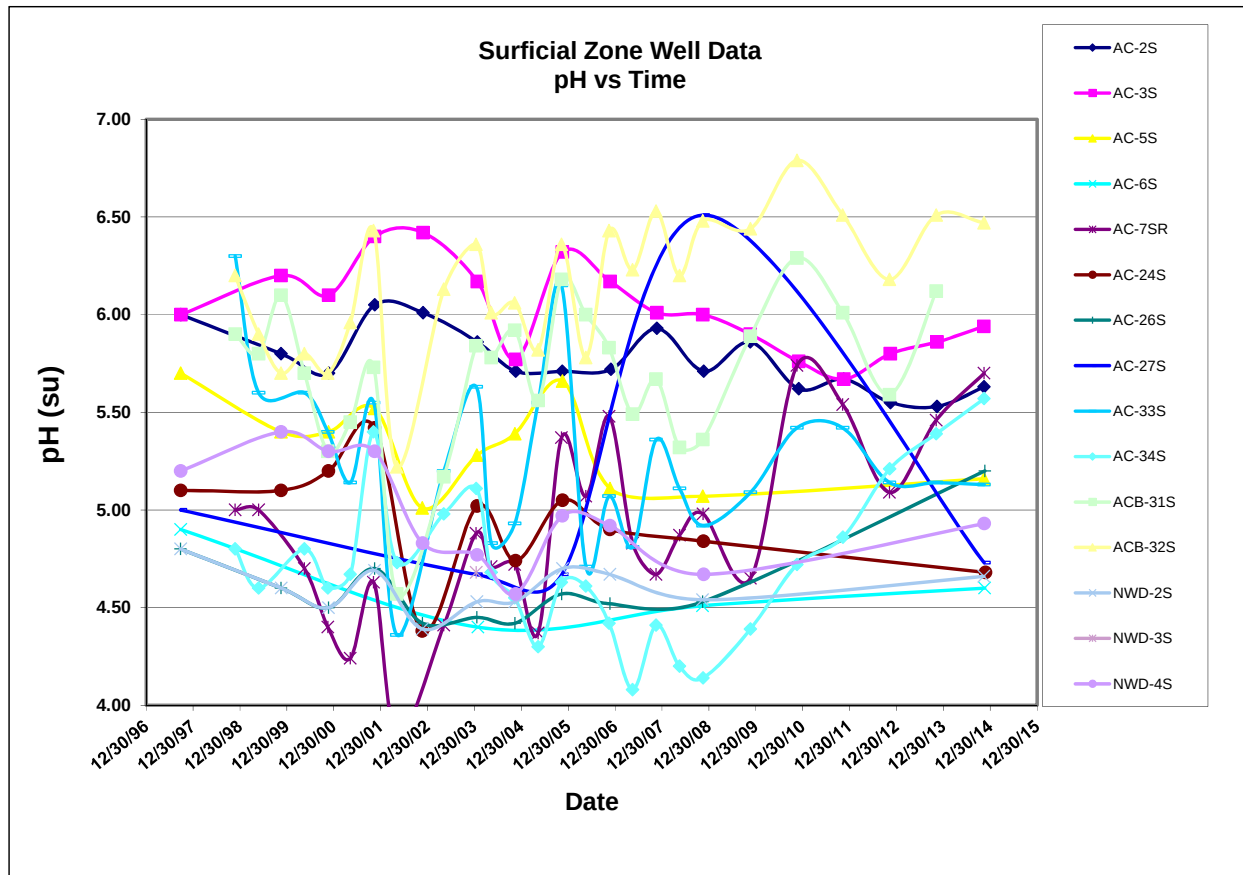


Main Producing Zone Groundwater:

The main producing zone groundwater pH vs. time chart is shown below.

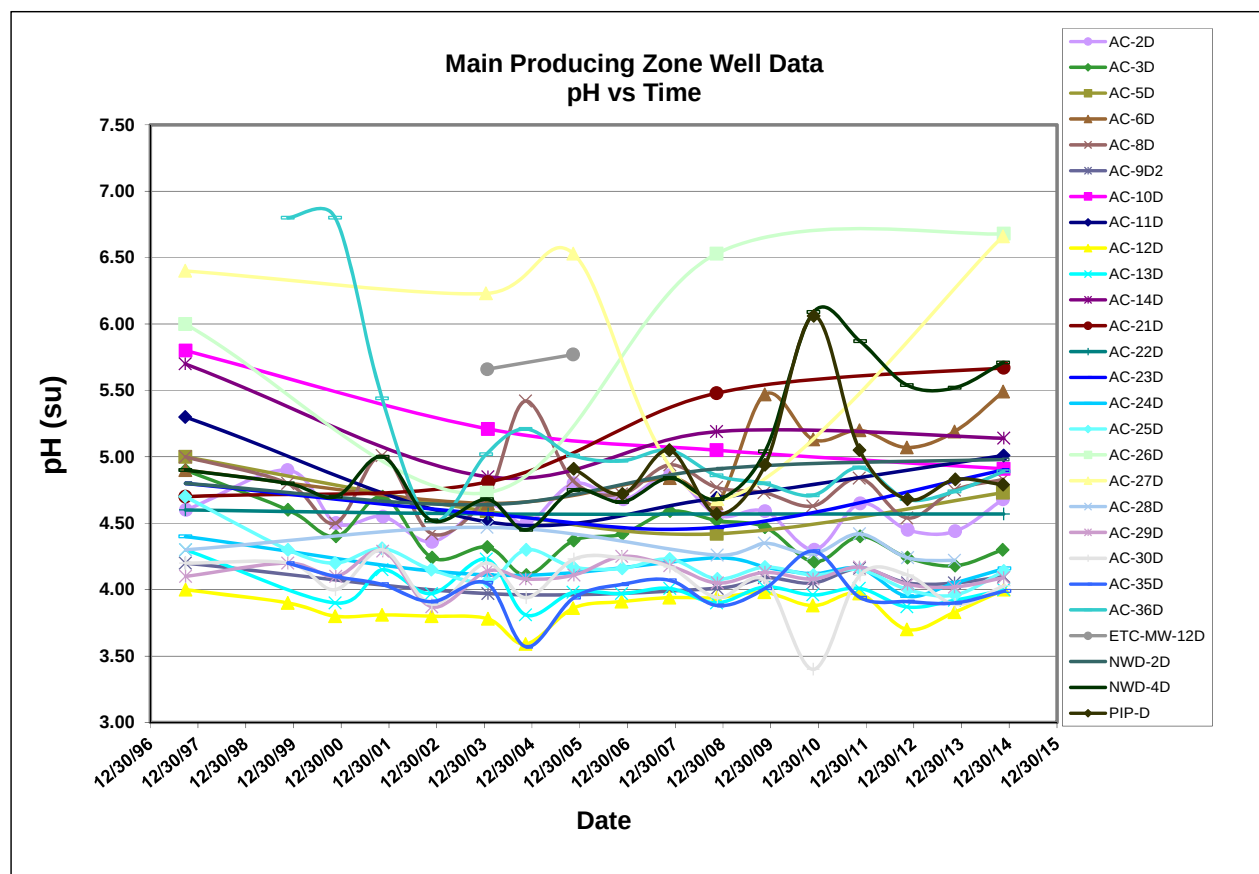

The following graph is updated from the original graph (URS, 2007) to show data from all sampling events conducted for the Agrico Site. The data points marked as red diamonds represent results from the November 2014 sampling event. The graph shows the relationship between pH and radium 228 concentrations whereby as the groundwater pH approaches about 5 to 4.5 su or lower, the radium 228 concentration generally exceeds the 5 pCi/L drinking water standard for combined radium 226 + radium 228. It should be noted that the use of a pH of 4.5 su to demonstrate this relationship is within the range of pH that the recoil process generally is activated. The recoil activation range is plus or minus a pH of 4.5 su (Zapacza and Szabo, 1988).

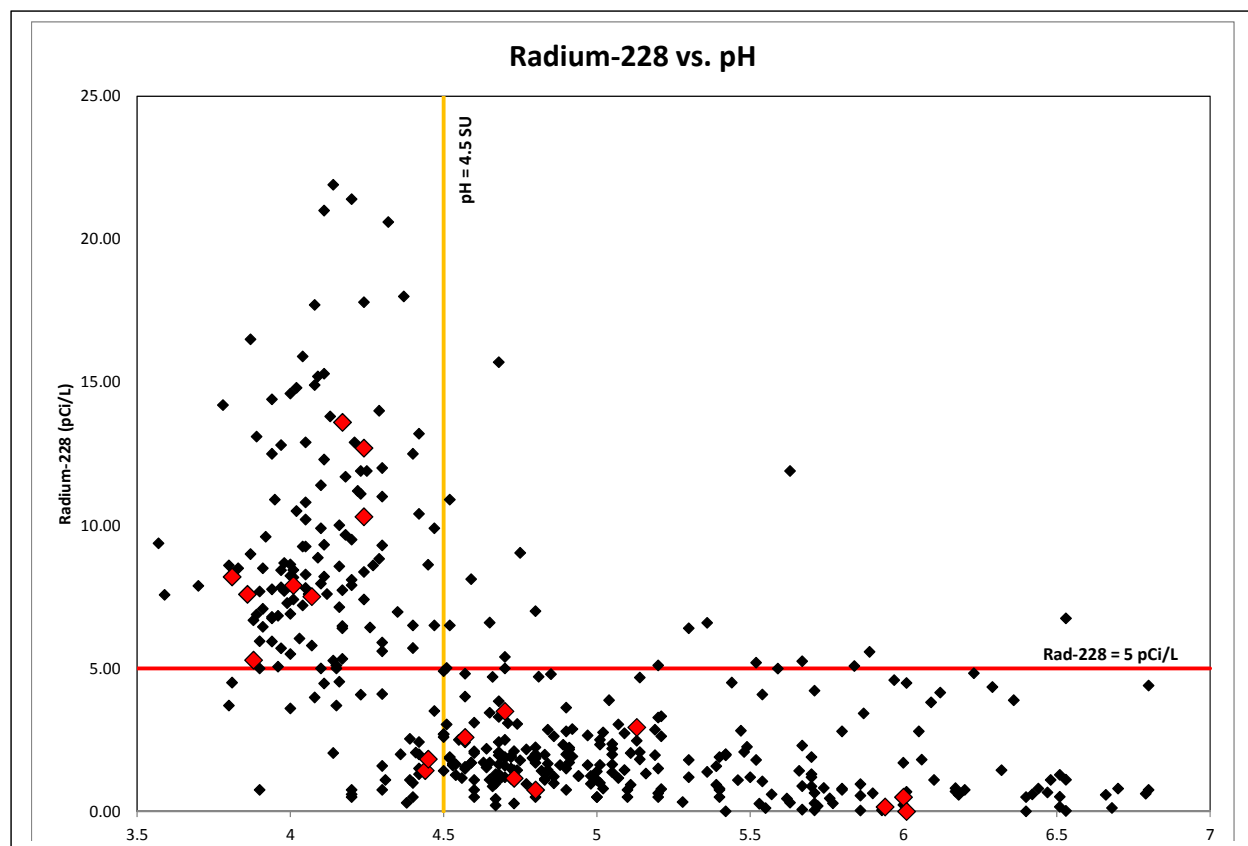


Acidic groundwater conditions are also associated with Site 348. This site is located approximately 3,000 feet south of the Agrico Site. Assessment reports for Site 348 (MACTEC, 2010) present pH and radium 228 data which show that low pH conditions result in exceedances of the radium standard of 5 pCi/L for combined radium 226 and radium 228. Data from Site 348 indicates that radium 228 is the predominant isotope present in the groundwater beneath Site 348. Site 348 is located in close proximity to nearby former municipal water supply wells. A 2008 sample collected by ECUA from the F & Scott well reported a combined radium 226 + 228 concentration of 5 pCi/L (www.ecua.fl.org – 2010 Water Quality Report).

5.5.3 Dissolved Oxygen

The solubility limit (saturation concentration) of oxygen in water (in equilibrium with air) at the temperatures, pressures, and salinities encountered in shallow groundwater at the Site is on the order of 8.5 mg/L (ppm). Oxygen's solubility limit increases as temperature decreases. Dissolved oxygen concentrations greater than 1 mg/L (aerobic conditions) are considered to support aerobic microbial metabolism, and conversely, DO concentrations less than 1 mg/L (anaerobic conditions) support anaerobic microbial systems.


Surficial Zone Groundwater:

The shallow groundwater DO vs. time chart is shown below.

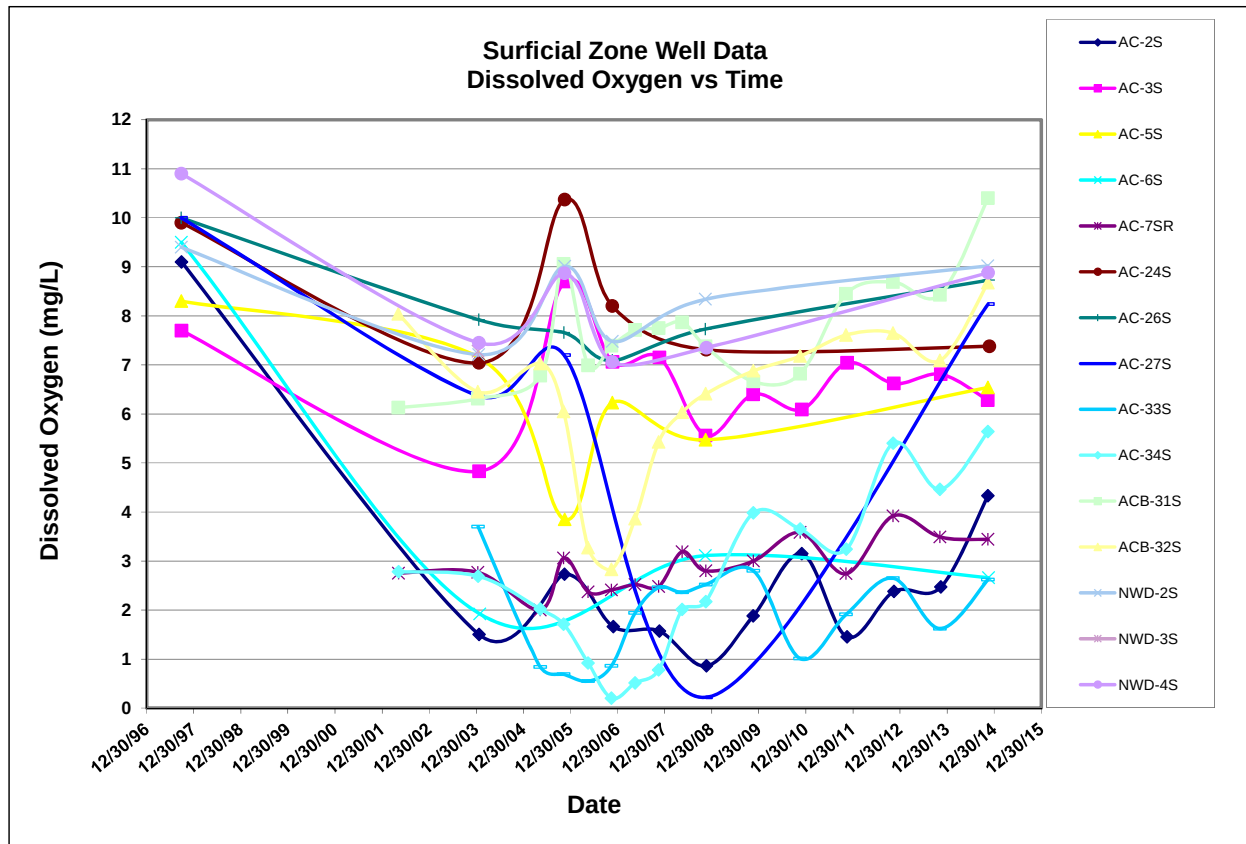

Main Producing Zone Groundwater:

The deep groundwater DO vs. time chart is shown below.

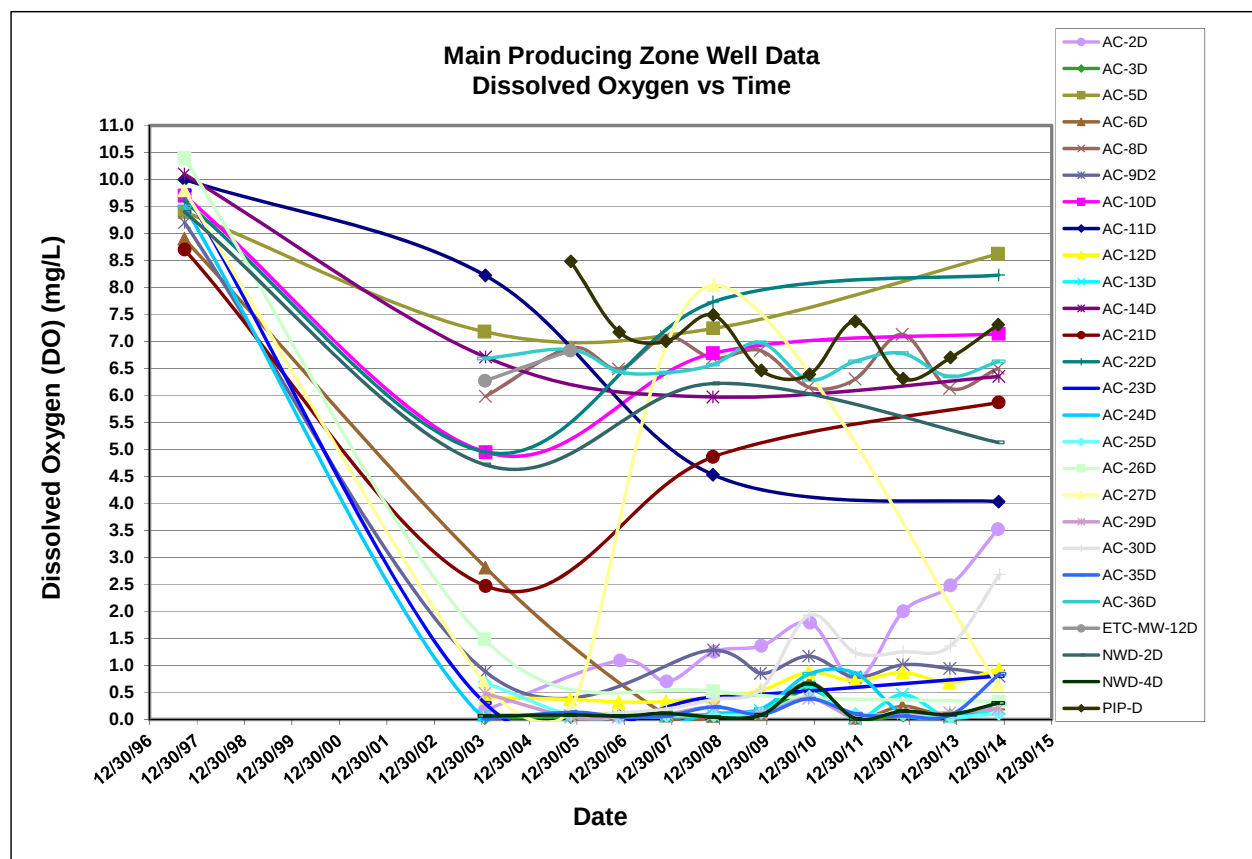

5.5.4 Oxidation-Reduction Potential

Oxidation-reduction potential (ORP) reactions control the behavior of many chemical constituents in groundwater. ORP refers to the electric potential required to transfer electrons from one compound or element (the oxidant) to another compound (the reductant). The process of oxidation involves losing electrons, while reduction involves gaining electrons. ORP is used as a qualitative measure of the state of oxidation in aqueous solutions. ORP (and Eh) are typically given in terms of millivolts (mV).

Although similar to ORP, Eh is reserved for consideration where the redox potential is measured with a relatively fragile standard hydrogen electrode (SHE). Positive Eh values indicate an oxidizing environment, while negative Eh values indicate a reducing environment. For field applications, ORP is typically measured using Ag/AgCl reference electrodes.


Field ORP readings can be converted to Eh values by adding the offset value provided by the manufacturer of the ORP calibration solution used (or by experimentation). ORP has been measured at the Site with an YSI (brand) instrument equipped with an Ag/AgCl electrode and calibrated against a Zobell 4M KCl solution where the offset to Eh is 200 mV. To convert the Site's field ORP readings to Eh, the offset value of 200 mV is added to the Site's ORP readings. For example, ORP readings of +150 and -172 mV translate to Eh values of +350 and +28 mV,

respectively. It is common for natural groundwater to present ORP between +300 mV to -400 mV (Eh between +500 mV to -200 mV).

Generally, oxygen-rich water is expected to exhibit positive ORP values (reflecting oxidizing conditions); and, conversely, anaerobic water often presents negative ORP values (reflecting reducing conditions). However, oxidation-reduction reaction couples are numerous and often competitive, so that natural environments affected by anthropogenic constituents can induce ORP behavior atypical of the otherwise classic correlation with dissolved oxygen. ORP is expected to reach equilibrium in groundwater that is at or approaching steady state. Changes in ORP can indicate a system that is out of equilibrium.


Surficial Zone Groundwater:

The shallow groundwater ORP vs. time chart is shown below.

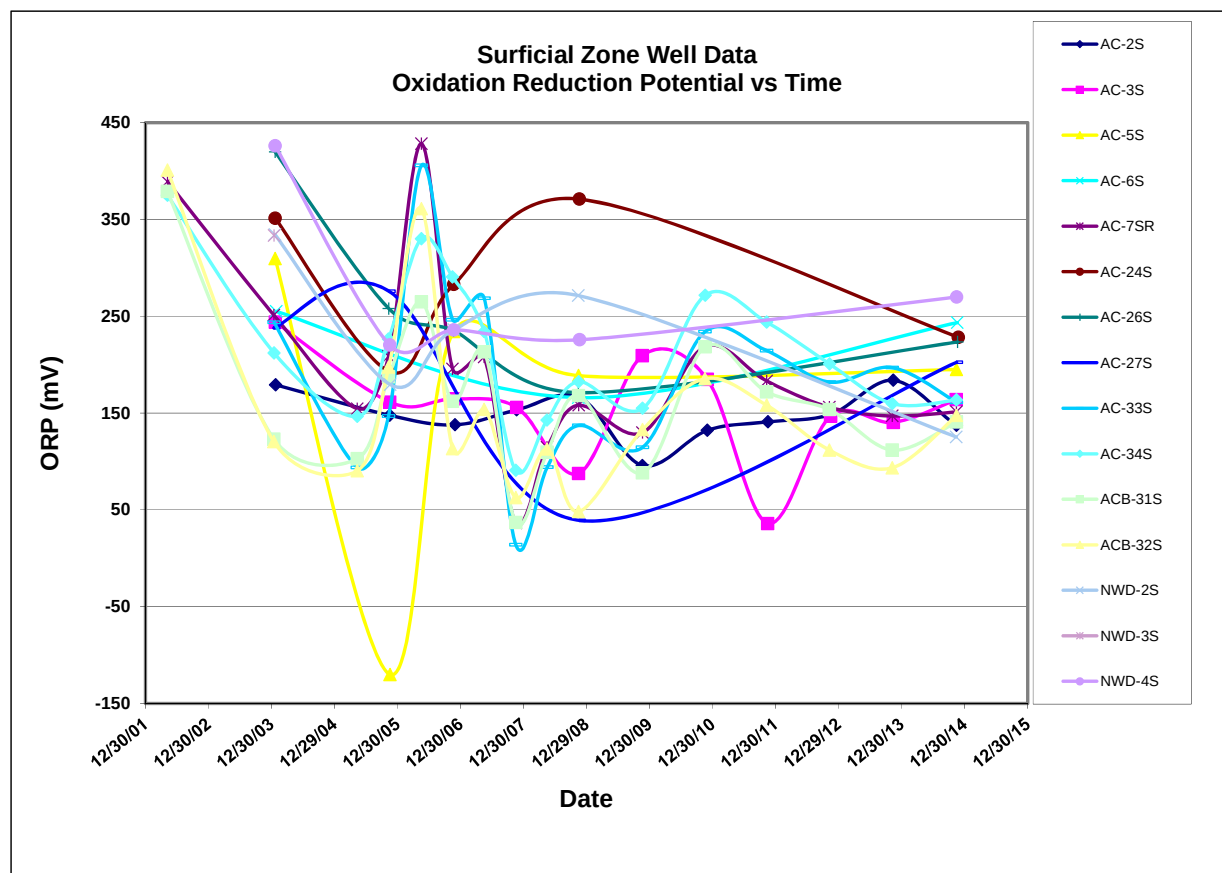

Main Producing Zone Groundwater:

The deep groundwater ORP vs. time chart is shown below.

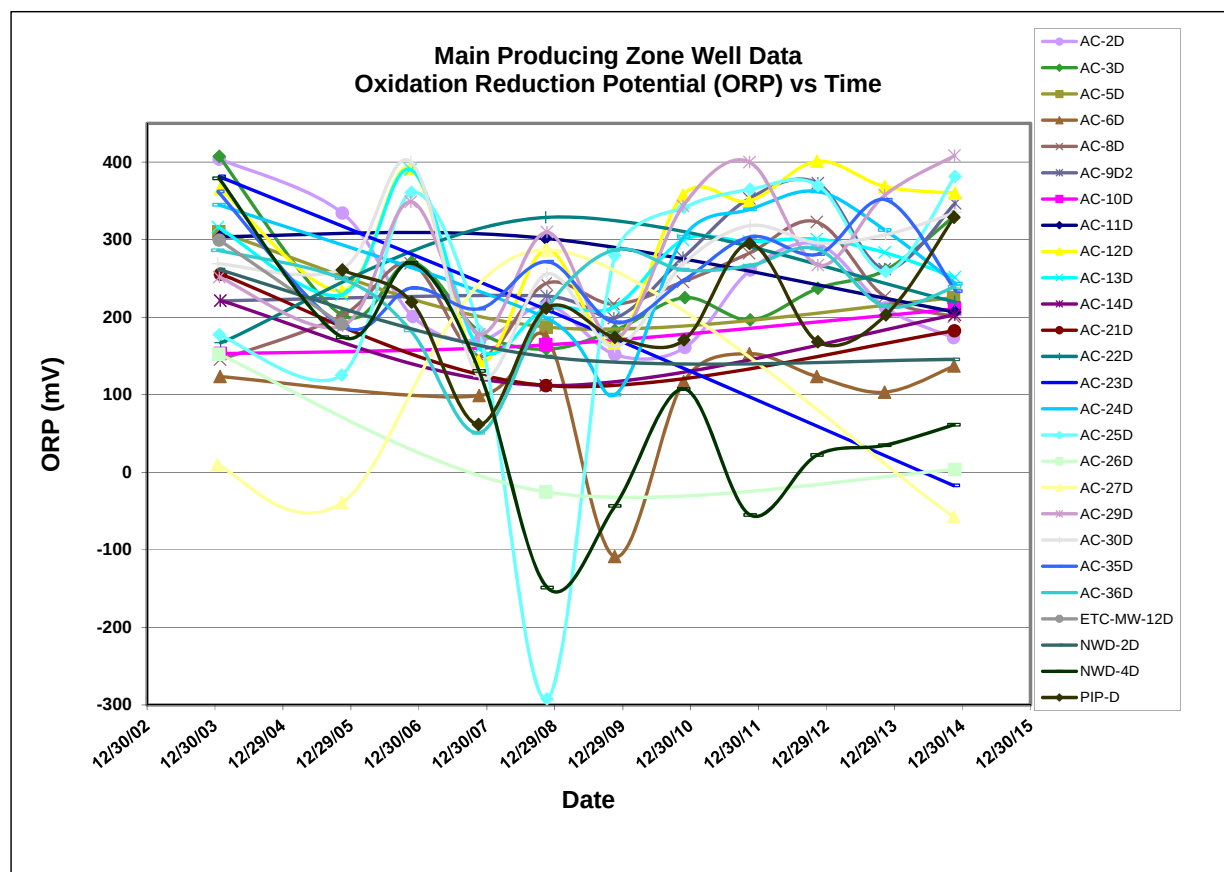

5.6 BAYOU TEXAR SAMPLING RESULTS

The long-term surface water monitoring network is composed of five sampling locations within Bayou Texar. Freshwater from Carpenter's Creek flows into the saline estuary, Bayou Texar. **Figure 1** shows the locations of the surface water sampling sites. Sampling for the standard annual list of COCs corresponding to those analyzed for groundwater was performed for surface water samples ACSW 1 and ACSW 2 during November 2014. Beginning in 2010, three new surface water stations were located in close proximity to ACSW-1 and were analyzed for fluoride only. These additional stations include BT-02, BT-107, and BT-127. These latter stations and ACSW-1 are located within the Agrico primary groundwater discharge reach of the bayou. ACSW-2 is located downstream of the primary discharge area and is considered a background station with regard to the Agrico constituents.

The surface water sampling results for Agrico COCs at the five stations are shown in **Table 5** (field parameters) and **Table 9** (sampling results). The COC results did not vary significantly from the previous four years of data. No COCs in surface water exceeded the surface water criteria. Laboratory analytical reports are contained in **Appendix A**.

5.7 QA/QC REVIEW

TestAmerica job numbers for this annual report include the following:

400-98308-1, 400-98371-1, 400-98418-1, 400-98478-1, 400-98525-1, 400-98593-1, 400-98663-1, 400-98714-1 and 400-98766-1. The following laboratory narratives describe the sample conditions and associated analytical QA/QC issues.

400-98308-1: All samples were received in good condition within temperature requirements, properly preserved and on ice. No issues regarding general chemistry or radiological analyses.

400-98371-1: All samples were received in good condition within temperature requirements, properly preserved and on ice. Samples ACB-31S (400-98371-5) and EQ-1 (400-98371-6) were inadvertently left off the chain of custody. No issues regarding general chemistry or radiological analyses.

400-98418-1: All samples were received in good condition within temperature requirements, properly preserved and on ice. Report revised to correct error for well ID. Report stated AC-72R and this should have been AC-7SR. Sample DUP-1 (400-98418-8) was inadvertently left off the chain of custody. No issues regarding general chemistry or radiological analyses.

400-98478-1: All samples were received in good condition within temperature requirements, properly preserved and on ice. No issues regarding general chemistry or radiological analyses.

400-98525-1: All samples were received in good condition within temperature requirements, properly preserved and on ice. No issues regarding general chemistry or radiological analyses.

400-98593-1: All samples were received in good condition within temperature requirements, properly preserved and on ice. No issues regarding general chemistry or radiological analyses.

400-98663-1: All samples were received in good condition within temperature requirements, properly preserved and on ice. No issues regarding general chemistry or radiological analyses.

400-98714-1: All samples were received in good condition within temperature requirements, properly preserved and on ice. The report was revised to remove the results labelled AC-28D. AC-28D well was not sampled. Instead an unknown shallow well was mistaken for AC-28D and sampled. The results are invalid and were removed from the report. No issues regarding general chemistry or radiological analyses. No issues regarding general chemistry or radiological analyses.

400-98766-1: All samples were received in good condition within temperature requirements, properly preserved and on ice.

400-98898-1: All samples were received in good condition within temperature requirements, properly preserved and on ice.

Seven QA/QC samples (five duplicates, two equipment blanks) were collected during the November 2014 sampling event. All duplicate samples showed acceptable agreement with their respective results, indicating adequate field and laboratory precision. Target analytes were reported below laboratory detection limits in equipment blank samples.

The locations where QA/QC samples were collected are listed below. Results of the QA/QC samples are included with the laboratory reports in **Appendix A**.

QA/QC Sample	Collection Location
DUP-1	AC-13D
DUP-1 (OU-1)	AC-34S
DUP-2	AC-8D
DUP- 3	NWD-2S
DUP- 4	AC-33S
EQ 1	AC-2S
EQ 2	NWD-4S

5.8 GROUNDWATER SAMPLING RESULTS

The 2014 annual results continue to support that source control actions at the former Agrico Site were effective and the MNA remedy is functioning as expected with Agrico COCs attenuating in groundwater under the former site and down-gradient of the site. Source control was completed as of April 1997. Long-term groundwater monitoring for the natural attenuation groundwater remedy was initiated in May 1997 for the OU-1 monitoring network and in November 1999 for the OU-2 network. In 2007, both the OU-1 and OU-2 networks were combined to form the site-wide network.

Surficial Zone

Within the surficial zone, the overall trend is downward and there is an overall shrinking of the area of impacts for this zone. The downward trend in concentrations is the direct result of effective source control. The surficial zone plume is captured by the vertical hydraulic component of the contaminant transport within less than one-half mile downgradient of the former site. Due to these conditions, the areal extent of impacts in the surficial zone is limited.

Presently, there are only two isolated areas where select COC concentrations are above target clean-up goals. These locations are ACB-31S and AC-2S. For ACB-31S, this is an up-gradient location where only the combined radium 226 + 228 concentration (5.02 pCi/L) slightly exceeds the 5.0 pCi/L goal. It is assumed that acidic conditions from the Escambia Treating Site (ETC) exists downgradient of the ETC Site and the lower pH is causing naturally occurring radium mineralogy to release radium into the groundwater. All other Agrico monitoring well locations on the former Agrico property are less than the clean-up target standard for all Agrico COCs further indicating this up-gradient location is being affected by an up-gradient source. At AC-2S, this location is directly down-gradient of the former Agrico Site and up-gradient of the area where the surficial zone is preferentially hydraulically connected to the deeper main producing zone. Fluoride (34 mg/L) and arsenic (0.02 mg/L) exceed the clean-up target levels of 4 mg/L and 0.01 mg/L, respectively at this location. For fluoride, concentrations are attenuating and the peak concentration of 210 mg/L occurred in 2002. Since that time, fluoride concentrations have been on a decreasing trend. For arsenic, the concentration has stabilized at about 0.2 mg/L since about 2005. The highest arsenic concentration of 0.74 mg/L occurred in 1990. The down-gradient location at AC-3S as well as the deeper cluster main producing zone well, AC-2D, have groundwater results which show that the clean-up target goals have been met.

Main Producing Zone

Within the main producing zone, the overall flattening of the trends is what was predicted in the Evaluation of Monitored Natural Attenuation by William Huber, Ph.D., Quantitative Decisions, (URS, 2009) and further confirmed by the evaluations by Huber in the October 23, 2013, Report #2 (URS, 2013b). This flattening should be expected to continue for some time and eventually evolve into a slowly decreasing trend, accelerating as time goes on. Slight upward or downward ticks in the trend for individual monitoring well results are to be expected. It is the long-term trend for each COC that is important. Radium appears to be on a slightly longer attenuation period than the other Agrico COC. This is due to the fact that radium exceedances occur as the result of a secondary reaction and was not the direct result of infiltration into the groundwater from the source area. Instead acidic wastewater infiltrated into the groundwater and contacted naturally occurring mineralogy with radium content. The radium in turn was released from the subsurface sediments to the groundwater as the acidic plume is transport downgradient contacting newly exposed aquifer material with the radium mineralogy. As the acidity approaches background conditions, this will stop the release of radium and attenuation of combined radium should progress on a faster path.

Figure 8 and **Figure 9** show the current extent of impacts for fluoride and combined radium 226 + 228, respectively. The area of the radium impacts is slightly larger than the fluoride impacts but this is primarily because of co-mingling of the ETC plume which displays low pH conditions (<4.5 su) and allows naturally occurring radium to be released to the groundwater. These releases associated with the ETC plume artificially increases the size of the radium plume that is attributable to the Agrico Site. The size of the Agrico main producing zone plume is best represented by the fluoride plume (**Figure 8**). All groundwater monitoring locations outside of these plume areas meet the Agrico target clean-up goals. Minimal occurrences (4 locations) of nitrate, sulfate or chloride occur at monitoring locations within the areas where fluoride and radium exceed the clean-up targets.

6.1 OU-1 REMEDY

The source area remedy was completed in 1997. Since that time, the property has remained secured; institutional controls have been filed on the property deed and are on record with Escambia County; the integrity of the constructed cap has not been compromised by erosion or settlement; the grass cover on the cap has matured and stabilized the soils; and the storm water controls remain intact, preventing storm water runoff from leaving the Site except through infiltration to groundwater in the North and South Ponds. Results of the water and sediment sampling in the infiltration ponds during January 2004 indicated that soils on-site are not affecting the quality of water infiltrating these ponds. Concentrations of all COCs in groundwater of the surficial zone immediately downgradient of the cap have decreased significantly since the remedial actions were completed. Based on all of the groundwater sampling results, the source area is controlled, and the remaining COC impacts are from residual impacts caused prior to the remedial action. Results from the 2014 sampling of monitoring wells downgradient of the cap area indicate that the OU-1 remedy remains effective and that source zone depletion is ongoing.

6.2 OU-2 REMEDY

Annual groundwater and surface water monitoring has been performed at established long-term monitoring locations since 1999. Comprehensive sampling has been performed in conjunction with each Five-Year Review. The groundwater monitoring continues to be an effective means of evaluating the natural attenuation remedy as well as source zone depletion. The evaluation of the long-term groundwater monitoring network (URS, 2006d), approved by EPA on September 11, 2007, provides further information regarding the defined plume area and downgradient progression. The recent evaluations of monitored natural attenuation associated with the Agrico plume (URS, August 2009 and October 2013) further supports that the mechanisms for attenuation are in place throughout the area and the effects of the source zone remedy are evident in the surficial zone of the former source area (OU-1) and are also being observed downgradient (OU-2), as expected. Decreases in concentrations have now been observed in the most upgradient groundwater and are imminent in the further downgradient wells.

6.2.1 Notifications

As part of the annual scope of work, notifications are provided to select groups. This includes issuing an Advisory Notice to contractors, a memorandum to local and regional agency contracts; and querying of NFWFMD permit records to determine if any new wells have been installed within the well construction moratorium area.

A standard advisory notice was distributed to contractors who potentially might be performing work related to new well installations in the area of OU-2. This notice informs the contractor of the boundaries of the existing moratorium on well construction. It also directs them to the NFWFMD, FDEP, or the Escambia County Health Department for more information.

According to NFWFMD permit records, no new irrigation wells were installed within the monitoring area during 2014.

On February 22, 2001, the NFWFMD Board passed a moratorium on drilling wells, including irrigation wells, in the Agrico OU-2 and the ETC groundwater plume areas. The moratorium

remains in effect and provides the most stringent institutional controls for the area impacted by the plume. The moratorium has no termination date and is part of the Prohibitions in Rule 40A-3. A memorandum was distributed to local and regional agencies requesting input on any rule changes that may affect any institutional controls for the moratorium area.

6.2.2 SAMPLING RESULTS – GROUNDWATER AND SURFACE WATER

The natural attenuation remedy is proceeding as anticipated, with 18 of the estimated 70 years elapsed (remediation of OU-1 was certified complete in April 1997). Conclusions from the monitored natural attenuation evaluations (URS, August 2009 and October 2013) indicate that much of the groundwater is expected to reach the target concentrations within two to three decades. Within the area of the Bayou Texar discharge boundary, the time to reach the targets may be longer. Fluoride results continue to exemplify cleanup progress for the Agrico Site. Additionally, it appears that the plume discharge area remains well defined and limited in areal extent. Groundwater results for November 2014 closely compared to historical results for both aquifer zones. Although slight increases in concentrations were detected at some monitoring well locations for some COCs, the increases are within the range of expected concentrations for a natural attenuation remedy where source control has been implemented and source zone depletion is ongoing.

Surficial Zone

The surficial zone plume does not migrate to Bayou Texar. The plume in this zone infiltrates to the main producing zone within less than 0.4 mile downgradient of the Site (**Figure 4**). Monitoring of the groundwater within the surficial zone is limited to the OU-1 area and the vicinity of the vertical diversion area between AC-2S and AC-3S. The only impacts remaining for the surficial zone plume are in close proximity of monitoring well AC-2S. Within the surficial zone, the overall trend in COC concentrations is downward and the overall area of impacts is shrinking. Due to the existing hydrogeologic/hydraulic conditions, the zone has limited areal impacts. For most of the OU-2 area, background conditions exist for the Agrico COCs within the surficial zone, since the potential for downgradient impacts beyond the surficial zone diversion area are absent. Any exceptions to background concentrations in these downgradient surficial zone wells are due to non-Agrico sources.

Main Producing Zone

Within the main producing zone, arsenic and lead plumes are not present at the Agrico Site. The primary indicator of the Agrico plume continues to be fluoride where concentrations exceed the performance standard of 4 mg/L. Also, elevated chloride and sulfate concentrations coexist with elevated fluoride concentrations, but presently only exceed the target cleanup standards for one or more of these constituents at four locations. Radium appears to be on a slightly longer attenuation period than the other Agrico COCs. This is due to the fact that radium (naturally occurring) exceedances occur as the result of a secondary geochemical reaction, not the direct result of infiltration into the groundwater from the source area. Instead low pH acidic wastewater infiltrated into the groundwater and contacted naturally occurring minerals with radium content. The naturally occurring radium was released from the subsurface saturated soil to the groundwater with the low pH acidic plume. As the pH approaches background conditions

(neutralizes) downgradient, the release of the naturally occurring radium will subside, and both the pH and radium plumes will continue to shrink. Monitoring wells AC-6D, AC-23D, NWD-4D only have radium exceedances and these elevated radium concentrations are suspected of being caused by up-gradient sources contributing to acidic groundwater conditions. The source areas include the Kaiser Site for AC-6D and the ETC Site for AC-23D and NWD-4D.

The main producing zone plume remains well defined, as the detailed evaluations (URS, 2006d, URS, August 2009, and URS, October 2013) confirmed, and exceedances of contaminant-specific performance standards only cover limited areal extents. Within the main producing zone, the stability and flattening of COC concentration trends is what was predicted and what is observed. The flattening/COC stability is expected to continue for some time. This trend will eventually evolve into a slowly decreasing trend, accelerating with time. Slight upward or downward ticks in COC trends for individual monitoring well results are to be expected as site conditions change (e.g. water level fluctuations, aquifer heterogeneity, etc.). It is the long-term trends for each COC in the impacted area that is important.

6.2.3 Bayou Texar

The 1993 Bayou Texar Assessment (Entrix, 1993a, 1993b, and 1993c) presented fluoride data that indicated groundwater originating from the Agrico Site was discharging to the bayou. The data also indicated that the discharge zone appeared to be well defined and limited in areal extent. EPA's review of the data concluded that fluoride would have to be discharging at a concentration of 4,050 mg/L or greater in order to exceed the surface water standard of 5 mg/L in the bayou. The maximum fluoride concentration in 2014 in groundwater along the western edge of Bayou Texar was only 110 mg/L in monitoring well AC-35D (**Figure 1**). The maximum historical fluoride concentration recorded for the Agrico plume was 180 mg/L also in AC-35D. Furthermore, in the OU-2 ROD, EPA (1994) concluded that it is unlikely that the discharge of the groundwater plume into Bayou Texar would result in impacts to fish or wildlife.

There are more than 60 storm water outfalls into Bayou Texar. Several studies have identified impacts caused by storm water from other locations contributing contaminants to the bayou. Mohrherr, et al. (2005) concluded that Bayou Texar is an urban water body that is impacted by a variety of pollutants and pollution sources. Mohrherr, et al. (2005) further concluded that their results corroborate the studies conducted for the Agrico Site indicating that fluoride levels are highest and increase with depth in the northern portion of the bayou where the Agrico plume discharges to the bayou. Mohrherr, et al. (2005) also concluded, as the long-term monitoring data for the bayou confirm, that the fluoride concentrations in the waters of Bayou Texar are below the Chapter 62-302, Class III Marine standard of 5 mg/L.

Surface Water

Surface water concentrations remain less than Chapter 62-302, Class III Marine Surface Water Standards for Agrico COCs, indicating that sufficient precipitation for the case of fluoride concentrations exists within the bayou. For other Agrico constituents, advection-dispersion is significantly affecting the COCs before and/or after it is discharged to the bayou so that the Agrico plume potential impacts are minimized with no significant risk to the bayou.

Summary of Ecological Impact Evaluation of Bayou Texar Downgradient of Agrico's Groundwater Fluoride Plume

On September 4, 2009, the results of the Phase I and Phase II Bayou Texar sampling for August 2008 and May 2009 were submitted to EPA. The results of the investigations indicated the following:

- Fluoride in the top 10 cm of sediment (the bioactive zone) within the groundwater plume discharge zone ranged from about 32 to 339 micrograms per gram (ug/g).
- Fluoride in the near-bottom surface water (the primary exposure regime for demersal fish) within the groundwater plume discharge zone was consistently less than the Florida Surface Water Quality Criterion for Class III Marine waters for fluoride, 5 mg/L. The concentration of fluoride in the majority of surface water samples was less than 1 mg/L.
- Fluoride in the sediment pore water in the bioactive zone (the primary exposure regime for benthic macro-invertebrates) within the groundwater plume discharge zone was less than 3 mg/L in 30 of the 40 stations sampled. Fluoride in pore water exceeded the 5 mg/L standard at only 3 of 40 stations. Spatial analysis determined that the surface area weighted average concentration of fluoride in the bioactive zone pore water was less than the 5 mg/L standard.

The conclusions of this assessment indicated that there is no significant risk to populations of demersal fish or to benthic macro-invertebrate communities that inhabit the reach of Bayou Texar where the Agrico groundwater discharges. Furthermore, the fluoride solubility in the majority of surface sediments and in all pore waters within the primary groundwater plume discharge reach is controlled by mineral precipitation reactions. These reactions are likely responsible for buffering dissolved concentrations of fluoride in near surface sediment pore water and the surface water in this reach of the bayou.

EPA has approved the ecological impact evaluation that was conducted for Bayou Texar (URS, 2009C). As part of the Third Five-Year review, EPA included four recommendations in the June 2010 Five-Year Report. These recommendations were as follows:

1. Continue annual groundwater monitoring.
2. Continue annual near-bottom Bayou Texar surface water monitoring at multiple stations including the 3 locations with pore water greater than 5 milligrams per liter as reported in the September 4, 2009 "Conceptual Site Model Ecological Impact Evaluation of Bayou Texar Downgradient of Agrico's Groundwater Fluoride Plume" (Phase II results).
3. If the levels of fluoride in near-bottom surface water or in adjacent Bayou Texar groundwater monitoring well, AC-35D, increase to levels significantly greater than that measured historically (maximum of 180 mg/L in 2010 and in 2014 a decrease to 110 mg/L), submit a work plan to evaluate the increase.
4. Conduct further risk evaluation studies will be conducted if the surface area weighted average for pore water is predicted to be greater than 5 milligrams per liter.

These first two recommendations are continuing tasks of the on-going long-term monitoring program for the Site. As of the November 2010 sampling event, the three locations where pore water results were greater than 5 mg/L were added to the long-term monitoring.

Since the surface water sampling was initiated for Bayou Texar and modified in 2010, no significant concentrations of fluoride have been detected as part of the near-bottom surface water sampling. For 2014, the fluoride concentrations ranged from 0.82 mg/L to 1.30 mg/L. The past five years of surface water fluoride concentrations further confirm that the Agrico groundwater discharges to Bayou Texar have no significant risk.

6.3 RECOMMENDATIONS

- It is recommended that groundwater monitoring frequency be changed from annual to every 5 years to correspond with the EPA Five-Year Reviews. This time span also corresponds to changes expected in COC concentrations as a result of natural attenuation processes and ongoing source zone depletion. It has been demonstrated that this is a slow process and concentrations in the main portion of the plume are not anticipated to reach significant decreases for at least 30 years or more, [based on the two Huber reports that evaluated natural attenuation of the Agrico plume (URS, 2009b, 2013b)]. The monitoring well network will consist of the same long-term and periodic monitoring wells that were sampled in November 2014. The wells will be sampled during November prior to the Five-Year Review Report issued in July of the year of the review. The results of the sampling will be reported in a MNA report and will be due to EPA by March 31st of the year of the review. The constituents to be sampled will continue to be fluoride, chloride, sulfate, nitrate, radium 226 and radium 228.
- It is recommended that the surface water sampling be discontinued in the Agrico monitoring program. Overall, groundwater concentrations continue to decrease and at any one monitoring location, the historical peaks have already occurred. Therefore, the conclusions reached in the previous surface water studies remain; there is no risk posed to Bayou Texar (URS, 2009c, Mohrherr, et.al. 2005, Entrix, 1993b)
- Recommended schedule - The next scheduled sampling event for the Agrico Site is proposed for November 2019, with a report to follow in March 2020. It is anticipated that the EPA Five-Year Review Report will be issued in July 2020.
- It is recommended that the notifications –Agency Coordination Memo and the FDOT inquiry for intrusive activity be change to every 5 years to correspond with the sampling activity.
- Operations and maintenance including mowing related to OU-1 will not change and will continue in accordance with the OU-1 O&M Plan as amended November 18, 2009 and approved by EPA on January 25, 2010.
- The advisory notice to contractors and the query of the NFWFMD well construction permit database will not change and will continue on an annual basis.
- Continue to work with EPA regarding the groundwater remediation at the ETC Site.
- Continue to work to understand the impacts associated with Site 348 (a FDEP site) and work with EPA on gathering information pertaining to Site 348.

- AMEC. 2013. Expanded Site Inspection Report – Palafox Street and Texar Dr. Ammonia Site, Pensacola, Escambia County, Florida; prepared for FDEP, Tallahassee, FL; FDEP Comet Site ID # 155367, EPA ID No. FLN000410706; June 2013.
- Bortone, Stephen A. 1996. Biophysical Monitoring at Bayou Texar: Bathymetric, Sedimentologic and Macroinvertebrate Evaluation at Twelve Outfalls, University of West Florida.
- Carmargo, J.A. 2003. Fluoride Toxicity to Aquatic Organisms: A Review. *Chemosphere* 50 (2003):251-264.
- Cameron-Cole, LLC, 2011. Site Assessment Report, Former Kaiser Agricultural Chemical Company, 2710 North Palafox Street, Pensacola, Florida; prepared for Mr. James W. Bradley and Mr. Donald W. Moore; September 15, 2011. CDM Federal Programs Corp. 1998. Remedial Investigation/Feasibility Study for Source Soils for the Escambia Treating Company Site, Pensacola, Florida. February 9, 1998.
- Camp, Dresser & McKee, Inc. (CDM) 1998. Final Remedial Investigation Feasibility Study for Source Soils for the Escambia Treating Company Site, Pensacola, Florida.
- Camp, Dresser & McKee, Inc. (CDM) 2004 Data Summary Report For OU1 Additional Soil Investigation Remedial Investigation/Feasibility Study for the Escambia Treating Company Site, Pensacola, Florida.
- Camp, Dresser & McKee, Inc. (CDM) 2005a. Final Feasibility Study Report for Source Soils, Operable Unit 1, Escambia Treating Company Site, Pensacola, Florida.
- Coffin, John E. 1982. Summary of Ground-Water and Surface-Water Data For City of Pensacola and Escambia County, Florida: U.S. Geological Survey Open-File Report 82-361.
- E² Inc., 2010. Five-Year Review Report (2005-2009) Third Five-Year Review Report for Agrico Chemical Company, FLD 980221857, Pensacola, Escambia County, Florida, June 2010. Prepared for United States Environmental Protection Agency, Region 4, Atlanta, Georgia.
- Entrix, Inc. 1993a. Final Bayou Study Work Plan: Phase 1a and 1b Sediment Sampling Program.
- Entrix, Inc. 1993b. Bayou Texar Study Phase I Report: Sediment and Pore water Sampling and Analysis. May 6, 1993.
- Entrix, Inc. 1993c. Bayou Texar Study Phase I Addendum Report: Bulk Metals Analyses with Additional Interpretation of Pore water Analyses. May 26, 1993.
- Florida Institute of Phosphate Research. 2004. Phosphate Primer.
- Geraghty & Miller, Inc. 1990. Remedial Investigation and Feasibility Study Work Plan. Pensacola Fertilizer Site. Pensacola, Florida. June 1, 1990.
- Geraghty & Miller, Inc. 1991a. Draft Remedial Investigation Additional Work Plan. Agrico Chemical Site. Pensacola, Florida. July 24, 1991.
- Geraghty & Miller, Inc. 1991b. Draft Remedial Investigation. Pensacola Fertilizer Site. Pensacola, Florida. March 28, 1991.

- Geraghty & Miller, Inc. 1992a. Final Phase I Remedial Investigation, Agrico Chemical Site, Pensacola, Florida. March 12, 1992.
- Geraghty & Miller, Inc. 1992b. Phase II Remedial Investigation, Agrico Chemical Site, Pensacola, Florida. September 18, 1992.
- Geraghty & Miller, Inc. 1993a. Final Feasibility Study. Agrico Chemical Site. Pensacola, Florida. June 23, 1993.
- Geraghty & Miller, Inc. 1993b. Final Phase 2 Remedial Investigation. Agrico Chemical Site. Pensacola, Florida. November 26, 1993.
- Gibbons, Robert D., 1994. Statistical Methods for Ground Water Monitoring, John Wiley & Sons, Inc.
- Henningson, Durham, and Richardson. 1974. Bayou Texar Restoration Study.
- Mactec Engineering & Consulting. 2010. Summary of Phase VIII Groundwater Investigation Findings Report, ECUA Well Field Site, Pensacola, Escambia County, Florida; prepared for FDEP (Site 348); February 2010.
- Mohrherr, Dr. Carl J., Dr. Johan Liebens, Dr. J. Eugene Lepo, and Dr. K. Ranga Rao. 2005. Profiles of Selected Pollutants in Bayou Texar, Pensacola, FL; a component of the "Assessment of Environmental Pollution and Community Health in Northwest Florida"; EPA Cooperative Agreement Award X-9745502; University of West Florida. May 10, 2005.
- Moshiri, Gerald A. and Salman Elawad. 1990. Physical, Biological, and Environmental Studies of Bayou Texar, Escambia County, Florida: Physical, Chemical and Biological Characteristics of the Water Column and Sediments; The Institute for Coastal and Estuarine Research, University of West Florida; Vol. II.
- Northwest Florida Water Management District. 1978. Evaluation of the Sedimentation and Hydraulic Characteristics of Bayou Texar and Carpenter's Creek. Escambia County, Florida: Technical File #78-3.
- Northwest Florida Water Management District. 1988. Storm water Evaluation for the Restoration of Bayou Texar. WRSR #88-3.
- Northwest Florida Water Management District. 1989. Ambient Ground Water Quality in Northwest Florida: Water Resources Special Report 87-1 (Revised edition).
- Northwest Florida Water Management District. 1996. Analysis of Ground Water Availability in the Cordova Park Area, Southeastern Escambia County, Florida. April 1996.
- Northwest Florida Water Management District. December 1999. Susceptibility of Public Supply Wells to Ground Water Contamination in Southern Escambia County, Florida.
- Northwest Florida Water Management District. (Countryman, Baker, Pratt, and Miller). October/November 2000. Potentiometric Surface of the Surficial Zone of the Sand-and-Gravel Aquifer, Escambia County, Florida. Water Resources Map Series 01-1.
- Northwest Florida Water Management District. (Countryman, Baker, Pratt, and Miller). October/November 2000. Potentiometric Surface of the Main Producing Zone of the Sand-and-Gravel Aquifer, Escambia County, Florida. Water Resources Map Series 01-2.

- Roaza, Honesto P., Thomas R. Pratt, Christopher J. Richards, Jay L. Johnson, and Jeffry R. Wagner. 1991. Conceptual Model of the Sand-and-Gravel Aquifer, Escambia County: Northwest Florida Water Management District, Water Resources Special Report 91-6.
- Roaza, Honesto P., Thomas R. Pratt, and Christopher J. Richards. 1993. Numerical Modeling of Ground Water Flow and Contaminant Transport in the Sand-and-Gravel Aquifer, Escambia County, Florida: Northwest Florida Water Management District, Water Resources Special Report 93-4.
- Richards, Christopher J., Thomas R. Pratt, and Katherine A. Milla. 1997. Wellhead Protection Area Delineation in Southern Escambia County, Florida: Northwest Florida Water Management District, Water Resource Special Report 97-4.
- Stone, Gregory W. and James P. Morgan. 1990. Physical, Biological, and Environmental Studies of Bayou Texar, Escambia County, Florida: Sedimentation, Bathymetric Changes and Tidal Variability in Bayou Texar. The Institute for Coastal and Estuarine Research. University of West Florida.
- Stone, Gregory W., Morgan, James P., Moshiri, Gerald A., and Elawad Salman. 1990. Physical, Biological, and Environmental Studies of Bayou Texar, Escambia County, Florida: Conclusions and Recommendations for Environmental Quality Improvement in Bayou Texar; The Institute for Coastal and Estuarine Research, University of West Florida. Vol. V.
- Trapp, H., Jr. 1975. Hydrology of the Sand-and-Gravel Aquifer in Central and Southern Escambia County, Florida. U.S. Geological Survey Open-File Report FL 74027.
- URS. January 2001. Annual Report. Ground Water Sampling Results –May and November 2000. Operable Unit One, Agrico Site, Pensacola, Florida.
- URS. March 9, 2001. Annual Report for 2000. Operable Unit Two (OU-2), Agrico Site, Pensacola, Florida.
- URS. March 1, 2002. Annual Report for 2001, Operable Unit Two (OU-2), Agrico Site, Pensacola, Florida.
- URS. March 1, 2002. Ground Water Sampling Results – May and November 2001. Operable Unit One, Agrico Site, Pensacola, Florida.
- URS. April 2, 2003. Annual Report for 2002. Operable Unit Two (OU-2), Agrico Site, Pensacola, Florida.
- URS. April 2, 2003. Annual Report for 2002. Operable Unit One (OU-1), Agrico Site, Pensacola, Florida.
- URS. April 2, 2004. Annual Report for 2003, Operable Unit One (OU-1), Agrico Site, Pensacola, Florida.
- URS. June 25, 2004. Annual Report for 2003, Operable Unit Two (OU-2), Agrico Site, Pensacola, Florida.
- URS. 2005a. Annual Report for 2004, Operable Unit One (OU-1), Agrico Site, Pensacola, Florida. February 11, 2005.
- URS. 2005b. Annual Report for 2004, Operable Unit Two (OU-2), Agrico Site, Pensacola, Florida. February 11, 2005.

- URS. 2006a. Annual Report for 2005, Operable Unit One (OU-1), Agrico Site, Pensacola, Florida. February 20, 2006.
- URS. 2006b. Annual Report for 2005, Operable Unit Two (OU-2), Agrico Site, Pensacola, Florida. April 6, 2006.
- URS. 2007. Annual Report for 2006, Operable Units One (OU-1) and Two (OU-2), Agrico Site, Pensacola, Florida. March 30, 2007.
- URS. 2006c. Technical Memorandum – Evaluation of Studies on Benthic Community Analysis and Sediment Toxicity Testing Conducted for Bayou Texar, Agrico Site, Pensacola, Florida. November 7, 2006.
- URS. 2006d. Technical Memorandum Report – Evaluation of Long-Term Groundwater Monitoring Network. Agrico Site, OU-1 and OU-2, Pensacola, Florida. November 30, 2006.
- URS. 2008. Annual Report for 2007, Operable Units One and Two (OU-1, OU-2), Agrico Site, Pensacola, Florida. March 28, 2008.
- URS. 2009a. Annual Report for 2008, Operable Units One and Two (OU-1, OU-2), Agrico Site, Pensacola, Florida. March 31, 2009.
- URS. 2009b. Evaluation of Monitored Natural Attenuation in Groundwater, Agrico Site, Pensacola, Florida. Prepared by William A. Huber, Ph.D. (Quantitative Decisions), August 19, 2009.
- URS. 2009c. Conceptual Site Model Ecological Impact Evaluation of Bayou Texar Downgradient of Agrico's Groundwater Fluoride Plume. In cooperation with Anchor-QEA; September 4, 2009.
- URS. 2010a. Annual Report for 2009, Operable Units One and Two (OU-1, OU-2), Agrico Site, Pensacola, Florida. March 15, 2010.
- URS, 2011, Annual Report for 2010, Operable Units One and Two (OU-1, OU-2), Agrico Site, Pensacola, Florida March 31, 2011.
- URS, 2012, Annual Report for 2011, Operable Units One and Two (OU-1, OU-2), Agrico Site, Pensacola, Florida. March 31, 2012.
- URS, 2013a, Annual Report for 2012, Operable Units One and Two (OU-1, OU-2), Agrico Site, Pensacola, Florida. March 29, 2013.
- URS, 2013b, Evaluation of Monitored Natural Attenuation in Groundwater, Report #2, October 23, 2013, Agrico Site, Pensacola, Florida, by Quantitative Decisions, William A. Huber, Ph.D., October 31, 2013.
- URS, 2014. Annual Report for 2013, Operable Units One and Two (OU-1, OU-2), Agrico Site, Pensacola, Florida, March 7, 2014.
- URS Greiner Woodward Clyde. January 1999. Annual Report. Ground Water Sampling Results – May and November 1998. Operable Unit One, Agrico Site, Pensacola, Florida.
- URS Greiner Woodward Clyde. December 1999. Annual Report. Ground Water Sampling Results – May and November 1999. Operable Unit One, Agrico Site, Pensacola, Florida.

- URS Greiner Woodward Clyde. 2000a. Remedial Action Implementation and First Annual Report (1999), OU-2, Agrico Site, Pensacola, Florida. February 2000.
- URS Greiner Woodward Clyde. 2000b. Five-Year Review, Agrico Site, Pensacola, Florida. February 2000.
- U.S. Army Corps of Engineers, Mobile District. 2005. Second Five-Year Review Report for Agrico Chemical Company, Operable Units 1 and 2, Pensacola, Escambia County, Florida, EPA ID: FLD980221857. Prepared for U.S. Environmental Protection Agency, Region 4. July 2005.
- U.S. Department of Agriculture and Tennessee Valley Authority. 1964. Superphosphate: Its History, Chemistry, and Manufacturing. December 1964.
- U.S. Environmental Protection Agency. 1992. Agrico Chemical Superfund Site, Record of Decision Operable Unit One. October 7, 1992.
- U.S. Environmental Protection Agency. 1994. Record of Decision for Operable Unit Two, Agrico Chemical Superfund Site, Pensacola, Escambia County, Florida. August 25, 1994.
- U. S. Environmental Protection Agency. 1994. Symposium on Natural Attenuation of Ground Water. 600/R-94/162.
- U.S. Environmental Protection Agency. 2006.. Record of Decision. Summary of Remedial Alternative Selection. Escambia Wood Treating Company Superfund Site. Operable Unit 01 (Soil). Pensacola, Escambia County, Florida. February 2006.
- U.S. Environmental Protection Agency. –2008. Record of Decision. Summary of Remedial Alternative Selection. Escambia Wood Treating Company Superfund Site. Operable Unit 2 (Groundwater). Pensacola, Escambia County, Florida, September 2008.
- Wagner, J.R., T.W. Allen, L.A. Clemens, and J.B. Dalton. 1984. Ambient Ground Water Monitoring Program - Phase I: NFWFMD, DER Contract No. WM65.
- Watts, G., J.M. Wilson, K. Busen, and W.H. Colona, III. 1988. Agrico Chemical, Inc., Escambia County: FDER Groundwater Investigation Report No. 88-08.
- Watts, Geoffrey B., and George E. Wiegand. 1989. Supplementary Contamination Report. Agrico Chemical Company - Escambia County: FDER, Site Investigation Section.
- Wilkins, K.T., Wagner, J.R., and T.W. Allen. 1985. Hydrogeologic Data for the Sand-and-Gravel Aquifer in Southern Escambia County, Florida: Northwest Florida Water Management District Technical File Report 85-2.
- Woodward-Clyde Consultants. 1993. Off-Site Monitoring Well Installation and Ground Water Sampling. Agrico Chemical Site. Pensacola, Florida: Technical Memorandum; Volumes 1 and 2.
- Woodward-Clyde Consultants. 1998. Annual Report. Ground Water Sampling Results – May and November 1997. Operable Unit One, Agrico Site, Pensacola, Florida.
- Woodward-Clyde Consultants. 1997. Work Plan - OU-2 Remedial Design. Agrico Chemical Site. Pensacola, Florida.
- Woodward-Clyde Consultants. 1997. Preliminary Design Analysis, Operable Unit Two Agrico Site. Pensacola, Florida.

Woodward-Clyde International- Americas. 1998. Intermediate Design Analysis, Operable Unit Two Agrico Site. Pensacola, Florida.

Woodward-Clyde International- Americas. 1998. Pre-Final Design Analysis, Operable Unit Two Agrico Site. Pensacola, Florida.

Woodward-Clyde International- Americas. 1998. Remedial Action Work Plan and Related Plans (including Management Plan, Sampling and Analysis Plan, Health and Safety Plan and Operation and Maintenance Plan). Operable Unit Two, Agrico Site, Pensacola, Florida.

Zapeczka, O.S. and Szabo, Zoltan, 1988. Natural radioactivity in groundwater – A Review in Moody, D.W., Chase, E.B., and Paulson, R.W., comp., National Summary 1986 – Ground-water quality: Hydrologic conditions and events: U.S. Geological Survey Water Supply Paper 2325.

TABLES

TABLE 1
GROUNDWATER MONITORING WELL NETWORK
LONG-TERM AND PERIODIC MONITORING WELLS

Agrico Site
Pensacola, Florida

Well I.D.	Network Component	Description	Aquifer Zone
AC-2D	OU-2 LTGWMW	Downgradient Site, Below PS Concentration	MPZ
AC-2S	OU-2 LTGWMW	Elevated Concentration Area Well	SZ
AC-3S	OU-2 LTGWMW	Flow Path Well, Below PS Concentration	SZ
AC-3D	OU-2 LTGWMW	Elevated Concentrations, Flow Path Well	MPZ
AC-5D	PERIODIC	Outside of Plume	MPZ
AC-5S	PERIODIC	Outside of Plume, Background	SZ
AC-6D	OU-2 LTGWMW	Outside of Plume; Potentially Impacted by Site 348 (Kaiser)	MPZ
AC-6S	PERIODIC	Outside of Plume; Potentially Impacted by Site 348 (Kaiser)	SZ
AC-7SR	OU-1 LTGWMW	In Residual Plume Area	SZ
AC-8D	OU-2 LTGWMW	Outside Plume, Sentry Well	MPZ
AC-9D2 ⁽¹⁾	OU-2 LTGWMW	In Plume	MPZ
AC-10D	PERIODIC	Outside of Plume, Effects by Site 348 (Kaiser) Possible	MPZ
AC-11D	PERIODIC	Outside of Plume	MPZ
AC-12D	OU-2 LTGWMW	Flow Path Well Inside Plume	MPZ
AC-13D	OU-2 LTGWMW	Leading Edge of Plume	MPZ
AC-14D	PERIODIC	Outside of Plume	MPZ
AC-21-D	PERIODIC	Outside of Plume, Potential Effects by Site 348 (Kaiser)	MPZ
AC-22D	PERIODIC	Outside of Plume, Effects by Site 348 (Kaiser) Possible	MPZ
AC-23D	PERIODIC	Sidegradient Fringe of Plume	MPZ
AC-24D	OU-2 LTGWMW	Flow Path Well Inside Plume	MPZ
AC-24S	PERIODIC	Outside of Plume, Downgradient of Diversion Area	SZ
AC-25D	OU-2 LTGWMW	Flow Path Well Inside Plume	MPZ
AC-26D	PERIODIC	Near Bayou Texar Outside of Plume	MPZ
AC-26S	PERIODIC	Outside of Plume, Downgradient of Diversion Area	SZ
AC-27D	PERIODIC	Located on East Side of Groundwater Divide	MPZ
AC-27S	PERIODIC	Located on East Side of Groundwater Divide	SZ
AC-28D	OU-2 LTGWMW	Flow Path Well Inside Plume	MPZ
AC-29D	OU-2 LTGWMW	Elevated Concentrations, Flow Path	MPZ
AC-30D	OU-2 LTGWMW	Flow Path, Inside Plume	MPZ
ACB-31S	OU-1 LTGWMW	Upgradient but not necessarily Background	SZ
ACB-32S	OU-1 LTGWMW	Upgradient but not necessarily Background	SZ
AC-33S	OU-1 LTGWMW	Downgradient Cap Area	SZ
AC-34S	OU-1 LTGWMW	Downgradient Cap Area	SZ
AC-35D	OU-2 LTGWMW	Elevated Concentration, Flow Path	MPZ
AC-36D	OU-2 LTGWMW	Adjacent Bayou, Outside Plume, Potential Discharge Area	MPZ
NWD-2D	PERIODIC	Outside of Plume, Effects by Site 348 (Kaiser) Possible	MPZ
NWD-2S	PERIODIC	Downgradient of Diversion Area, Outside of Plume	SZ
NWD-4D	OU-2 LTGWMW	Outside of Plume, Sentry Location	MPZ
NWD-4S	PERIODIC	Outside of Plume, Sentry Location	SZ
PIP-D	OU-2 LTGWMW	Upgradient but not necessarily Background	MPZ

NOTES:

MPZ = Main Producing Zone

SZ = Surficial Zone

PS = Performance Standard

Other wells associated with site were not located as of September 1997 and are assumed destroyed. Wells include AC-3D2, AC-21S, AC-23S, AC-25S, NWD-D, NWD-I

Well plugged with cement and abandoned according to NFWMD regulations include AC-1S, AC-1D, AC-4S, AC-4D, AC-7S, AC-7D, AC-9D.

Former Periodic Well NWD-3S destroyed between November 2005 and November 2006; New construction location covers the former monitoring well location.

LTGWMW = Long-Term Groundwater Monitoring Well

Periodic = Annual water levels and sampling during Five-Year Reviews.

Annual = Beginning Nov. 2009; sampling will be conducted annually to assist in MNA evaluation;

once MNA determinations made, these wells will revert to periodic.

⁽¹⁾ AC-9D2 is replacement well for AC-9D. AC-9D was plugged and abandoned on October 21, 1993.

TABLE 2
MONITORING WELL CONSTRUCTION DETAILS

Agrico Site
Pensacola, Florida

Well I.D.	Elevation Measuring Point (ft NGVD)⁵	Well Depth (ft bls)⁶	Screen Interval (ft bls) ²	Diameter (inches)²	Aquifer Zone
AC-2D ⁽⁴⁾	92.74	149	147.2-149	4	MPZ
AC-2S	88.65	70	50 - 70	4	SZ
AC-3S	88.06	79	59 - 79	4	SZ
AC-3D	88.07	170	150 - 170	4	MPZ
AC-5D	82.4	171	151 - 171	4	MPZ
AC-5S	82.34	69	49 - 69	4	SZ
AC-6D	69.19	170	150 - 170	4	MPZ
AC-6S	69.32	70	50 - 70	4	SZ
AC-7SR	90.59	70	50 - 70	2	SZ
AC-8D	76.44	220	190 - 222	4	MPZ
AC-9D2 ⁽¹⁾	64.13	198	179 - 198	4	MPZ
AC-10D	79.48	224	190 - 224	4	MPZ
AC-11D	73.17	200	200 - 220	4	MPZ
AC-12D	79.23	211	191 - 211	4	MPZ
AC-13D	74.65	223	203 - 223	4	MPZ
AC-14D	49.79	199	179 - 199	4	MPZ
AC-21D ⁽⁷⁾	75.47	170	160 - 169.5	4	MPZ
AC-22D	76.58	170	160 - 169.5	4	MPZ
AC-23D	79.51	170	160 - 169.5	4	MPZ
AC-24D	79.60	215	205 - 215	4	MPZ
AC-24S	79.50	80	70 - 80	4	SZ
AC-25D	39.75	180	170 - 180	4	MPZ
AC-26D	26.70	165	155 - 165	4	MPZ
AC-26S	26.75	35	25 - 35	4	SZ
AC-27D	18.55	150	140 - 150	4	MPZ
AC-27S	18.50	35	25 - 35	4	SZ
AC-28D	74.89	201	181 - 201	4	MPZ
AC-29D	82.26	211	191 - 211	4	MPZ
AC-30D	85.73	211	191 - 211	4	MPZ
ACB-31S	91.92	70	50 - 70	2	SZ
ACB-32S	88.16	69.5	49.5 - 69.5	2	SZ
AC-33S	89.18	69.5	49.5 - 69.5	2	SZ
AC-34S	89.09	70	50 - 70	2	SZ
AC-35D	10.49	145	125 - 145	4	MPZ
AC-36D	5.26	152	132 - 152	4	MPZ
NWD-2D ⁽³⁾	76.80	180	160 - 180	4	MPZ
NWD-2S ⁽³⁾	77.53	75	55 - 75	4	SZ
NWD-3S ⁽⁷⁾	80.40	75	55 - 75	4	SZ
NWD-4D	34.70	120	100 - 120	4	MPZ
NWD-4S	34.70	45	35 - 45	4	SZ
PIP-D	39.10	180	160 - 180	4	MPZ

NOTES:

ROW = Road Right-of-Way

MPZ = Main Producing Zone

SZ = Surficial Zone

⁽¹⁾ AC-9D2 is replacement well for AC-9D. AC-9D plugged and abandoned on October 21, 1993.

⁽²⁾ All wells are constructed of PVC casing and screen materials.

ft bls = feet below land surface

⁽³⁾ Elevations for NWD-2D and NWD-2S were corrected in this Annual Report based on information from the NFWFMD database.

⁽⁴⁾ Downhole Video Survey conducted in March 2004. Results indicate well filled in and only about 1 ft of screen remains.

⁽⁵⁾ ft NGVD = feet above National Geodetic Vertical Datum of 1988.

⁽⁶⁾ ft = feet

⁽⁷⁾ NWD-3S destroyed as of 2006; AC-21D damaged as of 2007 (measured depth 163 ft bls; only 3 ft of screen remains).

**TABLE 3
GROUNDWATER FIELD PARAMETER RESULTS**

**Agrico Site
Pensacola, Florida**

Well I.D.	Date	pH (su)	Conductivity (µS/cm)	Temperature (°C)	Dissolved Oxygen (mg/L)	Oxidation Reduction Potential (mV)	Turbidity (NTU)
AC-2D	09/30/97	4.60	100	24.00	9.70	NM	0.00
	11/16/99	4.90	110	22.00	NM	NM	0.00
	11/21/00	4.50	110	21.00	NM	NM	0.00
	11/15/01	4.55	102	21.20	NM	NM	0.00
	11/26/02	4.36	102	23.70	NM	NM	0.36
	01/23/04	4.64	105	23.07	0.17	403.9	2.60
	11/17/04	4.50	105	22.40	NM	NM	1.10
	11/14/05	4.80	91	23.32	2.41	334.2	3.34
	11/28/06	4.68	90	23.30	1.09	200.8	1.70
	11/21/07	4.86	91	22.86	0.70	170.0	0.00
	11/19/08	4.56	109	23.65	1.25	214.9	1.87
	11/18/09	4.59	97	23.37	1.36	151.8	1.18
	11/29/10	4.30	99	22.90	1.79	161.0	0.65
	11/16/11	4.65	99	23.61	0.72	260.9	3.14
	11/14/12	4.45	96	23.59	2.00	293.8	2.15
AC-2S	11/12/13	4.44	95	23.70	2.48	212.1	2.71
	11/12/14	4.68	94	21.28	3.52	173.6	1.31
	09/27/97	6.00	590	24.00	9.10	NM	2.00
	11/16/99	5.80	430	22.00	NM	NM	1.00
	11/21/00	5.70	520	21.00	NM	NM	1.00
	11/15/01	6.05	552	20.00	NM	NM	39.50
	11/26/02	6.01	507	25.90	NM	NM	4.90
	01/23/04	5.86	493	24.75	1.50	179.2	2.50
	11/17/04	5.71	400	23.66	NM	NM	3.31
	11/15/05	5.71	450	23.49	2.73	147.6	9.31
	11/28/06	5.72	478	24.04	1.66	137.8	0.81
	11/21/07	5.93	296	24.39	1.57	153.3	0.00
	11/19/08	5.71	388	24.41	0.86	166.2	1.01
	11/18/09	5.86	268	24.34	1.88	95.8	1.18
	11/29/10	5.62	270	24.48	3.15	132.1	0.07
AC-3D	11/16/11	5.67	344	24.77	1.45	140.9	3.96
	11/14/12	5.55	335	23.71	2.38	148.6	0.56
	11/12/13	5.53	317	23.99	2.47	183.8	1.07
	11/12/14	5.63	294	21.51	4.33	137.1	0.41
	09/27/97	4.90	1600	24.00	9.50	NM	0.00
	11/19/99	4.60	1200	23.00	NM	NM	0.00
	11/21/00	4.40	1200	21.00	NM	NM	0.00
	11/14/01	4.70	930	22.80	NM	NM	0.00
	11/26/02	4.24	1041	23.80	NM	NM	0.37
	01/22/04	4.32	1013	23.24	0.02	407.2	2.60
	11/17/04	4.11	872	22.81	NM	NM	3.24
	11/15/05	4.37	844	23.35	0.04	202.3	2.96
	11/22/06	4.42	819	23.48	0.06	270.9	1.30
	11/21/07	4.59	640	22.94	0.09	181.3	0.00
	11/13/08	4.52	572	23.77	0.07	158.7	2.20
AC-3S	11/18/09	4.47	523	23.61	0.10	183.2	0.81
	11/29/10	4.21	480	22.83	0.55	225.2	1.43
	11/15/11	4.40	451	23.53	0.02	196.5	2.04
	11/13/12	4.24	462	23.63	0.07	237.2	0.79
	11/12/13	4.18	407	23.69	0.06	260.9	1.25
	11/11/14	4.30	382	20.74	0.21	329.5	0.16
	09/27/97	6.00	150	26.00	7.70	NM	6.00
	11/16/99	6.20	90	24.00	NM	NM	0.00
	11/21/00	6.10	90	21.00	NM	NM	0.00
	11/14/01	6.40	153	22.90	NM	NM	300**
	11/26/02	6.42	128	23.50	NM	NM	3.30
	01/22/04	6.17	117	21.72	4.83	244.0	3.10
	11/17/04	5.77	128	23.13	NM	NM	3.20
	11/15/05	6.32	139	26.98	8.70	161.3	4.16
	11/22/06	6.17	159	25.19	7.06	164.8	1.28
	11/21/07	6.01	150	25.08	7.15	155.7	0.00
	11/13/08	6.00	116	24.91	5.56	87.5	2.62
	11/18/09	5.90	108	21.24	6.40	209.2	1.65
	11/29/10	5.76	134	22.24	6.09	184.7	4.17
	11/15/11	5.67	185	25.38	7.04	35.8	1.05
	11/13/12	5.80	139	26.23	6.62	146.8	0.60
	11/12/13	5.86	126	26.97	6.81	140.3	1.47
	11/11/14	5.94	146	25.17	6.28	163.9	1.18

**TABLE 3
GROUNDWATER FIELD PARAMETER RESULTS**

**Agrico Site
Pensacola, Florida**

Well I.D.	Date	pH (su)	Conductivity (µS/cm)	Temperature (°C)	Dissolved Oxygen (mg/L)	Oxidation Reduction Potential (mV)	Turbidity (NTU)
AC-5D	09/26/97	5.00	80	24.00	9.40	NM	0.00
	01/20/04	4.59	84	23.79	7.18	310.0	2.40
	11/13/08	4.42	86	23.99	7.24	187.2	0.76
	11/12/14	4.73	64	21.56	8.62	225	0.30
AC-5S	09/26/97	5.70	150	24.00	8.30	NM	1.00
	11/16/99	5.40	180	23.00	NM	NM	0.00
	11/20/00	5.40	170	23.00	NM	NM	0.00
	11/13/01	5.52	209	25.40	NM	NM	0.00
	11/20/02	5.01	124	26.20	NM	NM	0.13
	01/20/04	5.28	98	24.54	7.15	309.6	2.80
	11/10/04	5.39	208	24.97	NM	NM	0.00
	11/16/05	5.66	155	25.86	3.85	-120.2	3.33
	11/21/06	5.11	156	25.08	6.23	234.1	0.28
	11/13/08	5.07	196	25.58	5.47	188.6	0.18
AC-6D	11/12/14	5.16	146	23.39	6.54	195	0.53
	09/25/97	4.90	120	24.00	8.90	NM	NM
	01/27/04	4.65	154	22.67	2.81	123.4	0.00
	11/19/07	4.84	194	22.36	0.07	98.7	0.00
	11/12/08	4.65	193	23.10	0.06	174.3	2.53
	11/16/09	5.47	173	23.01	0.11	-108.8	10.60
	11/22/10	5.13	172	22.59	0.68	116.9	8.12
	11/10/11	5.20	181	23.41	0.03	152.8	9.38
	11/07/12	5.07	187	23.07	0.24	123.3	15.40
	11/07/13	5.19	193	23.25	0.07	103.2	70.40
AC-6S	11/14/14	5.49	162	20.65	0.29	137.0	21.7
	09/25/97	4.90	350	23.00	9.50	NM	NM
	01/27/04	4.40	509	23.58	1.92	255.0	2.40
	11/12/08	4.51	425	23.67	3.11	165.8	2.01
AC-7SR	11/17/14	4.60	216	20.39	2.66	243.4	1.87
	11/23/98	5.00	120	23.00	NM	NM	7.00
	05/25/99	5.00	170	25.00	NM	NM	2.00
	05/16/00	4.70	110	23.00	NM	NM	2.00
	11/14/00	4.40	180	21.00	NM	NM	3.00
	05/08/01	4.24	194	22.60	NM	NM	999*
	11/06/01	4.63	161	22.00	NM	NM	12.9
	05/07/02	3.84	143	22.20	2.75	389	17.6
	05/07/03	4.41	195	22.49	NM	NM	8.93
	01/13/04	4.88	161	23.29	2.77	251.1	3.30
	05/10/04	4.71	185	23.76	NM	NM	5.44
	11/09/04	4.72	205	23.08	NM	NM	3.41
	05/10/05	4.37	201	23.15	2.00	154.4	4.50
	11/08/05	5.37	158	23.91	3.06	208.6	3.59
	05/17/06	5.07	157	23.08	2.37	428.3	2.00
	11/14/06	5.48	165	22.99	2.41	195.5	1.61
	05/16/07	4.83	155	23.06	2.52	208.0	2.20
	11/15/07	4.67	138	22.24	2.48	36.3	2.50
	05/15/08	4.87	176	22.93	3.19	114.5	1.70
	11/14/08	4.98	172	23.30	2.80	158.1	0.88
	11/19/09	4.65	143	23.40	3.00	129.8	2.80
	11/17/10	5.74	146	22.48	3.58	218.9	0.36
	11/08/11	5.54	165	23.23	2.74	183.1	2.04
	11/06/12	5.09	163	23.39	3.92	156.0	1.06
	11/05/13	5.46	155	23.33	3.49	147.0	1.65
	11/13/14	5.70	144	20.00	3.44	151.2	1.56

**TABLE 3
GROUNDWATER FIELD PARAMETER RESULTS**

**Agrico Site
Pensacola, Florida**

Well I.D.	Date	pH (su)	Conductivity (µS/cm)	Temperature (°C)	Dissolved Oxygen (mg/L)	Oxidation Reduction Potential (mV)	Turbidity (NTU)
AC-8D	09/25/97	5.00	150	23.00	9.70	NM	0.00
	11/17/99	4.80	140	23.00	NM	NM	0.00
	11/17/00	4.50	140	22.00	NM	NM	0.00
	11/08/01	5.01	143	21.70	NM	NM	0.00
	11/25/02	4.42	140	23.60	NM	NM	0.76
	01/27/04	4.72	152	23.16	5.98	145.2	0.00
	11/10/04	5.42	164	22.12	NM	NM	0.44
	11/09/05	4.82	137	23.37	6.88	201.5	0.00
	11/16/06	4.72	131	23.13	6.49	269.3	0.31
	11/19/07	4.94	133	22.48	7.09	149.3	0.15
	11/11/08	4.77	126	23.24	6.69	243.4	2.59
	11/11/09	4.73	124	23.41	6.83	216.9	0.41
	11/18/10	4.63	121	22.53	6.15	245.6	1.05
	11/09/11	4.84	122	23.43	6.30	282.4	1.92
	11/07/12	4.54	119	23.25	7.13	322.8	1.05
AC-9D2	11/06/13	4.75	117	23.39	6.13	226.3	1.35
	11/13/14	4.83	113	20.63	6.50	200.9	0.36
	09/26/97	4.20	690	23.00	9.20	NM	NM
	01/28/04	3.97	798	23.07	0.88	221.0	0.00
	11/17/08	4.01	813	23.23	1.28	227.2	0.21
	11/12/09	4.09	756	23.33	0.85	198.6	0.41
	11/19/10	4.05	743	22.61	1.17	276.7	0.35
	11/10/11	4.16	722	23.61	0.78	353.1	0.43
AC-10D	11/12/12	4.05	737	23.36	1.01	372.6	0.32
	11/07/13	4.05	704	23.51	0.94	262.0	0.72
	11/20/14	4.10	708	20.89	0.80	346.9	0.23
	09/27/97	5.80	270	24.00	9.70	NM	0.00
	01/28/04	5.21	223	23.18	4.95	153.0	0.00
AC-11D	11/12/08	5.05	190	23.15	6.78	164.2	0.83
	11/18/14	4.91	161	20.53	7.14	210.6	0.35
	09/24/97	5.30	80	24.00	10.00	NM	2.00
	01/27/04	4.51	89	22.78	8.22	303.7	1.70
AC-12D	11/11/08	4.69	70	23.14	4.53	301.7	2.33
	11/18/14	5.01	76	20.32	4.03	206.7	0.19
	09/27/97	4.00	610	24.00	9.00	NM	NM
	11/18/99	3.90	700	23.00	NM	NM	0.00
	11/15/00	3.80	720	23.00	NM	NM	0.00
	11/08/01	3.81	653	21.30	NM	NM	0.00
	11/22/02	3.80	700	24.00	NM	NM	0.54
	01/28/04	3.78	745	23.36	0.40	365.6	1.68
	11/11/04	3.59	551	22.93	NM	NM	0.00
	11/10/05	3.86	749	23.85	0.37	233.6	3.00
	11/16/06	3.91	72	23.67	0.32	392.2	0.11
	11/16/07	3.94	766	22.92	0.33	143.5	0.00
	11/13/08	3.94	749	23.83	0.41	287.4	2.20
	11/12/09	3.98	708	23.77	0.53	166.4	0.52
	11/18/10	3.88	719	23.02	0.87	357.5	0.94
	11/09/11	3.97	661	24.04	0.71	349.9	1.81
	11/08/12	3.70	649	23.77	0.87	401.0	0.32
	11/06/13	3.83	656	23.85	0.68	368.5	1.18
	11/20/14	4.00	621	21.08	0.93	360.0	0.39

**TABLE 3
GROUNDWATER FIELD PARAMETER RESULTS**

**Agrico Site
Pensacola, Florida**

Well I.D.	Date	pH (su)	Conductivity (µS/cm)	Temperature (°C)	Dissolved Oxygen (mg/L)	Oxidation Reduction Potential (mV)	Turbidity (NTU)
AC-13D	09/27/97	4.30	580	24.00	9.50	NM	NM
	11/15/00	3.90	570	21.00	NM	NM	0.00
	11/08/01	4.15	565	23.10	NM	NM	0.00
	11/21/02	3.97	599	23.80	NM	NM	0.00
	01/16/04	4.23	629	23.29	0.08	316.2	0.55
	11/11/04	3.81	598	22.68	NM	NM	0.00
	11/10/05	3.98	706	23.81	0.07	228.9	0.17
	11/16/06	3.97	780	23.56	0.04	390.3	0.02
	11/19/07	4.01	796	22.82	0.05	159.7	0.00
	11/11/08	3.90	815	23.49	0.08	211.1	0.13
	11/12/09	4.02	781	23.66	0.16	213.1	0.22
	11/18/10	3.96	741	22.87	0.61	299.5	0.53
	11/09/11	4.01	810	23.97	0.01	297.3	0.54
AC-14D	09/24/97	5.70	150	24.00	10.10	NM	2.00
	01/28/04	4.85	186	22.73	6.71	221.3	1.75
	11/11/08	5.19	193	23.06	5.97	111.8	0.67
	11/19/14	5.14	171	20.63	6.35	203.0	0.84
AC-21D	09/26/97	4.70	180	22.00	8.70	NM	0.00
	01/29/04	4.81	173	22.92	2.47	255.4	2.24
	11/12/08	5.48	132	23.11	4.86	111.7	2.58
	11/17/14	5.67	111	20.34	5.87	182.3	0.91
AC-22D	09/25/97	4.60	140	23.00	9.60	NM	0.00
	01/29/04	4.57	105	22.72	4.95	167.0	0.26
	11/11/08	4.57	106	23.19	7.73	328.7	2.91
	11/18/14	4.57	138	20.56	8.23	219.9	6.48
AC-23D	09/26/97	4.80	150	24.00	9.80	NM	0.00
	01/22/04	4.57	129	22.93	0.30	381.3	2.30
	11/18/08	4.47	151	23.16	0.41	209.4	0.27
	11/11/14	4.90	124	20.67	0.80	-17.1	0.65
AC-24D	09/26/97	4.40	780	23.00	9.50	NM	0.00
	01/21/04	4.11	747	23.09	0.00	344.9	2.40
	11/18/08	4.24	776	22.77	0.11	198.5	0.32
	11/16/09	4.17	784	23.58	0.19	99.8	0.19
	11/23/10	4.12	753	22.80	0.84	303.8	0.30
	11/14/11	4.16	769	23.76	0.85	339.0	0.44
	11/09/12	3.95	848	22.53	0.10	362.1	1.17
	11/07/13	4.05	748	23.56	0.05	312.5	2.00
AC-24S	11/24/14	4.16	613	23.58	0.29	243.0	1.03
	09/26/97	5.10	80	23.00	9.90	NM	0.00
	11/16/99	5.10	70	23.00	NM	NM	0.00
	11/20/00	5.20	80	23.00	NM	NM	0.00
	11/14/01	5.42	69	21.70	NM	NM	0.00
	11/20/02	4.38	66	23.30	NM	NM	0.57
	01/21/04	5.02	69	23.20	7.04	351.3	2.30
	11/16/04	4.74	76	22.85	NM	NM	0.00
	11/17/05	5.05	90	22.83	10.37	192.5	2.17
	11/21/06	4.90	137	23.17	8.20	282.9	0.05
AC-25D	11/18/08	4.84	104	22.55	7.31	371.1	0.22
	11/24/14	4.68	99	23.39	7.38	228.3	0.77
	09/24/97	4.70	1100	24.00	10.40	NM	0.00
	11/19/99	4.30	1400	23.00	NM	NM	0.00
	11/15/00	4.20	1400	22.00	NM	NM	1.00
	11/08/01	4.31	1240	21.00	NM	NM	9.30
	11/21/02	4.15	1420	22.90	NM	NM	0.05
	01/22/04	4.06	1534	22.61	0.68	177.3	4.19
	11/15/04	4.30	1204	22.69	NM	NM	4.49
	11/10/05	4.17	1502	23.28	0.08	125.4	1.10
	11/20/06	4.16	1481	22.79	0.03	360.9	1.50
	11/20/07	4.23	1449	22.26	0.07	181.9	0.25
	11/18/08	4.08	1356	22.23	0.07	-292.3	0.82
	11/17/09	4.17	1398	22.74	0.12	279.6	0.29
	11/23/10	4.11	1388	22.31	0.42	341.2	2.31
	11/15/11	4.15	1422	23.11	0.10	364.9	0.47
	11/14/12	4.00	1371	23.07	0.09	369.8	0.40
	11/12/13	3.96	1326	23.10	0.04	258.7	0.78
	11/20/14	4.14	1287	20.74	0.10	381.4	0.77

**TABLE 3
GROUNDWATER FIELD PARAMETER RESULTS**

**Agrico Site
Pensacola, Florida**

Well I.D.	Date	pH (su)	Conductivity (µS/cm)	Temperature (°C)	Dissolved Oxygen (mg/L)	Oxidation Reduction Potential (mV)	Turbidity (NTU)
AC-26D	09/24/97	6.00	80	24.00	10.40	NM	3.00
	01/20/04	4.73	85	23.10	1.48	152.2	2.80
	11/12/08	6.53	106	23.18	0.52	-25.5	1.77
	11/19/14	6.68	99	20.61	0.33	3.4	0.33
AC-26S	09/24/97	4.80	100	24.00	10.00	NM	0.00
	11/16/99	4.60	130	23.00	NM	NM	1.00
	11/20/00	4.50	120	21.00	NM	NM	1.00
	11/14/01	4.70	139	21.00	NM	NM	0.00
	11/21/02	4.42	133	23.20	NM	NM	2.00
	01/20/04	4.45	142	22.50	7.92	419.9	3.10
	11/10/04	4.42	160	23.00	NM	NM	0.96
	11/09/05	4.57	130	23.77	7.66	257.9	0.73
	11/20/06	4.52	158	23.54	7.09	235.1	0.19
	11/12/08	4.53	109	23.76	7.73	171.1	1.60
	11/19/14	5.20	86	20.60	8.73	223.4	0.77
AC-27D	09/24/97	6.40	80	23.00	9.80	NM	0.00
	01/13/04	6.23	73	22.60	0.69	9.8	2.45
	11/11/05	6.53	77	22.87	0.19	-39.4	1.89
	11/18/08	4.68	118	22.87	8.04	286.9	0.55
	11/13/14	6.66	94	19.93	0.64	-57.5	3.16
AC-27S	09/24/97	5.00	70	23.00	10.00	NM	0.00
	01/13/04	4.67	93	22.30	6.37	238.0	1.34
	11/11/05	4.67	236	22.92	7.20	275.8	2.12
	11/17/08	6.51	83	22.21	0.22	39.1	1.50
	11/13/14	4.73	106	20.04	8.24	202.4	0.21
AC-28D	09/27/97	4.30	210	23.00	8.80	NM	NM
	01/21/04	4.47	205	23.20	NM	NM	0.00
	11/17/08	4.26	350	23.23	3.00	234.9	0.10
	11/12/09	4.35	287	23.34	3.29	191.5	0.19
	11/19/10	4.27	332	22.66	2.67	283.2	0.57
	11/10/11	4.42	345	23.60	2.98	349.0	0.47
	11/12/12	4.24	334	23.40	3.57	382.6	0.24
	11/06/13	4.22	317	23.50	3.12	288.8	0.64
	11/20/14	NM	NM	NM	NM	NM	NM
AC-29D	09/27/97	4.10	1700	23.00	9.10	NM	NM
	11/18/99	4.20	1500	22.00	NM	NM	0.00
	11/20/00	4.10	1300	22.00	NM	NM	1.00
	11/13/01	4.29	990	22.20	NM	NM	0.00
	11/25/02	3.87	1075	24.00	NM	NM	0.00
	01/23/04	4.14	1050	23.34	0.48	251.7	0.00
	11/12/04	4.08	797	22.61	NM	NM	2.74
	11/16/05	4.11	723	23.71	0.04	188.7	2.57
	11/17/06	4.25	744	23.68	0.05	348.8	0.00
	11/20/07	4.18	772	22.96	0.10	178.0	0.45
	11/18/08	4.05	790	23.55	0.23	309.6	0.11
	11/17/09	4.13	768	23.58	0.11	171.9	0.18
	11/19/10	4.08	782	23.02	0.39	343.5	0.62
	11/11/11	4.17	794	23.91	0.03	399.9	0.78
	11/13/12	4.04	762	23.74	0.11	267.0	0.30
	11/07/13	4.02	661	23.83	0.12	357.3	0.56
	11/17/14	4.09	655	21.13	0.20	408.3	0.81

**TABLE 3
GROUNDWATER FIELD PARAMETER RESULTS**

**Agrico Site
Pensacola, Florida**

Well I.D.	Date	pH (su)	Conductivity (µS/cm)	Temperature (°C)	Dissolved Oxygen (mg/L)	Oxidation Reduction Potential (mV)	Turbidity (NTU)
AC-30D	09/26/97	4.20	1600	23.00	9.60	NM	0.00
	11/22/99	4.20	1300	23.00	NM	NM	0.00
	11/17/00	4.00	1100	22.00	NM	NM	0.00
	11/13/01	4.30	920	21.70	NM	NM	0.00
	11/25/02	3.89	1022	23.90	NM	NM	0.00
	01/15/04	4.20	873	23.35	0.04	269.0	0.00
	11/16/04	3.94	610	22.19	NM	NM	0.00
	11/17/05	4.23	493	23.18	0.09	263.2	2.25
	11/17/06	4.24	373	23.73	0.12	400.4	0.00
	11/20/07	4.17	303	22.90	0.19	123.5	0.60
	11/18/08	3.94	337	23.60	0.37	255.9	0.12
	11/17/09	4.07	272	23.46	0.56	162.0	0.11
	11/22/10	3.40	226	23.00	1.93	269.4	0.28
	11/14/11	4.11	242	23.97	1.23	318.1	0.14
ACB-31S	11/14/12	4.11	268	23.75	1.25	295.8	0.12
	11/12/13	3.89	242	23.75	1.36	306.4	0.60
	11/25/14	4.03	200	23.62	2.68	335.0	0.09
	11/23/98	5.90	120	23.00	NM	NM	6.00
	05/25/99	5.80	220	26.00	NM	NM	2.00
	11/16/99	6.10	170	21.00	NM	NM	8.00
	05/16/00	5.70	130	24.00	NM	NM	7.00
	11/14/00	5.30	170	20.00	NM	NM	3.00
	05/08/01	5.45	176	22.50	NM	NM	999*
	11/06/01	5.73	111	22.10	NM	NM	4.6
	05/06/02	4.57	144	22.60	6.13	379	15.4
	05/07/03	5.17	108	22.83	NM	NM	7.2
	01/13/04	5.84	196	23.86	6.31	123	0.8
	05/10/04	5.78	208	24.76	NM	NM	10.2
	11/09/04	5.92	296	23.70	NM	NM	9.3
	05/10/05	5.56	248	23.12	6.78	103	5.1
	11/08/05	6.18	176	23.71	9.06	187	5.0
	05/17/06	6.00	218	23.19	6.99	265	2.0
	11/14/06	5.83	247	23.25	7.39	162	2.1
	05/16/07	5.49	223	23.14	7.71	213	2.4
ACB-32S	11/15/07	5.67	208	22.50	7.75	37	0.6
	05/15/08	5.32	218	23.19	7.87	109	0.9
	11/13/08	5.36	229	23.43	7.38	168	1.2
	11/19/09	5.89	220	23.38	6.66	88	2.1
	11/16/10	6.29	228	22.59	6.82	218	0.9
	11/08/11	6.01	220	23.61	8.45	172	3.5
	11/06/12	5.59	178	23.73	8.69	154	0.4
	11/05/13	6.12	172	23.83	8.43	112	1.2
	11/12/14	5.97	167	20.84	10.40	140.6	0.24
	11/23/98	6.20	100	23.00	NM	NM	30.00
	05/25/99	5.90	140	24.00	NM	NM	3.00
	11/16/99	5.70	170	21.00	NM	NM	21.00
	05/16/00	5.80	140	23.00	NM	NM	3.00
	11/14/00	5.70	160	22.00	NM	NM	4.00
	05/08/01	5.96	256	22.60	NM	NM	999*
	11/06/01	6.43	185	22.30	NM	NM	97
	05/06/02	5.22	133	23.20	8.04	401	19.3
	05/07/03	6.13	295	23.22	NM	NM	8.0
	01/13/04	6.36	322	24.10	6.45	120.4	6.9
	05/10/04	6.01	222	24.13	NM	NM	4.5
	11/09/04	6.06	294	23.46	NM	NM	2.7
	05/10/05	5.82	362	23.16	7.03	90.3	4.7
	11/08/05	6.36	173	23.90	6.05	197.4	2.4
	05/17/06	5.78	180	22.86	3.27	361.2	1.0
	11/14/06	6.43	122	24.22	2.83	113.2	0.6
	05/16/07	6.23	161	23.40	3.86	153.7	2.3
	11/15/07	6.53	174	23.27	5.43	62.6	1.8
	05/15/08	6.2	196	23.59	6.03	112.8	2.1
	11/13/08	6.48	208	24.17	6.41	48.1	2.0
	11/19/09	6.44	141	23.51	6.88	132.8	1.9
	11/16/10	6.79	137	22.79	7.18	185.5	0.7
	11/08/11	6.51	127	24.12	7.61	158.1	1.7
	11/06/12	6.18	100	24.00	7.65	111.7	1.9
	11/05/13	6.51	70	24.63	7.09	93.4	1.0
	11/13/14	6.47	132	19.90	8.68	147.5	0.78

**TABLE 3
GROUNDWATER FIELD PARAMETER RESULTS**

**Agrico Site
Pensacola, Florida**

Well I.D.	Date	pH (su)	Conductivity (µS/cm)	Temperature (°C)	Dissolved Oxygen (mg/L)	Oxidation Reduction Potential (mV)	Turbidity (NTU)
AC-33S	11/23/98	6.30	120	23.00	NM	NM	37.00
	05/25/99	5.60	90	24.00	NM	NM	4.00
	05/16/00	5.60	50	23.00	NM	NM	4.00
	11/14/00	5.40	80	21.00	NM	NM	2.00
	05/08/01	5.14	154	22.40	NM	NM	999*
	11/06/01	5.55	129	22.40	NM	NM	110
	05/06/02	4.36	88	22.20	4.93	421	16.2
	05/07/03	5.20	195	22.78	NM	NM	6.81
	01/14/04	5.63	405	23.76	3.70	243.7	0.95
	05/10/04	4.83	144	23.99	NM	NM	1.96
	11/09/04	4.93	160	23.02	NM	NM	3.21
	05/10/05	5.55	464	23.50	0.84	93.8	5.10
	11/08/05	6.15	360	24.27	0.69	146.9	5.27
	05/17/06	4.71	357	23.65	0.55	405.8	1.40
	11/14/06	5.07	97	24.97	0.86	246.4	2.08
	05/16/07	4.81	116	23.32	1.94	268.5	1.12
	11/15/07	5.36	120	22.66	2.46	13.9	0.60
	05/15/08	5.11	124	23.19	2.36	93.9	0.85
	11/14/08	4.92	125	23.37	2.52	137.3	0.36
	11/19/09	5.09	108	24.17	2.80	114.5	2.26
AC-34S	11/16/10	5.42	130	22.42	1.01	234.1	0.79
	11/08/11	5.42	116	23.35	1.91	214.5	1.21
	11/06/12	5.14	304	23.21	2.65	182.0	0.36
	11/05/13	5.14	102	23.44	1.62	197.0	0.99
	11/13/14	5.13	115	19.95	2.62	161.0	0.69
	11/23/98	4.80	150	23.00	NM	NM	26.00
	05/25/99	4.60	210	25.00	NM	NM	4.00
	05/16/00	4.80	120	24.00	NM	NM	3.00
	11/14/00	4.60	170	21.00	NM	NM	5.00
	05/08/01	4.67	200	22.30	NM	NM	999*
	11/06/01	5.40	219	22.20	NM	NM	199
	05/07/02	4.73	214	22.60	2.78	375	134
	05/07/03	4.98	207	22.69	NM	NM	8.49
	01/14/04	5.11	304	23.40	2.69	212.0	6.00
	05/10/04	4.68	353	23.52	NM	NM	4.21
	11/09/04	4.55	351	22.94	NM	NM	2.94
	05/10/05	4.30	407	23.54	2.02	146.6	4.20
	11/08/05	4.63	250	23.64	1.71	226.5	3.04
	05/17/06	4.61	310	23.41	0.92	330.2	0.00
	11/14/06	4.42	298	23.00	0.20	290.5	1.05
AC-35D	05/16/07	4.08	284	23.20	0.51	234.1	0.64
	11/15/07	4.41	240	22.29	0.78	90.7	1.30
	05/15/08	4.20	235	22.97	2.01	142.7	1.64
	11/14/08	4.14	210	23.26	2.17	182.3	1.19
	11/19/09	4.39	209	23.36	3.98	154.8	2.01
	11/17/10	4.72	246	22.35	3.65	271.7	1.64
	11/09/11	4.86	220	23.27	3.24	243.8	1.92
	11/07/12	5.21	202	23.22	5.40	200.7	1.01
	11/05/13	5.39	192	23.68	4.46	159.7	1.65
	11/13/14	5.57	168	20.28	5.64	163.5	2.08
	11/18/99	4.20	2200	22.00	NM	NM	8.00
	11/15/00	4.10	2200	22.00	NM	NM	0.00
	11/08/01	4.04	2010	21.40	NM	NM	3.80
	11/21/02	3.91	2037	22.80	NM	NM	2.80
	01/15/04	4.05	2060	22.36	0.01	362.0	0.80
	11/15/04	3.57	1607	21.95	NM	NM	3.89
	11/16/05	3.94	1889	22.87	0.13	187.8	9.20
	11/20/06	4.04	1818	22.89	0.05	237.7	2.20
	11/20/07	4.07	1725	22.25	0.06	210.8	0.00
	11/19/08	3.88	1749	22.75	0.23	271.6	0.91
	11/19/09	4.01	1736	22.97	0.09	193.1	1.43
	11/23/10	4.29	1737	22.36	0.38	247.7	8.99
	11/16/11	3.94	1611	22.98	0.10	303.7	0.24
	11/15/12	3.91	1545	22.93	0.06	281.4	0.28
	11/13/13	3.90	1495	23.00	0.08	351.5	0.59
	11/24/14	3.99	1381	23.16	0.84	233.6	0.65

**TABLE 3
GROUNDWATER FIELD PARAMETER RESULTS**

**Agrico Site
Pensacola, Florida**

Well I.D.	Date	pH (su)	Conductivity (µS/cm)	Temperature (°C)	Dissolved Oxygen (mg/L)	Oxidation Reduction Potential (mV)	Turbidity (NTU)
AC-36D	11/18/99	6.80	170	22.00	NM	NM	16.00
	11/15/00	6.80	180	21.00	NM	NM	5.00
	11/08/01	5.44	125	22.60	NM	NM	13.50
	11/20/02	4.52	122	22.70	NM	NM	5.20
	01/14/04	5.02	126	22.20	6.68	286.3	2.60
	11/11/04	5.21	272	22.67	NM	NM	2.01
	11/09/05	5.01	138	22.78	6.85	250.2	2.00
	11/16/06	4.97	129	22.66	6.44	182.9	0.21
	11/16/07	5.05	126	22.03	6.42	50.7	0.00
	11/11/08	4.86	144	22.66	6.57	210.1	1.11
	11/11/09	4.80	131	23.05	6.98	286.6	1.81
	11/18/10	4.71	136	22.24	6.29	261.0	1.60
NWD-2D	11/09/11	4.92	144	22.90	6.63	266.3	2.63
	11/06/12	4.68	139	22.76	6.78	288.3	3.24
	11/06/13	4.74	145	22.86	6.35	214.1	2.14
	11/18/14	4.89	151	20.31	6.63	238.9	4.21
NWD-2S	09/25/97	4.80	90	23.00	9.40	NM	0.00
	01/19/04	4.64	112	23.18	4.72	261.3	2.80
	11/13/08	4.91	112	23.50	6.22	148.9	1.98
	11/11/14	4.98	121	20.84	5.13	145.5	0.13
	09/25/97	4.70	120	23.00	9.90	NM	0.00
	11/17/99	4.60	150	24.00	NM	NM	0.00
	11/20/00	4.50	120	23.00	NM	NM	0.00
	11/14/01	4.69	125	21.70	NM	NM	0.00
	11/20/02	4.39	108	23.30	NM	NM	0.00
	01/19/04	4.53	158	22.87	7.21	334.5	9.60
	11/10/04	4.53	163	23.24	NM	NM	3.11
	11/17/05	4.70	143	23.15	9.01	179.4	3.12
NWD-4D	11/21/06	4.67	148	23.09	7.48	236.2	0.00
	11/12/08	4.54	120	23.34	8.34	271.4	2.31
	11/11/14	4.66	95	20.79	9.02	125.3	0.47
	09/26/97	4.90	210	24.00	10.10	NM	0.00
	11/17/99	4.80	220	22.00	NM	NM	0.00
	11/20/00	4.70	220	22.00	NM	NM	0.00
	11/13/01	5.00	226	20.60	NM	NM	4.00
	11/22/02	4.52	196	22.80	NM	NM	0.00
	01/21/04	4.68	229	22.32	0.06	378.9	2.57
	11/16/04	4.45	220	22.47	NM	NM	0.00
	11/15/05	4.75	220	22.60	0.08	174.1	2.47
	11/21/06	4.66	187	22.55	0.06	270.0	0.26
NWD-4S	11/19/07	4.84	184	21.99	0.11	130.5	0.00
	11/19/08	4.68	155	22.16	0.04	-148.9	0.41
	11/18/09	5.04	154	22.66	0.08	-43.6	0.24
	11/23/10	6.09	155	22.22	0.66	107.4	0.46
	11/15/11	5.87	163	22.88	0.01	-55.2	0.43
	11/08/12	5.54	188	22.75	0.15	22.1	0.18
	11/08/13	5.52	196	22.97	0.09	34.8	0.60
	11/14/14	5.71	183	20.51	0.30	61.3	3.48
	09/26/97	5.20	30	23.00	10.90	NM	2.00
	11/16/99	5.40	30	22.00	NM	NM	1.00
	11/20/00	5.30	40	22.00	NM	NM	0.00
	11/13/01	5.30	41	22.00	NM	NM	9.60
PIP-D	11/22/02	4.83	37	22.40	NM	NM	0.20
	01/21/04	4.77	55	22.02	7.45	426.1	2.50
	11/16/04	4.57	59	22.17	NM	NM	0.23
	11/15/05	4.97	70	22.48	8.87	220.4	2.28
	11/21/06	4.92	77	22.35	7.06	235.8	0.54
	11/19/08	4.67	66	22.06	7.35	225.7	0.85
	11/14/14	4.93	41	19.96	8.88	269.9	0.91
	11/14/05	4.91	65	22.60	8.48	260.9	8.45
	11/22/06	4.72	98	21.70	7.17	219.3	24.60
	11/16/07	5.05	77	20.11	7.00	61.5	2.50
	11/13/08	4.57	109	22.32	7.49	211.6	44.10
	11/18/09	4.94	80	21.47	6.46	173.8	18.10
	11/24/10	6.06	90	22.73	6.39	170.5	19.20
	11/11/11	5.05	66	21.07	7.37	294.9	28.30
	11/13/12	4.68	80	21.20	6.31	168.1	6.72
	11/13/13	4.83	90	20.00	6.70	202.8	1.28
	11/14/14	4.79	92	18.93	7.31	328.8	0.87

NOTES:
 su = standard units
 µS/cm=microSiemens per centimeter
 °C = Degrees Celsius
 mg/L = milligrams per Liter
 mV = millivolt
 NTU = Nephelometric Turbidity Units
 NM = Not Measured
 * = turbidity reading above instrument capabilities
 Wells purged with a bailer during the May 2001 sampling event
 ** = Well purged with a bailer

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
MAIN PRODUCING ZONE				
AC-2D	Sep-97	92.74	57.74	35.00
	Nov-99		61.09	31.65
	Nov-00		NM	NM
	Nov-01		63.02	29.72
	Nov-02		62.53	30.21
	Jan-04		57.36	35.38
	Nov-04		56.39	36.35
	Nov-05		49.02	43.72
	Nov-06		54.55	38.19
	Nov-07		57.49	35.25
	Nov-08		57.20	35.54
	Nov-09		52.65	40.09
	Nov-10		50.83	41.91
	Nov-11		49.11	43.63
	Nov-12		53.03	39.71
	Nov-13		53.03	39.71
	Nov-14		49.20	43.54
AC-3D	Sep-97	88.07	61.91	26.16
	Nov-99		63.15	24.92
	Nov-00		66.42	21.65
	Nov-01		67.42	20.65
	Nov-02		67.09	20.98
	Jan-04		62.17	25.90
	Nov-04		61.35	26.72
	Nov-05		55.02	33.05
	Nov-06		59.95	28.12
	Nov-07		62.71	25.36
	Nov-08		62.17	25.90
	Nov-09		60.78	27.29
	Nov-10		56.32	31.75
	Nov-11		60.06	28.01
	Nov-12		58.33	29.74
	Nov-13		58.41	29.66
	Nov-14		54.90	33.17
AC-5D	Sep-97	82.40	50.16	32.24
	Nov-99		53.21	29.19
	Nov-00		54.83	27.57
	Nov-01		57.58	24.82
	Nov-02		55.47	26.93
	Jan-04		50.67	31.73
	Nov-04		49.60	32.80
	Nov-05		44.83	37.57
	Nov-06		47.18	35.22
	Nov-07		51.22	31.18
	Nov-08		49.67	32.73
	Nov-09		48.40	34.00
	Nov-10		43.27	39.13
	Nov-11		47.48	34.92
	Nov-12		47.24	35.16
	Nov-13		46.90	35.50
	Nov-14		41.88	40.52

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
MAIN PRODUCING ZONE				
AC-6D	Sep-97	69.19	55.72	13.47
	Nov-99		50.20	18.99
	Nov-00		52.26	16.93
	Nov-01		53.43	15.76
	Nov-02		51.26	17.93
	Jan-04		47.22	21.97
	Nov-04		42.26	26.93
	Nov-05		40.98	28.21
	Nov-06		45.13	24.06
	Nov-07		47.60	21.59
	Nov-08		46.76	22.43
	Nov-09		44.71	24.48
	Nov-10		40.76	28.43
	Nov-11		45.21	23.98
	Nov-12		43.92	25.27
	Nov-13		43.74	25.45
	Nov-14		41.25	27.94
AC-8D	Sep-97	76.44	66.97	9.47
	Nov-99		63.81	12.63
	Nov-00		65.67	10.77
	Nov-01		65.88	10.56
	Nov-02		65.29	11.15
	Jan-04		61.30	15.14
	Nov-04		59.91	16.53
	Nov-05		56.35	20.09
	Nov-06		60.20	16.24
	Nov-07		61.93	14.51
	Nov-08		61.33	15.11
	Nov-09		59.89	16.55
	Nov-10		57.41	19.03
	Nov-11		60.63	15.81
	Nov-12		59.26	17.18
	Nov-13		58.71	17.73
	Nov-14		57.05	19.39
AC-9D2	Sep-97	64.13	55.27	8.86
	Nov-99		55.39	8.74
	Nov-00		56.68	7.45
	Nov-01		57.01	7.12
	Nov-02		56.87	7.26
	Jan-04		54.56	9.57
	Nov-04		54.02	10.11
	Nov-05		51.37	12.76
	Nov-06		53.83	10.30
	Nov-07		54.73	9.40
	Nov-08		54.36	9.77
	Nov-09		52.58	11.55
	Nov-10		51.46	12.67
	Nov-11		53.87	10.26
	Nov-12		52.88	11.25
	Nov-13		52.68	11.45
	Nov-14		51.47	12.66

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
MAIN PRODUCING ZONE				
AC-10D	Sep-97	79.48	70.39	9.09
	Nov-99		69.04	10.44
	Nov-00		70.67	8.81
	Nov-01		70.86	8.62
	Nov-02		70.53	8.95
	Jan-04		67.28	12.20
	Nov-04		66.79	12.69
	Nov-05		63.20	16.28
	Nov-06		66.47	13.01
	Nov-07		67.72	11.76
	Nov-08		67.24	12.24
	Nov-09		65.67	13.81
	Nov-10		63.93	15.55
	Nov-11		66.79	12.69
	Nov-12		65.55	13.93
	Nov-13		65.13	14.35
	Nov-14		63.66	15.82
AC-11D	Sep-97	73.17	67.10	6.07
	Nov-99		66.69	6.48
	Nov-00		67.69	5.48
	Nov-01		67.72	5.45
	Nov-02		67.45	5.72
	Jan-04		65.01	8.16
	Nov-04		64.58	8.59
	Nov-05		62.06	11.11
	Nov-06		64.73	8.44
	Nov-07		65.32	7.85
	Nov-08		65.03	8.14
	Nov-09		63.38	9.79
	Nov-10		62.65	10.52
	Nov-11		65.06	8.11
	Nov-12		64.01	9.16
	Nov-13		63.43	9.74
	Nov-14		62.44	10.73
AC-12D	Sep-97	79.23	67.46	11.77
	Nov-99		66.41	12.82
	Nov-00		68.29	10.94
	Nov-01		68.64	10.59
	Nov-02		68.38	10.85
	Jan-04		65.23	14.00
	Nov-04		64.78	14.45
	Nov-05		60.25	18.98
	Nov-06		63.79	15.44
	Nov-07		65.29	13.94
	Nov-08		64.78	14.45
	Nov-09		63.13	16.10
	Nov-10		60.87	18.36
	Nov-11		63.93	15.30
	Nov-12		62.62	16.61
	Nov-13		62.35	16.88
	Nov-14		60.48	18.75

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
MAIN PRODUCING ZONE				
AC-13D	Sep-97	74.65	67.25	7.40
	Nov-99		66.97	7.68
	Nov-00		68.21	6.44
	Nov-01		68.43	6.22
	Nov-02		68.23	6.42
	Jan-04		65.99	8.66
	Nov-04		65.44	9.21
	Nov-05		63.01	11.64
	Nov-06		65.37	9.28
	Nov-07		66.16	8.49
	Nov-08		65.78	8.87
	Nov-09		63.87	10.78
	Nov-10		63.11	11.54
	Nov-11		65.55	9.10
	Nov-12		64.57	10.08
	Nov-13		64.29	10.36
	Nov-14		63.24	11.41
AC-14D	Sep-97	49.79	45.49	4.30
	Nov-99		45.56	4.23
	Nov-00		46.05	3.74
	Nov-01		46.37	3.42
	Nov-02		46.13	3.66
	Jan-04		44.91	4.88
	Nov-04		44.30	5.49
	Nov-05		42.88	6.91
	Nov-06		44.52	5.27
	Nov-07		44.59	5.20
	Nov-08		44.45	5.34
	Nov-09		42.57	7.22
	Nov-10		42.73	7.06
	Nov-11		44.63	5.16
	Nov-12		43.93	5.86
	Nov-13		43.57	6.22
	Nov-14		43.16	6.63
AC-21D	Sep-97	75.47	48.23	27.24
	Nov-99		49.66	25.81
	Nov-00		51.21	24.26
	Nov-01		53.63	21.84
	Nov-02		51.62	23.85
	Jan-04		46.83	28.64
	Nov-04		45.82	29.65
	Nov-05		40.22	35.25
	Nov-06		43.75	31.72
	Nov-07		60.11	15.36
	Nov-08		NM	NM
	Nov-09		44.64	30.83
	Nov-10		39.86	35.61
	Nov-11		44.03	31.44
	Nov-12		43.52	31.95
	Nov-13		43.20	32.27
	Nov-14		38.50	36.97

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
MAIN PRODUCING ZONE				
AC-22D	Sep-97	76.58	63.27	13.31
	Nov-99		NM	NM
	Nov-00		NM	NM
	Nov-01		NM	NM
	Nov-02		61.81	14.77
	Jan-04		57.22	19.36
	Nov-04		56.59	19.99
	Nov-05		51.17	25.41
	Nov-06		55.56	21.02
	Nov-07		57.86	18.72
	Nov-08		57.04	19.54
	Nov-09		55.70	20.88
	Nov-10		52.15	24.43
	Nov-11		55.81	20.77
	Nov-12		54.33	22.25
	Nov-13		54.11	22.47
	Nov-14		51.68	24.90
AC-23D	Sep-97	79.51	58.46	21.05
	Nov-99		60.16	19.35
	Nov-00		62.83	16.68
	Nov-01		63.42	16.09
	Nov-02		63.18	16.33
	Jan-04		59.35	20.16
	Nov-04		58.73	20.78
	Nov-05		53.34	26.17
	Nov-06		58.17	21.34
	Nov-07		60.00	19.51
	Nov-08		59.72	19.79
	Nov-09		58.05	21.46
	Nov-10		54.68	24.83
	Nov-11		58.01	21.50
	Nov-12		56.11	23.40
	Nov-13		56.23	23.28
	Nov-14		53.64	25.87
AC-24D	Sep-97	79.60	65.14	14.46
	Nov-99		66.17	13.43
	Nov-00		68.29	11.31
	Nov-01		68.78	10.82
	Nov-02		68.55	11.05
	Jan-04		65.33	14.27
	Nov-04		64.78	14.82
	Nov-05		60.70	18.90
	Nov-06		64.35	15.25
	Nov-07		69.78	9.82
	Nov-08		65.50	14.10
	Nov-09		63.84	15.76
	Nov-10		61.46	18.14
	Nov-11		64.41	15.19
	Nov-12		62.86	16.74
	Nov-13		62.77	16.83
	Nov-14		60.85	18.75

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
MAIN PRODUCING ZONE				
AC-25D	Sep-97	39.75	33.71	6.04
	Nov-99		34.28	5.47
	Nov-00		35.44	4.31
	Nov-01		35.76	3.99
	Nov-02		35.48	4.27
	Jan-04		33.99	5.76
	Nov-04		33.22	6.53
	Nov-05		31.30	8.45
	Nov-06		33.42	6.33
	Nov-07		33.83	5.92
	Nov-08		33.69	6.06
	Nov-09		32.07	7.68
	Nov-10		31.33	8.42
	Nov-11		33.27	6.48
	Nov-12		32.42	7.33
	Nov-13		32.17	7.58
	Nov-14		31.51	8.24
AC-26D	Sep-97	26.70	20.11	6.59
	Nov-99		19.08	7.62
	Nov-00		20.47	6.23
	Nov-01		20.61	6.09
	Nov-02		20.40	6.30
	Jan-04		19.65	7.05
	Nov-04		19.02	7.68
	Nov-05		18.17	8.53
	Nov-06		18.98	7.72
	Nov-07		19.30	7.40
	Nov-08		19.08	7.62
	Nov-09		17.23	9.47
	Nov-10		17.27	9.43
	Nov-11		18.96	7.74
	Nov-12		18.53	8.17
	Nov-13		18.55	8.15
	Nov-14		17.94	8.76
AC-27D	Sep-97	18.55	13.57	4.98
	Nov-99		13.46	5.09
	Nov-00		14.97	3.58
	Nov-01		15.05	3.50
	Nov-02		14.90	3.65
	Jan-04		14.13	4.42
	Nov-04		13.66	4.89
	Nov-05		12.42	6.13
	Nov-06		14.13	4.42
	Nov-07		13.91	4.64
	Nov-08		13.46	5.09
	Nov-09		11.22	7.33
	Nov-10		12.51	6.04
	Nov-11		13.91	4.64
	Nov-12		13.63	4.92
	Nov-13		13.43	5.12
	Nov-14		13.25	5.30

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
MAIN PRODUCING ZONE				
AC-28D	Sep-97	74.89	65.34	9.55
	Nov-99		65.70	9.19
	Nov-00		67.07	7.82
	Nov-01		67.43	7.46
	Nov-02		67.29	7.60
	Jan-04		64.96	9.93
	Nov-04		NM	NM
	Nov-05		61.72	13.17
	Nov-06		64.19	10.70
	Nov-07		65.12	9.77
	Nov-08		64.78	10.11
	Nov-09		63.02	11.87
	Nov-10		61.83	13.06
	Nov-11		64.21	10.68
	Nov-12		63.20	11.69
	Nov-13		63.02	11.87
	Nov-14		NM	NM
AC-29D	Sep-97	82.26	62.17	20.09
	Nov-99		62.86	19.40
	Nov-00		65.62	16.64
	Nov-01		66.29	15.97
	Nov-02		66.18	16.08
	Jan-04		61.62	20.64
	Nov-04		61.06	21.20
	Nov-05		55.47	26.79
	Nov-06		59.95	22.31
	Nov-07		62.30	19.96
	Nov-08		61.75	20.51
	Nov-09		60.21	22.05
	Nov-10		56.50	25.76
	Nov-11		60.12	22.14
	Nov-12		58.44	23.82
	Nov-13		58.37	23.89
	Nov-14		55.54	26.72
AC-30D	Sep-97	85.73	71.39	14.34
	Nov-99		72.13	13.60
	Nov-00		74.17	11.56
	Nov-01		74.64	11.09
	Nov-02		74.48	11.25
	Jan-04		71.28	14.45
	Nov-04		70.75	14.98
	Nov-05		66.83	18.90
	Nov-06		70.27	15.46
	Nov-07		71.66	14.07
	Nov-08		71.35	14.38
	Nov-09		69.72	16.01
	Nov-10		67.34	18.39
	Nov-11		70.33	15.40
	Nov-12		68.92	16.81
	Nov-13		68.81	16.92
	Nov-14		66.94	18.79

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
MAIN PRODUCING ZONE				
AC-35D	Sep-97	10.49	NM	NM
	Nov-99		5.22	5.27
	Nov-00		6.15	4.34
	Nov-01		6.36	4.13
	Nov-02		6.27	4.22
	Jan-04		5.11	5.38
	Nov-04		4.68	5.81
	Nov-05		3.50	6.99
	Nov-06		4.68	5.81
	Nov-07		5.07	5.42
	Nov-08		4.67	5.82
	Nov-09		3.06	7.43
	Nov-10		2.88	7.61
	Nov-11		4.30	6.19
	Nov-12		4.13	6.36
	Nov-13		4.06	6.43
	Nov-14		3.33	7.16
AC-36D	Sep-97	5.26	NM	NM
	Nov-99		2.32	2.94
	Nov-00		2.90	2.36
	Nov-01		3.13	2.13
	Nov-02		2.90	2.36
	Jan-04		2.24	3.02
	Nov-04		1.66	3.60
	Nov-05		1.01	4.25
	Nov-06		1.98	3.28
	Nov-07		1.84	3.42
	Nov-08		1.72	3.54
	Nov-09		0.00	5.26
	Nov-10		0.50	4.76
	Nov-11		1.93	3.33
	Nov-12		1.55	3.71
	Nov-13		1.23	4.03
	Nov-14		1.21	4.05
NWD-2D	Sep-97	76.80	51.69	25.11
	Nov-99		51.58	25.22
	Nov-00		53.63	23.17
	Nov-01		55.32	21.48
	Nov-02		53.89	22.91
	Jan-04		51.37	25.43
	Nov-04		50.51	26.29
	Nov-05		44.75	32.05
	Nov-06		48.84	27.96
	Nov-07		52.14	24.66
	Nov-08		50.87	25.93
	Nov-09		49.51	27.29
	Nov-10		45.09	31.71
	Nov-11		49.11	27.69
	Nov-12		48.02	28.78
	Nov-13		47.73	29.07
	Nov-14		44.15	32.65

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
MAIN PRODUCING ZONE				
NWD-4D	Sep-97	34.70	19.52	15.18
	Nov-99		20.92	13.78
	Nov-00		22.36	12.34
	Nov-01		22.74	11.96
	Nov-02		22.12	12.58
	Jan-04		20.32	14.38
	Nov-04		NM	NM
	Nov-05		16.92	17.78
	Nov-06		20.11	14.59
	Nov-07		20.55	14.15
	Nov-08		16.92	17.78
	Nov-09		18.81	15.89
	Nov-10		17.32	17.38
	Nov-11		19.68	15.02
	Nov-12		18.21	16.49
	Nov-13		18.19	16.51
	Nov-14		16.91	17.79
PIP-D	Sep-97	86.05	NM	NM
	Nov-99		NM	NM
	Nov-00		NM	NM
	Nov-01		NM	NM
	Nov-02		NM	NM
	Jan-04		NM	NM
	Nov-04		NM	NM
	Nov-05		NM	NM
	Nov-06		NM	NM
	Nov-07		NM	NM
	Nov-08		47.63	38.42
	Nov-09		46.74	39.31
	Nov-10		41.05	45.00
	Nov-11		45.23	40.82
	Nov-12		43.24	42.81
	Nov-13		43.53	42.52
	Nov-14		39.15	46.90

NOTES:

ft NGVD = feet above National Geodetic Vertical Datum of 1988.

ft btoc = feet below top of casing.

NM = Not Measured

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
SURFICIAL ZONE				
AC-2S	May-97	88.65	NM	NM
	Sep-97		51.40	37.25
	Nov-97		NM	NM
	May-98		NM	NM
	Nov-98		NM	NM
	May-99		NM	NM
	Nov-99		49.81	38.84
	May-00		NM	NM
	Nov-00		58.68	29.97
	May-01		59.37	29.28
	Nov-01		59.94	28.71
	May-02		61.29	27.36
	Nov-02		60.22	28.43
	May-03		NM	NM
	Jan-04		53.90	34.75
	May-04		54.44	34.21
	Nov-04		52.71	35.94
	May-05		46.87	41.78
	Nov-05		44.76	43.89
	May-06		NM	NM
	Nov-06		50.61	38.04
	May-07		52.94	35.71
	Nov-07		53.89	34.76
	May-08		53.02	35.63
	Nov-08		53.57	35.08
	Nov-09		55.93	32.72
	Nov-10		46.73	41.92
	Nov-11		46.73	41.92
	Nov-12		48.74	39.91
	Nov-13		49.19	39.46
	Nov-14		44.74	43.91
AC-3S	May-97	88.06	54.49	33.57
	Sep-97		55.44	32.62
	Nov-97		NM	NM
	May-98		50.19	37.87
	Nov-98		50.21	37.85
	May-99		56.37	31.69
	Nov-99		57.31	30.75
	May-00		NM	NM
	Nov-00		61.93	26.13
	May-01		NM	NM
	Nov-01		62.97	25.09
	May-02		NM	NM
	Nov-02		63.37	24.69
	May-03		NM	NM
	Jan-04		56.37	31.69
	May-04		57.53	30.53
	Nov-04		56.10	31.96
	May-05		41.03	47.03
	Nov-05		47.79	40.27
	May-06		50.15	37.91
	Nov-06		53.68	34.38
	May-07		56.20	31.86
	Nov-07		57.44	30.62
	May-08		61.65	26.41
	Nov-08		56.90	31.16
	Nov-09		55.84	32.22
	Nov-10		49.74	38.32
	Nov-11		49.74	38.32
	Nov-12		52.24	35.82
	Nov-13		52.24	35.82
	Nov-14		47.85	40.21

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
SURFICIAL ZONE				
AC-5S	May-97	82.34	43.86	38.48
	Sep-97		43.87	38.47
	Nov-97		NM	NM
	May-98		42.60	39.74
	Nov-98		42.32	40.02
	May-99		45.66	36.68
	Nov-99		46.65	35.69
	May-00		49.45	32.89
	Nov-00		50.98	31.36
	May-01		51.58	30.76
	Nov-01		52.09	30.25
	May-02		53.45	28.89
	Nov-02		51.73	30.61
	May-03		NM	NM
	Jan-04		46.17	36.17
	May-04		46.71	35.63
	Nov-04		44.94	37.40
	May-05		38.01	44.33
	Nov-05		36.86	45.48
	May-06		39.01	43.33
	Nov-06		42.38	39.96
	May-07		44.83	37.51
	Nov-07		45.34	37.00
	May-08		44.86	37.48
	Nov-08		45.49	36.85
	Nov-09		44.35	37.99
	Nov-10		38.33	44.01
	Nov-11		42.20	40.14
	Nov-12		40.62	41.72
	Nov-13		41.05	41.29
	Nov-14		36.75	45.59
AC-6S	May-97	69.32	NM	NM
	Sep-97		43.97	25.35
	Nov-97		NM	NM
	May-98		NM	NM
	Nov-98		NM	NM
	May-99		NM	NM
	Nov-99		44.75	24.57
	May-00		NM	NM
	Nov-00		47.75	21.57
	May-01		NM	NM
	Nov-01		48.10	21.22
	May-02		NM	NM
	Nov-02		48.25	21.07
	May-03		NM	NM
	Jan-04		41.81	27.51
	May-04		NM	NM
	Nov-04		41.10	28.22
	May-05		NM	NM
	Nov-05		34.63	34.69
	May-06		NM	NM
	Nov-06		39.56	29.76
	May-07		NM	NM
	Nov-07		42.32	27.00
	May-08		NM	NM
	Nov-08		41.17	28.15
	Nov-09		40.47	28.85
	Nov-10		35.84	33.48
	Nov-11		39.58	29.74
	Nov-12		38.10	31.22
	Nov-13		37.59	31.73
	Nov-14		34.78	34.54

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
SURFICIAL ZONE				
AC-7SR	May-97	90.59	52.58	38.01
	Sep-97		NM	NM
	Nov-97		53.29	37.30
	May-98		51.04	39.55
	Nov-98		51.05	39.54
	May-99		54.11	36.48
	Nov-99		54.76	35.83
	May-00		57.93	32.66
	Nov-00		59.70	30.89
	May-01		60.38	30.21
	Nov-01		60.90	29.69
	May-02		62.35	28.24
	Nov-02		61.09	29.50
	May-03		59.64	30.95
	Jan-04		54.99	35.60
	May-04		55.55	35.04
	Nov-04		53.70	36.89
	May-05		47.23	43.36
	Nov-05		45.68	44.91
	May-06		48.27	42.32
	Nov-06		51.46	39.13
	May-07		54.04	36.55
	Nov-07		55.04	35.55
	May-08		54.09	36.50
	Nov-08		54.75	35.84
	Nov-09		53.81	36.78
	Nov-10		47.79	42.80
	Nov-11		47.79	42.80
	Nov-12		49.71	40.88
	Nov-13		50.23	40.36
	Nov-14		45.79	44.80
AC-24S	May-97	79.50	NM	NM
	Sep-97		57.32	22.18
	Nov-97		NM	NM
	May-98		NM	NM
	Nov-98		NM	NM
	May-99		NM	NM
	Nov-99		59.29	20.21
	May-00		NM	NM
	Nov-00		62.81	16.69
	May-01		NM	NM
	Nov-01		63.35	16.15
	May-02		NM	NM
	Nov-02		63.86	15.64
	May-03		NM	NM
	Jan-04		57.97	21.53
	May-04		NM	NM
	Nov-04		NM	NM
	May-05		NM	NM
	Nov-05		51.10	28.40
	May-06		NM	NM
	Nov-06		56.82	22.68
	May-07		NM	NM
	Nov-07		59.45	20.05
	May-08		NM	NM
	Nov-08		59.19	20.31
	Nov-09		57.75	21.75
	Nov-10		57.86	21.64
	Nov-11		57.08	22.42
	Nov-12		54.74	24.76
	Nov-13		54.86	24.64
	Nov-14		51.68	27.82

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
SURFICIAL ZONE				
AC-26S	May-97	26.75	NM	NM
	Sep-97		19.62	7.13
	Nov-97		NM	NM
	May-98		NM	NM
	Nov-98		NM	NM
	May-99		NM	NM
	Nov-99		20.36	6.39
	May-00		NM	NM
	Nov-00		20.74	6.01
	May-01		NM	NM
	Nov-01		20.88	5.87
	May-02		NM	NM
	Nov-02		20.58	6.17
	May-03		NM	NM
	Jan-04		20.04	6.71
	May-04		NM	NM
	Nov-04		19.36	7.39
	May-05		NM	NM
	Nov-05		18.29	8.46
	May-06		NM	NM
	Nov-06		19.60	7.15
	May-07		NM	NM
	Nov-07		19.54	7.21
	May-08		NM	NM
	Nov-08		19.61	7.14
	Nov-09		17.99	8.76
	Nov-10		18.26	8.49
	Nov-11		19.80	6.95
	Nov-12		19.12	7.63
	Nov-13		18.82	7.93
	Nov-14		18.52	8.23
AC-27S	May-97	18.50	NM	NM
	Sep-97		13.94	4.56
	Nov-97		NM	NM
	May-98		NM	NM
	Nov-98		NM	NM
	May-99		NM	NM
	Nov-99		14.52	3.98
	May-00		NM	NM
	Nov-00		15.24	3.26
	May-01		NM	NM
	Nov-01		15.53	2.97
	May-02		NM	NM
	Nov-02		15.24	3.26
	May-03		NM	NM
	Jan-04		14.55	3.95
	May-04		NM	NM
	Nov-04		13.75	4.75
	May-05		NM	NM
	Nov-05		12.63	5.87
	May-06		NM	NM
	Nov-06		14.19	4.31
	May-07		NM	NM
	Nov-07		13.98	4.52
	May-08		NM	NM
	Nov-08		13.98	4.52
	Nov-09		11.78	6.72
	Nov-10		12.77	5.73
	Nov-11		14.09	4.41
	Nov-12		13.43	5.07
	Nov-13		13.63	4.87
	Nov-14		12.89	5.61

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
SURFICIAL ZONE				
AC-33S	May-97	89.18	50.54	38.64
	Sep-97		NM	NM
	Nov-97		51.25	37.93
	May-98		48.93	40.25
	Nov-98		48.86	40.32
	May-99		52.12	37.06
	Nov-99		52.80	36.38
	May-00		55.96	33.22
	Nov-00		57.66	31.52
	May-01		58.32	30.86
	Nov-01		58.90	30.28
	May-02		60.43	28.75
	Nov-02		58.71	30.47
	May-03		57.60	31.58
	Jan-04		52.97	36.21
	May-04		53.56	35.62
	Nov-04		51.60	37.58
	May-05		45.37	43.81
	Nov-05		43.65	45.53
	May-06		46.42	42.76
	Nov-06		49.59	39.59
	May-07		52.17	37.01
	Nov-07		52.89	36.29
	May-08		52.12	37.06
	Nov-08		52.80	36.38
	Nov-09		51.79	37.39
	Nov-10		45.88	43.30
	Nov-11		45.88	43.30
	Nov-12		47.70	41.48
	Nov-13		48.30	40.88
	Nov-14		43.95	45.23
AC-34S	May-97	89.09	51.35	37.74
	Sep-97		NM	NM
	Nov-97		52.09	37.00
	May-98		49.89	39.20
	Nov-98		49.93	39.16
	May-99		52.91	36.18
	Nov-99		53.62	35.47
	May-00		56.63	32.46
	Nov-00		58.46	30.63
	May-01		59.20	29.89
	Nov-01		59.73	29.36
	May-02		61.13	27.96
	Nov-02		60.01	29.08
	May-03		58.45	30.64
	Jan-04		53.74	35.35
	May-04		54.27	34.82
	Nov-04		52.48	36.61
	May-05		46.18	42.91
	Nov-05		44.42	44.67
	May-06		46.90	42.19
	Nov-06		50.14	38.95
	May-07		52.69	36.40
	Nov-07		53.47	35.62
	May-08		52.77	36.32
	Nov-08		53.34	35.75
	Nov-09		52.41	36.68
	Nov-10		46.39	42.70
	Nov-11		46.39	42.70
	Nov-12		48.44	40.65
	Nov-13		48.92	40.17
	Nov-14		44.44	44.65

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
SURFICIAL ZONE				
NWD-2S	May-97	77.53	NM	NM
	Sep-97		39.75	37.78
	Nov-97		NM	NM
	May-98		NM	NM
	Nov-98		NM	NM
	May-99		NM	NM
	Nov-99		41.72	35.81
	May-00		NM	NM
	Nov-00		45.82	31.71
	May-01		NM	NM
	Nov-01		46.77	30.76
	May-02		NM	NM
	Nov-02		47.15	30.38
	May-03		NM	NM
	Jan-04		45.67	31.86
	May-04		NM	NM
	Nov-04		44.49	33.04
	May-05		NM	NM
	Nov-05		37.09	40.44
	May-06		NM	NM
	Nov-06		42.60	34.93
	May-07		NM	NM
	Nov-07		46.25	31.28
	May-08		NM	NM
	Nov-08		45.55	31.98
	Nov-09		44.70	32.83
	Nov-10		38.84	38.69
	Nov-11		42.82	34.71
	Nov-12		NM	NM
	Nov-13		41.32	36.21
	Nov-14		37.36	40.17
NWD-4S	May-97	34.70	NM	NM
	Sep-97		19.33	15.37
	Nov-97		NM	NM
	May-98		NM	NM
	Nov-98		NM	NM
	May-99		NM	NM
	Nov-99		20.68	14.02
	May-00		NM	NM
	Nov-00		22.21	12.49
	May-01		NM	NM
	Nov-01		22.58	12.12
	May-02		NM	NM
	Nov-02		21.89	12.81
	May-03		NM	NM
	Jan-04		20.16	14.54
	May-04		NM	NM
	Nov-04		NM	NM
	May-05		NM	NM
	Nov-05		16.59	18.11
	May-06		NM	NM
	Nov-06		19.92	14.78
	May-07		NM	NM
	Nov-07		20.22	14.48
	May-08		NM	NM
	Nov-08		16.59	18.11
	Nov-09		18.59	16.11
	Nov-10		17.17	17.53
	Nov-11		19.48	15.22
	Nov-12		17.96	16.74
	Nov-13		17.93	16.77
	Nov-14		16.61	18.09

TABLE 4
GROUNDWATER ELEVATIONS
November 10, 2014

Agrico Site
Pensacola, Florida

Well I.D.	Date	Elevation TOC (ft NGVD)	Water Level (ft btoc)	Water Level Elevation (ft NGVD)
SURFICIAL ZONE				
ACB-31S	May-97	91.92	50.26	41.66
	Sep-97		NM	NM
	Nov-97		51.22	40.70
	May-98		48.78	43.14
	Nov-98		48.50	43.42
	May-99		51.84	40.08
	Nov-99		52.74	39.18
	May-00		55.84	36.08
	Nov-00		57.22	34.70
	May-01		57.94	33.98
	Nov-01		58.53	33.39
	May-02		60.31	31.61
	Nov-02		57.38	34.54
	May-03		57.36	34.56
	Jan-04		53.11	38.81
	May-04		53.62	38.30
	Nov-04		51.34	40.58
	May-05		43.27	48.65
	Nov-05		43.34	48.58
	May-06		46.50	45.42
	Nov-06		49.48	42.44
	May-07		52.25	39.67
	Nov-07		50.98	40.94
	May-08		52.11	39.81
	Nov-08		52.37	39.55
	Nov-09		51.14	40.78
	Nov-10		45.76	46.16
	Nov-11		45.76	46.16
	Nov-12		47.70	44.22
	Nov-13		48.28	43.64
	Nov-14		44.00	47.92
ACB-32S	May-97	88.16	48.11	40.05
	Sep-97		NM	NM
	Nov-97		48.92	39.24
	May-98		46.60	41.56
	Nov-98		46.52	41.64
	May-99		49.84	38.32
	Nov-99		50.62	37.54
	May-00		53.71	34.45
	Nov-00		55.41	32.75
	May-01		56.18	31.98
	Nov-01		56.77	31.39
	May-02		58.30	29.86
	Nov-02		56.65	31.51
	May-03		55.49	32.67
	Jan-04		50.81	37.35
	May-04		51.26	36.90
	Nov-04		49.25	38.91
	May-05		41.13	47.03
	Nov-05		40.99	47.17
	May-06		43.50	44.66
	Nov-06		46.77	41.39
	May-07		49.56	38.60
	Nov-07		49.32	38.84
	May-08		49.64	38.52
	Nov-08		49.95	38.21
	Nov-09		48.83	39.33
	Nov-10		42.83	45.33
	Nov-11		42.83	45.33
	Nov-12		45.18	42.98
	Nov-13		45.67	42.49
	Nov-14		41.20	46.96

NOTES:

ft NGVD = feet above National Geodetic Vertical Datum of 1988.

ft btoc = feet below top of casing.

NM = Not Measured

TABLE 5
SURFACE WATER FIELD PARAMETER RESULTS

Agrico Site
Pensacola, Florida

Surface Water Location	Date	pH (su)	Conductivity (µs/cm)	Temperature (°C)	Dissolved Oxygen (mg/L)	Oxidation Reduction Potential (mV)	Turbidity (NTU)	Salinity (ppt)
ACSW-1 Bayou Texar (Brackish Water)	11/24/1999	6.30	35,000	22.00	NM	NM	0	22.00
	11/30/2000	7.20	30,000	19.00	NM	NM	0	19.00
	11/7/2001	7.10	34,300	24.50	NM	NM	21.1	20.60
	12/3/2002	6.95	22,388	16.90	NM	NM	5.3	13.51
	1/29/2004	6.88	21,805	14.60	7.71	225	3.97	NM
	11/18/2004	5.54	6,575	20.40	NM	NM	NM	3.55
	11/21/2005	6.92	18,575	17.55	7.9	93.8	12.9	NM
	11/27/2006	6.72	17,348	19.80	6.69	141.6	7.71	11.54
	11/20/2007	7.00	29,785	22.40	6.46	141.3	4.4	18.52
	11/20/2008	7.71	37,362	18.40	7.87	185	8.51	23.61
	11/13/2009	6.91	19,505	20.45	6.93	177.3	6.78	11.67
	11/17/2010	7.33	28,783	21.26	5.89	251.6	17.1	17.8
	11/17/2011	7.62	34,043	21.70	7.79	14.1	13.2	21.25
	11/8/2012	7.03	32,649	23.43	5.93	73.8	12.3	20.75
	11/11/2013	7.59	25,388	22.42	6.67	84.9	12.5	NM
	11/21/2014	7.39	34,830	17.64	8.13	135.7	6.14	21.50
ACSW-2 Bayou Texar (Brackish Water)	11/24/1999	7.10	38,000	21.00	NM	NM	0	24.00
	11/30/2000	7.90	32,000	18.00	NM	NM	0	20.00
	11/7/2001	8.43	43,000	22.50	NM	NM	3.3	27.80
	12/3/2002	7.06	27,167	15.80	NM	NM	4.7	16.73
	1/29/2004	7.68	23,182	13.60	7.83	161.1	6.4	NM
	11/18/2004	4.90	9,788	21.17	NM	NM	NM	5.73
	11/21/2005	7.67	30,500	17.07	7.96	115.6	10.4	NM
	11/27/2006	7.40	28,104	19.03	7.9	157.6	8.17	17.3
	11/20/2007	7.66	35,752	21.57	7.12	73.6	5.4	22.57
	11/20/2008	7.64	35,968	19.05	7.6	173.9	10	22.73
	11/13/2009	7.30	30,925	20.97	3.87	-121.8	8.64	19.2
	11/17/2010	7.71	30,305	20.85	5.87	292.4	8.36	19.0
	11/17/2011	7.90	36,363	21.28	8.52	41.5	5.36	23.02
	11/8/2012	7.83	37,364	20.58	7.59	66.7	10.5	23.74
	11/11/2013	7.59	34,042	22.13	7.96	87.6	8.33	NM
	11/21/2014	7.17	30,444	16.14	100.8	124.7	4.94	18.64
BT-02 Bayou Texar (Brackish Water)	11/17/2010	7.44	28,836	21.43	6.07	180.4	7.98	17.74
	11/17/2011	7.63	33,288	21.92	8.15	-9.5	11.30	20.84
	11/8/2012	7.58	36,769	22.35	7.39	70.8	12.10	23.24
	11/11/2013	7.08	27,605	22.12	7.39	84.0	30.50	NM
	11/21/2014	7.23	33,886	17.31	102.3	122.0	5.67	21.49
BT-107 Bayou Texar (Brackish Water)	11/17/2010	7.39	29,165	21.45	6.14	193.5	5.30	18.05
	11/17/2011	7.51	32,523	21.61	7.96	9.9	9.80	20.48
	11/8/2012	7.23	36,230	22.27	7.01	73.6	10.80	22.94
	11/11/2013	6.89	28,619	22.69	6.37	81.2	7.85	NM
	11/21/2014	7.85	35,026	17.39	92.9	119.7	5.75	22.04
BT-127 Bayou Texar (Brackish Water)	11/17/2010	7.33	28,735	21.31	5.87	240.7	6.21	17.64
	11/17/2011	7.69	35,000	21.73	7.94	-1.8	10.40	22.07
	11/8/2012	7.37	36,564	22.60	7.44	67.5	10.30	22.95
	11/11/2013	6.87	28,952	22.86	6.53	84.9	5.86	NM
	11/21/2014	6.96	34,062	17.53	7.73	117.6	9.27	21.43

TABLE 5
SURFACE WATER FIELD PARAMETER RESULTS

Agrico Site
Pensacola, Florida

Surface Water Location	Date	pH (su)	Conductivity (µs/cm)	Temperature (°C)	Dissolved Oxygen (mg/L)	Oxidation Reduction Potential (mV)	Turbidity (NTU)	Salinity (ppT)
ACSW-BL Carpenter's Creek (Freshwater)	11/24/1999	7.20	360	22.00	NM	NM	0.00	0.00
	11/29/2000	7.10	380	19.00	NM	NM	0.00	0.00
	11/7/2001	6.11	69	18.70	NM	NM	0.00	0.00
	11/26/2002	5.67	80	20.40	NM	NM	1.70	NM
	1/29/2004	6.56	68	15.88	7.34	126.1	5.49	NM
	11/12/2004	5.86	92	20.12	NM	NM	NM	0.04
	11/22/2005	6.47	87	16.03	9.38	61.4	7.78	0.04
	11/21/2006	5.95	88	17.13	7.9	130.5	1.35	NM
	11/20/2007	6.51	90	20.31	7.59	73.6	1.80	0.04
	11/20/2008	6.14	104	17.13	8.32	125	3.97	0.05
	11/12/2009	6.08	45	18.87	8.71	187.8	3.00	NM
	11/17/2010	Discontinued						

NOTES:

SU = Standard Units

µs/cm= microsiemens per centimeter

°C = Degrees Celsius

mg/L = milligram per Liter

mV = milliVolt

NTU = Nephelometric Turbidity Units

ppT=parts per thousand

NM = not measured

TABLE 6

**ADVISORY NOTICE DISTRIBUTION LIST
WATER WELL, IRRIGATION/PLUMBING, AND POOL CONTRACTORS**

**OU-2 AGRICO SITE
PENSACOLA, FLORIDA**

NAME	COMPANY NAME	ADDRESS	CITY	STATE	POSTAL CODE
	FLORIDA IRRIGATION SUPPLY INC	2810 COPTER ROAD	PENSACOLA	FL	32514
	STOVALL & COMPANY	3901 N. PACE BLVD.	PENSACOLA	FL	32505-4340
	WALLACE SPRINKLER INC	3607 ANDREW AVE	PENSACOLA	FL	32505-4108
	D & L LAWN SERVICES	207 CAROLYN WAY	PENSACOLA	FL	32505-2823
	ALL SEASONS POOL SERVICE	29 ADKINSON DR	PENSACOLA	FL	32506
	ALL SERVICES POOL SPA	5585 WINDHAM RD	MILTON	FL	32507
	AMERICAN LIFESTYLE POOL, INC	5053 RING ROSE CT	GULF BREEZE	FL	32563-8935
	AVALON POOLS	4230 TANFIELD RD	MILTON	FL	32583
	COASTAL POOLS	6031 CHAPMAN CIR	PENSACOLA	FL	32504-7950
	PACE POOL & SPA SERVICES, INC.	4873 WEST SPENCER FIELD RD.	PACE	FL	32571-1232
	DOLPHIN POOLS	3210 GULF BREEZE PKWY	GULF BREEZE	FL	32563-2730
	FAMILY POOL AND SPA & BILLIARD CENTE	3920 N. DAVIS HIGHWAY	PENSACOLA	FL	32503
	JOHNSON POOLS, INC	401 MASSACHUSETTS AVE	PENSACOLA	FL	32505-4207
	PARKER POOLS	PO BOX 11769	PENSACOLA	FL	32524-1769
	WHOLESALE SPA & POOL OUTLETS	2323 COPTER RD.	PENSACOLA	FL	32514-5802
	PENSACOLA POOLS INC	4412 HIGHWAY 90	PACE	FL	32571
	PENSACOLA POOLS INC	3480 GULF BREEZE PKWY	GULF BREEZE	FL	32563-3406
	PENSACOLA POOLS INC	501 E. HOLLYWOOD BLVD.	MARY ESTHER	FL	32569-2078
	PINCH A PENNY POOL PATIO SPA	7859 PINE FOREST RD.	PENSACOLA	FL	32526-8701
	PINCH A PENNY POOL PATIO SPA	3307 GULF BREEZE PKWY	GULF BREEZE	FL	32563
	SUNSET POOLS SPAS & WHIRLPOOL BATH	4382 HIGHWAY 90	PACE	FL	32571
	BEDROCK WELLS - AAA SPRINKLERS & LA	6201 N. BLUE ANGEL PKWY	PENSACOLA	FL	32526-8006
	MCGOWAN WATER WORKS INC	3041 E. KINGSFIELD RD.	PENSACOLA	FL	32514-9753
	COFFEY S G WELL SVCE	331 BURNT PINE RD	BREWTON	AL	36426-5817
	COFFEY'S GEORGE WELL SERVICE	680 TRAVIS RD	BREWTON	AL	36426-5120
	J & S SPRINKLERS & WELL DRILLING	7251 E BAY BLVD.	NAVARRE	FL	32566-9015
	RUSSELLS WELL AND PUMP SERVICES	4053 KENTWOOD ST.	MILTON	FL	32571-2432
	WINDHAM & SON PUMPING SUPPLY	5800 MULDOON RD.	PENSACOLA	FL	32526-1699
ALAN ARD	ARD'S CLOSED LOOP	1931 TILLIMAN LN	PENSACOLA	FL	32506
GLENN ASHLEY	ASHLEY WELL DRILLING	8056 WAKULLA SPGS RD	TALLAHASSEE	FL	32305
GREG BAILEY	GREG'S IRRIGATION	4264 BARLOW RD	CRESTVIEW	FL	32536
RONNIE BARLOW		4575 J BARLOW ROAD	JAY	FL	32565
BOBBY BARLOW	BARLOW WATER SERVICES	P O BOX 539	WEWAHITCHKA	FL	32465
FREDERICK BASFORD	BASFORD WELL DRILLING	4513 LAFAYETTE ST	MARIANNA	FL	32446
CHARLES BASFORD	BASFORD WELL DRILLING	4513 LAFAYETTE ST	MARIANNA	FL	32446
LESTER BASFORD	BASFORD WELL DRILLING	4513 LAFAYETTE ST	MARIANNA	FL	32446
MACK H BEASLEY	MACK H BEASLEY WATER WELL SERVICE	4940 BECK AVE	JAY	FL	32565
TERRY BERRY	BERRY'S WELL SERVICE	225 SPENCER DR	FT WALTON BEACH	FL	32547
DAVIS L BOOTH		903 W TENNESSEE ST	TALLAHASSEE	FL	32304
PAUL BRANSON	COFFEY'S WELL SERVICE	P O BOX 564	JAY	FL	32565
TERRY BRANTON	BRANTON BROTHERS WELL DRILLING	755 MALVERN RD	DOTHAN	AL	36301
NEAL BRICKNER		9393 EAST RIVER DR	NAVARRE	FL	32566
MORGAN BROWN		28 MOONEY ROAD NE	FT WALTON BEACH	FL	32547
DOCK L BRYANT JR	B & B WELL DRILLING	108 FETTING AVE	FT WALTON BEACH	FL	32547
BYRON BUTLER		P O BOX 2820	HAINES CITY	FL	33845
TROY E BYRD		P O BOX 371	ATMORE	AL	36504
JOHN G CATON	UNIVERSAL SPRINKLER & LANDSCAPING	5344 SOUNDSIDE DRIVE	GULF BREEZE	FL	32563
HERBERT CHRISTIAN	CHRISTIAN TESTING LABS INC	P O BOX 3218	MONTGOMERY	AL	36109
JL CLANTON	CLANTON'S WELL DRILLING	6512 LOIS ST	PANAMA CITY	FL	32404
MARK COBB	C & S WELL SERVICE	2712 TWILIGHT AVE	PANAMA CITY	FL	32405
SANDRA COFFEY	S G COFFEY WELL SERVICE	409 BURNT PINE RD	BREWTON	AL	35425-5859
JIMMY H COFIELD	JIM'S WELL DRILLING	P O BOX 93	FLOMATON	AL	36441
TE COLLEY		5558 ORIOLE ST	MILTON	FL	32570
ARTHUR COLLINGSWORTH		6806 KEITHLEY RD	PANAMA CITY	FL	32404
JAMES R CONNER	JAMIE CONNER WELL DRILLING SERVICES	1278 LEAVINS RD	WESTVILLE	FL	32464
JOHN COOKE	COOKE'S WELL DRILLING SERVICE	4924 SATIN DR	BASCOM	FL	32423
VERNON CREAMER	COASTAL WELL DRILLING	11939 RACoon RD	SOUTHPORT	FL	32409
DON CRUTCHFIELD	PENSACOLA TESTING LAB	217 E BRENT LN	PENSACOLA	FL	32503
WILLIAM DAVIS	BILL DAVIS DRILLING SERVICES	32 SHORELINE DRIVE	PANACEA	FL	32346
ROBERT DE VALCOURT	PERDIDO HEATING & AIR	5555 BAUER RD	PENSACOLA	FL	32507
ROBIN DEAN	ROBIN DEAN WELL DRILLING	1904 WAX MYRTLE RD	TALLAHASSEE	FL	32310
WESLEY DEAN	DEAN'S WELL DRILLING	PO BOX 1469	WOODVILLE	FL	32362-1469
RANDALL DEAN		PO BOX 448	WOODVILLE	FL	32362

TABLE 6

**ADVISORY NOTICE DISTRIBUTION LIST
WATER WELL, IRRIGATION/PLUMBING, AND POOL CONTRACTORS**

**OU-2 AGRICO SITE
PENSACOLA, FLORIDA**

NAME	COMPANY NAME	ADDRESS	CITY	STATE	POSTAL CODE
WESLEY DONALDSON	DONALDSON WELL DRILLING	1321 BLUE ANGEL PKY	PENSACOLA	FL	32506
ROBERT M DORRIETY		5251 COY BURGESS RD	DEFUNIAK SPRINGS	FL	32435
CURT DOYLE	GEOTECHNICAL SERVICES INC	904 BUTLER DR	MOBILE	AL	36693
HARRY DYE	HARRY'S WELL SERVICE	400 KELSON RD	PENSACOLA	FL	32514
BOB ECHOLD	NORTHWEST FLORIDA WATER MANGEME	5453 DAVISSON RD	MILTON	FL	32583-5329
MATT GARCIA		1426 LOLA DR	TALLAHASSEE	FL	32301
DAN GARY	DAN GARY WELL DRILLING	RTE 1 BOX 164	GENEVA	AL	36340
DONALD GELDBAUGH	SOUTHERN COMPANY SERVICES INC	ONE ENERGY PLACE	PENSACOLA	FL	32520
ALPHA GIPSON	ALPHA GIPSON	6131 AGELENA RD	PENSACOLA	FL	32504
TOMMIE GLASS		3804 W BLOUNT ST	PENSACOLA	FL	32505
EM GLOVER	E. M. GLOVER DRILLING	243 GLOVER LN	CRAWFORDVILLE	FL	32327
WENDELL HALL		6620 CHIPEWA ST	PANAMA CITY	FL	32404
JOSEPH HARRELL JR	GEO ENERGY DRILLING INC	P O BOX 1454	CRAWFORDVILLE	FL	32326
HOWARD HAYES		20181 SE CL CAPPS RD	BLOUNTSTOWN	FL	32424
STEVE HOLT	HOLT WELL SERVICE	8331 HWY 189 N	BAKER	FL	32531
EDGAR HUGHES		6302 CR 636	CHANCELLOR	AL	36316
LEWIS C JOHNSON		4537 JAY BARLOW RD	JAY	FL	32565
LEWIS G JOHNSON	AMERICAN WELL DRILLING	7116 NELSON ST	NAVARRE	FL	32566
DAVID L JOHNSON	JOHNSON WELL DRILLING	5056 OAK DR	BASCOM	FL	32423
SAMUEL JOHNSON	JOHNSON WELL DRILLING	P O BOX 93	BASCOM	FL	32423
JAMES JOHNSON		7716 SUNSHINE HILL RD	MOLINO	FL	32577
DON JONES	LARRY JACOBS & ASSOCIATES	328 E GADSDEN ST	PENSACOLA	FL	32501
BILL KIGHT		3511 N CENTRY BLVD	MCDavid	FL	32568
EDDIE LAWRENCE	TOWN & COUNTRY WELL DRILLING	19512 RIDGE RD	FOUNTAIN	FL	32438
EVERETTE LEAVINS	EVERETTE B LEAVINS WELL DRILLING	1239 LEAVINS RD	WESTVILLE	FL	32464
JAMES T LEWIS	ADVANCED BORING INC	4931 WOOD CLIFF DR	PENSACOLA	FL	32504
ROBERT LIVINGSTON		4909 PARK ST	PANAMA CITY	FL	32404
JOHN MARTIN		P O BOX 623	DEFUNIAK SPRINGS	FL	32435
SAM MARTIN	SAM MARTIN WELL DRILLING	P O BOX 623	DEFUNIAK SPRINGS	FL	32435
BILLY MCCLAIN	FLORIDA DEPARTMENT OF ENVIRONMENT	2600 BLAIR STONE ROAD	TALLAHASSEE	FL	32399
GENE MCGOWAN		3041 E KINGSFIELD RD	PENSACOLA	FL	32526
MICHAEL MCGUYRE	MCGUYRE'S WELL DRILLING	4090 BUFORD LN	MILTON	FL	32583
CRAIG MCLEAN		P O BOX 700	FREEPORT	FL	32439
WILLIAM MCLEAN	CRAIG'S WELL SERVICE	P O BOX 700	FREEPORT	FL	32439
TE MILLS	MILLS WELL DRILLING & PUMPS	5355 TOWER RD	TALLAHASSEE	FL	32303
BRICE MOODY	BRICEY MOODY WELL DRILLING	160 SAN MARCOS DR	CRAWFORDVILLE	FL	32327
MAJOR MOORE	MOORE ELECTRIC COMPANY	1110 W WASHINGTON ST	QUINCY	FL	32351
JOHN A MORRILL		3805 A SPRINGHILL RD	TALLAHASSEE	FL	32310
FRANK J MOSLEY	MOSLEY WELL & PUMP	7685 FAIRBANKS FERRY RD	HAVANA	FL	32333
CLYFTON MYERS	MYERS PUMP & INSTALLATION	1391 ACORN LN	PENSACOLA	FL	32514
JAMES PEEL	SOUTHERN TESTING & DRILLING INC	1419 ORANGE HILL RD	CHIPLEY	FL	32428
TONY POWELL		P O BOX 116	URIAH	AL	36480
DOUGLAS RAY	FREETIME IRRIGATION	107 22ND STREET	NICEVILLE	FL	32578
HARVEY REAVES		P O BOX 426	WOODVILLE	FL	32362
CARL REVELL JR	REVELL WELL DRILLING	P O BOX 123	SOPCHOPPY	FL	32358
ROBERT ROACH	BOYLES BROTHERS DRILLING CO	P O BOX 1111	NORTHPORT	AL	35476
RICHARD ROWE		P O DRAWER 1389	TALLAHASSEE	FL	32302
LAMAR ROWE	ROWE DRILLING COMPANY INC	P O DRAWER 1389	TALLAHASSEE	FL	32302
ROBERT SCRIBNER	KCW ELECTRIC CO INC	4765 SHELFER RD	TALLAHASSEE	FL	32310
WAYNE SIMMONS	SIMMONS WELL DRILLING	3152 BOB SIKES ROAD	DEFUNIAK SPRINGS	FL	32435
MILFORD SIMS		3606 S LAKEWOOD DR	TALLAHASSEE	FL	32310
STEVE SMALLEY	NORTH FLORIDA WELL DRILLING	24396 LONE STAR CT	TALLAHASSEE	FL	32310
DONALD SMITH	DONALD SMITH COMPANY INC	746 E MAIN	HEADLAND	FL	36345
FILBERT SMITH	ARDAMAN AND ASSOCIATES	3175 W THARPE ST	TALLAHASSEE	FL	32303
MIKE SPIVA	MIKE'S WATER WORKS	PO BOX 1299	SANTA ROSA BEACH	FL	32459-1289
MICHAEL SUGGS		936 PIONEER RD	CHIPLEY	FL	32428
CLIFFORD TAYLOR	POLLOCK WELL DRILLING INC	7307 EVEREST ST	PANAMA CITY	FL	32404
JAMES THOMASON		328 SEMINOLE ST	FT WALTON BEACH	FL	32547
VJ THOMPSON III	THOMASON DEEP WELL DRILLING	P O DRAWER 91537	MOBILE	AL	36691
VONNIE TOLBERT	VONNIE'S WELLS	7621 SAMANTHA CIRCLE	NAVARRE	FL	32566
JAMES TRINDELL		6 THREE SISTERS ROAD	CRAWFORDVILLE	FL	32327
DEN A TRUMBULL JR	CULLIGAN WATER SERVICES INC	315 E 15TH ST	PANAMA CITY	FL	32405
VICTOR C WALLACE	WALLACE SPRINKLER & SUPPLY INC	P O BOX 1313	GULF BREEZE	FL	32562

TABLE 6

**ADVISORY NOTICE DISTRIBUTION LIST
WATER WELL, IRRIGATION/PLUMBING, AND POOL CONTRACTORS**

**OU-2 AGRICO SITE
PENSACOLA, FLORIDA**

NAME	COMPANY NAME	ADDRESS	CITY	STATE	POSTAL CODE
ALEX WALTERS		10704 ALEX DRIVE	FOUNTAIN	FL	32438
CHALES M WARD	CLYDE'S WELL SERVICE INC	4537 J BARLOW ROAD	JAY	FL	32565
JAMES W WESTBROOK	J & W WELL DRILLING	P O BOX 135	BASCOM	FL	32423
CHARLES WINDHAM	WILLIAMSON WELL DRILLING INC	5800 MULDOON RD	PENSACOLA	FL	32506
TERRY WOODWARD	TERRY'S WELL SERVICE	5001 CHIMES WAY	PENSACOLA	FL	32507
CHARLES WYCKOFF		12751 SMITH YOUNG RD	MOBILE	AL	36695
ACE PLUMBING & DRAIN		8861 GULF BEACH HWY	PENSACOLA	FL	32507
AGGRESSIVE PLUMBING BY R BROADLEY		1015 E LAKEVIEW AVE	PENSACOLA	FL	32503
ARNO'S PLUMBING AND HEATING		6917 SEA CRAB CIRCLE	NAVARRE	FL	32566
ARTO'S SEWER AND DRAIN PLUMBING CO INC		P O BOX 18116	PENSACOLA	FL	32523
BARBERI PLUMBING		1022 UNDERWOOD AVE	PENSACOLA	FL	32504
BELLVIEW PLUMBING CO INC		3101 MULDOON RD	PENSACOLA	FL	32526
BOYD PLUMBING		2464 S HWY 29	CANTONMENT	FL	32533
BRADLEY PLUMBING AND HEATING		2709 GRAINGER AVENUE	PENSACOLA	FL	32507
CLYDE'S SERVICES		815 N 77TH AVE	PENSACOLA	FL	32506
COKER PLUMBING CO		521 MILLS AVE	PENSACOLA	FL	32507
COOPER GARY PLUMBING		5676 COUNTRY SQUIRE DR	MILTON	FL	32570
DAVIDSON PLUMBING		8830 UNTREINER AVE	PENSACOLA	FL	32534
EAST BAY PLUMBING CO		6255 EAST BAY BLVD	GULF BREEZE	FL	32561
ELECTRIC ROTO		2376 W NINE MILE RD	PENSACOLA	FL	32534
ESCAMBIA PLUMBING AND HEATING CO		1860 ATWOOD DR	PENSACOLA	FL	32514
FAVORITE PLUMBING CO		2828 N T STREET	PENSACOLA	FL	32505
JIM'S PLUMBING OF NAVARRE INC		1888 COMMODORE ST	NAVARRE	FL	32566
JOHNSON LEON PLUMBING CO		7108 WHIRLEYBIRD AVE	PENSACOLA	FL	32504
MMI MECHANICAL CONTRACTOR		4904 W SPENCER FIELD	PACE	FL	32571
MCCLUSKEY PLUMBING CO		808 W ZARRAGOSSA STREET	PENSACOLA	FL	32501
PAYNE & SON PLUMBING, HEATING, AIR CONDITIONING		P O BOX 2575	PENSACOLA	FL	32513
PENSACOLA PLUMBING CONTRACTORS		2313 BROOKWOOD PLACE	PENSACOLA	FL	32533
QUALITY ONE PLUMBING CO		5724 PALMETTO PL	MILTON	FL	32570
ROOT-A-SEWER INC		2701 LONG LEAF DR	PENSACOLA	FL	32526
S & S PLUMBING AND MECHANICAL INC		7845 PINE FOREST RD	PENSACOLA	FL	32526
SANTA ROSA PLUMBING		5510 TOM SAWYER RD	MILTON	FL	32583
SMITH PLUMBING & HEATING CO INC		2510 N PACE BLVD	PENSACOLA	FL	32505
SPIVEY & SON PLUMBING INC		9820 VONNA JO DR	PENSACOLA	FL	32506
VAN PLUMBING		3248 CLEMSON RD	GULF BREEZE	FL	32561
WARRINGTON PLUMBING INC		910 W MAIN	PENSACOLA	FL	32501
BRAUN'S SPRINKLER SERVICE		10852 BERRYHILL RD	PENSACOLA	FL	32506
GORMAN CO INC		4149 WAREHOUSE LANE	PENSACOLA	FL	32505
PHOENIX LANDSCAPE & IRRIGATION INC		P O BOX 924	GULF BREEZE	FL	32562
RAINFALL LANDSCAPE & SPRINKLER		9850 NORTH LOOP RD	PENSACOLA	FL	32507
TIECO GULF COAST INC		540 W MICHIGAN AVE	PENSACOLA	FL	32505
DOUG MERRITT IRRIGATION		2600 W MICHIGAN AVE, LOT 35E	PENSACOLA	FL	32526
TRIM A LAWN LAWN & GARDEN CENTER		1405 GULF BEACH HIGHWAY	PENSACOLA	FL	32507
MCGOWAN IRRIGATION		3041 E KINGSFIELD RD	PENSACOLA	FL	32526
GARVEY IRRIGATION		PO BOX 250	MOLINO	FL	32577-0250
KEN GRIFFIN LANDSCAPE CONTRACTORS INC		3004 WESTFIELD RD	GULF BREEZE	FL	32563
PENSACOLA LANDSCAPING & LAWN CARE		7795 GROW DR	PENSACOLA	FL	32514
WATER WORKS SPRINKLER SYSTEMS & PONDS		4669 ANNA SIMPSON RD	MILTON	FL	32583
C & H PLUMBING		5239 OLD BERRYHILL RD	MILTON	FL	32570
DEALE PLUMBING		7019 WOODLEY DR	PENSACOLA	FL	32503
DOWNES PLUMBING & GAS	LARRY DOWNES	5840 MULDOON RD	PENSACOLA	FL	32526
ELECTRIC ROTO ROOTER SEWER & DRAIN CLEANING		2376 W NINE MILE ROAD	PENSACOLA	FL	32534
FLORIDA AIR CONDITIONING & PLUMBING		9310 BRIDLEWOOD RD	PENSACOLA	FL	32526
THE FRIENDLY PLUMBER OF FLORIDA INC		4300 HOLLYWOOD AVENUE	PENSACOLA	FL	32505

TABLE 6

**ADVISORY NOTICE DISTRIBUTION LIST
WATER WELL, IRRIGATION/PLUMBING, AND POOL CONTRACTORS**

**OU-2 AGRICO SITE
PENSACOLA, FLORIDA**

NAME	COMPANY NAME	ADDRESS	CITY	STATE	POSTAL CODE
HIGH TECH PLUMBING & HEATING		8375 RALEIGH CIRCLE	PENSACOLA	FL	32534
HOMEOWNERS' ASSURANCE INC		4382 HIGHWAY 90	PACE	FL	32571
PACE PLUMBING		4274 BELL LANE	PACE	FL	32571
PETTRY PLUMBING & GAS SERVICE		P.O. BOX 3422	PENSACOLA	FL	32516
ROTO-ROOTER SERVICE & DRAIN CLEANING		2376 W NINE MILE RD	PENSACOLA	FL	32534
TERRY SMITH PLUMBING INC		22 W NINE & ONE HALF MILE RD	PENSACOLA	FL	32534
ENSLEY SEPTIC TANK SERVICE		10491 BETMARK RD	PENSACOLA	FL	32534
AFFORDABLE SPRINKLERS		4155 KINGBERRY ROAD	PENSACOLA	FL	32504
ALTERNATE RAIN SYSTEMS		5353 N BLUE ANGEL PARKWAY	PENSACOLA	FL	32526
AMORE SPRINKLER CO		3652 GARDENVIEW RD	PACE	FL	32571
IRRIGATION ENGINEERING		920 E LLOYD ST	PENSACOLA	FL	32503
KILLER WELLS, INC.		2600 W. MICHIGAN AVE, LOT 35E	PENSACOLA	FL	32525-2282
PERDIDO IRRIGATION SYSTEMS		5555 BAUER ROAD	PENSACOLA	FL	32507
RIKER IRRIGATION		1144 W NINE MILE RD	PENSACOLA	FL	32534
A1 LAWN SPRINKLER CO		15 REDWOOD CIRCLE	PENSACOLA	FL	32506
M7N VENDING SERVICE		440 W. HANNAH STREET	PENSACOLA	FL	32534
GLASS COAT INC		3180 HOWELL RD	PENSACOLA	FL	32568
GULF COAST POOL & SPA INC		2461 LANGLEY AVE	PENSACOLA	FL	32504
MANNING BROS POOL INC		9465 PENSACOLA BLVD	PENSACOLA	FL	32534
PANAMA POOLS OF NORTHWEST FLORIDA		291 POWELL ADAMS RD	PENSACOLA	FL	32413
PENSACOLA POOLS INC		8514 PENSACOLA BLVD	PENSACOLA	FL	32534
VAUGHN'S INC OF PENSACOLA		1290 NINE MILE ROAD	PENSACOLA	FL	32534
ALLPOOLS		8062 BRIOR OAK DRIVE	PENSACOLA	FL	32514
AVALON POOLS		4230 TANFIELD ROAD	MILTON	FL	32583
COX POOLS		22656 F CANAL ROAD	ORANGE BEACH	AL	36561
D K POOLS INC		4111 LILLIAN HWY	PENSACOLA	FL	32505-2202
L W POOLS		11600 MOBILE HIGHWAY	PENSACOLA	FL	32526
PINCH A PENNY POOL PATIO SPA		8090 N 9th AVE	PENSACOLA	FL	32514
SOUTHLAND POOLS		4333 BARCLAY PLACE	PACE	FL	32571
SUNSET POOLS SPAS & WHIRLPOOL BATHS		4382 HIGHWAY 90	PACE	FL	32571
SOUTH CENTRAL POOL SUPPLY		8808 Grow Dr	PENSACOLA	FL	32514
FANTASY POOLS & SPA		1350 S Blue Angel Pkwy	PENSACOLA	FL	32506
JOHNSON POOLS INC.		401 Massachusetts Ave	PENSACOLA	FL	32505
FAGANS CUSTOM POOLS INC.		13440 Serenity Cir	PENSACOLA	FL	32506
ATLANTIS POOL & SPA		2075 Elaine Cir	PENSACOLA	FL	32504
SUPERIOR POOLS PRODUCTS		3338 Mclemore Dr	PENSACOLA	FL	32514
WHOLESALE SPA & POOL OUTLETS		2323 Copter Rd	PENSACOLA	FL	32514
AFFORDABLE TREE LAWN & POOL		2011 W. Garden Street	PENSACOLA	FL	32502
EMERALD COAST IRRIGATION LLC		3041 Kingsfield Road	PENSACOLA	FL	32514
JERRY PATE TURF & IRRIGATION INC.		301 Schubert Drive	PENSACOLA	FL	32504
GULFSIDE LANDSCAPING INC		8221 Kipling Street	PENSACOLA	FL	32514
GONZALEZ PLUMBING & SPRINKLER		1801 Government Street	PENSACOLA	FL	32502
AIR DESIGN SYSTEMS INC.		400 Lurton St	PENSACOLA	FL	32505
ALL PRO PLUMBING & DRAIN		1765 E Nine Mile Rd Ste 1	PENSACOLA	FL	32514
ARTO'S SEWER & DRAIN SERVICE INC		2923 Rhythm St	PENSACOLA	FL	32505
CERTIFIED PLUMBING SEWER & GAS		7075 N Blue Angel Pkwy	PENSACOLA	FL	32526
PRICHARDS PLUMBING		40 Olive Rd	PENSACOLA	FL	32514
AGGRESSIVE PLUMBING		1220 Maura St	PENSACOLA	FL	32503
Terry Lambert Plumbing & Gas Service Inc		8145 Whitnir Dr	PENSACOLA	FL	32514
BATTLES PLUMBING LLC		2083 Downing Dr	PENSACOLA	FL	32505
KIMMON PLUMBING INC.		2560 Gulf Breeze Ave	PENSACOLA	FL	32507
NELSON PLUMBING CONTRACTORS		211 Brent Ln	PENSACOLA	FL	32503
GMC PLUMBING CONTRACTOR		664 Whitney Dr	PENSACOLA	FL	32503
CASEY HYMAN PLUMBING INC		5650 Dixie Dr	PENSACOLA	FL	32503
BALDWIN PLUMBING WORKS INC		3521 Bauer Rd	PENSACOLA	FL	32506
COASTAL PLUMBING & SEWER INC.		3010 Keats Dr	PENSACOLA	FL	32503
LARRY DOWNS JR PLUMBING CO		1949 Athens Ave	PENSACOLA	FL	32507
PLUMBERSMITH		9312 Bridlewood Rd	PENSACOLA	FL	32526
AQUA PRODUCTS INC.		3983 N.W. Street	PENSACOLA	FL	32505
VIP POOLS		3303 N. Davis Hwy.	PENSACOLA	FL	32503
AFFORDABLE POOL & SPA REPAIR INC.		7208 W. Fairfield Drive	PENSACOLA	FL	32506

TABLE 6

**ADVISORY NOTICE DISTRIBUTION LIST
WATER WELL, IRRIGATION/PLUMBING, AND POOL CONTRACTORS**

**OU-2 AGRICO SITE
PENSACOLA, FLORIDA**

NAME	COMPANY NAME	ADDRESS	CITY	STATE	POSTAL CODE
POOL CARE		600 Careondelay Drive	PENSACOLA	FL	32506
LESLIE'S SWIMMING POOL SUPPLIES		9251 University Pkwy	PENSACOLA	FL	32514
KENNY SMITHS POOL CARE		7134 Inniswold Drive	PENSACOLA	FL	32526
LORING IRRIGATION		2406 Escambia Avenue	PENSACOLA	FL	32503
AA IRRIGATION REPAIR		4301 N. Davis Hwy	PENSACOLA	FL	32503
THE FINISH LINE COMPANIES		3370 Pursell Lane	PENSACOLA	FL	32526
VEREN IRRIGATION PUMP SERVICE		10160 Candlestick Lane	PENSACOLA	FL	32514
PROFESSIONAL SPRINKLER SYSTEMS INC		1125 Corsa Terrace	PENSACOLA	FL	32514
GULF STREAM LANDSCAPING & IRRIGATION		8449 Old Palafox Street	PENSACOLA	FL	32504
KEN GRIFFIN LANDSCAPE CONTRACTORS		3004 Westfield Road	GULF BREEZE	FL	32563
LAYNE CHRISTENSEN CO		3720 N. Palafox Street	PENSACOLA	FL	32505
CLARK DRILLING		1040 Aquamarine Drive	GULF BREEZE	FL	32563
PRO POOLS INC.		1752 Old Bainbridge Road	TALLAHASSEE	FL	32303
BRYANT CHEMICAL COMPANY		6206 Vicksburg Drive	PENSACOLA	FL	32503
K C W WATER WELL SERVICE		4765 Sheller Road	TALLAHASSEE	FL	32305
DRILLING SOLUTIONS IINC.		5624 Pasture Lane	JAY	FL	32565
AQUA POOL & PATIO		5904 N. Palafox St	PENSACOLA	FL	32503
SURFSIDE POOLS		6677 Old Bagdad Hwy.	MILTON	FL	32583

**TABLE 7
IRRIGATION WELL INFORMATION**

**Agrico Site
Pensacola, Florida**

ID	PERMIT	NAME	STREET	DIAMETER (INCHES)	DEPTH FT. BLS	CASING FT. BLS	AQUIFER	ABANDONMENT OFFER LETTER SENT	IRRIGATION WELL SAMPLED	DATE SAMPLED	WELL ABANDONED	REMARKS
1		C.E. Anderson	905 TEXAR DRIVE	2	85	75	SZ	NO	NO			Outside of area of expected impacts for SZ
2	41(HC-1)	Holy Cross Cemetery Diocese of Pensacola	1300 E. HAYES	4	160	140	MPZ	YES	YES	11/28/2000		Two wells exist for cemetery, for sampling purposes labeled HC-1 and HC-2
	41(HC-2)	Holy Cross Cemetery Diocese of Pensacola	1300 E. HAYES	4	160	140	MPZ	YES	YES	11/28/2000		Two wells exist for cemetery, for sampling purposes labeled HC-1 and HC-2
3	81	C. Hass	349 SILVER ROAD	4	82	82	SZ	NO	NO			Outside of area of expected impacts for SZ
4	82	W.S. VanMetre	1221 TEXAR	4	95	95	SZ	NO	NO			Outside of area of expected impacts for SZ
5	97	O. English	3803 N. 10TH AVE.	4	71	130	120	yes	YES	3/13/01		
6	103	Dr. D. McGraw	1680 TEXAR	4	71	61	SZ	NO	NO			Outside of area of expected impacts for SZ
7	109	K. Wolfersterger	2700 MAGNOLIA AVE.	4	115	100	MPZ	YES	NO			
8	110	F & Kathleen Edsel, Jr	2721 BLACKSHEAR	4	UNK	UNK	UNK	RETURNED	NO			
9	111	J. Colley	1750 E. TEXAR DR.	2	85	80	SZ	NO	NO			Outside of area of expected impacts for SZ
10		Curry	2701 N. 16TH AVE.	4	158	143	MPZ	YES	YES	3/15/2001		
11	123	D. Lavin	3632 MENENDEZ DR.	4	73	63	SZ	NO	NO			Outside of area of expected impacts for SZ
12	124	Dr. B. Beidleman	2909 BLACKSHEAR	4	87	77	SZ	NO	NO			Outside of area of expected impacts for SZ
13	127	F. McCallister	2706 BLACKSHEAR	4	85	75	SZ	NO	NO			Outside of area of expected impacts for SZ
14	135	J. Klocke	2914 BLACKSHEAR	2	50	45	SZ	NO	NO			Outside of area of expected impacts for SZ
15	139	R. Moulton	3970 MENENDEZ DR.	4	110	100	MPZ	YES	NO			Well capped under land surface. Not Used
16	140	M. Johnson	1650 E. HAYES ST.	4	120	110	MPZ	YES	YES	11/28/2000		
17	142	L. Fishman	3003 MAGNOLIA AVE	NA	NA	NA	NA	YES	NA	NA		No well found at location
18	143	F. Clayborn	1640 E. HAYES ST.	4	125	110	MPZ	YES	NO		2/27/2001	Well exists. Irrigation System Not Used.
19	144	Dr. Willis (Family Practice)	915 E. FAIRFIELD DR	4	120	110	MPZ	YES	YES	5/10/2001		
20	160	B. Hodnelle, Jr.	3966 MENENDEZ	4	117	107	MPZ	YES	NO			
21		E. Davis	4130 MENENDEZ	2	45	40	SZ	NO	NO			Outside of area of expected impacts for SZ
22	194	D. Conkle	3080 BLACKSHEAR AVE	2	68	63	SZ	NO	NO			Outside of area of expected impacts for SZ
23	P9407748	Henry Langhorn	1725 EAST MAURA ST	4	140	120	MPZ	YES	NO			
24	P9503948	Floral Tree Gardens	3601 NORTH DAVIS HWY.	4	115	100	MPZ	YES	NO			
25	T8301727	Fred Levin	3600 MENENDEZ	2	35	30	SZ	NO	NO			Outside of area of expected impacts for SZ
26	T8402575	W.L. Glaze	2675 N. 17TH AVENUE	4	140	120	MPZ	RETURNED	NO			
27	T8403811	Mrs. Dorothy Bearman	1501 GAMARA ROAD	4	110	100	MPZ	YES	NO			
28	T8707396	Richard and Sarah Sanchez	1221 DURNFORD PLACE	4	140	130	MPZ	YES	YES	3/1/2001		
29	T8800778	William C. Baker	1250 DRIFTWOOD DRIVE	4	110	90	MPZ	YES	NO			

**TABLE 7
IRRIGATION WELL INFORMATION**

**Agrico Site
Pensacola, Florida**

ID	PERMIT	NAME	STREET	DIAMETER (INCHES)	DEPTH FT. BLS	CASING FT. BLS	AQUIFER	ABANDONMENT OFFER LETTER SENT	IRRIGATION WELL SAMPLED	DATE SAMPLED	WELL ABANDONED	REMARKS
30	T8905178	Leroy Gamlin	1005 TUNIS STREET	4	116	106	MPZ	YES	NO			
31	T9005951	Joseph Bores	4100 MENENDEZ DRIVE	4	130	120	MPZ	YES	YES	11/28/2000		
32	T9103343	Charles R. Earnest	1900 EAST LEONARD ST.	4	151	121	MPZ	YES	YES	11/28/2000		Well Resampled 5-10-01 to confirm PCE detection
33	T9104961	Dr. Peter C. Delevett	1660 TEXAR DRIVE	2	84	74	SZ	NO	NO			
34	T9104962	Paul Williams	800 E. BAARS ST	4	120	60	MPZ	YES	NO			808 E. Baars sharing well at 800 E. Baars
35	T9206908	John C. Sowers	3090 BLACKSHEAR AVE	2	90	80	SZ	NO	NO			Outside of area of expected impacts for SZ
36	T9304906	J.E. Boatwright Jr.	2575 PARADISE POINT DR	4	120	100	MPZ	YES	YES	3/1/2001		
37	T9701332	Elisabeth Holmes	1781 E. LEONARD ST.	2	UNK	UNK	UNK	YES	NO			
38	T9800088	James T. Baer	1775 EAST TEXAR DR	4	UNK	UNK	UNK	YES	YES	11/29/2000		
39	P9405922	Randy Head	2015 E. Maura St	NA			NA	YES	NA			No well found at location
40	158	N. Kinder	1227 BARCIA DR.	UNK	UNK	UNK	UNK	YES	NO			
41	162	W. Veasie	1271 DRIFTWOOD DR.	4	96	73	SZ	NO	no			Outside of area of expected impacts for SZ
42	171	D. Tringas	2621 PARADISE POINT	UNK	UNK	UNK	UNK	YES	YES	3/1/2001		
43	172	B. Samples	1009 EAST TUNIS	UNK	UNK	UNK	UNK	YES	YES	11/28/2000		
44	178	C. Davis	1555 EAST CROSS ST.	2	UNK	UNK	UNK	YES	NO			
45		Moss & Bessie Wilson	3510 N. 9TH AVE	NA	NA	NA	NA	NO	NA			No well found at location
46		John & Priscilla Snyder	2912 BLACKSHEAR AVE	UNK	UNK	UNK	UNK	YES	NO			
47		David & Jean Mayo	3030 BLACKSHEAR AVE	UNK	UNK	UNK	UNK	YES	YES	3/1/2001		
48		Neroy & Lois Anderson	1301 E FISHER ST	UNK	UNK	UNK	UNK	YES	NO			
49		Jude & Nancy White	1710 E CROSS ST	4	140		UNK	YES	YES	8/25/1999		Results in the First annual report OU-2 (2/2000)
50		Mr. Glen McDonald	2860 BLACKSHEAR AVE	UNK	UNK	UNK	UNK	RETURNED	NO			
51		John & Sue Woodward	2710 BLACKSHEAR AVE	4	100	90	MPZ	YES	YES	3/1/2001		
52	159	Amos & Clementine Prevatt	2712 BLACKSHEAR AVE	2	55	45	SZ	NO	NO			Outside of area of expected impacts for SZ
53	80	Howard & Joyce Rein	2101 E CROSS ST	4	130	120	MPZ	YES	YES	11/28/2001		
54		Diocese of Pensacola	1231 DURNFORD PL	UNK	UNK	UNK	UNK	YES	YES	11/28/2001		Bishop's Residence
55		Larry & Catherine Parks	1210 DURNFORD PL	4	145	130	MPZ	YES	NO		2/27/2001	

**TABLE 7
IRRIGATION WELL INFORMATION**

**Agrico Site
Pensacola, Florida**

ID	PERMIT	NAME	STREET	DIAMETER (INCHES)	DEPTH FT. BLS	CASING FT. BLS	AQUIFER	ABANDONMENT OFFER LETTER SENT	IRRIGATION WELL SAMPLED	DATE SAMPLED	WELL ABANDONED	REMARKS
56		Dennis & Betty Peters	3990 MENENDEZ DR	4	78	65	SZ	NO	NO			Outside of area of expected impacts for SZ
57		Jack & Carolyn Fleming	4010 MENENDEZ DR	UNK	UNK	UNK	UNK	YES	YES	11/28/2000		
58		Richard & Page Ciordia	4020 MENENDEZ DR	4	92	82	SZ	NO	NO			Outside of area of expected impacts for SZ
59		Garrett & Joyce Boyd	1261 STOW AVE	UNK	UNK	UNK	UNK	YES	NO			
60		Gene Schmidt	4141 MENENDEZ DR	4	115	100	MPZ	YES	YES	11/29/2000		
62		C.E. Davis	808 BAARS ST.	UNK	UNK	UNK	UNK	YES	YES	3/13/2001		
63	P200104- 707	Escambia County Park Service	CARRIE MILLER PARK	4	90	70	SZ	NO	NO			Downgradient of FDEP Kaiser Site; drilled after moratory initiated.

- (1) ID = Map ID number for Figure 2
(2) Permit = Northwest Florida Water Management District Permit Number
(3) Aquifer = SZ = Surficial zone of Sand-and-Gravel Aquifer; MPZ = Main producing zone of Sand-and-Gravel Aquifer;
(4) Unknown = No well construction information available ; UNK= Data Unknown
*(5) NA = Not Applicable
*(6) ft. bls = feet below land surface

SUMMARY

TOTAL

1. NUMBER OF NOTIFICATIONS OF VOLUNTARY ABANDONMENT OFFER	41
2. NUMBER OF LOCATION WHERE SURFICIAL ZONE IRRIGATION WELLS EXIST BUT NO POTENTIAL FOR IMPACTS BY AGRICO-RELATED CONSTITUENTS	8
3. WRONG INFORMATION - NO WELL PRESENT AT LOCATION	1
4. NUMBER OF ADDITIONAL IRRIGATION WELLS IDENTIFIED (1 additional well identified at Holy Cross Cemetery)	1
5. TOTAL NUMBER OF IRRIGATION WELLS IDENTIFIED	60
6. TOTAL NUMBER OF WELLS ABANDONED THROUGH FEBRUARY 2001.	0
7. NUMBER OF WELLS SAMPLED THROUGH FEBRUARY 2001.	12

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Surficial Zone										
ACB-31S	5/9/1997	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/10/1997	<0.2	<0.010	<0.0050	NA	NA	NA	NA	NA	NA
	5/4/1998	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/23/1998	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/25/1999	<0.2	<0.01	<0.005	NA	NA	NA	NA	NA	NA
	11/17/1999	<0.2	<0.010	<0.0050	NA	NA	NA	NA	NA	NA
	5/15/2000	<0.2	<0.010	<0.0050	NA	NA	NA	NA	NA	NA
	11/14/2000	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/9/2001	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/15/2001	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/15/2002	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/19/2002	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/7/2003	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	1/13/2004	< 0.2 U	< 0.01 U	< 0.005 U	4.9	50	3.4 J	0.67 J+/- 0.21	5.08 +/- 0.92	5.8
	5/11/2004	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/9/2004	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/10/2005	0.2	0.01	0.005	NA	NA	NA	NA	NA	NA
	11/8/2005	< 0.2 U	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	5/15/2006	<0.2 U	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/14/2006	< 0.2 U	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	5/16/2007	< 0.1 U	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/15/2007	< 0.2 U	< 0.01 U	< 0.005 U	7.9	50	4.8	0.829 +/- 0.16	5.25 +/- 0.61	6.08
	5/15/2008	< 0.2 U	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/13/2008	< 0.2 U	< 0.01 U	< 0.005 U	5.1	51	6.5	0.68 +/- 0.16	6.59 +/- 0.63	7.27
	11/19/2009	< 0.1 U	< 0.01 U	NA	5.3	44	4.9	0.708 +/- 0.18	5.58 +/- 0.55	6.29
	11/16/2010	<0.10	NA	NA	3.2	43	6.8	0.611 +/- 0.21	4.35 +/- 0.71	4.96
	11/8/2011	<0.10	NA	NA	5.5	52	3.4	0.498 +/- 0.18	4.49 +/- 0.93	4.99
	11/6/2012	<0.10	NA	NA	3.5	39	1.9	0.474 +/- 0.19	4.99 +/- 0.81	5.46
	11/5/2013	<0.10	NA	NA	3.1	36	2.4	0.184 +/- 0.17	4.15 +/- 0.74	4.33
	11/12/2014	<0.10	NA	NA	2.1	37	2.4	0.43 +/- 0.17	4.59 +/- 0.79	5.02

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Surficial Zone										
ACB-32S	5/9/1997	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/10/1997	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/4/1998	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/23/1998	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/15/1999	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/17/1999	< 0.2	< 0.010	< 0.0050	NA	NA	NA	NA	NA	NA
	5/15/2000	< 0.2	< 0.010	< 0.0050	NA	NA	NA	NA	NA	NA
	11/14/2000	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/9/2001	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/1/2001	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/15/2002	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/19/2002	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/7/2003	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	1/13/2004	< 0.2 U	0.011	< 0.005 U	7.2	55	8.3 J	0.62 J+/- 0.21	3.89 +/- 0.88	4.5
	5/11/2004	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/9/2004	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/10/2005	< 0.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/8/2005	< 0.2 U	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	5/15/2006	< 0.2 U	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/14/2006	< 0.2 U	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	5/16/2007	< 0.1 U	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/15/2007	< 0.2 U	< 0.01 U	< 0.005 U	3.7	16	1.7	0.195 +/- 0.0690	1.11 +/- 0.34	1.31
	5/15/2008	< 0.2 U	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/13/2008	< 0.2 U	< 0.01 U	< 0.005 U	3.1	18	2.2	0.104 +/- 0.0870	1.1 +/- 0.30	1.2
	11/19/2009	< 0.1 U	< 0.01 U	NA	2	10	1.3	0.164 +/- 0.12	0.796 +/- 0.37	0.960
	11/16/2010	0.11	NA	NA	1.6	14	0.78	0.199 +/- 0.12	0.619 +/- 0.48	0.818
	11/8/2011	0.1	NA	NA	1.5	8.3	0.85	-0.0461 +/- 0.11	1.28 +/- 0.39	1.23
	11/6/2012	0.11	NA	NA	1	4.5	0.93	0.206 +/- 0.13	0.580 +/- 0.40	0.786
	11/5/2013	< 0.10	NA	NA	1.2	2.8	0.34	0.290 +/- 0.16	0.517 +/- 0.43	0.807
	11/13/2014	0.12	NA	NA	1.4	13	0.55	0.194 +/- 0.11	0.663 +/- 0.32	0.857

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Surficial Zone										
AC-33S	5/9/1997	0.81	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/10/1997	0.82	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/4/1998	1.7	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/23/1998	0.47	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/15/1999	0.29	0.017	0.0063	NA	NA	NA	NA	NA	NA
	11/17/1999	0.26	< 0.010	< 0.0050	NA	NA	NA	NA	NA	NA
	5/16/2000	0.25	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/14/2000	0.22	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/9/2001	0.32	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/15/2001	0.4	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/15/2002	0.33	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/19/2002	0.5	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/7/2003	0.63	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	1/14/2004	0.71	< 0.01 U	< 0.005 U	26	94	1.7	3.27 +/- 0.54	11.9 +/- 1.50	15.2
	5/11/2004	1.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/9/2004	2.7	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/10/2005	0.6	0.01	0.005	NA	NA	NA	NA	NA	NA
	11/8/2005	0.75	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	5/15/2006	0.27	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/14/2006	1.4	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	5/16/2007	1.4	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/15/2007	0.64	< 0.01 U	< 0.005 U	7.5	26	1.5	0.437 +/- 0.14	1.38 +/- 0.34	1.82
	5/15/2008	0.94	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/14/2008	0.94	< 0.01 U	< 0.005 U	7.7	27	1.6	0.673 +/- 0.15	1.92 +/- 0.39	2.59
	11/19/2009	1.6	< 0.01 U	NA	6.5	23	1	0.475 +/- 0.13	2.73 +/- 0.41	3.21
	11/16/2010	0.77	NA	NA	8.5	25	0.59	0.522 +/- 0.19	1.99 +/- 0.50	2.51
	11/8/2011	0.61	NA	NA	1.9	20	0.45	0.391 +/- 0.15	2.00 +/- 0.44	2.39
	11/6/2012	0.67	NA	NA	6.6	90	0.36	0.930 +/- 0.28	4.68 +/- 0.78	5.61
	11/5/2013	0.78	NA	NA	5.7	20	0.24	0.410 +/- 0.20	2.07 +/- 0.47	2.48
	11/13/2014	0.63	NA	NA	3.4	28	0.18	0.435 +/- 0.15	2.47 +/- 0.50	2.91

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Surficial Zone										
AC-34S	5/9/1997	16	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/10/1997	9.5	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/4/1998	6.3	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/23/1998	3.8	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/15/1999	3.5	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/17/1999	2.5	< 0.010	< 0.0050	NA	NA	NA	NA	NA	NA
	5/16/2000	2.6	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/14/2000	1.6	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/9/2001	1.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/15/2001	1.6	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/15/2002	1.4	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/19/2002	1.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/7/2003	1.9	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	1/14/2004	2	< 0.01 U	< 0.005 U	9.3	80	6.5	0.38 J+/- 0.18	2.04 +/- 0.58	2.42
	5/11/2004	9.7	0.011	< 0.005	NA	NA	NA	NA	NA	NA
	11/9/2004	9.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/10/2005	8	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/8/2005	7.3	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	5/15/2006	6.4	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/14/2006	5.6	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	5/16/2007	4.6	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/15/2007	4.2	< 0.01 U	< 0.005 U	8.6	74	2.4	0.261 +/- 0.12	2.06 +/- 0.43	2.32
	5/15/2008	3.1	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/14/2008	2.4	< 0.01 U	< 0.005 U	7.2	68	2.8	0.159 +/- 0.0990	2.04 +/- 0.38	2.20
	11/19/2009	1.6	< 0.01 U	NA	5.9	60	2.3	0.152 +/- 0.12	2.54 +/- 0.42	2.69
	11/17/2010	1.9	NA	NA	5.1	68	6.6	0.149 +/- 0.085	1.14 +/- 0.34	1.29
	11/9/2011	1	NA	NA	3.3	67	2.9	0.296 +/- 0.15	0.984 +/- 0.31	1.28
	11/7/2012	0.97	NA	NA	2.1	37	2.8	0.152 +/- 0.12	0.785 +/- 0.29	0.937
	11/5/2013	0.77	NA	NA	4.1	52	2.1	0.218 +/- 0.14	0.927 +/- 0.36	1.15
	11/13/2014	1.2	NA	NA	3.2	39	2.6	0.0455 +/- 0.084	0.593 +/- 0.28	0.64

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Surficial Zone										
AC-7SR	5/9/1997	19	0.014	0.012	NA	NA	NA	NA	NA	NA
	11/10/1997	9.1	0.012	0.011	NA	NA	NA	NA	NA	NA
	5/4/1998	10	0.017	0.028	NA	NA	NA	NA	NA	NA
	11/23/1998	6.7	< 0.01	0.011	NA	NA	NA	NA	NA	NA
	5/15/1999	7.4	0.02	0.022	NA	NA	NA	NA	NA	NA
	11/17/1999	6.4	<0.010	<0.0050	NA	NA	NA	NA	NA	NA
	5/16/2000	5.6	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/14/2000	5.1	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/9/2001	5.8	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/15/2001	5.6	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/15/2002	6.5	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/19/2002	4.8	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/7/2003	6.1	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	1/14/2004	6.4	< 0.01 U	< 0.005 U	6.4	38	2.8	0.58 J+/- 0.21	1.62 +/- 0.52	2.2
	5/11/2004	9.4	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	11/9/2004	9.2	< 0.01	< 0.005	NA	NA	NA	NA	NA	NA
	5/10/2005	5.4	0.01	0.005	NA	NA	NA	NA	NA	NA
	11/8/2005	5.3	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	5/15/2006	4.4	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/14/2006	5.7	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	5/16/2007	4.1	< 0.01 U	< 0.005 U	NA	NA	NA	NA	NA	NA
	11/15/2007	3.6	< 0.01 U	< 0.005 U	6.9	35	2.3	0.339 +/- 0.12	0.974 +/- 0.34	1.31
	5/15/2008	6	< 0.01 U	0.0056	NA	NA	NA	NA	NA	NA
	11/14/2008	3.3	< 0.01 U	< 0.005 U	6.8	46	2.1	0.188 +/- 0.10	1.24 +/- 0.39	1.43
	11/19/2009	3.1	< 0.01 U	NA	7	32	2.1	0.239 +/- 0.10	1.11 +/- 0.31	1.35
	11/17/2010	3.7	NA	NA	5.1	27	1.7	0.240 +/- 0.11	0.820 +/- 0.30	1.06
	11/8/2011	2.9	NA	NA	3.8	30	1.8	0.322 +/- 0.14	1.05 +/- 0.30	1.37
	11/6/2012	0.94	NA	NA	5.8	34	1.9	0.272 +/- 0.16	1.45 +/- 0.44	1.72
	11/5/2013	2.4	NA	NA	5.0	28	1.4	0.172 +/- 0.16	1.09 +/- 0.36	1.26
	11/13/2014	1.8	NA	NA	3.3	28	1.2	0.324 +/- 0.12	0.877 +/- 0.30	1.20

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Surficial Zone										
AC-2S	4/15/1987	16	0.010	NA	7.4	143	NA	NA	NA	NA
	10/1/1990	63	0.74	<0.005	18	260	12	NA	NA	NA
	2/4/1992	94	0.164	< 0.005	20	290	15	0.4 +/- 0.10	1.2 +/- 1	1.6
	9/28/1997	130	0.058	NA	10	150	9	< 0.6 +/- 0.03	1.7 +/- 0.48	2.3
	11/17/1999	98	0.029	NA	7	57	5	< 1. +/- 0.94	< 1.5 +/- 0.90	2.5
	11/21/2000	150	0.048	NA	6.8	48	5.6	0.5 +/- 0.20	1.9 +/- 1.50	2.4
	11/15/2001	190	0.036	NA	6	23	3.8	0.1 +/- 0.07	2.8 +/- 1	2.9
	11/26/2002	210	0.042	NA	5.7	22	3.6	0.1 +/- 0.07	0. +/- 0.60	0.1
	1/23/2004	170	0.046	< 0.005 U	5.7	15	3.5	< 0.25 U +/- 0.17	< 1.1 U +/- 0.66	0.79
	11/17/2004	100	0.027	NA	7.1	< 5.	3	0.134 +/- 0.08	0.286 +/- 0.31	0.420
	11/15/2005	73	0.021	NA	8.8	59	3.9	0.103 J +/- 0.0690	0.649 J +/- 0.34	0.752
	11/28/2006	85	0.029	NA	9.1	69	4	0.032 +/- 0.0750	-0.382 +/- 0.19	-0.35
	11/21/2007	50	0.016	NA	5.3	< 5. U	1.9	0.041 +/- 0.0790	0.0402 +/- 0.13	0.081
	11/19/2008	54	0.02	< 0.005 U	7.6	< 5. U	3.2	0.0442 +/- 0.0860	-0.0882 +/- 0.21	-0.0440
	11/18/2009	44	0.017	NA	4.9	31	2.7	0.191 +/- 0.11	0.0314 +/- 0.19	0.222
	11/29/2010	48	0.024	NA	6.1	44	3.4	0.0772 +/- 0.082	0.449 +/- 0.26	0.526
	11/16/2011	68	0.024	NA	7.5	54	6.2	0.168 +/- 0.13	0.0656 +/- 0.27	0.234
	11/14/2012	43	0.016	NA	4.3	62	4.6	0.0957 +/- 0.16	0.118 +/- 0.24	0.214
	11/12/2013	36	0.016	NA	3.8	59	3.3	0.0439 +/- 0.13	0.273 +/- 0.27	0.317
	11/12/2014	34	0.02	NA	4.2	73	3.1	0.0951 +/- 0.10	0.309 +/- 0.40	0.404

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Surficial Zone										
AC-3S	4/15/1987	0.65	<0.004	NA	4.1	59	1.9	NA	NA	NA
	10/1/1990	0.21	<0.01	<0.005	15	22	4	NA	NA	NA
	2/5/1992	< 0.2	< 0.01	0.0081	5.5	27	2.9	1.4 +/- 0.10	0.8 +/- 0.90	2.2
	9/28/1997	1.4	< 0.01	NA	3.8	24	0.92	< 0.6 +/- 0.05	< 1. +/- 0.46	1.6
	11/17/1999	< 0.2	< 0.01	NA	5.7	14	1.1	< 1. +/- 0.79	< 1.5 +/- 0.60	2.5
	11/21/2000	< 0.2	< 0.01	NA	11	16	2.7	0.3 +/- 0.10	1.1 +/- 1.20	1.4
	11/14/2001	< 0.2	< 0.01	NA	7.7	17	2.3	0.1 +/- 0.09	0. +/- 0.70	0.1
	11/26/2002	< 0.2	< 0.01	NA	3.4	13	1.1	0.4 +/- 0.07	0.6 +/- 0.70	1
	1/22/2004	< 0.2 U	< 0.01 U	< 0.005 U	2.9	7.9	1. J	< 0.34 U+/- 0.18	< 1.4 U+/- 0.86	1.22
	11/17/2004	< 0.2	< 0.01	NA	4.2	13	2.1	0.25 +/- 0.0820	0.285 +/- 0.30	0.54
	11/15/2005	< 0.2 U	< 0.01 U	NA	12	15	2.8	0.0862 U+/- 0.10	1.44 +/- 0.40	1.53
	11/22/2006	< 0.2 U	< 0.01 U	NA	8.9	16	2.8	0.243 +/- 0.15	0.81 +/- 0.29	1.1
	11/21/2007	< 0.2 U	< 0.01 U	NA	5.5	20	2	0.191 +/- 0.11	0.687 +/- 0.25	0.878
	11/13/2008	< 0.2 U	< 0.01 U	< 0.005 U	3.6	11	1.1	0.204 +/- 0.10	0.226 +/- 0.27	0.430
	11/18/2009	< 0.1 U	< 0.01 U	NA	3.7	11	1.8	0.14 +/- 0.0790	0.634 +/- 0.38	0.77
	11/29/2010	< 0.1	< 0.01	NA	6.7	17	7.3	0.248 +/- 0.10	0.453 +/- 0.26	0.701
	11/15/2011	< 0.1	< 0.01	NA	3.8	30	3.9	0.147 +/- 0.11	0.888 +/- 0.35	1.04
	11/13/2012	<0.1	<0.010	NA	2.9	21	1.7	0.266 +/- 0.18	0.798 +/- 0.37	1.06
	11/12/2013	<0.1	<0.010	NA	2.4	17	1.5	0.229 +/- 0.16	0.955 +/- 0.41	1.18
	11/11/2014	<0.1	<0.0050	NA	2.5	15	2	0.030 +/- 0.082	0.159 +/- 0.38	0.19

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Surficial Zone										
AC-5S	4/15/1987	0.26	NA	NA	7	90	NA	NA	NA	NA
	10/1/1990	<0.2	<0.01	<0.005	12	25	12	NA	NA	NA
	1/31/1992	< 0.2	< 0.01	< 0.005	9.3	27	6.4	NA	NA	NA
	9/26/1997	< 0.2	< 0.01	NA	8.6	27	4.3	< 0.6 +/- 0.05	1.3 +/- 0.44	1.9
	11/17/1999	< 0.2	< 0.01	NA	19	29	5.9	< 1. +/- 0.66	1.9	2.9
	11/21/2000	< 0.2	< 0.01	NA	24	30	4.9	0.5 +/- 0.20	0.8 +/- 1	1.3
	11/13/2001	< 0.2	< 0.01	NA	35	31	1.5	0.7 +/- 0.10	1.8 +/- 0.90	2.5
	11/20/2002	< 0.2	< 0.01	NA	17	21	2.1	0.5 +/- 0.10	1. +/- 0.80	1.5
	1/20/2004	< 0.2 U	< 0.01 U	< 0.005 U	14	10	0.9	< 0.26 U+/- 0.18	< 0.66 U+/- 0.40	0.59
	11/10/2004	< 0.2	< 0.01	NA	46	13	1.2	0.481 +/- 0.11	1.58 +/- 0.30	2.06
	11/16/2005	< 0.2 U	< 0.01 U	NA	27	12	1.5	0.352 J+/- 0.13	1.42 +/- 0.43	1.77
	11/21/2006	< 0.2 U	< 0.01 U	NA	18	24	4.5	0.461 +/- 0.17	0.928 +/- 0.30	1.39
	11/13/2008	< 0.2 U	< 0.01 U	< 0.005 U	12	19	6.8	0.539 +/- 0.13	1.17 +/- 0.33	1.71
	11/12/2014	<0.10	NA	NA	9	24	4.5	0.596 +/- 0.21	1.32 +/- 0.48	1.92
Surficial Zone										
AC-6S	4/15/1987	1.04	NA	NA	24.3	74	21.9	NA	NA	NA
	10/1/1990	1.9	<0.01	0.0072	24	32	24	NA	NA	NA
	2/2/1992	0.6	< 0.01	< 0.005	15	28	6.7	NA	NA	NA
	9/25/1997	0.75	< 0.01	NA	12	47	5.3	0.88 +/- 0.07	1.6 +/- 0.48	2.48
	1/27/2004	0.85	< 0.01 U	< 0.005 U	30	130	14	2.22 +/- 0.45	5.71 +/- 0.91	7.93
	11/12/2008	0.71	< 0.01 U	< 0.005 U	31	110	11	1.3 +/- 0.20	5.01 +/- 0.54	6.31
	11/17/2014	0.48	NA	NA	11	38	5.7	0.937 +/- 0.32	2.04 +/- 0.58	2.98

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Surficial Zone										
AC-24S	2/19/1992	< 0.2	< 0.01	< 0.005	8	7.4	1.6	NA	NA	NA
	9/27/1997	< 0.2	< 0.01	NA	8.4	9.7	1.4	< 0.6 +/- 0.03	< 1. +/- 0.45	1.6
	11/17/1999	< 0.2	< 0.01	NA	8	8.8	1.1	< 1. +/- 0.82	< 1.5 +/- 0.68	2.5
	11/21/2000	< 0.2	< 0.01	NA	8	6.7	1.7	0.4 +/- 0.10	5.1 +/- 1.10	5.5
	11/14/2001	< 0.2	< 0.01	NA	8.1	5.9	1.9	0.2 +/- 0.09	0. +/- 0.70	0.2
	11/20/2002	< 0.2	< 0.01	NA	9.2	4.3 J	1.8	0.3 +/- 0.10	0.3	0.6
	1/21/2004	< 0.2 U	< 0.01 U	< 0.005 U	9.9	< 5. U	1.8	< 0.29 U +/- 0.19	< 1.6 U +/- 0.9980	1.6
	11/16/2004	< 0.2	< 0.01	NA	8.9	< 5.	2.5	0.207 +/- 0.0850	1.44 +/- 0.32	1.65
	11/17/2005	< 0.2 U	< 0.01 U	NA	11	7.2	3.6	0.596 J +/- 0.18	2.36 +/- 0.53	2.96
	11/21/2006	< 0.2 U	< 0.01 U	NA	17	5.2	6.8	0.595 +/- 0.18	2. +/- 0.40	2.60
	11/18/2008	< 0.2 U	< 0.01 U	< 0.005 U	20	11	1.9	0.33 +/- 0.0990	1.42 +/- 0.33	1.8
	11/24/2014	< 0.10	NA	NA	7.6	12	3.6	0.263 +/- 0.20	1.96 +/- 0.48	2.22
Surficial Zone										
AC-26S	2/11/1992	< 0.2	< 0.01	< 0.005	10	13	0.95	NA	NA	NA
	9/24/1997	< 0.2	< 0.01	NA	12	21	2.9	< 0.6 +/- 0.06	< 1. +/- 0.47	1.6
	11/17/1999	< 0.2	< 0.01	NA	20	17	2.1	1.8	3.1 +/- 0.76	4.9
	11/21/2000	< 0.2	< 0.01	NA	25	15	1.6	0.6 +/- 0.10	4.9 +/- 1.20	5.5
	11/14/2001	< 0.2	< 0.01	NA	23	23	2.3	0.6 +/- 0.10	2.5 +/- 0.90	3.1
	11/21/2002	< 0.2	< 0.01	NA	19	22	1.7	0.7 +/- 0.20	1.5 +/- 1	2.2
	1/20/2004	< 0.2 U	< 0.01 U	< 0.005 U	20	21	1.2	0.82 J +/- 0.25	1.83 +/- 0.42	2.7
	11/10/2004	< 0.2	< 0.01	NA	22	20	2.6	0.722 +/- 0.14	2.43 +/- 0.36	3.15
	11/9/2005	< 0.2 U	< 0.01 U	NA	18	20	1.7	0.444 J +/- 0.14	1.56 +/- 0.35	2.00
	11/20/2006	< 0.2 U	< 0.01 U	NA	26	19	2.9	0.512 +/- 0.19	1.85 +/- 0.39	2.36
	11/12/2008	< 0.2 U	< 0.01 U	< 0.005 U	11	19	0.74	0.424 +/- 0.12	1.62 +/- 0.43	2.04
	11/19/2014	< 0.10	NA	NA	7.3	13	1	0.0821 +/- 0.11	0.634 +/- 0.33	0.72
Surficial Zone										
AC-27S	4/8/1992	< 0.2	< 0.01	< 0.005	18	< 5.	1.9	NA	NA	NA
	9/24/1997	< 0.2	< 0.01	NA	14	4.3	1.5	< 0.6 +/- 0.05	1.1 +/- 0.45	1.7
	1/13/2004	< 0.2 U	< 0.01 U	< 0.005 U	4.5	< 5. U	0.19	0.18 J +/- 0.12	< 0.88 U +/- 0.55	0.88
	11/11/2005	< 0.2 U	< 0.01 U	NA	47	< 5. U	6.4	1.71 +/- 0.38	0.418U +/- 0.29	2.13
	11/17/2008	< 0.2 U	< 0.01 U	< 0.005 U	4.7	8.6	0.089	0.167 +/- 0.09	0.157 +/- 0.23	0.324
	11/13/2014	< 0.10	NA	NA	19	4.5	1.5	0.785 +/- 0.25	2.11 +/- 0.48	2.9

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Surficial Zone										
NWD-2S	10/1/1990	0.78	<0.01	<0.005	8.6	25	5.7	NA	NA	NA
	2/3/1992	4.2	< 0.01	< 0.005	8.2	19	4.6	NA	NA	NA
	9/25/1997	5.2	< 0.01	NA	4	25	3	< 0.6 +/- 0.07	1.2 +/- 0.42	1.8
	11/17/1999	4.5	< 0.01	NA	7.1	30	3.5	1.1 +/- 0.59	< 1.5 +/- 0.06	2.6
	11/21/2000	4.2	< 0.01	NA	4.3	32	3.4	1.56 +/- 0.30	2.6 +/- 0.90	4.2
	11/14/2001	3.7	< 0.01	NA	5.1	28	3.6	0.8 +/- 0.20	1.2 +/- 0.80	2
	11/20/2002	3.1	< 0.01	NA	4.4	28	2.8	0.7 +/- 0.10	1.1	1.8
	1/19/2004	3.2	< 0.01 U	< 0.005 U	12	26	5	0.66 J+/- 0.19	1.61 +/- 0.60	2.3
	11/10/2004	2.7	< 0.01	NA	14	28	5.1	0.628 +/- 0.15	1.67 +/- 0.32	2.30
	11/17/2005	2.2	< 0.01 U	NA	11	35	4	0.237 J+/- 0.11	1.86 +/- 0.46	2.10
	11/21/2006	2.1	< 0.01 U	NA	15	27	5.3	0.48 +/- 0.22	1.3 +/- 0.34	1.8
	11/12/2008	2	< 0.01 U	< 0.005 U	12	19	3.4	0.616 +/- 0.14	1.27 +/- 0.35	1.89
	11/11/2014	1.6	NA	NA	8.3	13	2.1	0.339 +/- 0.16	0.875 +/- 0.33	1.21
Surficial Zone										
NWD-4S	2/7/1992	< 0.2	< 0.01	0.0054	6.1	< 5.	1.3	0.7 +/- 0.20	1.5 +/- 0.80	2.2
	9/26/1997	< 0.2	< 0.01	NA	4.7	< 5.	0.41	< 0.6 +/- 0.04	< 1. +/- 0.40	1.6
	11/17/1999	< 0.2	< 0.01	NA	7.2	< 5.	0.31	1.4	< 1.5 +/- 0.81	2.9
	11/21/2000	< 0.2	< 0.01	NA	5.5	< 5.	0.4	0.5 +/- 0.10	6.4 +/- 1.20	6.9
	11/13/2001	< 0.2	< 0.01	NA	5	< 5.	0.44	0.5 +/- 0.10	1.8 +/- 0.80	2.3
	11/22/2002	< 0.2	< 0.01	NA	5.5	< 5.	0.35	0.6 +/- 0.20	1.1 +/- 0.80	1.7
	1/21/2004	< 0.2 U	< 0.01 U	< 0.005 U	9.6	< 5. U	1.2	0.5 J+/- 0.22	2.17 +/- 0.95	2.7
	11/16/2004	< 0.2	< 0.01	NA	9.8	< 5.	0.61	0.583 +/- 0.15	1.49 +/- 0.33	2.07
	11/15/2005	< 0.2 U	< 0.01 U	NA	15	< 5. U	0.28	0.741 J+/- 0.23	1.62 +/- 0.46	2.36
	11/21/2006	< 0.2 U	< 0.01 U	NA	17	< 5. U	1.2	0.79 +/- 0.19	0.973 +/- 0.34	1.8
	11/19/2008	< 0.2 U	< 0.01 U	< 0.005 U	9.4	< 5. U	2.6	0.951 +/- 0.15	1.08 +/- 0.31	2.03
	11/14/2014	<0.10	NA	NA	4.3	4.8	0.41	0.515 +/- 0.22	1.17 +/- 0.37	1.69

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-2D	4/15/1987	5.1	<0.004	NA	14.7	22	3.37	NA	NA	NA
	10/1/1990	5.1	<0.01	<0.005	15	10	3.5	NA	NA	NA
	2/4/1992	5.2	< 0.01	0.0057	16	7.4	3.5	2.8 +/- 0.30	7. +/- 1.30	9.8
	9/30/1997	2.9	< 0.01	NA	12	26	5.6	0.6	< 1. +/- 0.45	1.6
	11/17/1999	3.5	< 0.01	NA	11	15	3.6	< 1. +/- 0.49	< 1.5 +/- 0.83	2.5
	11/21/2000	3	< 0.01	NA	9.8	19	4.4	1. +/- 0.20	2.7 +/- 0.90	3.7
	11/15/2001	3	< 0.01	NA	9.4	17	3.5	1. +/- 0.20	2.5 +/- 1	3.5
	11/26/2002	3.2	< 0.01	NA	9.1	18	2.5	1.1 +/- 0.20	2. +/- 0.80	3.1
	1/23/2004	2.9	< 0.01 U	< 0.005 U	9	13	2.5	1.05 +/- 0.25	1.54 +/- 0.71	2.59
	11/17/2004	2.7	< 0.01	NA	9.1	14	2.6	1.09 +/- 0.17	1.42 +/- 0.37	2.51
	11/14/2005	2.3	< 0.01 U	NA	9.2	16	2.8	0.983 J +/- 0.27	1.85 +/- 0.51	2.83
	11/28/2006	2.2	< 0.01 U	NA	8.2	15	2.5	0.896 +/- 0.14	1.16 +/- 0.28	2.06
	11/21/2007	2.5	< 0.01 U	NA	7.8	16	3.3	0.843 +/- 0.17	1.22 +/- 0.28	2.06
	11/19/2008	2	< 0.01 U	< 0.005 U	8.8	13	2.5	0.994 +/- 0.16	1.17 +/- 0.31	2.16
	11/18/2009	2	< 0.01 U	NA	8.4	15	2.3	1.2 +/- 0.18	1.7 +/- 0.34	2.9
	11/29/2010	2.3	NA	NA	8.3	16	2.6	1.31 +/- 0.39	1.59 +/- 0.39	2.90
	11/16/2011	2.3	NA	NA	7.6	17	2	1.06 +/- 0.22	1.71 +/- 0.42	2.77
	11/14/2012	2.2	NA	NA	6.9	17	2.1	0.744 +/- 0.27	1.94 +/- 0.54	2.68
	11/12/2013	2.3	NA	NA	7.0	17	5.3	0.887 +/- 0.27	1.43 +/- 0.41	2.32
	11/12/2014	2.2	NA	NA	6.8	16	2	0.911 +/- 0.25	1.31 +/- 0.45	2.22

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-3D	4/15/1987	105	0.041	NA	376	686	52.2	NA	NA	NA
	10/1/1990	75	<0.01	<0.005	150	680	47	NA	NA	NA
	2/5/1992	80	< 0.01	0.0059	270	500	42	8.4 +/- 0.40	12	20.4
	9/28/1997	46	< 0.01	NA	110	460	27	0.81 +/- 0.07	NA	0.81
	11/19/1999	14	< 0.01	NA	19	< 5.	12	< 1. +/- 0.54	2.1	3.1
	11/21/2000	18	< 0.01	NA	32	240	15	1. +/- 0.20	6.5 +/- 1.20	7.5
	11/14/2001	13	< 0.01	NA	22	250	12	0.4 +/- 0.10	5.4 +/- 1.10	5.8
	11/26/2002	46	< 0.01	NA	64	380	16	1.3 +/- 0.20	17.8 +/- 2	19.1
	1/22/2004	34	< 0.01 U	< 0.005 U	48	300	13. J	5.04 +/- 0.77	20.6 +/- 2.50	25.6
	11/17/2004	36	< 0.01	NA	48	310	14	0.934 +/- 0.16	12.3 +/- 1.10	13.2
	11/15/2005	23	< 0.01 U	NA	36	300	12	0.994 J +/- 0.28	18. +/- 2.30	19.0
	11/22/2006	27	< 0.01 U	NA	39	330	12	0.939 +/- 0.27	13.2 +/- 0.89	14.1
	11/21/2007	22	< 0.01 U	NA	24	220	7.8	1.06 +/- 0.22	8.12 +/- 0.56	9.18
	11/13/2008	18	< 0.01 U	< 0.005 U	25	180	8.5	1.22 +/- 0.19	10.9 +/- 0.79	12.1
	11/18/2009	15	< 0.01 U	NA	20	160	6.9	0.951 +/- 0.18	9.9 +/- 0.69	10.1
	11/29/2010	16	NA	NA	22	160	7.8	1.74 +/- 0.44	12.9 +/- 1.8	14.6
	11/15/2011	17	NA	NA	20	130	7.8	1.59 +/- 0.26	12.5 +/- 0.90	14.1
	11/13/2012	16	NA	NA	20	140	7.2	1.38 +/- 0.39	12.7 +/- 1.7	14.1
	11/12/2013	15	NA	NA	16	130	6.1	1.14 +/- 0.36	9.67 +/- 1.3	10.8
	11/11/2014	14	NA	NA	16	230	5.9	0.902 +/- 0.26	11.0 +/- 1.5	11.9

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
NWD-4D	2/7/1992	< 0.2	< 0.01	< 0.005	13	14	7.6	4.5 +/- 0.30	5. +/- 0.70	9.5
	9/26/1997	< 0.2	< 0.01	NA	4	11	1.8	0.9 +/- 0.08	1.5 +/- 0.46	2.4
	11/18/1999	< 0.2	< 0.01	NA	6.2	< 5.	0.27	< 1. +/- 0.52	< 1.5 +/- 0.32	2.5
	11/21/2000	< 0.2	< 0.01	NA	4.9	< 5.	0.35	0.8 +/- 0.40	1.9 +/- 3	2.7
	11/13/2001	< 0.2	< 0.01	NA	8.3	< 5.	0.53	0.9 +/- 0.20	0.5 +/- 0.70	1.4
	11/22/2002	< 0.2	< 0.01	NA	13	29	9.7	3.7 +/- 0.40	6.5 +/- 0.80	10.2
	1/21/2004	< 0.2 U	< 0.01 U	< 0.005 U	12	30	11	4.35 +/- 0.71	15.7 +/- 2.20	20.1
	11/16/2004	< 0.2	< 0.01	NA	7	32	10	3.78 +/- 0.28	8.62 +/- 0.62	12.4
	11/15/2005	< 0.2 U	< 0.01 U	NA	9.8	41	8.3	2.93 +/- 0.62	9.04 +/- 1.30	12.0
	11/21/2006	< 0.2 U	< 0.01 U	NA	8.2	52	5.8	1.75 +/- 0.28	4.7 +/- 0.52	6.45
	11/19/2007	< 0.2 U	< 0.01 U	NA	7.7	42	7	1.86 +/- 0.28	2.86 +/- 0.47	4.72
	11/19/2008	< 0.2 U	< 0.01 U	< 0.005 U	8.6	39	1.5	1.91 +/- 0.19	3.85 +/- 0.50	5.76
	11/18/2009	< 0.1 U	< 0.01 U	NA	8.6	39	0.96	1.85 +/- 0.24	3.89 +/- 0.51	5.74
	11/23/2010	< 0.1 U	NA	NA	8.1	40	0.21	1.96 +/- 0.49	3.81 +/- 0.69	5.77
	11/15/2011	< 0.1	NA	NA	7.9	35	0.13	1.45 +/- 0.23	3.43 +/- 0.47	4.88
	11/8/2012	<0.1	NA	NA	8	47	<0.010	1.91 +/- 0.44	4.09 +/- 0.07	6.00
	11/8/2013	<0.1	NA	NA	8.2	53	<0.010	2.05 +/- 0.60	5.20 +/- 0.86	7.25
	11/14/2014	<0.1	NA	NA	10	28	<0.050	1.85 +/- 0.57	4.22 +/- 0.69	6.07

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-6D	10/1/1990	<0.2	<0.01	<0.005	13	75	8.6	NA	NA	NA
	2/2/1992	< 0.2	< 0.01	< 0.005	12	51	6.4	NA	NA	NA
	9/25/1997	< 0.2	< 0.01	NA	9.1	18	4.6	2.7 +/- 0.12	2.8 +/- 0.54	5.5
	1/27/2004	< 0.2 U	< 0.01 U	< 0.005 U	11	16	7.7	4.58 +/- 0.69	6.6 +/- 1.30	11.18
	11/19/2007	< 0.2 U	< 0.01 U	NA	12	36	6.6	3.07 +/- 0.34	1.67 +/- 0.39	4.74
	11/12/2008	< 0.2 U	< 0.01 U	< 0.005 U	13	42	5.9	3.79 +/- 0.32	3.45 +/- 0.48	7.24
	11/17/2009	< 0.1 U	< 0.01 U	NA	12	31	4	3.64 +/- 0.35	2.82 +/- 0.53	6.46
	11/22/2010	< 0.1 U	NA	NA	12	32	5	4.59 +/- 0.92	2.94 +/- 0.60	7.53
	11/10/2011	< 0.1 U	NA	NA	10	29	5	5.14 +/- 0.45	3.28 +/- 0.54	8.42
	11/7/2012	< 0.1 U	NA	NA	11	37	5.1	4.10 +/- 0.93	3.04 +/- 0.58	7.14
	11/7/2013	< 0.1 U	NA	NA	12	37	5.0	3.65 +/- 0.83	2.86 +/- 0.60	6.51
	11/14/2014	<0.1	NA	NA	7	43	4.7	3.41 +/- 0.95	2.26 +/- 0.54	5.67

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-8D	4/15/1987	0.21	<0.002	NA	14	40	NA	NA	NA	NA
	10/1/1990	<0.2	<0.01	<0.005	4.9	4	<0.05	NA	NA	NA
	4/10/1992	< 0.2	< 0.01	< 0.005	14	5.7	7.1	NA	NA	NA
	9/25/1997	< 0.2	< 0.01	NA	14	< 5.	6.7	< 0.6 +/- 0.07	< 1. +/- 0.44	1.6
	11/18/1999	< 0.2	< 0.01	NA	17	< 5.	8.1	1.7	1.9	3.6
	11/17/2000	< 0.2	< 0.01	NA	16	< 5.	9.1	0.9 +/- 0.20	2.7 +/- 0.90	3.6
	11/13/2001	< 0.2	< 0.01	NA	16	< 5.	8.9	1. +/- 0.20	2.5 +/- 1	3.5
	11/25/2002	< 0.2	< 0.01	NA	17	< 5.	9.1	1.5 +/- 0.20	2. +/- 0.90	3.5
	1/27/2004	< 0.2 U	< 0.01 U	< 0.005 U	18	< 5. U	9.3	1.28 +/- 0.28	1.94 +/- 0.54	3.22
	11/10/2004	< 0.2	< 0.01	NA	18	< 5.	9.4	1.04 +/- 0.15	1.96 +/- 0.35	3.00
	11/9/2005	< 0.2 U	< 0.01 U	NA	16	< 5. U	8.1	0.837 J +/- 0.23	1.42 +/- 0.35	2.26
	11/16/2006	< 0.2 U	< 0.01 U	NA	15	< 5. U	8.9	0.805 +/- 0.15	1.5 +/- 0.40	2.3
	11/19/2007	< 0.2 U	< 0.01 U	NA	15	< 5. U	7.8	0.74 +/- 0.19	1.23 +/- 0.39	2.0
	11/11/2008	< 0.2 U	< 0.01 U	< 0.005 U	16	< 5. U	7.0	0.776 +/- 0.19	0.96 +/- 0.34	1.7
	11/11/2009	< 0.1 U	< 0.01 U	NA	15	3.3	7.4	0.933 +/- 0.17	1.16 +/- 0.40	2.09
	11/18/2010	< 0.1 U	NA	NA	14	3.5	6.1	0.668 +/- 0.18	1.71 +/- 0.44	2.38
	11/9/2011	< 0.1 U	NA	NA	13	3.7	6.5	0.863 +/- 0.22	1.45 +/- 0.36	2.31
	11/7/2012	< 0.1	NA	NA	12	4.2	6.3	0.918 +/- 0.28	1.65 +/- 0.43	2.57
	11/6/2013	< 0.1	NA	NA	13	4.5	5.3	0.941 +/- 0.37	1.79 +/- 0.45	2.73
	11/13/2014	< 0.1	NA	NA	13	4.8	5.3	0.207 +/- 0.11	1.14 +/- 0.35	1.35

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-9D2	9/27/1997	1	< 0.01	NA	5.3	5.6	0.45	< 0.6 +/- 0.04	< 1. +/- 0.44	1.6
	1/28/2004	37	< 0.01 U	< 0.005 U	56	230	13	3.06 +/- 0.49	12.8 +/- 1.60	15.9
	11/17/2008	33	< 0.01 U	< 0.005 U	47	220	13	1.51 +/- 0.24	7.9 +/- 0.67	9.4
	11/12/2009	36	< 0.01 U	NA	50	250	14	2.03 +/- 0.27	8.87 +/- 0.70	10.9
	11/19/2010	40	NA	NA	47	250	13	2.06 +/- 0.47	7.81 +/- 1.1	9.87
	11/10/2011	42	NA	NA	44	230	13	1.52 +/- 0.26	8.56 +/- 0.67	10.1
	11/12/2012	36	NA	NA	43	260	13	1.34 +/- 0.097	8.28 +/- 1.1	9.90
	11/7/2013	41	NA	NA	39	270	10	1.59 +/- 0.40	9.26 +/- 1.3	10.9
	11/20/2014	29	NA	NA	36	240	11	1.86 +/- 0.54	7.96 +/- 1.1	9.8
Main Producing Zone										
AC-12D	10/1/1990	24	<0.01	<0.005	28	290	13	NA	NA	NA
	4/9/1992	2.6	< 0.01	< 0.005	8.2	39	2.8	NA	NA	NA
	9/27/1997	8.8	0.012	NA	20	320	11	1.5 +/- 0.09	6.9 +/- 0.58	8.4
	11/19/1999	0.52	< 0.01	NA	6.4	7.8	2.4	< 1. +/- 0.09	< 1.5 +/- 0.68	2.5
	11/17/2000	6.7	< 0.01	NA	15	130	6.8	0.5 +/- 0.10	3.7 +/- 1	4.2
	11/8/2001	1.7	< 0.01	NA	7.3	30	3.7	0.4 +/- 0.20	4.5 +/- 1.10	4.9
	11/22/2002	11	0.011	NA	22	310	10	1.9 +/- 0.30	8.6 +/- 1	10.5
	1/28/2004	10	0.015	0.0052	20	280	11	4.13 +/- 0.61	14.2 +/- 1.80	18.3
	11/11/2004	11	< 0.01	NA	20	310	12	1.84 +/- 0.22	7.57 +/- 0.59	9.41
	11/10/2005	15	< 0.01 U	NA	23	290	12	1.65 +/- 0.40	7.59 +/- 1.10	9.24
	11/16/2006	13	< 0.01 U	NA	21	310	12	1.26 +/- 0.18	7.08 +/- 0.65	8.34
	11/16/2007	20	< 0.01 U	NA	22	300	12	1.62 +/- 0.21	7.76 +/- 0.60	9.38
	11/13/2008	17	< 0.01 U	< 0.005 U	23	310	12	1.73 +/- 0.21	6.75 +/- 0.59	8.48
	11/12/2009	15	< 0.01 U	NA	22	280	12	1.57 +/- 0.25	7.7 +/- 0.68	9.3
	11/18/2010	14	NA	NA	22	280	11	1.34 +/- 0.38	6.68 +/- 1.3	8.0
	11/9/2011	14	NA	NA	18	240	10	4.80 +/- 0.69	8.43 +/- 0.75	13.2
	11/8/2012	15	NA	NA	18	250	9.6	1.43 +/- 0.39	7.88 +/- 1.1	9.31
	11/6/2013	14	NA	NA	19	260	9.0	1.27 +/- 0.40	8.50 +/- 1.2	9.77
	11/20/2014	10	NA	NA	16	230	8.6	2.23 +/- 0.55	8.63 +/- 1.2	10.86

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-13D	10/1/1990	8.6	<0.01	<0.005	16	220	8.3	NA	NA	NA
	2/3/1992	5.3	< 0.01	< 0.005	16	150	8.9	4.7 +/- 0.30	3.6 +/- 1.10	8.3
	9/27/1997	4.9	< 0.01	NA	20	260	12	1.3 +/- 0.09	4.1 +/- 0.59	5.4
	11/16/2000	4.6	< 0.01	NA	19	220	11	2.8 +/- 0.30	5	7.8
	11/8/2001	4.7	< 0.01	NA	17	210	10	1.9 +/- 0.20	3.7 +/- 1.10	5.6
	11/21/2002	6.7	< 0.01	NA	20	250	11	1.3 +/- 0.20	5.7 +/- 0.80	7
	1/16/2004	6.3	< 0.01 U	< 0.005 U	22	230	12	1.67 +/- 0.36	11.1 +/- 1.70	12.77
	11/11/2004	7.8	< 0.01	NA	23	260	12	1.55 +/- 0.19	8.2 +/- 0.64	9.75
	11/10/2005	11	< 0.01 U	NA	25	260	12	2.18 +/- 0.53	8.68 +/- 1.20	10.86
	11/16/2006	14	< 0.01 U	NA	28	290	14	1.55 +/- 0.22	7.83 +/- 0.78	9.38
	11/19/2007	17	< 0.01 U	NA	27	300	18	1.64 +/- 0.23	7.41 +/- 0.67	9.05
	11/11/2008	15	< 0.01 U	< 0.005 U	28	360	13	1.32 +/- 0.21	5.95 +/- 0.59	7.27
	11/12/2009	15	0.011	NA	28	300	14	2.28 +/- 0.31	10.5 +/- 0.95	12.78
	11/18/2010	14	NA	NA	23	290	12	1.45 +/- 0.39	6.84 +/- 1.0	8.29
	11/9/2011	14	NA	NA	26	300	13	1.64 +/- 0.25	8.18 +/- 0.69	9.82
	11/7/2012	15	NA	NA	24	290	12	2.05 +/- 0.54	8.99 +/- 1.3	11.0
	11/6/2013	14	NA	NA	24	310	11	1.98 +/- 0.50	9.60 +/- 1.4	11.6
	11/19/2014	12	NA	NA	21	250	11	1.23 +/- 0.39	8.24 +/- 1.3	9.47
Main Producing Zone										
AC-24D	2/19/1992	36	< 0.01	0.005	200	50	1.9	NA	NA	NA
	9/27/1997	8.5	< 0.01	NA	31	8.8	1.3	0.63 +/- 0.06	< 1. +/- 0.42	1.63
	1/21/2004	57	< 0.01 U	< 0.005 U	180	37	3.7	2.32 +/- 0.47	15.3 +/- 2.20	17.6
	11/18/2008	56	< 0.01 U	< 0.005 U	200	65	6.8	2.98 +/- 0.28	7.41 +/- 0.62	10.4
	11/16/2009	59	< 0.01 U	NA	190	79	5.8	2.44 +/- 0.25	6.4 +/- 0.60	8.8
	11/23/2010	77	NA	NA	190	84	6.4	2.09 +/- 0.50	7.60 +/- 1.1	9.7
	11/14/2011	65	NA	NA	160	76	6.8	2.96 +/- 0.35	10.0 +/- 0.86	13.0
	11/9/2012	67	NA	NA	190	78	5.5	1.48 +/- 0.42	10.9 +/- 1.5	12.4
	11/7/2013	68	NA	NA	170	86	4.5	2.02 +/- 0.53	10.2 +/- 1.4	12.2
	11/24/2014	51	NA	NA	130	75	4.2	2.12 +/- 0.64	7.14 +/- 1.0	9.26

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-25D	2/15/1992	19	NA	<0.0050	120	7.1	11	NA	NA	7.9
	9/24/1997	20	< 0.01	NA	270	44	2.1	2. +/- 0.10	3.5 +/- 0.52	5.5
	11/19/1999	2.6	< 0.01	NA	45	< 5.	1.9	< 1. +/- 0.62	< 1.5 +/- 0.75	2.5
	11/17/2000	3.3	< 0.01	NA	46	13	5.5	0.6 +/- 0.10	0.6 +/- 0.80	1.2
	11/13/2001	2.9	< 0.01	NA	32	9.4	2.3	0.4 +/- 0.10	1.1 +/- 0.80	1.5
	11/21/2002	48	< 0.01	NA	410	80	2	2.9 +/- 0.30	5.1 +/- 0.80	8.0
	1/22/2004	52	< 0.01 U	< 0.005 U	410	65	2.3 J	4.48 +/- 0.72	7.6 +/- 1.20	12
	11/15/2004	57	< 0.01	NA	440	83	2.2	2.46 +/- 0.23	5.6 +/- 0.54	8.1
	11/10/2005	59	< 0.01 U	NA	390	81	3.1	2.31 +/- 0.52	7.73 +/- 1.20	10.0
	11/20/2006	77	< 0.01 U	NA	430	80	3.1	2.5 +/- 0.35	4.53 +/- 0.55	7.03
	11/20/2007	90	< 0.01 U	NA	390	80	3.7	1.85 +/- 0.29	4.08 +/- 0.49	5.93
	11/18/2008	71	< 0.01 U	< 0.005 U	480	77	3.7	2.2 +/- 0.25	3.98 +/- 0.51	6.18
	11/17/2009	77	< 0.01 U	NA	420	88	3.5	1.84 +/- 0.24	5.33 +/- 0.55	7.17
	11/23/2010	110	NA	NA	440	89	4.3	2.29 +/- 0.62	4.47 +/- 0.73	6.76
	11/15/2011	100	NA	NA	390	78	4.7	2.31 +/- 0.29	5.0 +/- 0.56	7.3
	11/14/2012	100	NA	NA	370	94	4.2	2.38 +/- 0.55	5.50 +/- 0.85	7.88
	11/12/2013	96	NA	NA	370	80	4.4	2.64 +/- 0.75	5.06 +/- 0.83	7.70
	11/20/2014	76	NA	NA	320	91	3.7	1.7 +/- 0.52	5.27 +/- 0.88	6.97
Main Producing Zone										
AC-28D	10/14/1993	3.1	NA	NA	NA	13	NA	NA	NA	NA
	9/27/1997	0.42	< 0.01	NA	14	< 5.	6.1	1. +/- 0.08	5.9 +/- 0.59	6.9
	1/21/2004	5.9	< 0.01 U	< 0.005 U	26	24	6	1.93 +/- 0.43	6.5 +/- 1.30	8.4
	11/17/2008	7.6	< 0.01 U	< 0.005 U	31	49	6.8	2.07 +/- 0.24	6.43 +/- 0.59	8.5
	11/12/2009	8.1	< 0.01 U	NA	31	55	6.7	2.29 +/- 0.26	6.97 +/- 0.64	9.26
	11/19/2010	9.5	NA	NA	30	67	6.7	2.70 +/- 0.56	8.60 +/- 0.56	11.3
	11/10/2011	9.3	NA	NA	23	56	6.8	3.27 +/- 0.35	10.4 +/- 0.81	13.7
	11/12/2012	9.5	NA	NA	30	74	6.4	3.48 +/- 0.99	10.3 +/- 1.4	13.8
	11/6/2013	9.6	NA	NA	28	69	5.5	3.57 +/- 1.0	11.2 +/- 1.6	14.8
	11/20/2014	NA	NA	NA	NA	NA	NA	NA	NA	NA

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-29D	9/27/1997	65	< 0.01	NA	180	340	20	0.66 +/- 0.05	9.9 +/- 0.65	10.56
	11/19/1999	65	< 0.01	NA	110	< 5.	14	2.3	8.1	10.4
	11/21/2000	45	< 0.01	NA	300	260	14	1.3 +/- 0.10	11.4 +/- 1.10	12.7
	11/13/2001	48	< 0.01	NA	100	280	13	1.4 +/- 0.20	14. +/- 1.60	15
	11/25/2002	59	< 0.01	NA	100	340	16	1.7 +/- 0.20	16.5 +/- 1.70	18
	1/23/2004	52	< 0.01 U	< 0.005 U	93	310	16	3.42 +/- 0.55	21.9 +/- 2.50	25.3
	11/12/2004	45	< 0.01 U	NA	84	290	14	1.52 +/- 0.19	17.7 +/- 0.96	19.2
	11/16/2005	30	< 0.01 U	NA	58	220	9.8	1.53 +/- 0.37	21. +/- 2.70	22.5
	11/17/2006	34	< 0.01 U	NA	67	200	12	1.48 +/- 0.18	11.9 +/- 0.90	13.4
	11/20/2007	42	< 0.01 U	NA	63	220	12	1.45 +/- 0.26	11.7 +/- 0.77	13.2
	11/18/2008	31	< 0.01 U	< 0.005 U	65	200	11	1.54 +/- 0.20	10.8 +/- 0.76	12.3
	11/17/2009	30	< 0.01 U	NA	61	220	9.5	1.54 +/- 0.21	13.8 +/- 0.83	15.3
	11/19/2010	39	NA	NA	62	240	11	1.64 +/- 0.37	14.9 +/- 1.9	16.5
	11/11/2011	41	NA	NA	54	220	12	1.76 +/- 0.27	13.6 +/- 0.81	15.4
	11/13/2012	35	NA	NA	52	230	10	1.08 +/- 0.30	15.9 +/- 2/1	17.0
	11/7/2013	36	NA	NA	45	220	8.1	0.836 +/- 0.27	14.8 +/- 2.0	15.6
	11/17/2014	30	NA	NA	39	74	8.3	1.53 +/- 0.47	15.2 +/- 2.0	16.7

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-30D	9/26/1997	15	< 0.01	NA	60	100	11	3. +/- 0.12	7.9 +/- 0.61	10.9
	11/22/1999	18	< 0.01	NA	70	130	12	2.5	9.5	12
	11/17/2000	11	< 0.01	NA	50	100	11	2.6 +/- 0.30	14.6 +/- 1.70	17.2
	11/13/2001	11	< 0.01	NA	44	92	9.8	3.4 +/- 0.30	9.3 +/- 1.40	12.7
	11/25/2002	61	< 0.01	NA	120	250	16	2.8 +/- 0.30	13.1 +/- 1.50	15.9
	1/15/2004	46	0.017	< 0.005 U	94	190	15	6.96 +/- 0.97	21.4 +/- 2.40	28.4
	11/16/2004	34	< 0.01	NA	56	180	15	1.98 +/- 0.21	12.5 +/- 0.78	14.5
	11/17/2005	16	< 0.01 U	NA	44	120	9.2	1.48 +/- 0.34	11.9 +/- 1.60	13.4
	11/17/2006	11	< 0.01 U	NA	29	91	7.9	1.27 +/- 0.17	8.37 +/- 0.73	9.64
	11/20/2007	12	< 0.01 U	NA	25	64	7.2	1.62 +/- 0.25	6.48 +/- 0.57	8.10
	11/18/2008	8	< 0.01 U	< 0.005 U	25	60	6	1.69 +/- 0.22	6.8 +/- 0.63	8.49
	11/17/2009	6.7	< 0.01 U	NA	20	55	5.1	1.71 +/- 0.25	7.51 +/- 0.66	9.22
	11/22/2010	7.2	NA	NA	19	51	4.7	1.81 +/- 0.41	7.13 +/- 1.1	8.94
	11/14/2011	7	NA	NA	11	27	5.7	2.05 +/- 0.34	9.32 +/- 0.93	11.4
	11/14/2012	8	NA	NA	18	64	5.5	2.00 +/- 0.55	8.21 +/- 1.2	10.2
	11/12/2013	7.1	NA	NA	17	48	5.2	1.80 +/- 0.46	6.88 +/- 1.0	8.68
	11/25/2014	5	NA	NA	13	40	3.8	1.62 +/- 0.47	6.04 +/- 0.92	7.66

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-35D	11/19/1999	23	< 0.01	NA	160	130	3.1	< 1. +/- 0.53	< 1.5 +/- 0.95	2.5
	11/16/2000	150	< 0.01	NA	120	220	12	1.5 +/- 0.20	5. +/- 1.20	6.5
	11/8/2001	160	0.012	NA	520	220	13	1.9 +/- 0.20	7.2 +/- 1.40	9.1
	11/21/2002	170	< 0.01	NA	550	230	11	2. +/- 0.30	8.5 +/- 1	10.5
	1/15/2004	160	0.015	< 0.005 U	530	210	13	4.58 +/- 0.69	12.9 +/- 1.60	17.5
	11/15/2004	170	< 0.01	NA	520	260	14	2.22 +/- 0.21	9.37 +/- 0.69	11.6
	11/16/2005	150	< 0.01 U	NA	430	260	12	2.01 +/- 0.50	14.4 +/- 1.90	16.4
	11/20/2006	160	< 0.01 U	NA	460	270	12	1.83 +/- 0.31	9.26 +/- 0.77	11.1
	11/20/2007	150	< 0.01 U	NA	420	190	12	2.01 +/- 0.29	5.8 +/- 0.53	7.81
	11/19/2008	120	0.01	< 0.005 U	460	190	11	1.78 +/- 0.20	5.29 +/- 0.57	7.07
	11/19/2009	120	< 0.01 U	NA	430	200	9.3	2.33 +/- 0.28	8.44 +/- 0.68	10.8
	11/23/2010	180	NA	NA	580	240	13	2.52 +/- 0.64	8.83 +/- 1.2	11.4
	11/16/2011	130	NA	NA	370	170	11	1.71 +/- 0.28	5.94 +/- 0.61	7.65
	11/15/2012	130	NA	NA	350	200	9.6	1.91 +/- 0.51	6.45 +/- 0.98	8.36
	11/13/2013	120	NA	NA	360	190	9.5	2.01 +/- 0.54	7.69 +/- 1.1	9.70
	11/24/2014	110	NA	NA	300	190	9.6	2.59 +/- 0.64	7.28 +/- 1.1	9.87

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-36D	11/18/1999	0.79	< 0.01	NA	28	120	3.1	< 1. +/- 0.53	< 1.5 +/- 0.55	2.5
	11/16/2000	< 0.2	< 0.01	NA	10	14	4.6	0.6 +/- 0.09	4.4 +/- 0.70	5
	11/8/2001	< 0.2	< 0.01	NA	10	15	5.1	0.6 +/- 0.20	4.5 +/- 1.10	5.1
	11/15/2002	<0.20	<0.010	NA	11	17	5.9	1.0 +/- 0.1	1.9 +/- 0.6	2.9
	11/14/2004	< 0.2 U	< 0.01 U	< 0.005 U	11	12	5.9	1.46 +/- 0.30	2.76 +/- 0.58	4.22
	11/11/2004	< 0.2	< 0.01	NA	14	15	5.2	1.02 +/- 0.17	2.63 +/- 0.38	3.65
	11/9/2005	< 0.2 U	< 0.01 U	NA	11	19	5.9	1.07 +/- 0.27	2.34 +/- 0.52	3.41
	11/16/2006	< 0.2 U	< 0.01 U	NA	11	18	5.9	1.21 +/- 0.20	2.66 +/- 0.49	3.87
	11/16/2007	< 0.2 U	< 0.01 U	NA	11	15	5.7	1.08 +/- 0.21	1.99 +/- 0.35	3.07
	11/11/2008	< 0.2 U	< 0.01 U	< 0.005 U	12	19	5.2	1.19 +/- 0.22	2.63 +/- 0.41	3.82
	11/11/2009	< 0.1 U	< 0.01 U	NA	12	16	5.6	1.05 +/- 0.18	2.24 +/- 0.46	3.29
	11/18/2010	< 0.1 U	NA	NA	12	16	5.3	1.52 +/- 0.45	3.09 +/- 0.59	4.61
	11/9/2011	< 0.1 U	NA	NA	12	17	5.7	1.45 +/- 0.26	2.88 +/- 0.43	4.33
	11/6/2012	<0.10	NA	NA	11	16	5.2	1.28 +/- 0.37	3.30 +/- 0.65	4.58
	11/6/2013	<0.10	NA	NA	12	20	4.9	1.73 +/- 0.53	3.06 +/- 0.59	4.79
	11/18/2014	<0.10	NA	NA	10	21	5	1.48 +/- 0.47	2.33 +/- 0.60	3.81
Main Producing Zone										
PIP-D	11/14/2005	< 0.2 U	< 0.01 U	NA	7.8	< 5. U	3.4	0.835 +/- 0.336	2.23 +/- 0.57	2.83
	11/22/2006	< 0.2 U	< 0.01 U	NA	12	< 5. U	5.3	1.19 +/- 0.22	1.89 +/- 0.35	3.08
	11/16/2007	< 0.2 U	< 0.01 U	NA	7.6	5.3	3.8	0.85 +/- 0.20	1.64 +/- 0.32	2.5
	11/13/2008	< 0.2 U	< 0.01 U	< 0.005 U	10	8.2	4.1	1.32 +/- 0.21	2.41 +/- 0.45	3.73
	11/18/2009	< 0.1 U	< 0.01 U	NA	8.9	5	3.5	0.994 +/- 0.18	1.24 +/- 0.33	2.23
	11/24/2010	< 0.1 U	NA	NA	9.8	4.9	3.7	1.28 +/- 0.37	1.81 +/- 0.47	3.09
	11/11/2011	< 0.1 U	NA	NA	3.3	2.1	2.9	1.01 +/- 0.20	1.37 +/- 0.39	2.38
	11/13/2012	<0.10	NA	NA	9.1	4.4	3.5	0.957 +/- 0.31	2.07 +/- 0.48	3.03
	11/13/2013	<0.10	NA	NA	9.3	5.4	4.1	1.11 +/- 0.30	1.98 +/- 0.44	3.09
	11/14/2014	<0.10	NA	NA	9	5.6	3.7	1.39 +/- 0.42	1.86 +/- 0.41	3.25

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-10D	10/1/1990	<0.2	<0.01	0.013	9.7	140	5.2	NA	NA	NA
	4/9/1992	< 0.2	< 0.01	< 0.005	10	65	3.6	NA	NA	NA
	9/27/1997	< 0.2	< 0.01	NA	12	97	6.6	0.93 +/- 0.07	2.8 +/- 5.20	3.7
	1/28/2004	< 0.2 U	< 0.01 U	< 0.005 U	14	42	7.7	1.91 +/- 0.36	3.32 +/- 0.81	5.23
	11/12/2008	< 0.2 U	< 0.01 U	< 0.005 U	8	29	6.1	1.13 +/- 0.18	2.2 +/- 0.40	3.32
	11/18/2014	<0.10	NA	NA	11	22	5	1.02 +/- 0.29	2.17 +/- 0.51	3.19
Main Producing Zone										
AC-11D	10/1/1990	<0.2	<0.01	0.0058	10	<5	4.3	NA	NA	NA
	4/9/1992	< 0.2	< 0.01	< 0.005	9.5	< 5.	3.5	NA	NA	NA
	9/24/1997	< 0.2	< 0.01	NA	11	< 5.	3.8	0.66 +/- 0.06	1.2 +/- 0.45	1.9
	1/27/2004	< 0.2 U	< 0.01 U	< 0.005 U	11	< 5. U	4.9	1.28 +/- 0.29	3.04 +/- 0.75	4.32
	11/11/2008	< 0.2 U	< 0.01 U	< 0.005 U	10	< 5. U	3	0.828 +/- 0.19	1.93 +/- 0.41	2.76
	11/18/2014	<0.10	NA	NA	8.9	1.4	2.3	0.851 +/- 0.25	1.63 +/- 0.46	2.48
Main Producing Zone										
AC-14D	10/1/1990	0.028	<0.01	<0.005	9	34	4.2	NA	NA	NA
	4/8/1992	< 0.2	< 0.01	0.0219	9.4	33	3.5	NA	NA	NA
	9/24/1997	< 0.2	< 0.01	NA	10	18	4.2	< 0.6 +/- 0.07	1.2 +/- 0.44	1.8
	1/28/2004	< 0.2 U	< 0.01 U	< 0.005 U	11	39	5.8	2.05 +/- 0.37	4.8 +/- 1	6.9
	11/11/2008	< 0.2 U	< 0.01 U	< 0.005 U	12	32	5.5	1.89 +/- 0.30	1.97 +/- 0.40	3.86
	11/19/2014	<0.10	NA	NA	11	26	5.3	1.41 +/- 0.39	1.82 +/- 0.47	3.23

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-21D	10/1/1990	<0.2	<0.01	0.0053	15	9.8	6	NA	NA	NA
	2/2/1992	< 0.2	< 0.01	< 0.005	13	11	5.5	NA	NA	NA
	9/26/1997	< 0.2	< 0.01	NA	21	11	5.9	2.3 +/- 0.12	3.5 +/- 0.50	5.8
	1/29/2004	< 0.2 U	< 0.01 U	< 0.005 U	19	16	8.1	3.72 +/- 0.57	4.71 +/- 0.79	8.43
	11/12/2008	< 0.2 U	< 0.01 U	< 0.005 U	10	24	4	2.03 +/- 0.23	2.08 +/- 0.38	4.11
	11/17/2014	<0.10	NA	NA	7.5	9.8	3.1	1.69 +/- 0.39	2.30 +/- 0.52	3.99
Main Producing Zone										
AC-22D	10/1/1990	2.2	<0.01	<0.005	15	17	8.6	NA	NA	NA
	9/25/1997	0.81	< 0.01	NA	14	6	7.7	0.65 +/- 0.06	1.1 +/- 0.47	1.8
	1/29/2004	1.2	< 0.01 U	< 0.005 U	8.9	10	5	1.55 +/- 0.33	4.01 +/- 0.68	5.56
	11/11/2008	3.1	< 0.01 U	< 0.005 U	9.4	15	3.9	1.34 +/- 0.23	2.65 +/- 0.42	3.99
	11/18/2014	5	NA	NA	12	13	4.4	1.11 +/- 0.30	2.59 +/- 0.56	3.7
Main Producing Zone										
AC-23D	10/1/1990	<0.2	<0.01	<0.005	24	28	4.5	NA	NA	NA
	2/6/1992	< 0.2	< 0.01	< 0.005	26	17	5.8	NA	NA	NA
	9/26/1997	< 0.2	< 0.01	NA	12	9.5	3.1	1. +/- 0.08	1.7 +/- 0.43	2.7
	1/22/2004	< 0.2 U	< 0.01 U	< 0.005 U	8.9	15	5.2J	3.74 +/- 0.63	4.81 +/- 0.9950	8.55
	11/18/2008	< 0.2 U	< 0.01 U	< 0.005 U	10	20	4.6	2.96 +/- 0.26	3.51 +/- 0.44	6.47
	11/11/2014	<0.10	NA	NA	9.1	20	2.5	2.51 +/- 0.62	3.63 +/- 0.66	6.14

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE
Highlighted Results Meet Performance Standard
(see last page for footnotes)
Agrico Site, Pensacola, Florida

Well ID	Date	Fluoride (mg/L)	Arsenic (mg/L)	Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate-N (mg/L)	Radium 226 (pCi/L)	Radium 228 (pCi/L)	Combined Radium 226 + 228 (pCi/L)
PERFORMANCE STANDARD		4	0.01	0.015	250	250	10	--	--	5
Main Producing Zone										
AC-26D	2/11/1992	< 0.2	< 0.01	< 0.005	6.2	6.9	1.1	NA	NA	NA
	9/24/1997	< 0.2	< 0.01	NA	3.3	10	0.18	< 0.6 +/- 0.04	< 1. +/- 0.43	1.6
	1/20/2004	< 0.2 U	< 0.01 U	< 0.005 U	4.9	< 5. U	1.4	< 0.21 U +/- 0.15	< 0.55 U +/- 0.32	0.21
	11/12/2008	< 0.2 U	< 0.01 U	< 0.005 U	3.8	9.8	0.07	0.161 +/- 0.0760	0.0167 +/- 0.14	0.178
	11/19/2014	<0.10	NA	NA	2.8	7.5	<0.050	0.0322 +/- 0.11	0.122 +/- 0.24	0.154
Main Producing Zone										
AC-27D	4/8/1992	< 0.2	< 0.01	0.0272	6.7	11	0.3	NA	NA	NA
	9/24/1997	< 0.2	< 0.01	NA	4.7	14	<0.05	< 0.6 +/- 0.06	< 1. +/- 0.41	1.6
	1/13/2004	< 0.2 U	< 0.01 U	< 0.005 U	16	5	3	1.09 +/- 0.26	4.83 +/- 0.92	5.92
	11/11/2005	< 0.2 U	< 0.01 U	NA	4.6	9.6	0.12	0.266 J +/- 0.11	6.75 +/- 1	7.02
	11/18/2008	< 0.2 U	< 0.01 U	< 0.005 U	29	< 5. U	2	1.12 +/- 0.18	2.43 +/- 0.40	3.55
	11/13/2014	0.1	NA	NA	4	10	0.095	0.136 +/- 0.096	0.582 +/- 0.36	0.718
Main Producing Zone										
AC-5D	10/1/1990	<0.2	<0.01	<0.005	10	<5	5.4	NA	NA	NA
	1/31/1992	< 0.2	< 0.01	< 0.005	13	6.4	5.1	NA	NA	NA
	9/26/1997	3.6	< 0.01	NA	9.7	< 5.	3.8	< 0.6 +/- 0.04	1.4 +/- 0.44	2.0
	1/20/2004	< 0.2 U	< 0.01 U	< 0.005 U	10	< 5. U	4.5	1.15 +/- 0.28	1.7 +/- 0.46	2.9
	11/13/2008	< 0.2 U	< 0.01 U	< 0.005 U	7.9	< 5. U	3.6	0.922 +/- 0.17	1.3 +/- 0.38	2.2
	11/12/2014	<0.10	NA	NA	7	1.4	2.8	0.660 +/- 0.19	1.44 +/- 0.5	2.1
Main Producing Zone										
NWD-2D	10/1/1990	<0.2	<0.01	<0.005	11	5.8	4.9	NA	NA	NA
	2/3/1992	0.2	< 0.01	< 0.005	9.5	< 5.	4.4	NA	NA	NA
	9/25/1997	< 0.2	< 0.01	NA	8.8	< 5.	3.9	< 0.6 +/- 0.06	2. +/- 0.44	2.6
	1/19/2004	< 0.2 U	< 0.01 U	< 0.005 U	10	7.5	5.6	0.79 J +/- 0.21	2.19 +/- 0.60	3.0
	11/13/2008	< 0.2 U	< 0.01 U	< 0.005 U	11	13	5.2	0.901 +/- 0.17	1.71 +/- 0.44	2.61
	11/11/2014	<0.10	NA	NA	12	7.6	6	0.813 +/- 0.25	0.966 +/- 0.32	1.78

TABLE 8
COMPARISON OF COC RESULTS AT GROUNDWATER MONITORING
LOCATIONS FOR SURFICIAL ZONE AND MAIN PRODUCING ZONE

Agrico Site
Pensacola, Florida

Notes:

Monitoring wells ACB-31S, ACB-32S, AC-33S, AC-34S and AC-7SR sampled semiannually from May 1997 through May 2008 and samples analyzed for fluoride, arsenic, and lead only (OU-1 COCs); Beginning in November 2007, these wells incorporated into OU-2 network and samples analyzed for fluoride, arsenic, lead, chloride, sulfate, nitrate, radium 226 and radium 228.

* Radium samples analyzed by STL St Louis for January 2004 event were determined by STL to be biased high results

** Nitrite determined not be part of Agrico plume constituents; Analysis change to nitrate only as per 1/07 EPA approval

COC = constituent of concern

mg/L = milligrams per Liter

pCi/L = picocuries per Liter

BOLD = exceeds constituent performance standard

Highlight = Below performance standard.

NA = Not Analyzed

NS = Not Sampled

I = The reported value is between the laboratory method detection limit and the practical quantitation limit.

J = Estimated Value

Q = Sample was analyzed outside recommended analytical holdtime criteria.

V = The analyte was detected in both the sample and the associated method blank.

<, U = Analyzed for but not detected above limiting criteria of 0.256

1 = First date for arsenic is 1990 data results

Radium 226 + 228 Analytical Laboratories:

1987 State of Florida Department of Environmental Regulation Laboratory

1992 Savannah Laboratories - Contract Lab Unknown

1997 Savannah Laboratories - Contract Lab Unknown

1999 General Engineering Laboratory - Charleston, SC

2000 KNL, Tampa, FL

2001 KNL, Tampa, FL

2002 KNL, Tampa, FL

1/2004 STL - St. Louis

11/2004 through 2014 - STL/TA Richland

TABLE 9
COMPARISON OF COC RESULTS AT LONG-TERM MONITORING LOCATIONS FOR SURFACE WATER

Agrico Site
Pensacola, Florida

Sample Location ID	Date	Fluoride (mg/L)	Total Arsenic (mg/L)	Total Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate + Nitrite (before 2007) Nitrate (2007 and later) (mg/L)	Combined Radium 226 + 228 (pCi/L)
ACSW-1 Bayou Texar (Brackish Water)	11/1999	1.2	<0.010	NA	14000 ⁽¹⁾	2300 ⁽¹⁾	0.74	1.69
	11/2000	1	<0.010	NA	26000	1700	0.14	2.0
	11/2001	1.1	0.0065	NA	1000	1700	0.26	1.5
	11/2002	1.3	<0.010	NA	8400	1200	0.49	0.9
	1/2004	1.5	<0.010	<0.0050	8900	1300	0.45	<1.0
	11/2004	1.3	<0.010	NA	3900	900	0.43	1.44
	11/2005	1.1	<0.010	NA	8600	1200	0.52	1.18
	11/2006	1.3	<0.010	NA	4900	1100	0.63	1.45
	11/2007	1.1	<0.010	NA	10000	1500	0.74	1.33
	11/2008	0.89	<0.010	<0.0050	14000	2000	0.21	0.748
	11/2009	0.99	<0.010	NA	7500	890	0.46	0.989
	11/2010	0.94	NA	NA	27000	1600	0.27	1.376
	11/2011	0.78	NA	NA	12000	1700	0.23	0.58
	11/2012	1.3	NA	NA	13000	1700	0.31	1.08
	11/2013	0.91	NA	NA	8700	1200	0.47	1.41
	11/21/2014	1.1	NA	NA	18000	1900	0.45	1.40

TABLE 9
COMPARISON OF COC RESULTS AT LONG-TERM MONITORING LOCATIONS FOR SURFACE WATER

Agrico Site
Pensacola, Florida

Sample Location ID	Date	Fluoride (mg/L)	Total Arsenic (mg/L)	Total Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate + Nitrite (before 2007) Nitrate (2007 and later) (mg/L)	Combined Radium 226 + 228 (pCi/L)
ACSW-2 Bayou Texar (Brackish Water)	11/1999	0.82	<0.010	NA	15000	2300	0.15	<1.5
	11/2000	0.63	<0.010	NA	21000	1700	0.39	<1.8
	11/2001	0.74	<0.010	NA	14000	2200	<0.050	2.0
	11/2002	0.59	<0.010	NA	9300	1400	0.15	<1.0
	1/2004	0.66	<0.010	<0.0050	10000	1400	0.19	0.38
	11/2004	0.69	<0.010	NA	5900	1100	0.19	0.572
	11/2005	0.80	<0.010	NA	11000	1700	0.32	1.66
	11/2006	0.73	<0.010	NA	5200	1200	0.38	1.04
	11/2007	0.82	<0.010	NA	12000	1600	0.27	0.95
	11/2008	0.60	<0.010	<0.0050	15000	2200	0.68	0.641
	11/2009	0.59	<0.010	NA	12000	1500	0.13	0.712
	11/2010	0.65	NA	NA	28000	1800	0.082	0.894
	11/2011	0.73	NA	NA	13000	730	0.17	1.277
	11/2012	0.73	NA	NA	14000	1900	0.066	0.691
	11/2013	0.78	NA	NA	13000	1800	0.19	1.21
	11/2014	0.82	NA	NA	17000	1800	0.45	0.945

TABLE 9
COMPARISON OF COC RESULTS AT LONG-TERM MONITORING LOCATIONS FOR SURFACE WATER

Agrico Site
Pensacola, Florida

Sample Location ID	Date	Fluoride (mg/L)	Total Arsenic (mg/L)	Total Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate + Nitrite (before 2007) Nitrate (2007 and later) (mg/L)	Combined Radium 226 + 228 (pCi/L)
BT-02⁽³⁾ Bayou Texar (Brackish Water)	08/2008	0.56	NA	NA	NA	NA	NA	NA
	11/2010	0.83	NA	NA	NA	NA	NA	NA
	11/2011	0.77	NA	NA	NA	NA	NA	NA
	11/2012	0.89	NA	NA	NA	NA	NA	NA
	11/2013	0.94	NA	NA	NA	NA	NA	NA
	11/2014	1.30	NA	NA	NA	NA	NA	NA
BT-107⁽³⁾ Bayou Texar (Brackish Water)	05/2009	0.58	NA	NA	NA	NA	NA	NA
	11/2010	0.89	NA	NA	NA	NA	NA	NA
	11/2011	0.81	NA	NA	NA	NA	NA	NA
	11/2012	1.30	NA	NA	NA	NA	NA	NA
	11/2013	0.99	NA	NA	NA	NA	NA	NA
	11/2014	1.30	NA	NA	NA	NA	NA	NA
BT-127⁽³⁾ Bayou Texar (Brackish Water)	05/2009	0.60	NA	NA	NA	NA	NA	NA
	11/2010	1.00	NA	NA	NA	NA	NA	NA
	11/2011	0.81	NA	NA	NA	NA	NA	NA
	11/2012	1.20	NA	NA	NA	NA	NA	NA
	11/2013	1.20	NA	NA	NA	NA	NA	NA
	11/2014	1.30	NA	NA	NA	NA	NA	NA

TABLE 9
COMPARISON OF COC RESULTS AT LONG-TERM MONITORING LOCATIONS FOR SURFACE WATER

Agrico Site
Pensacola, Florida

Sample Location ID	Date	Fluoride (mg/L)	Total Arsenic (mg/L)	Total Lead (mg/L)	Chloride (mg/L)	Sulfate (mg/L)	Nitrate + Nitrite (before 2007) Nitrate (2007 and later) (mg/L)	Combined Radium 226 + 228 (pCi/L)
ACSW-BL⁽²⁾ Carpenter Creek (Freshwater)	11/1999	<0.20	<0.010	NA	9.4	<5.0	2.1	<1.5
	11/2000	<0.20	<0.010	NA	9.4	8.8	1.4	2.5
	11/2001	<0.20	<0.010	NA	8.0	<5.0	1.8	2.4
	11/2002	<0.20	<0.010	NA	8.8	<5.0	1.2	2.4
	1/2004	<0.20	<0.010	<0.0050	8.5	5.1	1.4	1.53
	11/2004	<0.20	<0.010	NA	8.7	7.1	1.1	1.08
	11/2005	<0.20	<0.010	NA	10	5.1	1.2	2.08
	11/2006	<0.20	<0.010	NA	11	<5.0	1.1	1.55
	11/2007	<0.20	<0.010	NA	9.8	<5.0	1.4	1.67
	11/2008	<0.20	<0.010	<0.0050	9.2	5.9	1.1	1.926
	11/2009	<0.20	<0.010	NA	7.3	5.7	0.73	0.895
	11/2010	Discontinued Sampling						

TABLE 9
COMPARISON OF COC RESULTS AT LONG-TERM MONITORING LOCATIONS FOR SURFACE WATER

Agrico Site
Pensacola, Florida

- (1) Bayou Texar naturally occurring brackish water from Pensacola Bay
(2) Station Discontinued after 2009.
(3) Stations added in 2010; analysis is for fluoride only.

Notes:

COC = constituent of concern

mg/L = milligrams per Liter

pCi/L = picocuries per Liter

NA = Not Analyzed

Radium 226 + 228 Analytical Laboratories:

1992 Savannah Laboratories - Contract Lab Unknown

1997 Savannah Laboratories - Contract Lab Unknown

1999 General Engineering Laboratory - Charleston, SC

2000 KNL, Tampa, FL

2001 KNL, Tampa, FL



2001 KNL, Tampa 11/21/2014

2002 KNL, Tampa, FL

1/2004 STL - St. Louis

11/2004 through 2014- STL/TA Richland

FIGURES

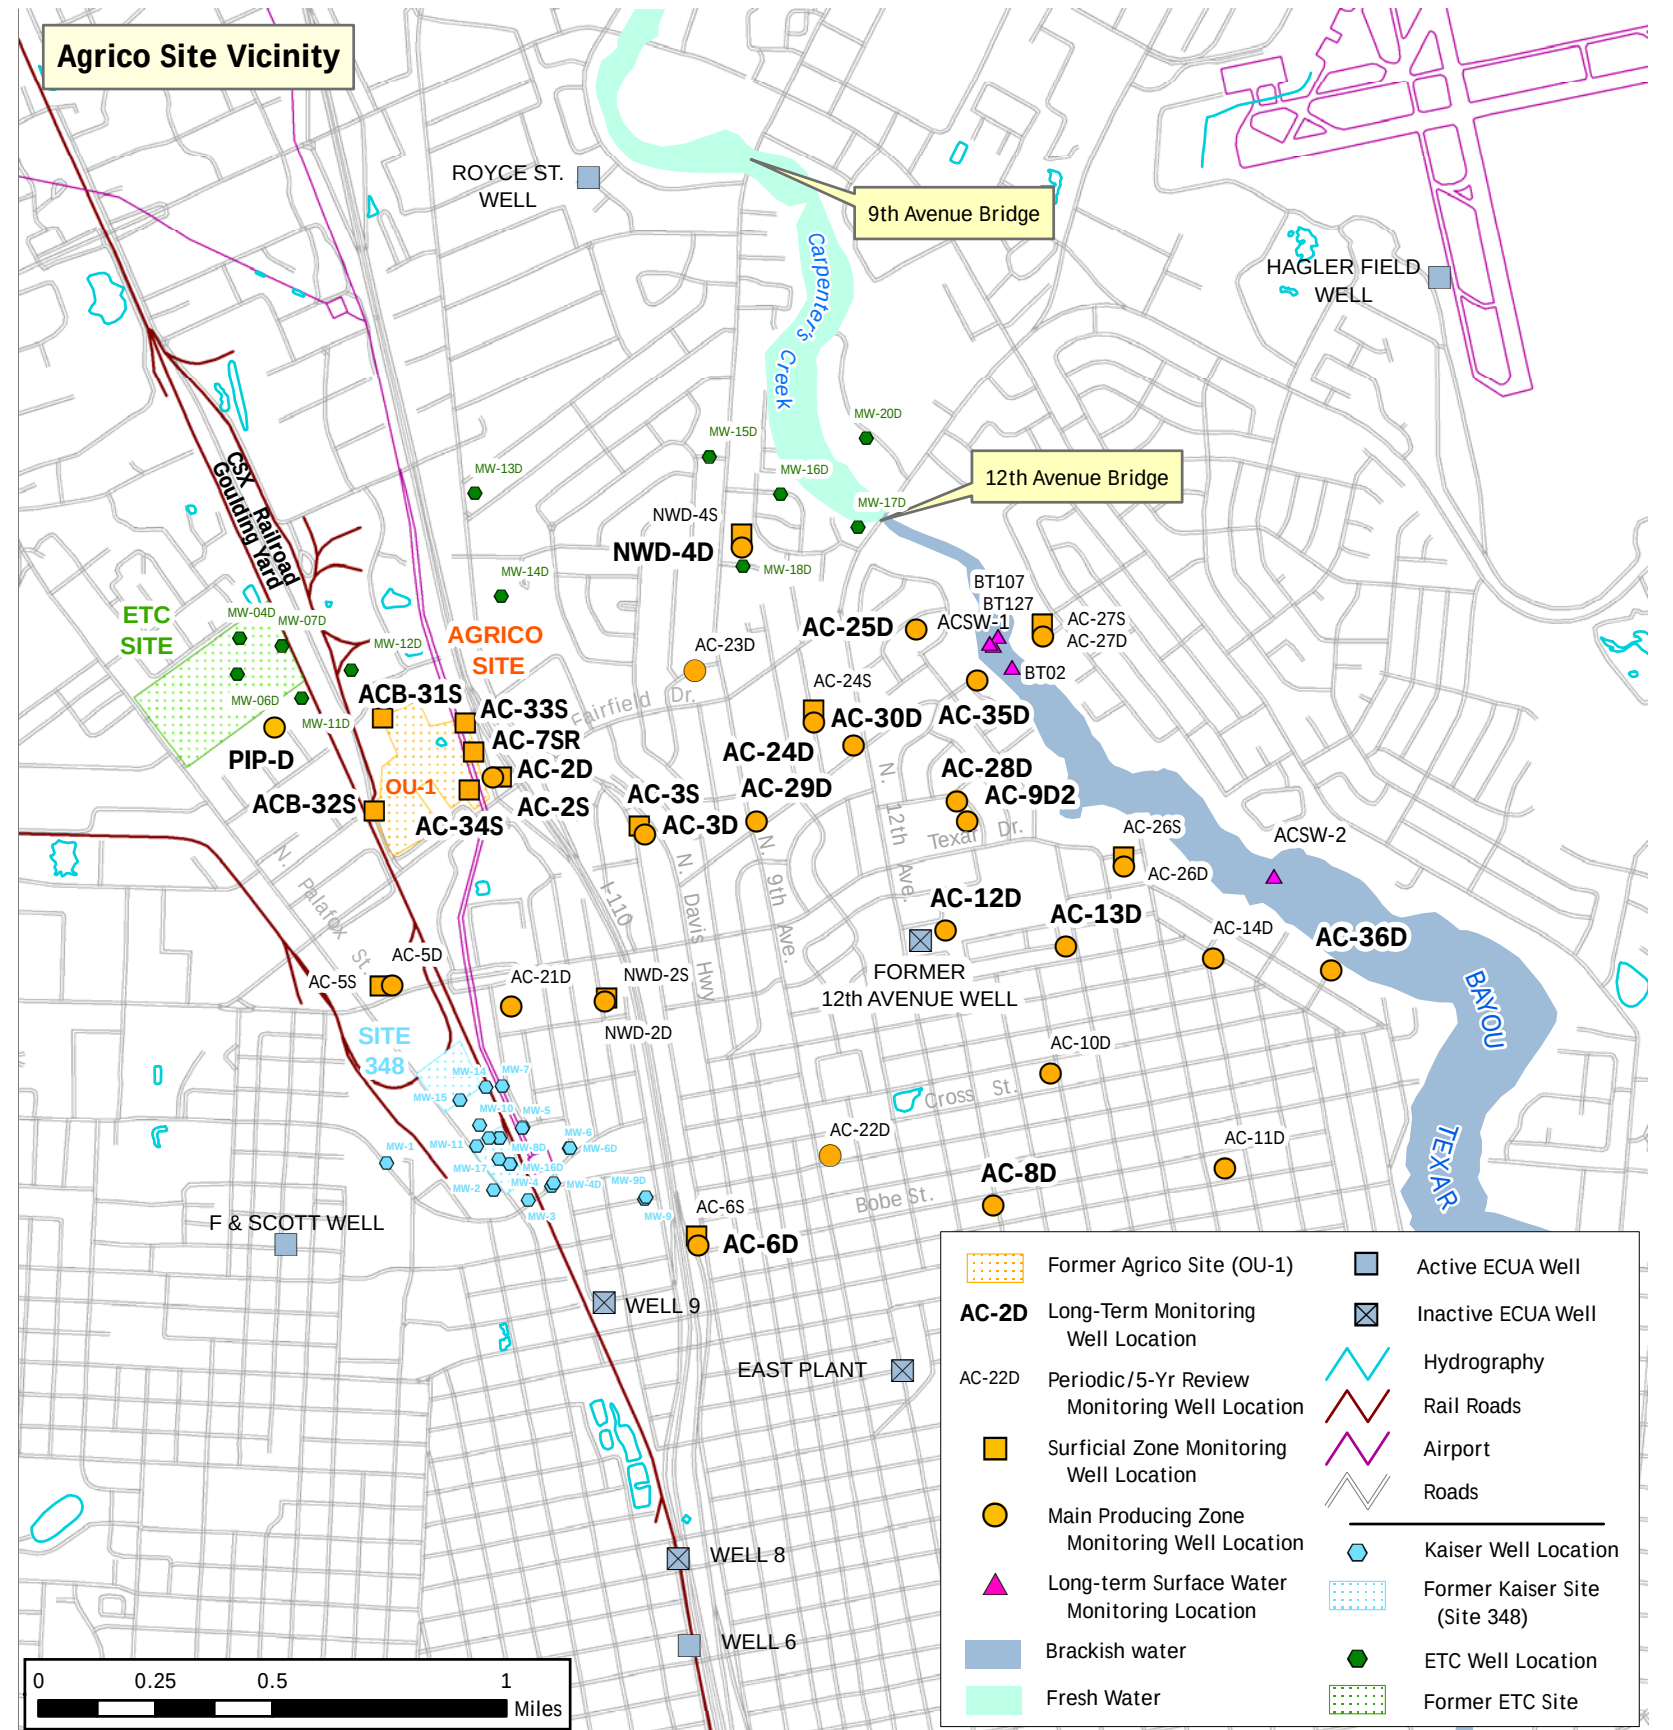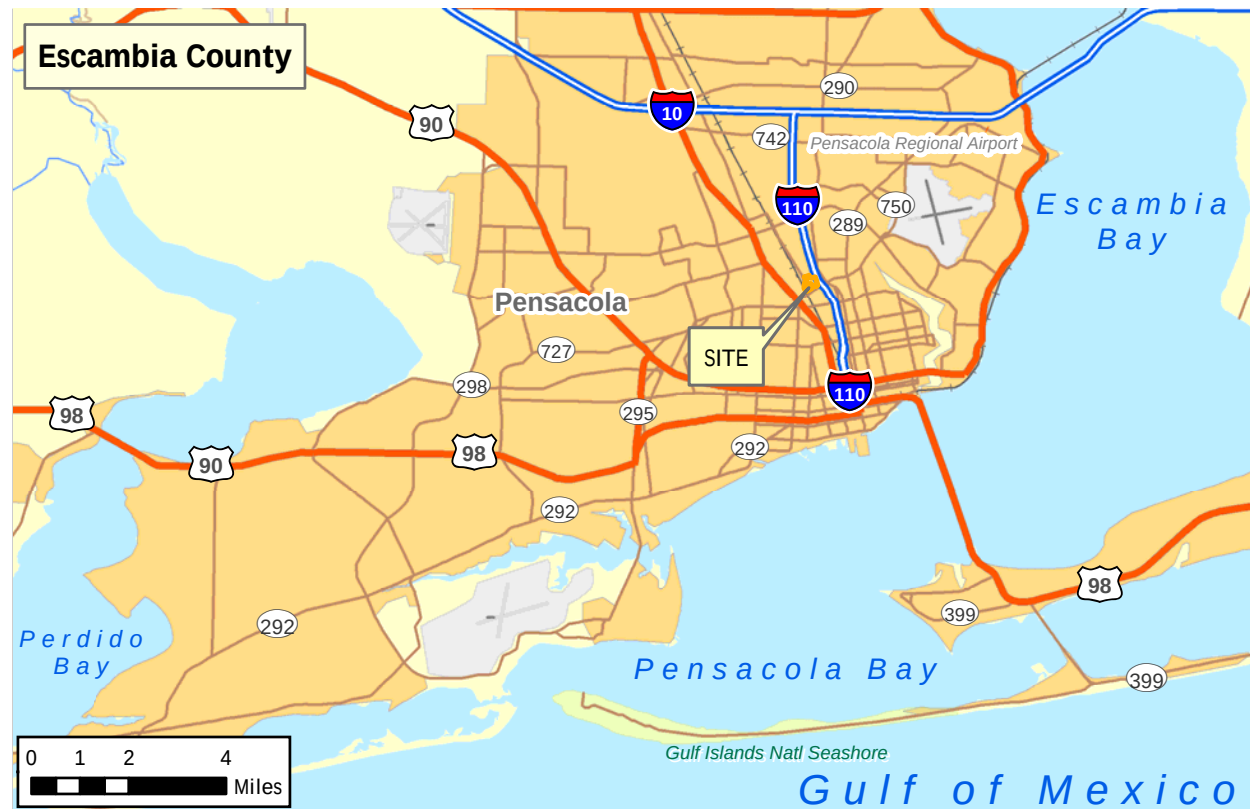

**OU-1 and OU-2
AGRICO SITE
PENSACOLA, FLORIDA**





Base Map Data Provided By:
Florida Department of Environmental Protection
and Northwest Florida Water Management District
Aerial Source: ESRI



SITE LOCATION AND SITE-WIDE MONITORING LOCATIONS OU-1 AND OU-2


FIGURE
1

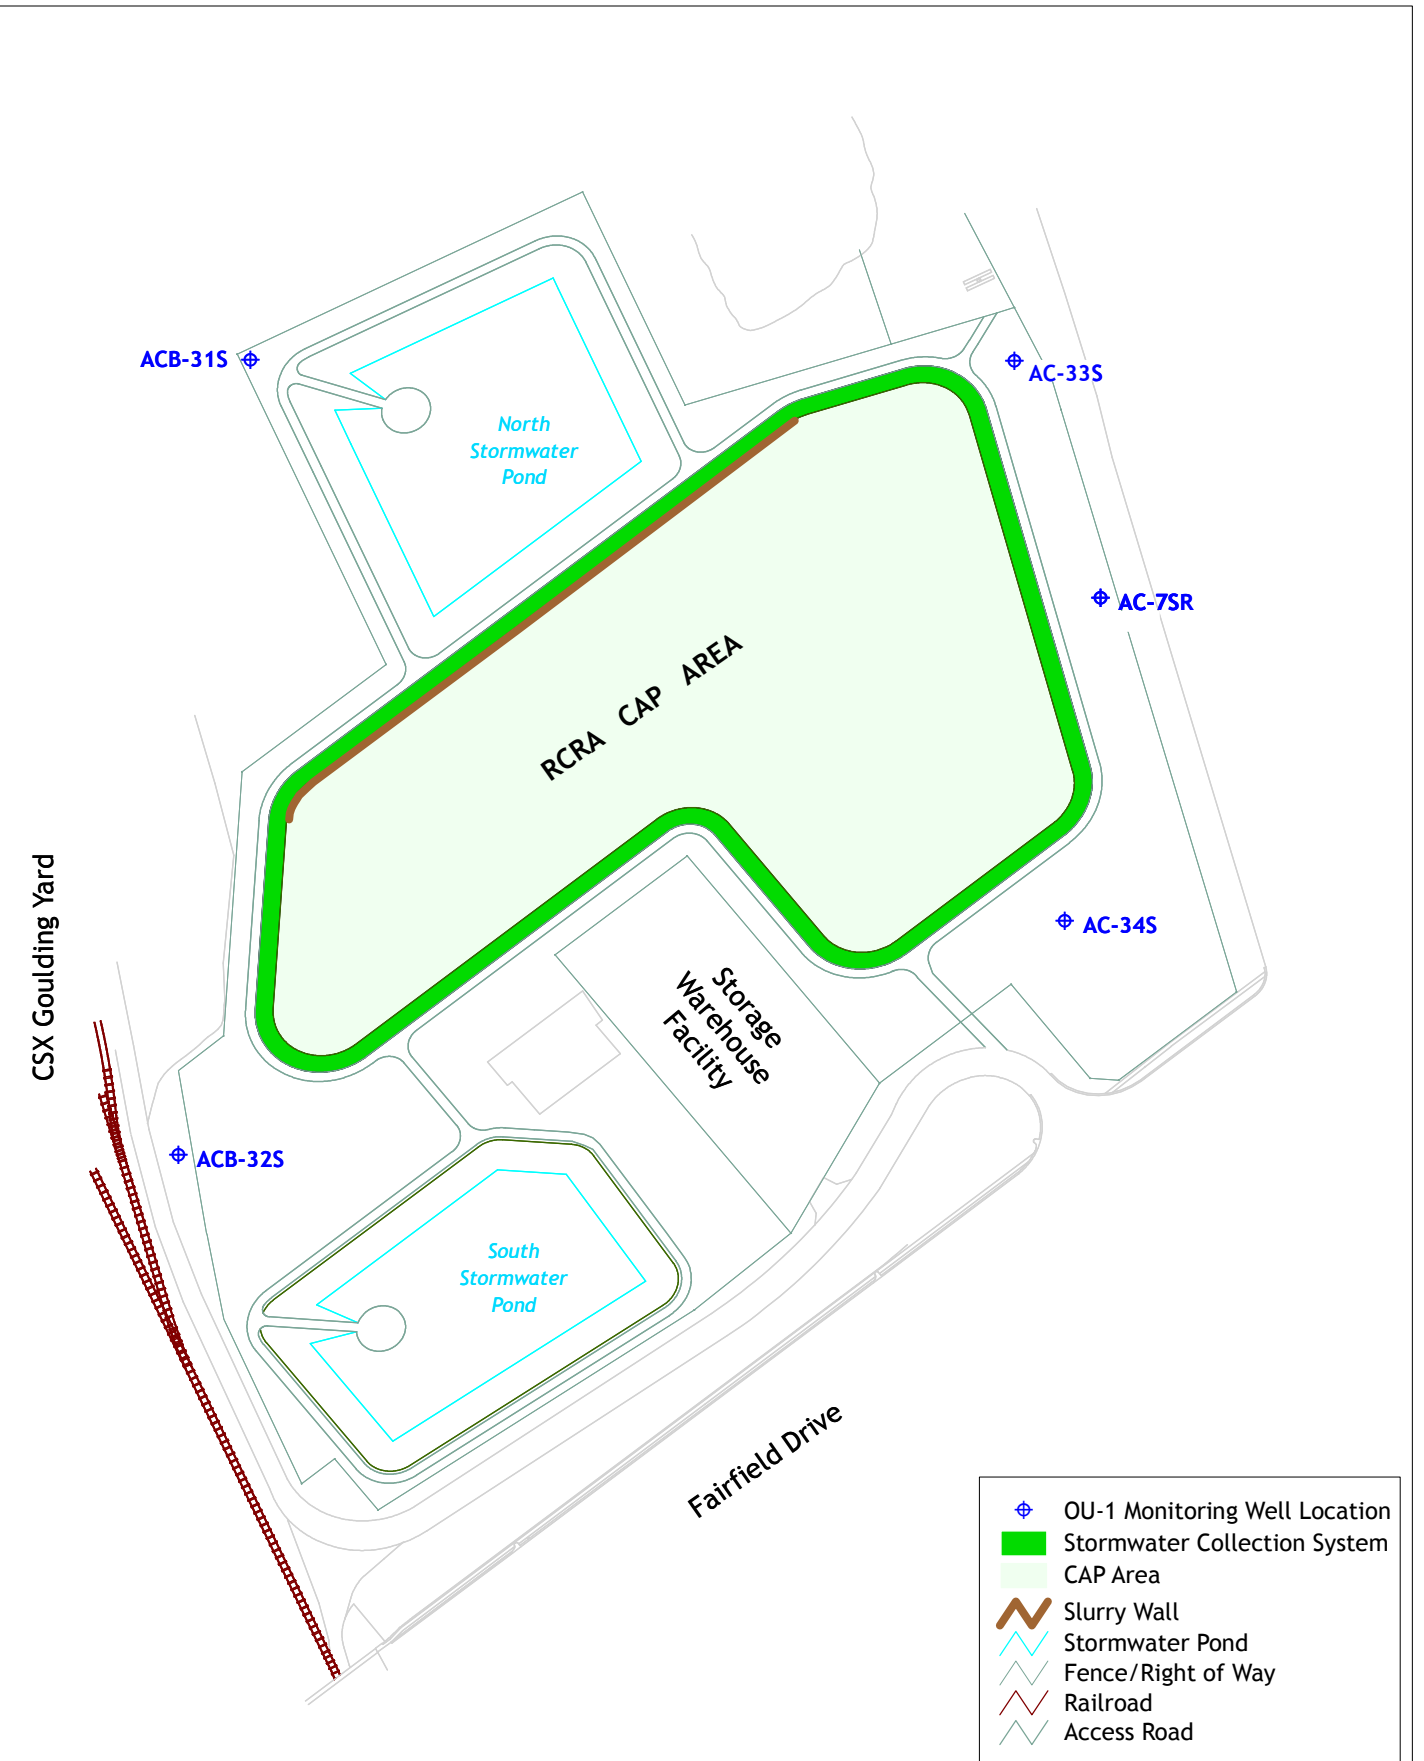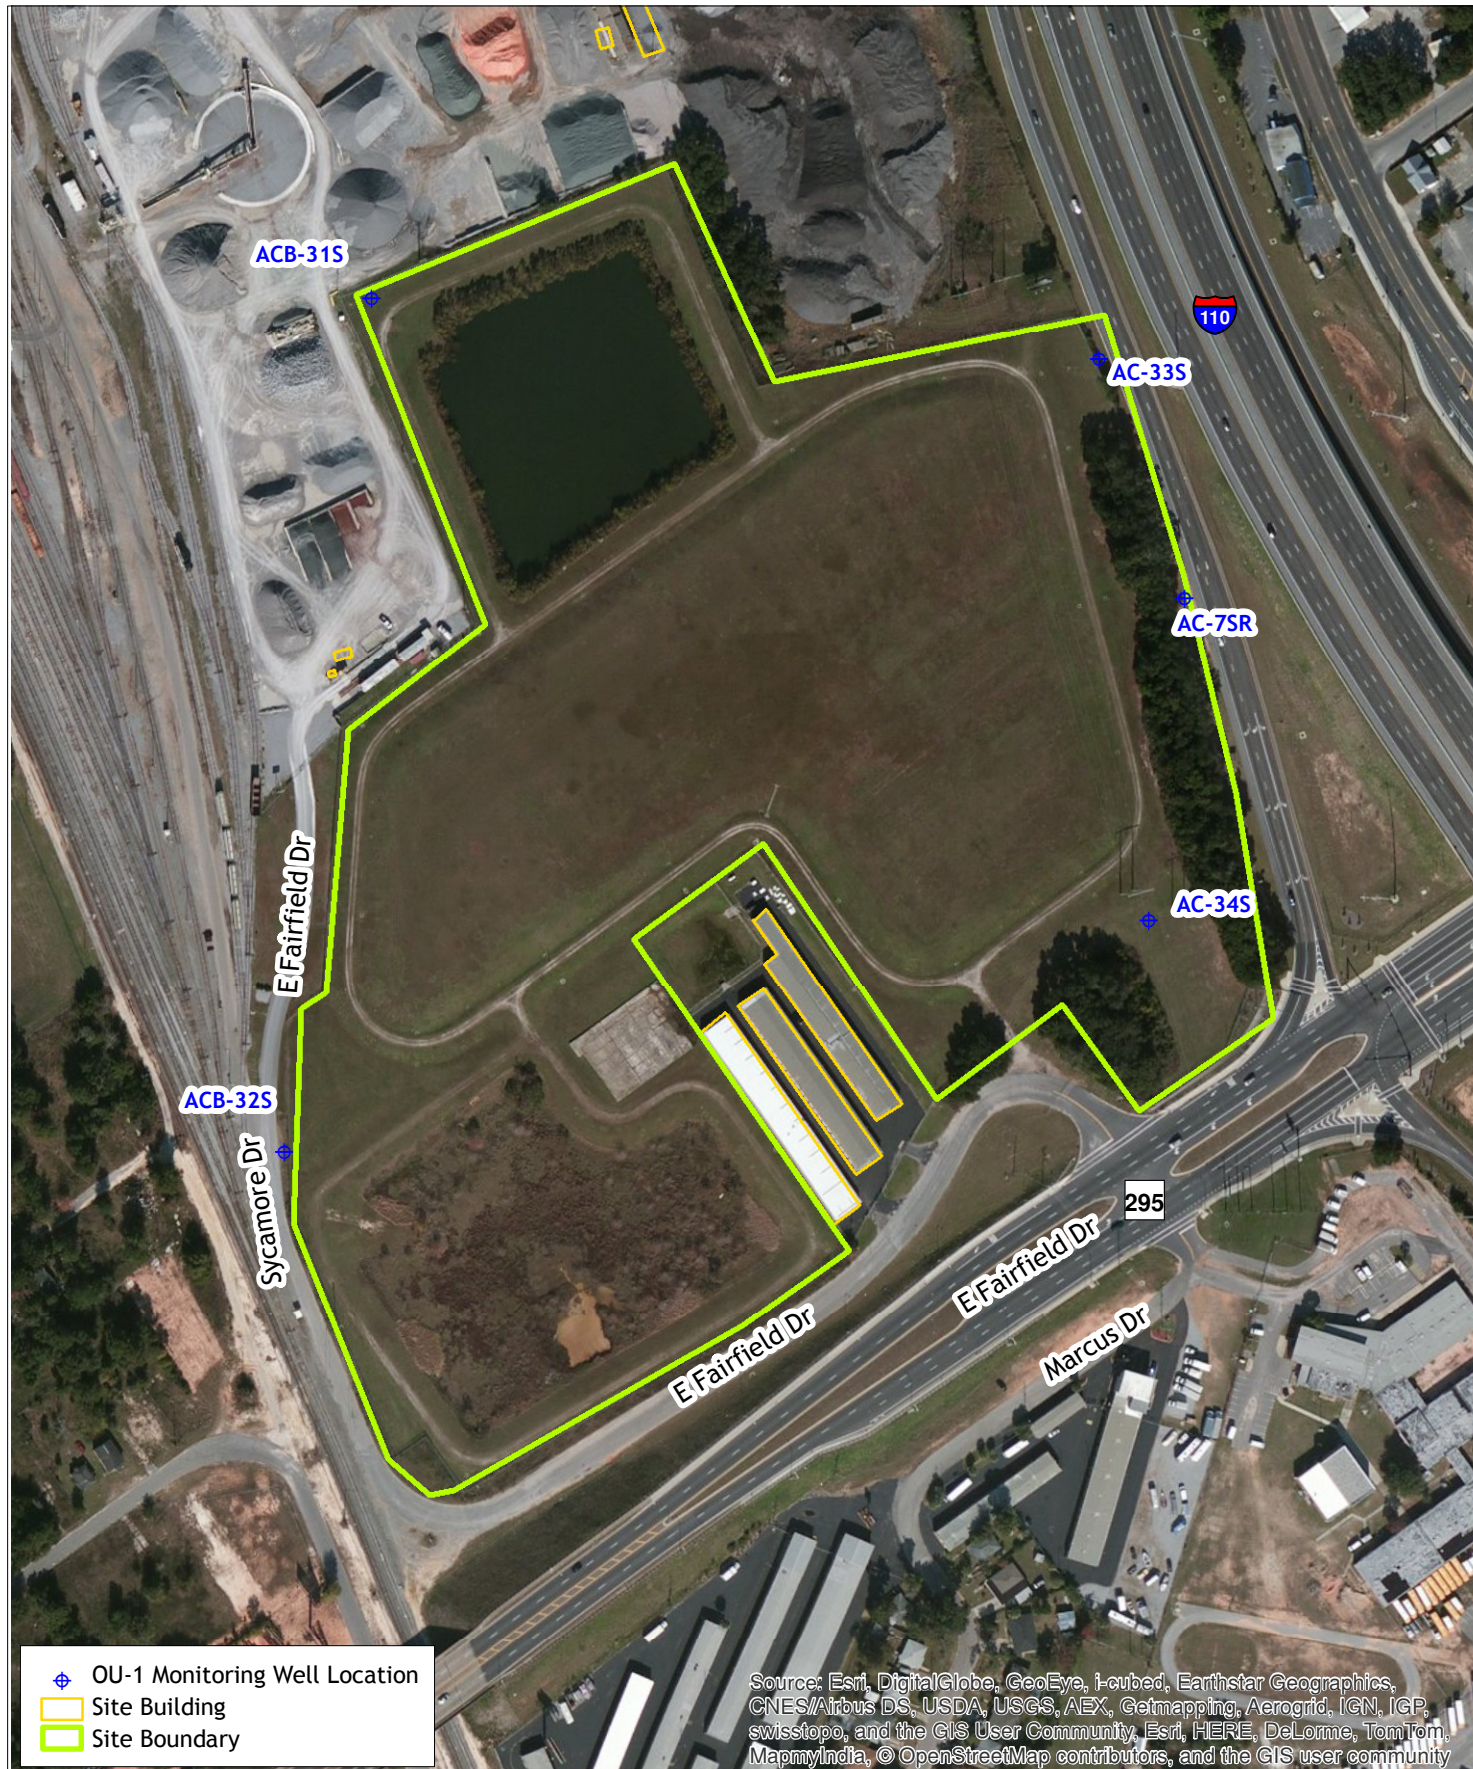

**OU-1 and OU-2
AGRICO SITE
PENSACOLA, FLORIDA**




Base Map Data Provided By:
Florida Department of Environmental Protection
and Northwest Florida Water Management District
Aerial Source: ESRI



**VIEW OF OU-1
(Former Facility Area)
With Current Features**

**FIGURE
2**

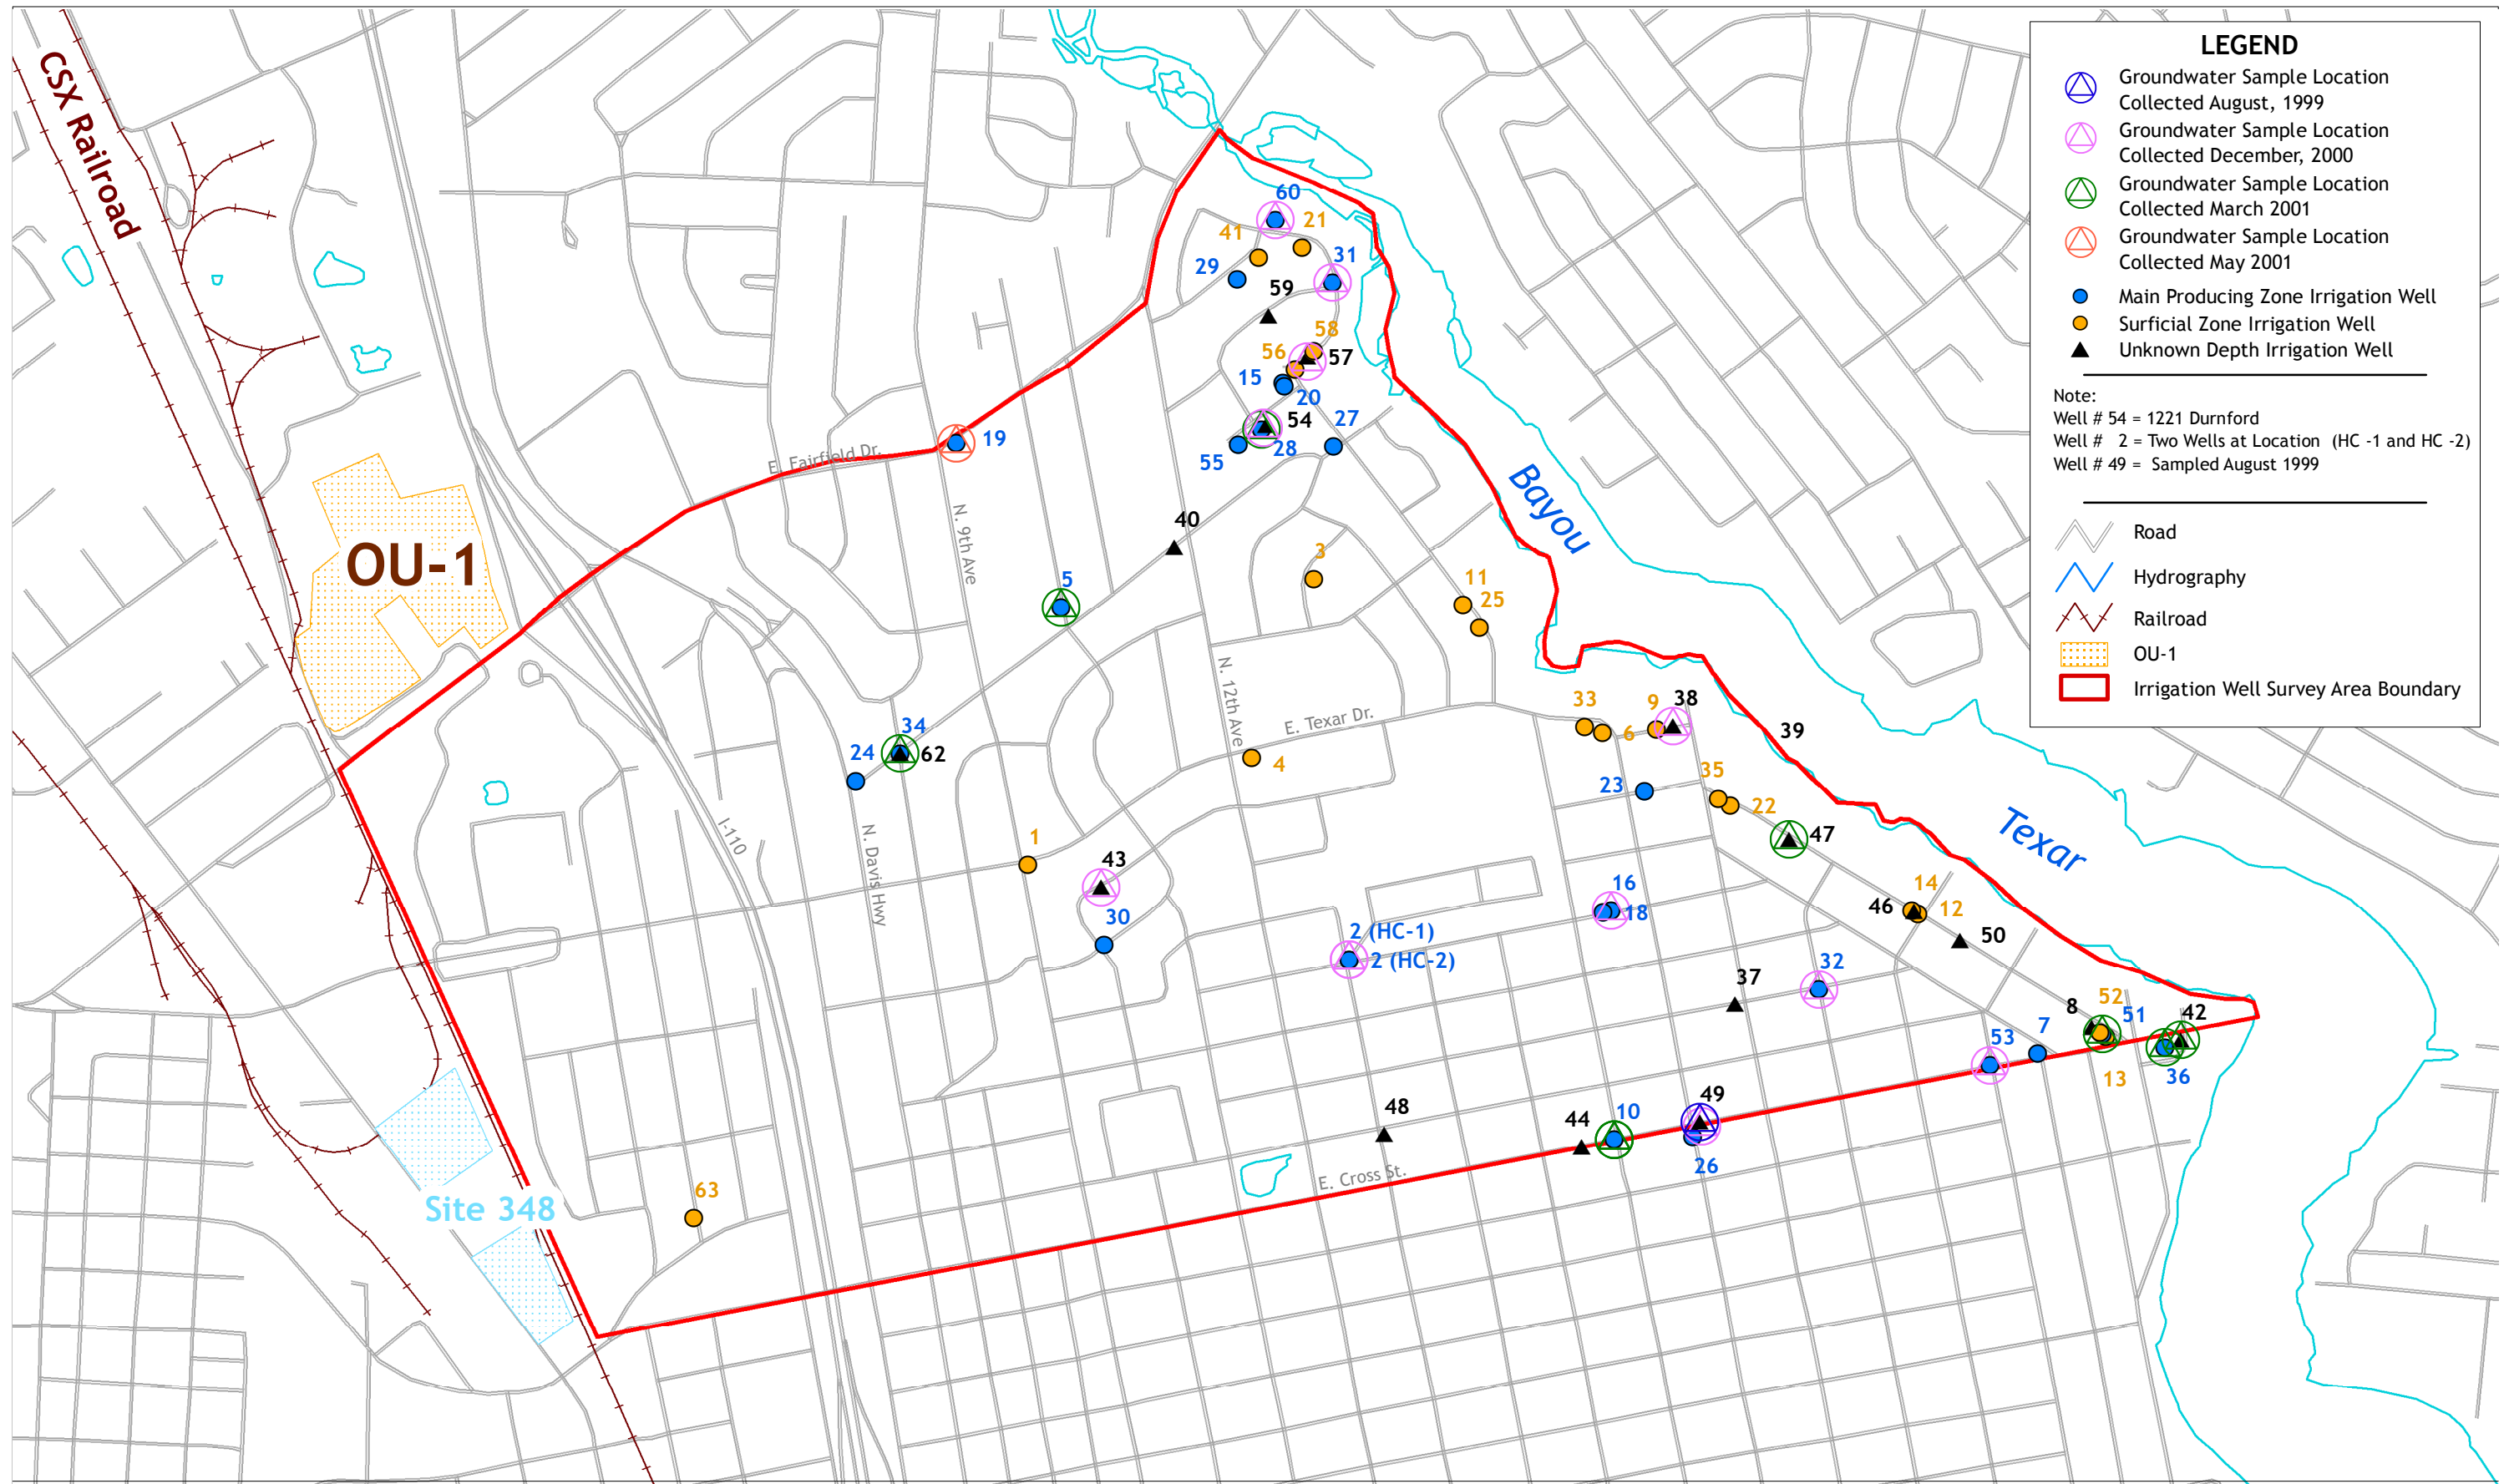

LEGEND

- Groundwater Sample Location Collected August, 1999
- Groundwater Sample Location Collected December, 2000
- Groundwater Sample Location Collected March 2001
- Groundwater Sample Location Collected May 2001
- Main Producing Zone Irrigation Well
- Surficial Zone Irrigation Well
- Unknown Depth Irrigation Well


Note:
 Well # 54 = 1221 Durnford
 Well # 2 = Two Wells at Location (HC -1 and HC -2)
 Well # 49 = Sampled August 1999

- Road
- Hydrography
- Railroad
- OU-1
- Irrigation Well Survey Area Boundary

OU-1 and OU-2
 AGRICO SITE
 PENSACOLA, FLORIDA





Base Map Data Provided By:
 Florida Department of Environmental Protection
 and Northwest Florida Water Management District



IRRIGATION WELL
 LOCATIONS

FIGURE
 3

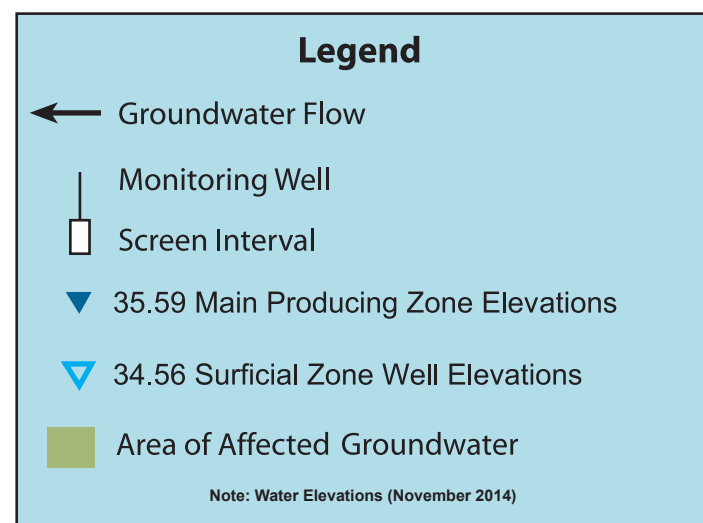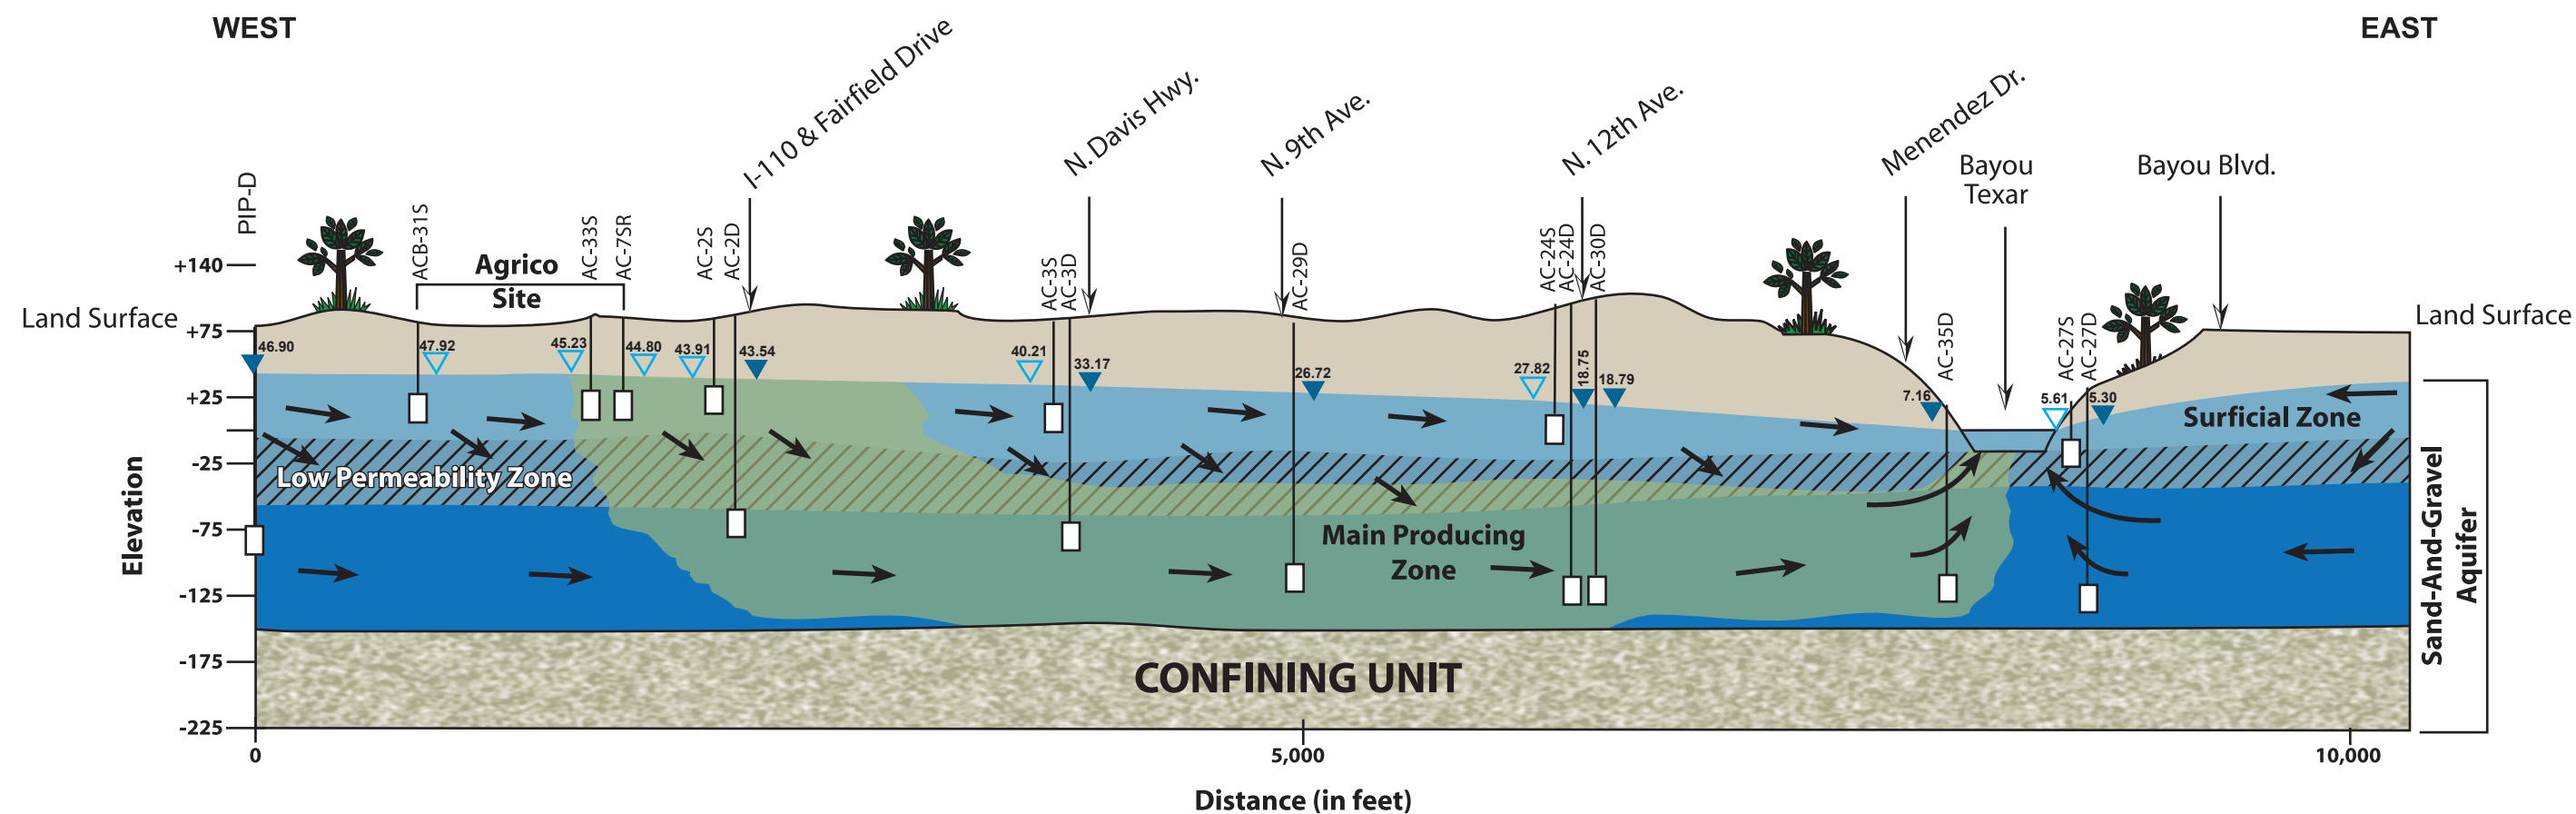


OU-1 and OU-2
AGRICO SITE
PENSACOLA, FLORIDA



HYDROGEOLOGIC CONCEPTUAL MODEL
FROM AGRICO SITE TO BAYOU TEXAR


FIGURE
4

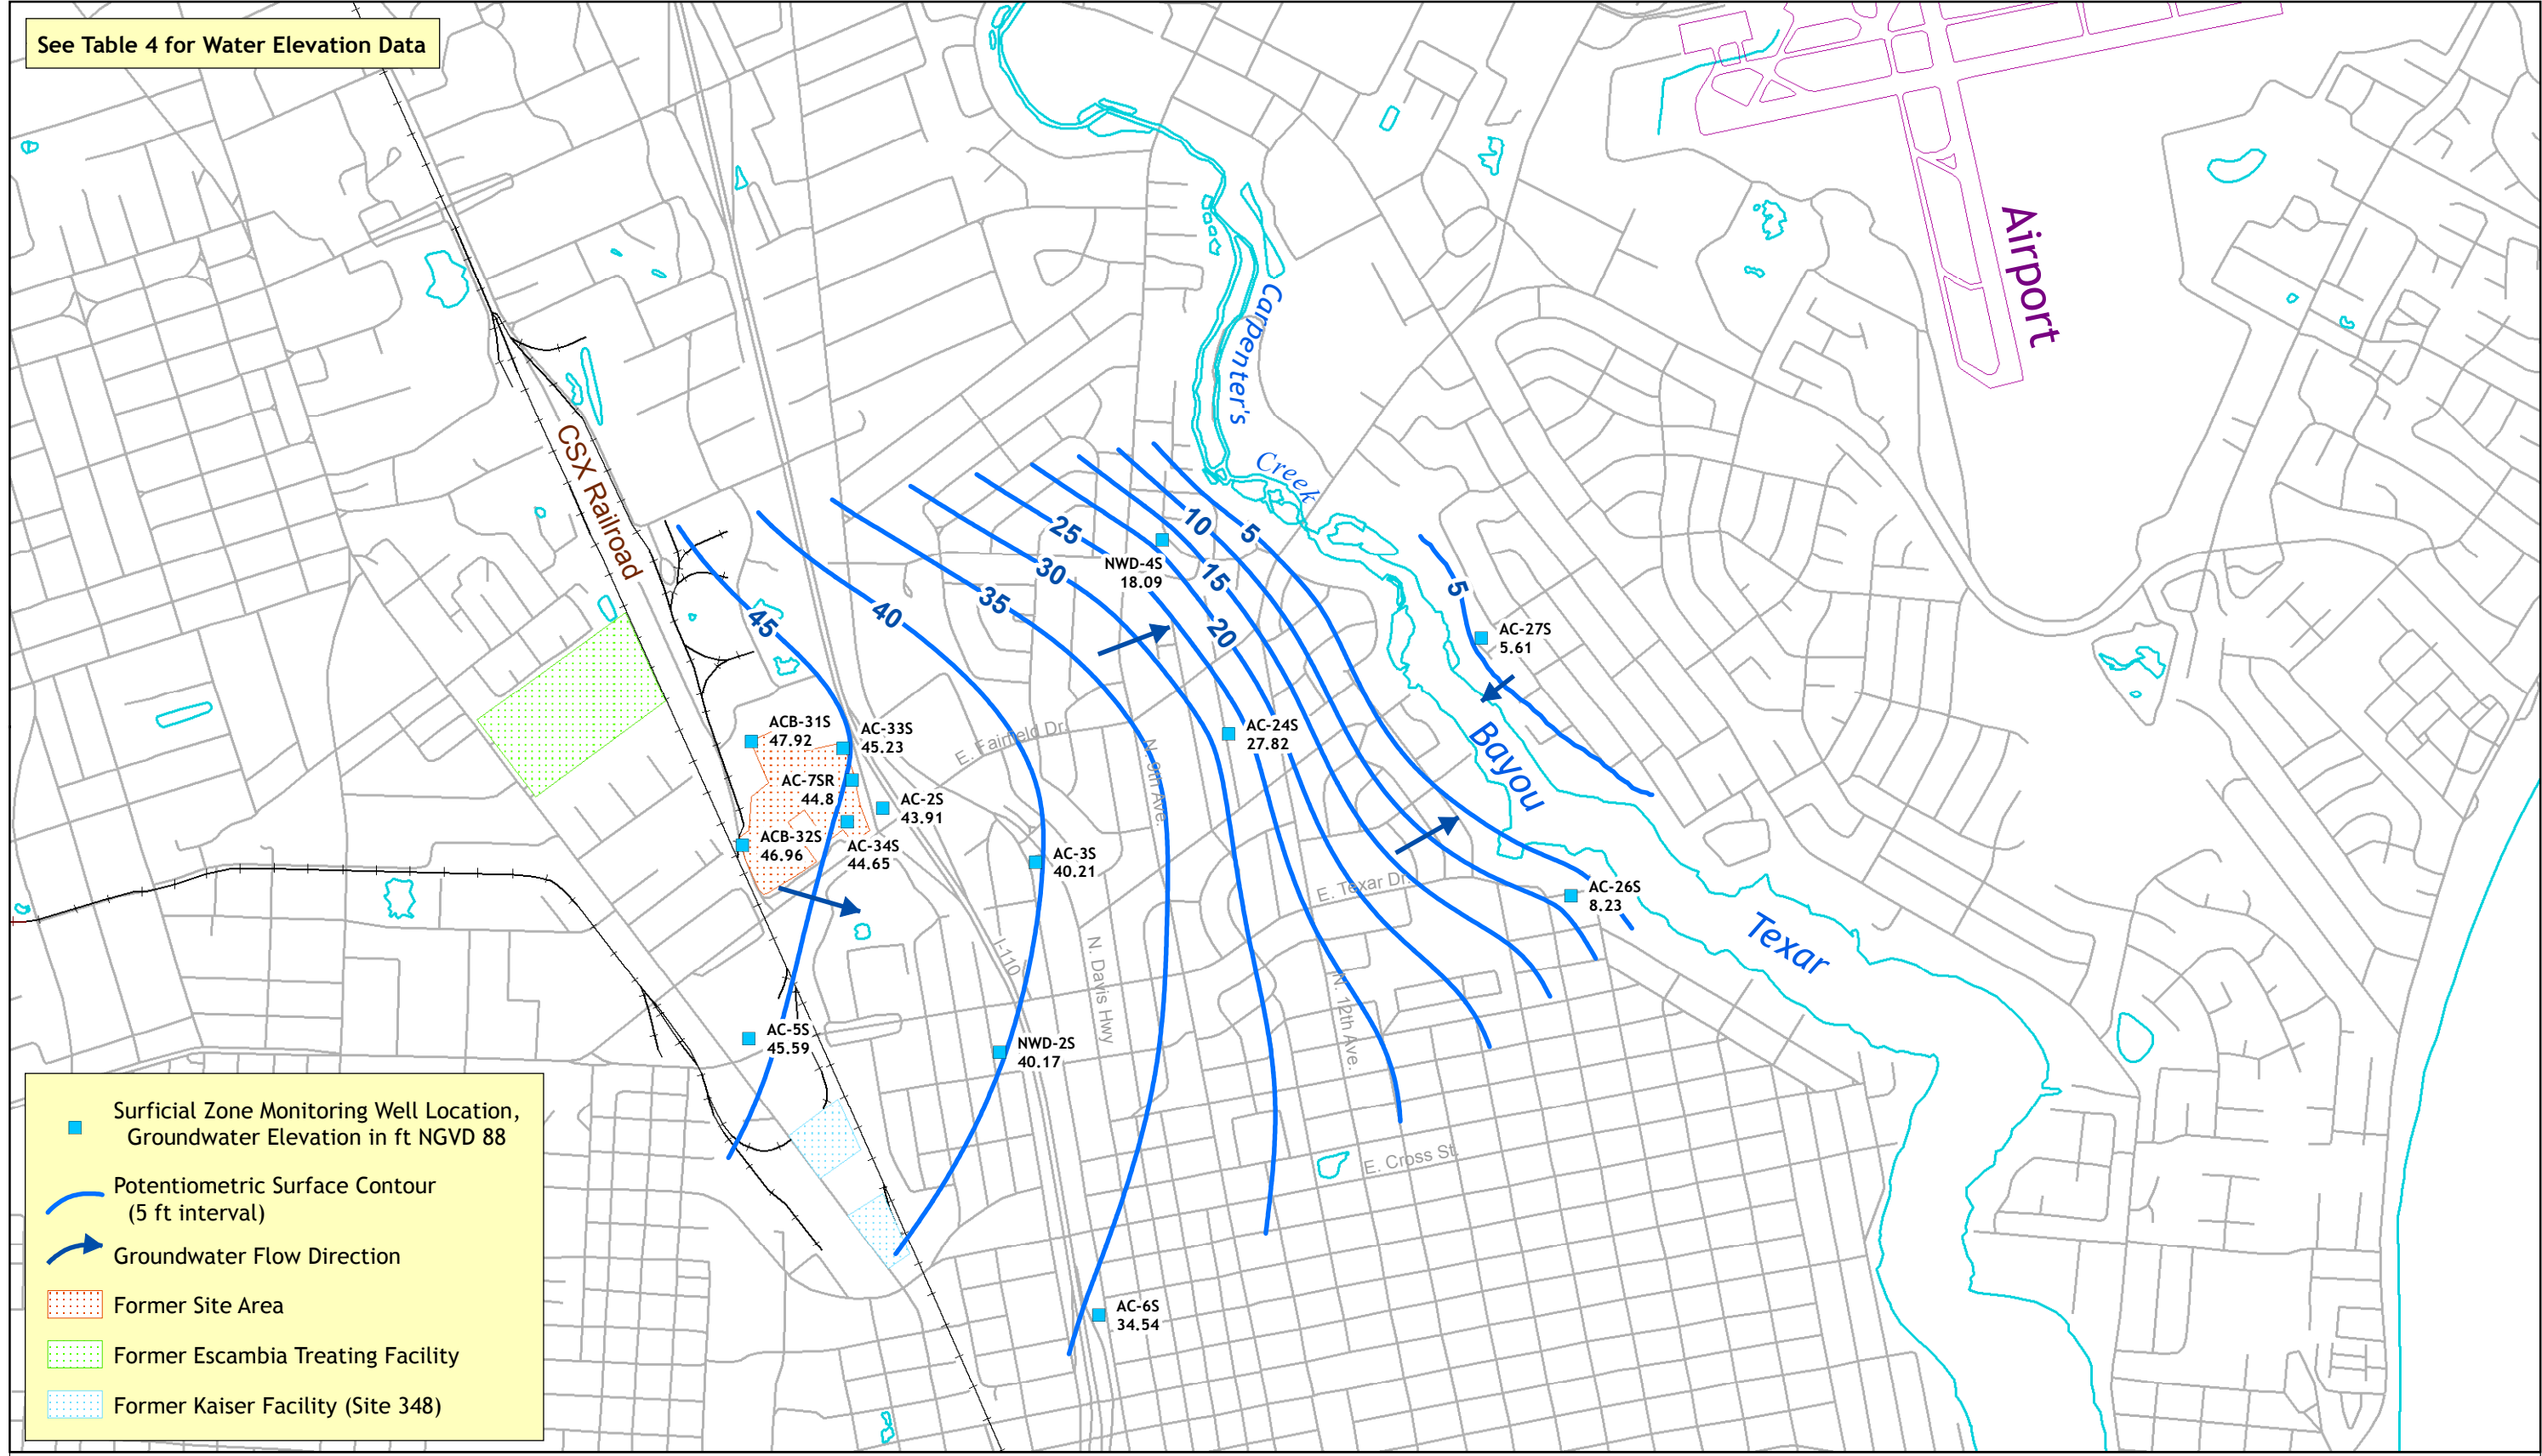

**OU-1 and OU-2
AGRICOLA SITE
PENSACOLA, FLORIDA**

URS

Base Map Data Sources:
Florida Department of Environmental Protection
Northwest Florida Water Management District



**POTENTIOMETRIC SURFACE
SURFICIAL ZONE
November 2014**

**FIGURE
5**

See Table 4 for Water Elevation Data

- Main Producing Zone Monitoring Well Location, Groundwater Elevation in ft NGVD 88
- Potentiometric Surface Contour (5 ft interval)
- ➔ Groundwater Flow Direction
- ▨ Former Site Area
- ▨ Former Escambia Treating Facility
- ▨ Former Kaiser Facility (Site 348)

URS

Base Map Data Provided By:
Florida Department of Environmental Protection
and Northwest Florida Water Management District




0.5 0.25 0 Miles


Coordinate System: UTM, Zone 16, NAD27

POTENTIOMETRIC SURFACE
MAIN PRODUCING ZONE
November 2014

FIGURE
6

Figure 7
Annual Rainfall and Cumulative Departure from Normal
NOAA Rainfall Station
Pensacola, Florida

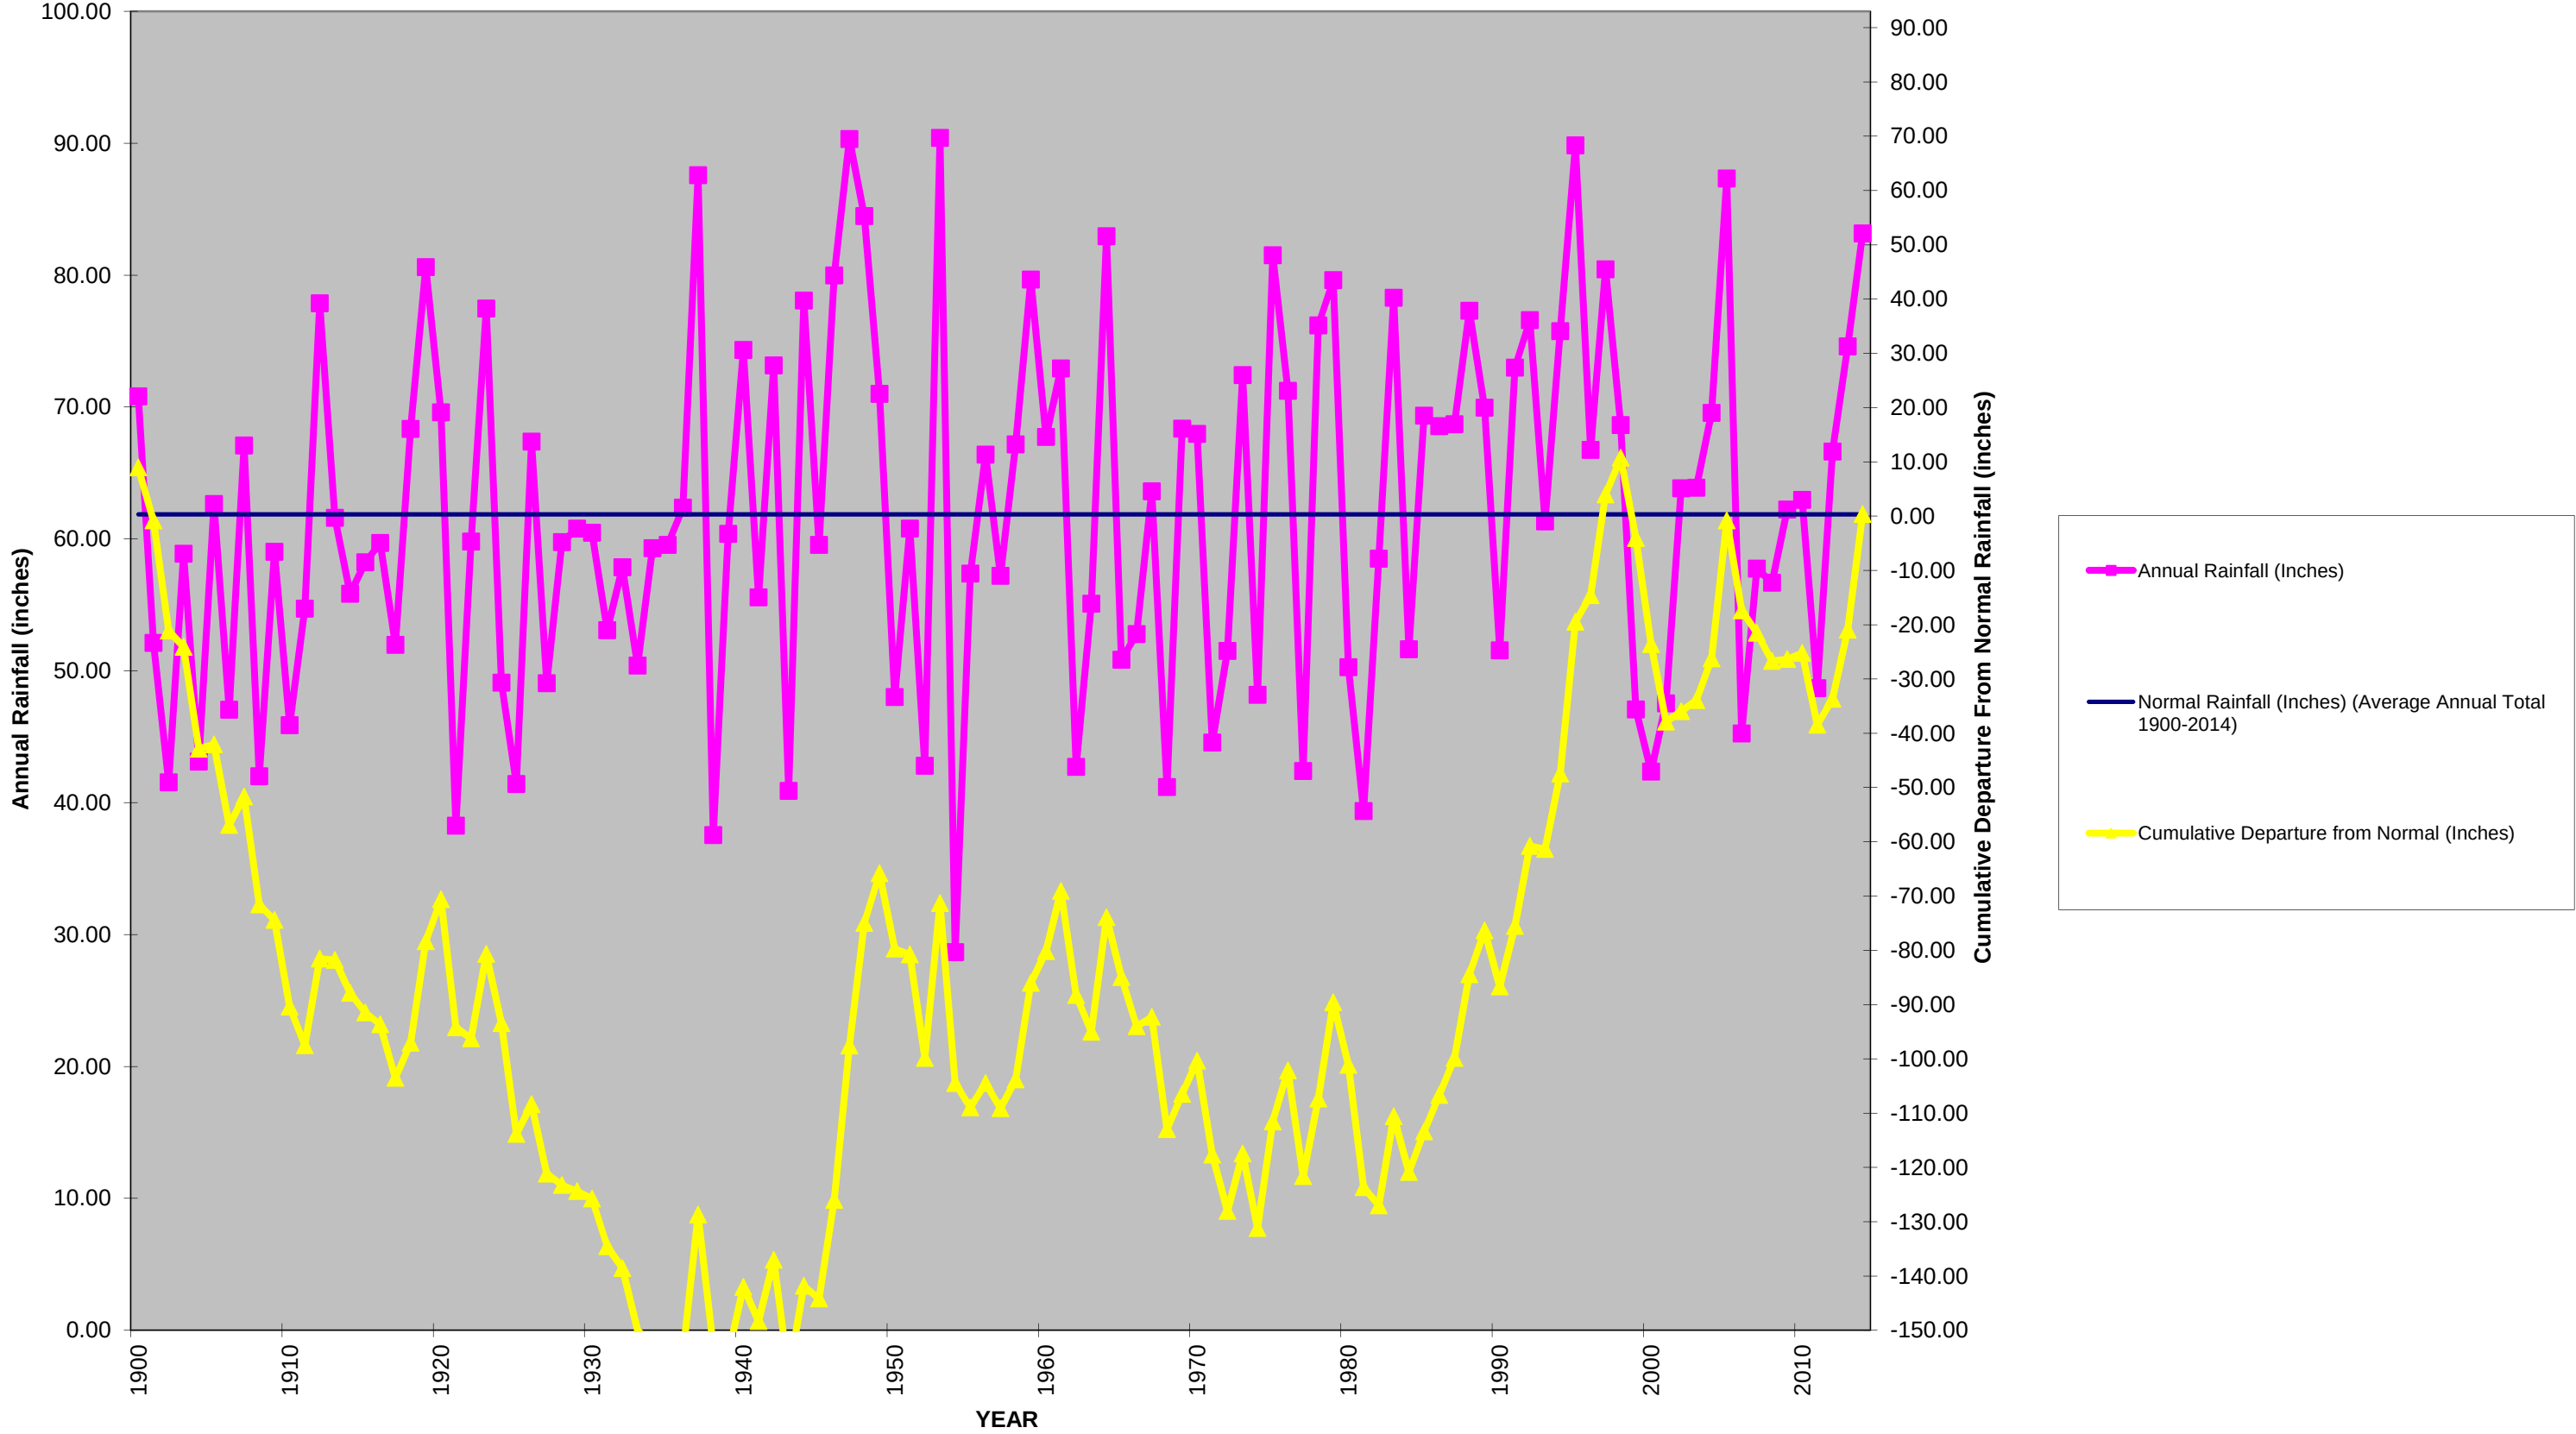


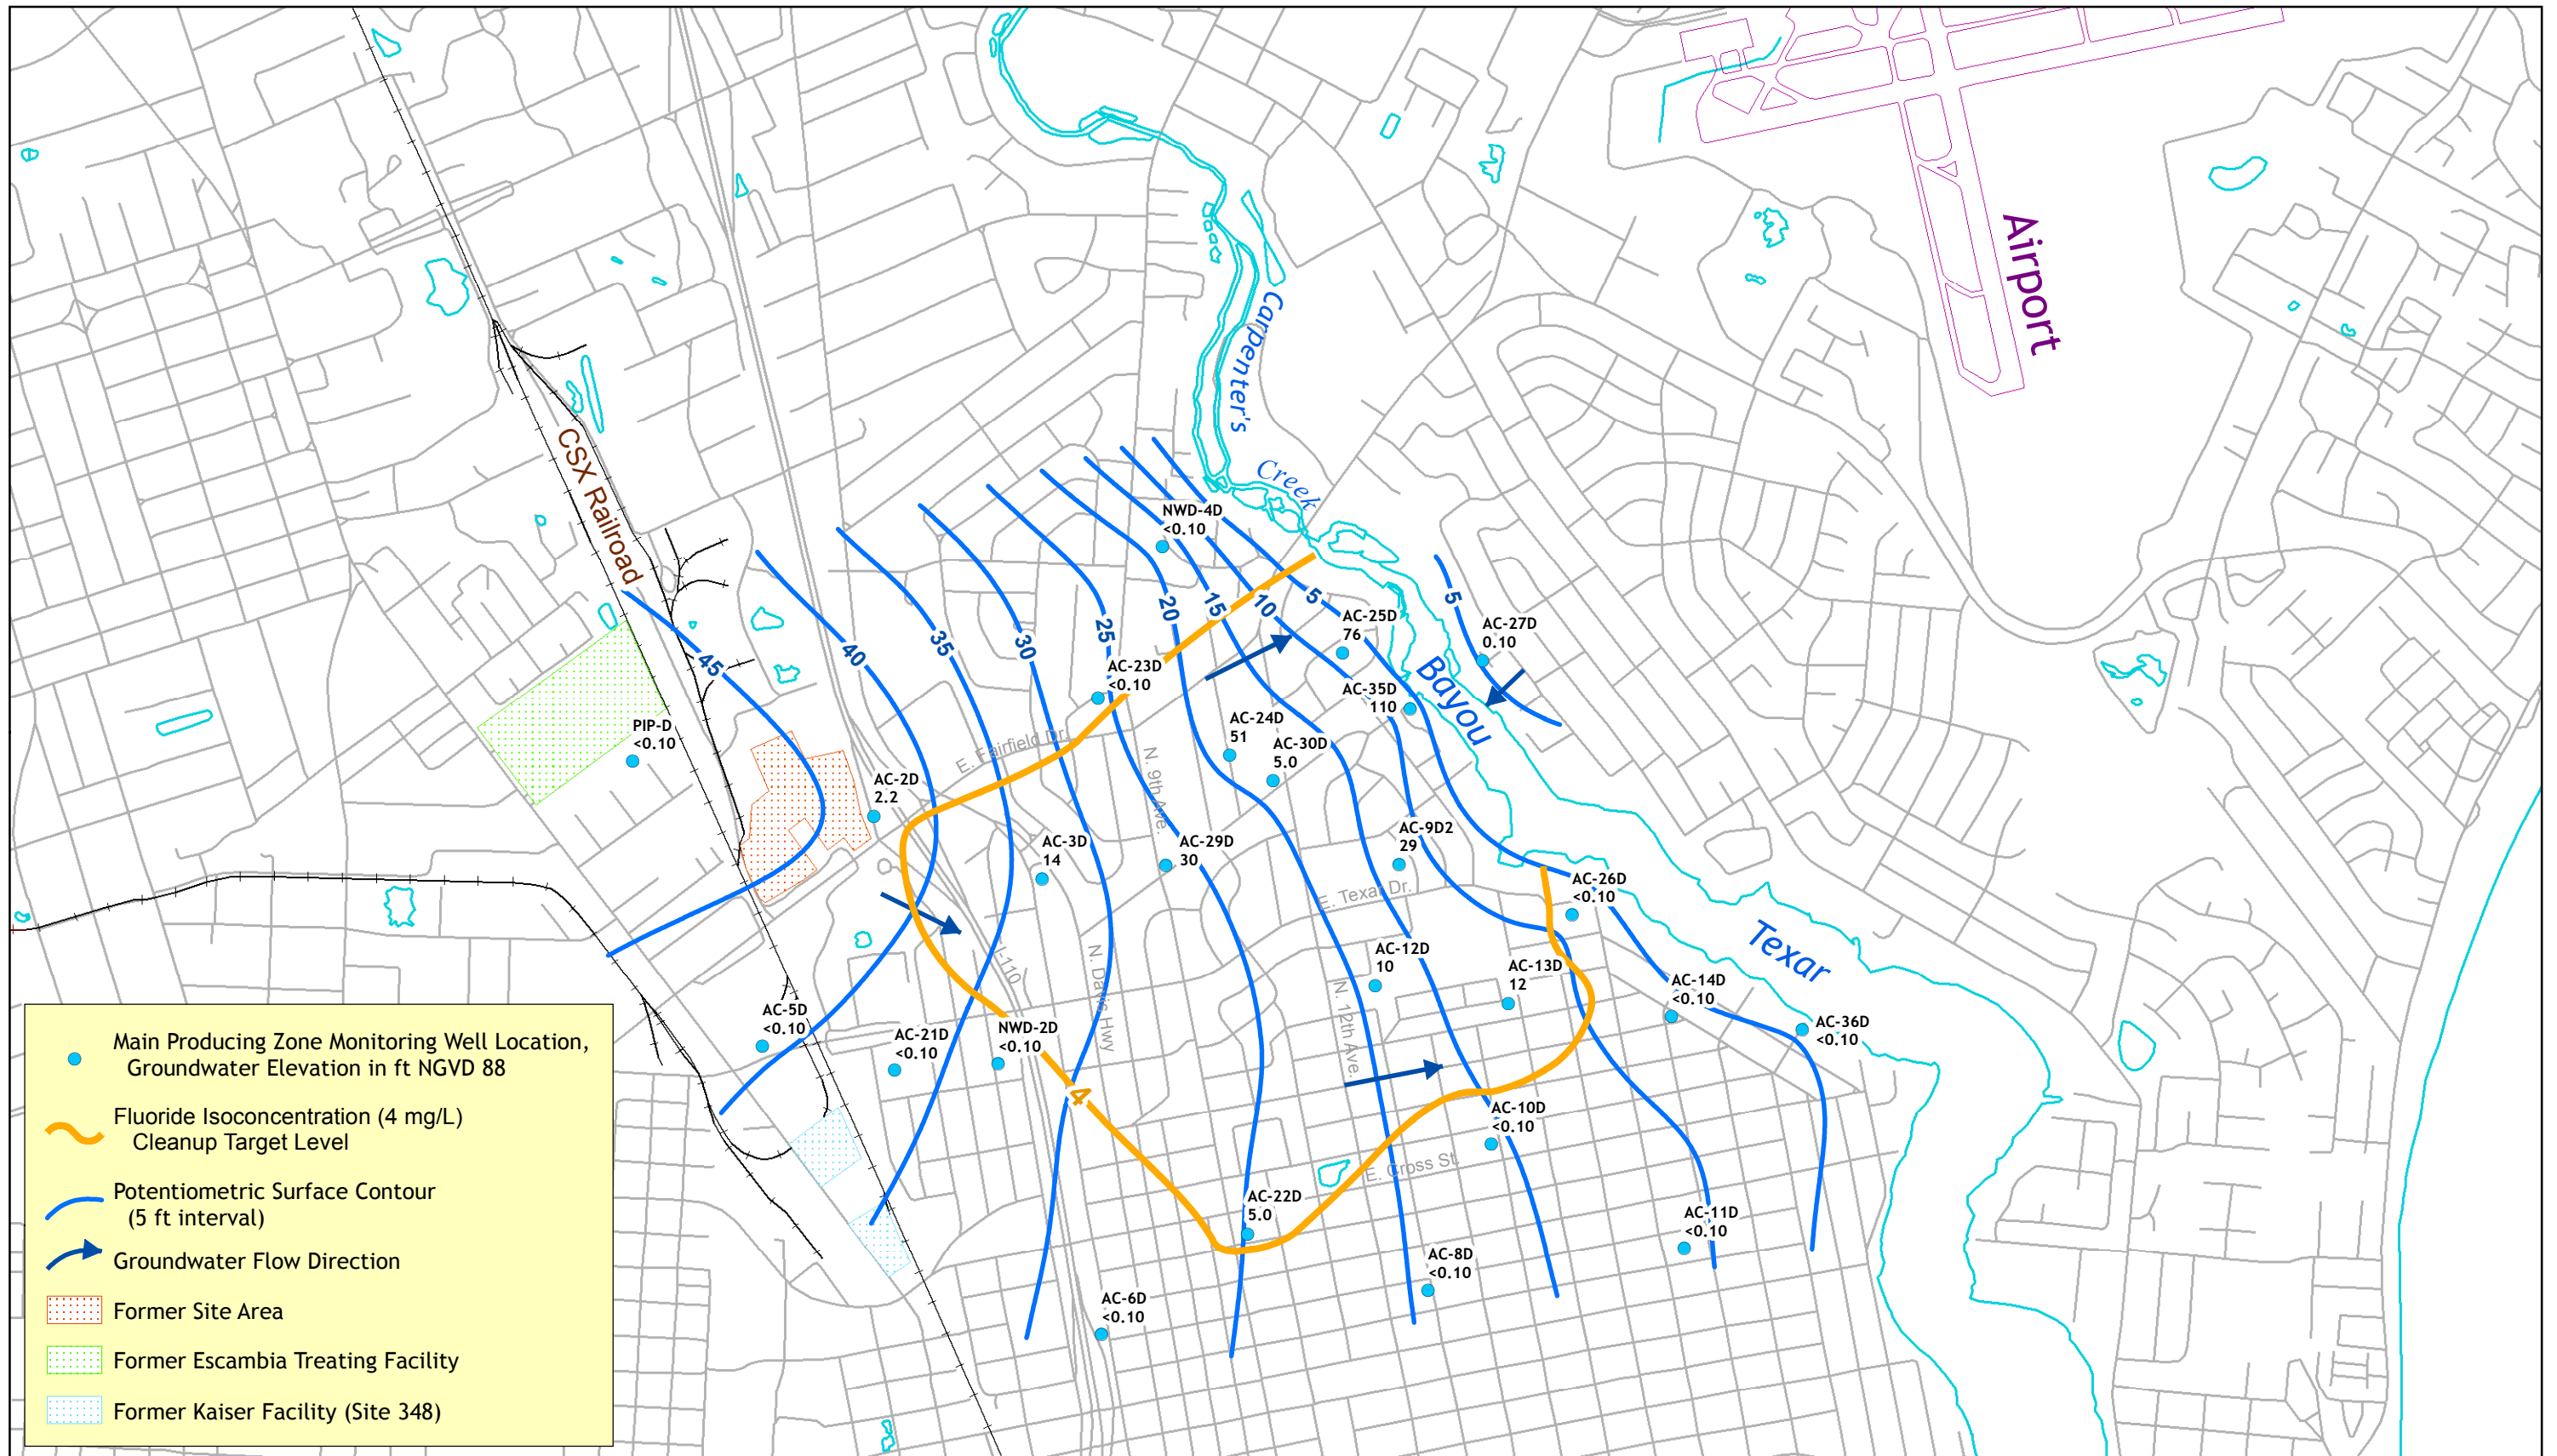

**OU-1 and OU-2
AGRICOLA SITE
PENSACOLA, FLORIDA**




Base Map Data Provided By:
Florida Department of Environmental Protection
and Northwest Florida Water Management District



**FLUORIDE CONCENTRATION
DELINEATION
November 2014**


**FIGURE
8**

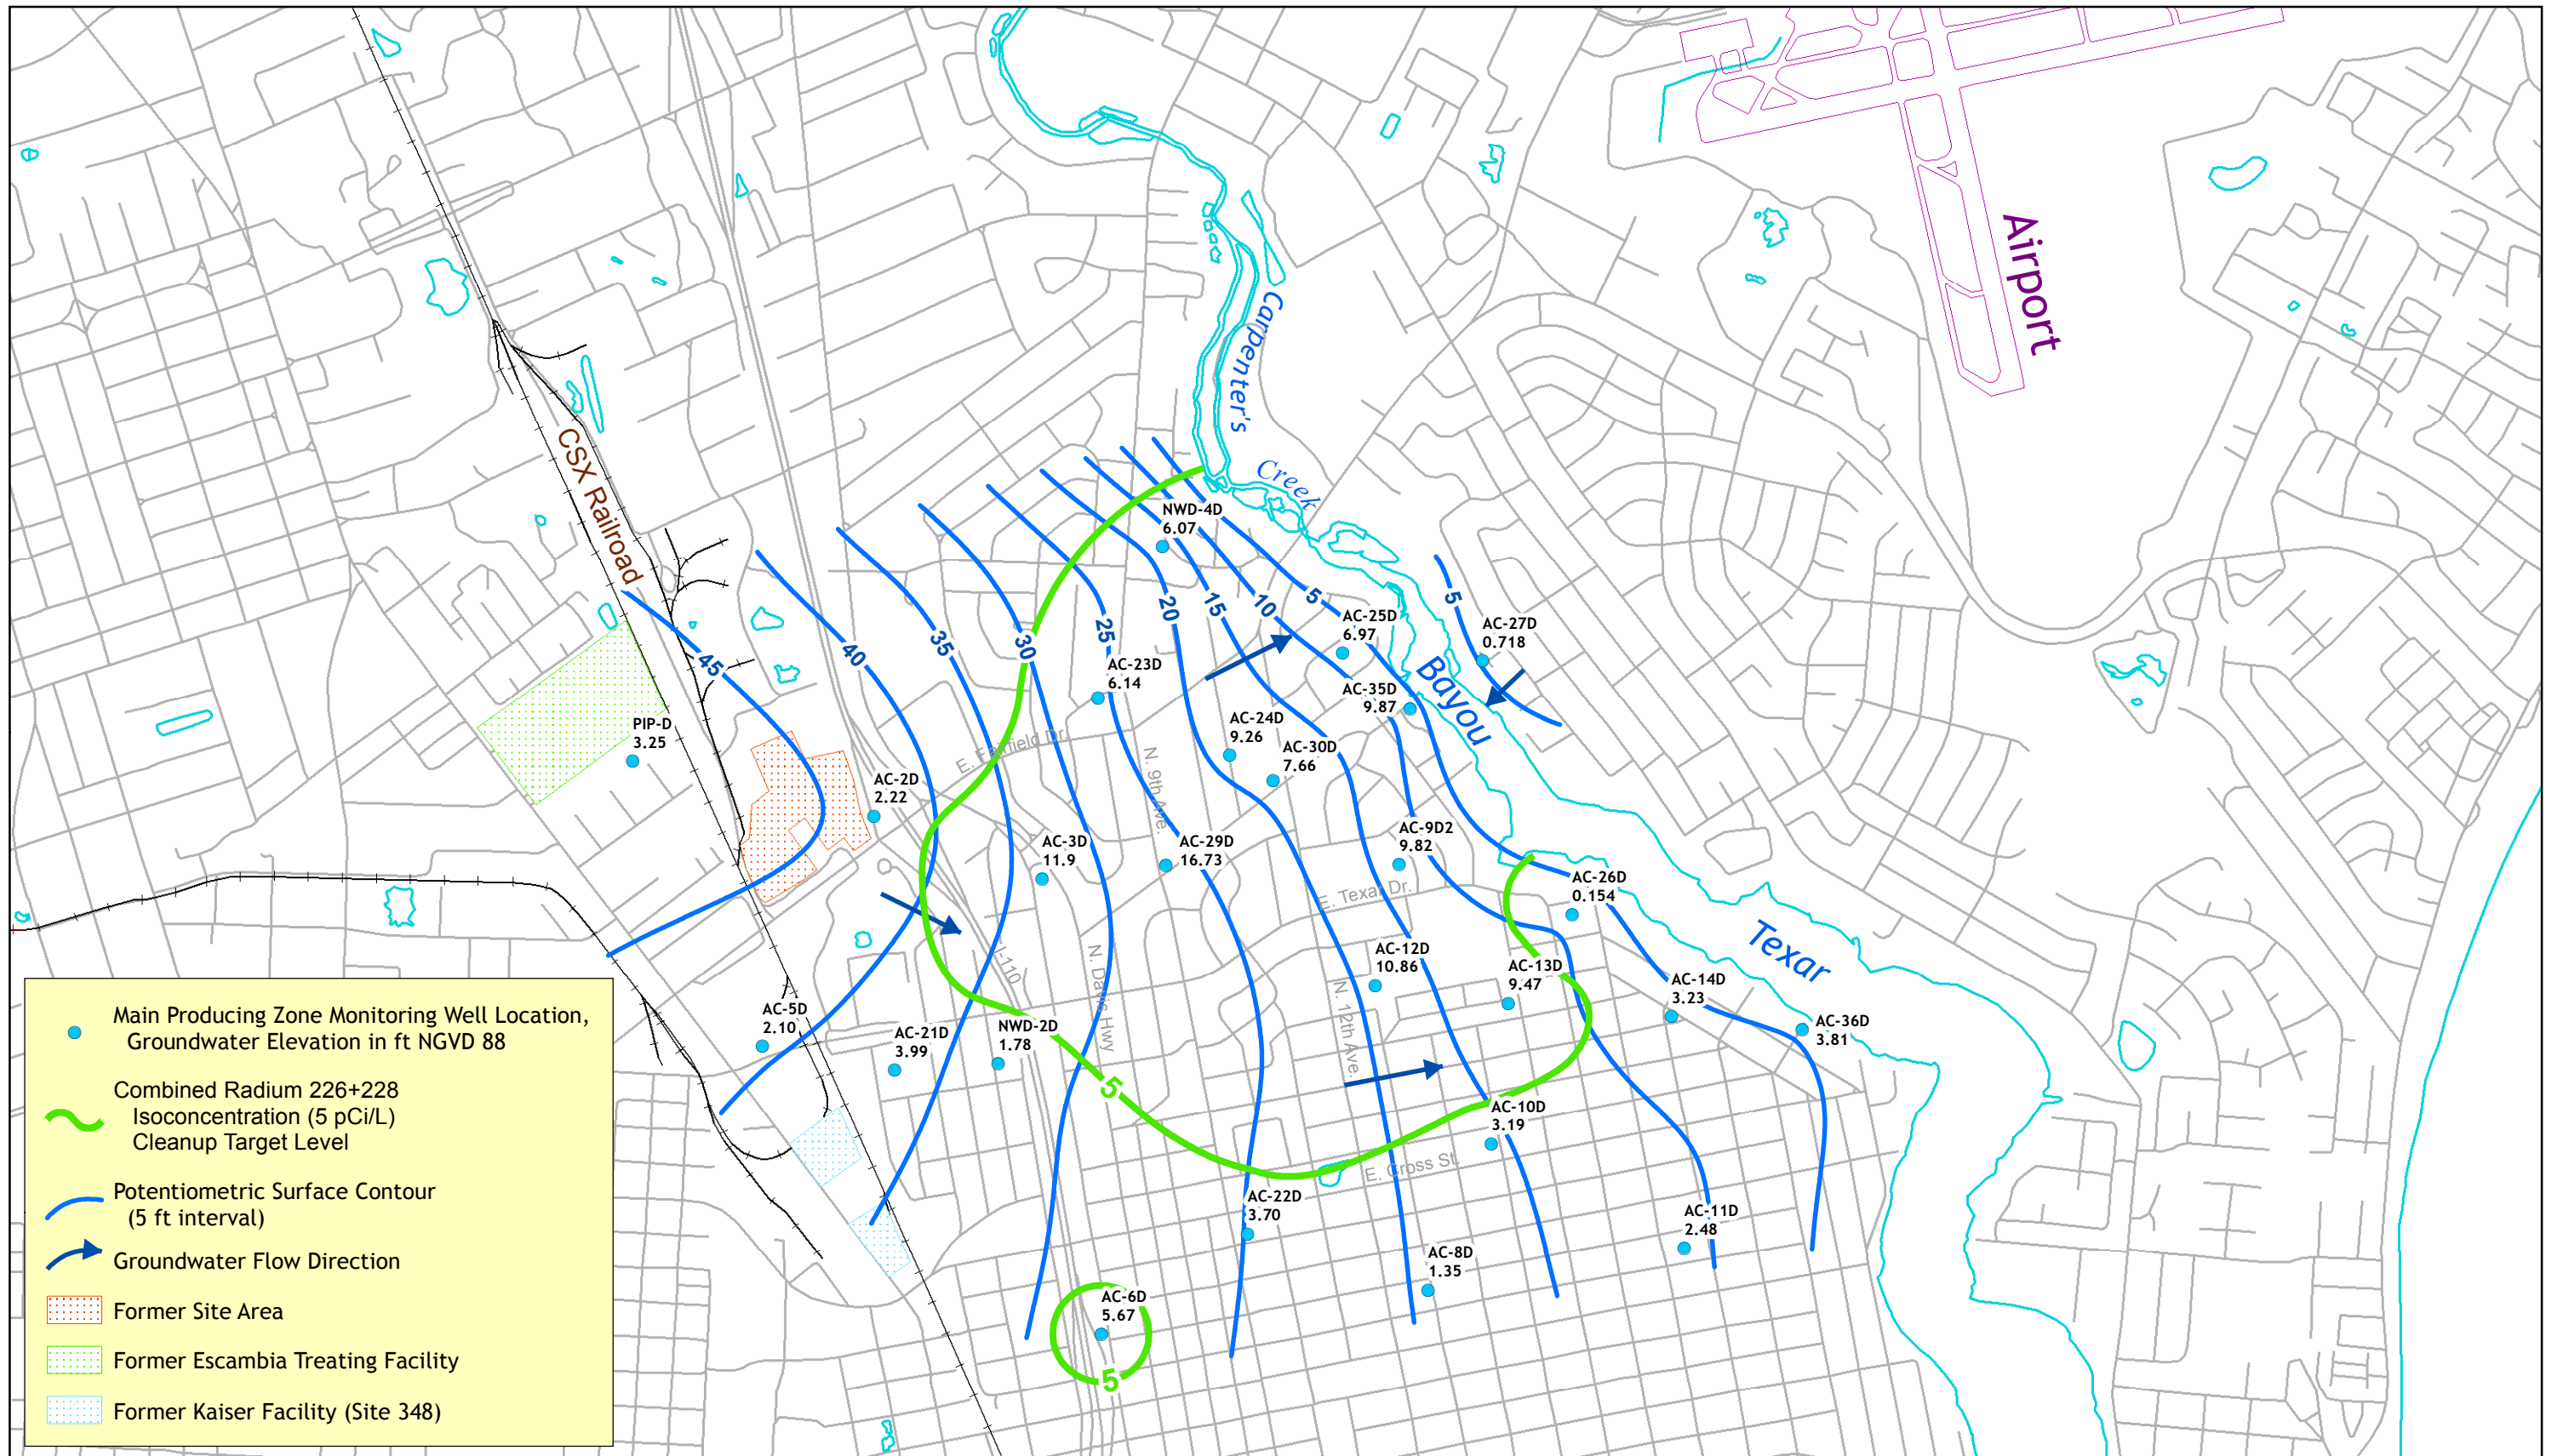

**OU-1 and OU-2
AGRICOLA SITE
PENSACOLA, FLORIDA**



Base Map Data Provided by:
Florida Department of Environmental Protection
and Northwest Florida Water Management District



**COMBINED RADIUM 226+228
CONCENTRATION DELINEATION
November 2014**

**FIGURE
9**

APPENDIX A

TestAmerica

THE LEADER IN ENVIRONMENTAL TESTING

ANALYTICAL REPORT

TestAmerica Laboratories, Inc.

TestAmerica Pensacola

3355 McLemore Drive

Pensacola, FL 32514

Tel: (850)474-1001

TestAmerica Job ID: 400-98308-1

Client Project/Site: Agrico Pensacola

For:

URS Corporation

1625 Summit Lake Drive

Suite 200

Tallahassee, Florida 32317

Attn: Mr. Jeff Wagner



Authorized for release by:

12/29/2014 2:33:59 PM

Noel Savoie, Project Manager I

(850)878-3994

noel.savoie@testamericainc.com

LINKS

Review your project
results through

TotalAccess

Have a Question?



Visit us at:

www.testamericainc.com

The test results in this report meet all 2003 NELAC and 2009 TNI requirements for accredited parameters, exceptions are noted in this report. This report may not be reproduced except in full, and with written approval from the laboratory. For questions please contact the Project Manager at the e-mail address or telephone number listed on this page.

This report has been electronically signed and authorized by the signatory. Electronic signature is intended to be the legally binding equivalent of a traditionally handwritten signature.

Results relate only to the items tested and the sample(s) as received by the laboratory.

Table of Contents

Cover Page	1
Table of Contents	2
Definitions	3
Case Narrative	4
Sample Summary	5
Client Sample Results	6
QC Sample Results	8
Chronicle	11
Method Summary	13
Subcontract Data	14
Chain of Custody	32



Definitions/Glossary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98308-1

Glossary

Abbreviation	These commonly used abbreviations may or may not be present in this report.
□	Listed under the "D" column to designate that the result is reported on a dry weight basis
%R	Percent Recovery
CFL	Contains Free Liquid
CNF	Contains no Free Liquid
DER	Duplicate error ratio (normalized absolute difference)
Dil Fac	Dilution Factor
DL, RA, RE, IN	Indicates a Dilution, Re-analysis, Re-extraction, or additional Initial metals/anion analysis of the sample
DLC	Decision level concentration
MDA	Minimum detectable activity
EDL	Estimated Detection Limit
MDC	Minimum detectable concentration
MDL	Method Detection Limit
ML	Minimum Level (Dioxin)
NC	Not Calculated
ND	Not detected at the reporting limit (or MDL or EDL if shown)
PQL	Practical Quantitation Limit
QC	Quality Control
RER	Relative error ratio
RL	Reporting Limit or Requested Limit (Radiochemistry)
RPD	Relative Percent Difference, a measure of the relative difference between two points
TEF	Toxicity Equivalent Factor (Dioxin)
TEQ	Toxicity Equivalent Quotient (Dioxin)

Case Narrative

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98308-1

Job ID: 400-98308-1

Laboratory: TestAmerica Pensacola

Narrative

Job Narrative 400-98308-1

Comments

No additional comments.

Receipt

The samples were received on 11/11/2014 5:23 PM; the samples arrived in good condition, properly preserved and, where required, on ice. The temperatures of the 2 coolers at receipt time were 0.4° C and 1.9° C.

HPLC/IC

Method 300.0: The following sample was diluted to bring the concentration of target analytes within the calibration range: AC-3D (400-98308-1). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Metals

No analytical or quality issues were noted, other than those described in the Definitions/Glossary page.

General Chemistry

Method SM 4500 NO3 F: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-3D (400-98308-1), AC-3S (400-98308-2), AC-23D (400-98308-3), NWD-2D (400-98308-5), NWD-2S (400-98308-4), and DUP-3 (400-98308-6). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Subcontract Work

Methods Radium 226 by EPA Method 903.1, Radium 228 by EPA Method 904.0: These methods were subcontracted to TestAmerica Richland. Report attached.

Sample Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98308-1

Lab Sample ID	Client Sample ID	Matrix	Collected	Received
400-98308-1	AC-3D	Water	11/11/14 09:38	11/11/14 17:23
400-98308-2	AC-3S	Water	11/11/14 10:54	11/11/14 17:23
400-98308-3	AC-23D	Water	11/11/14 13:00	11/11/14 17:23
400-98308-4	NWD-2S	Water	11/11/14 15:10	11/11/14 17:23
400-98308-5	NWD-2D	Water	11/11/14 15:41	11/11/14 17:23
400-98308-6	DUP-3	Water	11/11/14 00:00	11/11/14 17:23

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98308-1

Client Sample ID: AC-3D

Date Collected: 11/11/14 09:38

Date Received: 11/11/14 17:23

Lab Sample ID: 400-98308-1

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	16		1.0		mg/L			11/25/14 17:42	1
Sulfate	230		10		mg/L			11/26/14 10:59	10

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	14		0.20		mg/L			11/19/14 16:27	2
Nitrate Nitrite as N	5.9		0.25		mg/L			11/12/14 18:24	5
Nitrate as N	5.9		0.050		mg/L			11/12/14 17:59	1
Nitrite as N	<0.10		0.10		mg/L			11/12/14 09:59	1

Client Sample ID: AC-3S

Date Collected: 11/11/14 10:54

Date Received: 11/11/14 17:23

Lab Sample ID: 400-98308-2

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	2.5		1.0		mg/L			11/25/14 18:05	1
Sulfate	15		1.0		mg/L			11/25/14 18:05	1

Method: 6010C - Metals (ICP) - Total Recoverable

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Arsenic	<0.0050		0.0050		mg/L		11/12/14 11:58	11/14/14 15:59	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/18/14 13:01	1
Nitrate Nitrite as N	2.0		0.10		mg/L			11/12/14 18:16	2
Nitrate as N	2.0		0.050		mg/L			11/12/14 17:53	1
Nitrite as N	<0.10		0.10		mg/L			11/12/14 09:59	1

Client Sample ID: AC-23D

Date Collected: 11/11/14 13:00

Date Received: 11/11/14 17:23

Lab Sample ID: 400-98308-3

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	9.1		1.0		mg/L			11/25/14 18:28	1
Sulfate	20		1.0		mg/L			11/25/14 18:28	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/18/14 13:03	1
Nitrate Nitrite as N	2.5		0.10		mg/L			11/12/14 18:22	2
Nitrate as N	2.5		0.050		mg/L			11/12/14 17:54	1
Nitrite as N	<0.10		0.10		mg/L			11/12/14 09:59	1

TestAmerica Pensacola

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98308-1

Client Sample ID: NWD-2S

Lab Sample ID: 400-98308-4

Date Collected: 11/11/14 15:10

Matrix: Water

Date Received: 11/11/14 17:23

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	8.3		1.0		mg/L			11/25/14 18:51	1
Sulfate	13		1.0		mg/L			11/25/14 18:51	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	1.6		0.10		mg/L			11/18/14 13:06	1
Nitrate Nitrite as N	2.1		0.10		mg/L			11/12/14 18:25	2
Nitrate as N	2.1		0.050		mg/L			11/12/14 18:00	1
Nitrite as N	<0.10		0.10		mg/L			11/12/14 09:59	1

Client Sample ID: NWD-2D

Lab Sample ID: 400-98308-5

Date Collected: 11/11/14 15:41

Matrix: Water

Date Received: 11/11/14 17:23

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	12		1.0		mg/L			11/25/14 19:13	1
Sulfate	7.6		1.0		mg/L			11/25/14 19:13	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/19/14 16:48	1
Nitrate Nitrite as N	6.0		0.25		mg/L			11/12/14 18:26	5
Nitrate as N	6.0		0.050		mg/L			11/12/14 18:07	1
Nitrite as N	<0.10		0.10		mg/L			11/12/14 09:59	1

Client Sample ID: DUP-3

Lab Sample ID: 400-98308-6

Date Collected: 11/11/14 00:00

Matrix: Water

Date Received: 11/11/14 17:23

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	8.2		1.0		mg/L			11/25/14 19:36	1
Sulfate	13		1.0		mg/L			11/25/14 19:36	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	1.6		0.10		mg/L			11/19/14 16:51	1
Nitrate Nitrite as N	2.1		0.10		mg/L			11/12/14 18:27	2
Nitrate as N	2.1		0.050		mg/L			11/12/14 18:08	1
Nitrite as N	<0.10		0.10		mg/L			11/12/14 09:59	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98308-1

Method: 300.0 - Anions, Ion Chromatography

Lab Sample ID: MB 400-237963/4

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			11/25/14 12:44	1
Sulfate	<1.0		1.0		mg/L			11/25/14 12:44	1

Lab Sample ID: LCS 400-237963/5

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	10.5		mg/L		105	90 - 110
Sulfate	10.0	9.32		mg/L		93	90 - 110

Lab Sample ID: LCSD 400-237963/6

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	10.6		mg/L		106	90 - 110	1	15
Sulfate	10.0	9.29		mg/L		93	90 - 110	0	15

Method: 6010C - Metals (ICP)

Lab Sample ID: MB 400-236480/1-A

Matrix: Water

Analysis Batch: 236970

Client Sample ID: Method Blank

Prep Type: Total Recoverable

Prep Batch: 236480

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Arsenic	<0.0050		0.0050		mg/L		11/12/14 11:58	11/14/14 14:51	1

Lab Sample ID: LCS 400-236480/2-A

Matrix: Water

Analysis Batch: 236970

Client Sample ID: Lab Control Sample

Prep Type: Total Recoverable

Prep Batch: 236480

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Arsenic	1.00	1.07		mg/L		107	80 - 120

Lab Sample ID: 400-98308-2 MS

Matrix: Water

Analysis Batch: 236970

Client Sample ID: AC-3S

Prep Type: Total Recoverable

Prep Batch: 236480

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Arsenic	<0.0050		1.00	1.04		mg/L		104	75 - 125

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98308-1

Method: 340.2 - Fluoride

Lab Sample ID: MB 400-237167/3
Matrix: Water
Analysis Batch: 237167

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/18/14 12:09	1

Lab Sample ID: LCS 400-237167/4
Matrix: Water
Analysis Batch: 237167

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.39		mg/L		110	90 - 110

Lab Sample ID: MB 400-237352/3
Matrix: Water
Analysis Batch: 237352

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/19/14 16:02	1

Lab Sample ID: LCS 400-237352/4
Matrix: Water
Analysis Batch: 237352

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.30		mg/L		108	90 - 110

Method: 353.2 - Nitrogen, Nitrate-Nitrite

Lab Sample ID: MB 400-236548/47
Matrix: Water
Analysis Batch: 236548

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/12/14 17:36	1

Lab Sample ID: LCS 400-236548/48
Matrix: Water
Analysis Batch: 236548

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.536		mg/L		107	90 - 110

Lab Sample ID: MRL 400-236548/12
Matrix: Water
Analysis Batch: 236548

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	0.0529		mg/L		106	50 - 150

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98308-1

Method: SM 4500 NO2 B - Nitrogen, Nitrite

Lab Sample ID: MB 400-236545/113

Matrix: Water

Analysis Batch: 236545

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/12/14 17:31	1

Lab Sample ID: MB 400-236545/6

Matrix: Water

Analysis Batch: 236545

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/12/14 09:55	1

Lab Sample ID: MB 400-236545/64

Matrix: Water

Analysis Batch: 236545

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/12/14 15:51	1

Lab Sample ID: LCS 400-236545/114

Matrix: Water

Analysis Batch: 236545

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.282		mg/L		94	90 - 110

Lab Sample ID: LCS 400-236545/7

Matrix: Water

Analysis Batch: 236545

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.280		mg/L		93	90 - 110

Lab Sample ID: MRL 400-236545/3

Matrix: Water

Analysis Batch: 236545

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.100	<0.10		mg/L		98	50 - 150

Lab Sample ID: 400-98308-6 DU

Matrix: Water

Analysis Batch: 236545

Client Sample ID: DUP-3

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	DU Result	DU Qualifier	Unit	D	RPD	RPD Limit
Nitrite as N	<0.10		<0.10		mg/L		NC	9

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98308-1

Client Sample ID: AC-3D

Date Collected: 11/11/14 09:38

Date Received: 11/11/14 17:23

Lab Sample ID: 400-98308-1

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/25/14 17:42	TAJ	TAL PEN
Total/NA	Analysis	300.0		10	237963	11/26/14 10:59	TAJ	TAL PEN
Total/NA	Analysis	340.2		2	237352	11/19/14 16:27	SLT	TAL PEN
Total/NA	Analysis	353.2		5	236548	11/12/14 18:24	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	236549	11/12/14 17:59	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236545	11/12/14 09:59	LSS	TAL PEN

Client Sample ID: AC-3S

Date Collected: 11/11/14 10:54

Date Received: 11/11/14 17:23

Lab Sample ID: 400-98308-2

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/25/14 18:05	TAJ	TAL PEN
Total Recoverable	Prep	3005A			236480	11/12/14 11:58	KWN	TAL PEN
Total Recoverable	Analysis	6010C		1	236970	11/14/14 15:59	SLM	TAL PEN
Total/NA	Analysis	340.2		1	237167	11/18/14 13:01	SLT	TAL PEN
Total/NA	Analysis	353.2		2	236548	11/12/14 18:16	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	236549	11/12/14 17:53	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236545	11/12/14 09:59	LSS	TAL PEN

Client Sample ID: AC-23D

Date Collected: 11/11/14 13:00

Date Received: 11/11/14 17:23

Lab Sample ID: 400-98308-3

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/25/14 18:28	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237167	11/18/14 13:03	SLT	TAL PEN
Total/NA	Analysis	353.2		2	236548	11/12/14 18:22	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	236549	11/12/14 17:54	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236545	11/12/14 09:59	LSS	TAL PEN

Client Sample ID: NWD-2S

Date Collected: 11/11/14 15:10

Date Received: 11/11/14 17:23

Lab Sample ID: 400-98308-4

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/25/14 18:51	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237167	11/18/14 13:06	SLT	TAL PEN
Total/NA	Analysis	353.2		2	236548	11/12/14 18:25	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	236549	11/12/14 18:00	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236545	11/12/14 09:59	LSS	TAL PEN

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98308-1

Client Sample ID: NWD-2D

Date Collected: 11/11/14 15:41

Date Received: 11/11/14 17:23

Lab Sample ID: 400-98308-5

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/25/14 19:13	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 16:48	SLT	TAL PEN
Total/NA	Analysis	353.2		5	236548	11/12/14 18:26	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	236549	11/12/14 18:07	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236545	11/12/14 09:59	LSS	TAL PEN

Client Sample ID: DUP-3

Date Collected: 11/11/14 00:00

Date Received: 11/11/14 17:23

Lab Sample ID: 400-98308-6

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/25/14 19:36	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 16:51	SLT	TAL PEN
Total/NA	Analysis	353.2		2	236548	11/12/14 18:27	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	236549	11/12/14 18:08	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236545	11/12/14 09:59	LSS	TAL PEN

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Method Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98308-1

Method	Method Description	Protocol	Laboratory
300.0	Anions, Ion Chromatography	MCAWW	TAL PEN
6010C	Metals (ICP)	SW846	TAL PEN
340.2	Fluoride	MCAWW	TAL PEN
353.2	Nitrogen, Nitrate-Nitrite	MCAWW	TAL PEN
Nitrate by calc	Nitrogen, Nitrate	SM	TAL PEN
SM 4500 NO2 B	Nitrogen, Nitrite	SM	TAL PEN
Rad 226-Method 903.1 (Richland)	RAD-226 (RCH)	NONE	TAL RCH
Rad 228-Method 904.0 (Richland)	RAD-228 (RCH)	NONE	TAL RCH

Protocol References:

MCAWW = "Methods For Chemical Analysis Of Water And Wastes", EPA-600/4-79-020, March 1983 And Subsequent Revisions.

NONE = NONE

SM = "Standard Methods For The Examination Of Water And Wastewater",

SW846 = "Test Methods For Evaluating Solid Waste, Physical/Chemical Methods", Third Edition, November 1986 And Its Updates.

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Analytical Data Package Prepared For

TestAmerica Pensacola

Radiochemical Analysis By

TestAmerica Inc

2800 G.W. Way, Richland Wa, 99354, (509)-375-3131.

Assigned Laboratory Code: TARL

Data Package Contains _____ Pages

Report No.: 63980

Results in this report relate only to the sample(s) analyzed.

SDG No.	Order No.	Client Sample ID (List Order)	Lot-Sa No.	Work Order	Report DB ID	Batch No.
49002		AC-23D(400-98308-3)	J4K170417-3	M5JDL1AA	9M5JDL10	4322035
		AC-23D(400-98308-3)	J4K170417-3	M5JDL1AC	9M5JDL10	4322036
		AC-3D(400-98308-1)	J4K170417-1	M5JDJ1AA	9M5JDJ10	4322035
		AC-3D(400-98308-1)	J4K170417-1	M5JDJ2AC	9M5JDJ20	4345065
		AC-3S(400-98308-2)	J4K170417-2	M5JDK1AA	9M5JDK10	4322035
		AC-3S(400-98308-2)	J4K170417-2	M5JDK1AC	9M5JDK10	4322036
		DUP-3(400-98308-6)	J4K170417-6	M5JDP1AA	9M5JDP10	4322035
		DUP-3(400-98308-6)	J4K170417-6	M5JDP1AC	9M5JDP10	4322036
		NWD-2D(400-98308-5)	J4K170417-5	M5JDN1AA	9M5JDN10	4322035
		NWD-2D(400-98308-5)	J4K170417-5	M5JDN1AC	9M5JDN10	4322036
		NWD-2S(400-98308-4)	J4K170417-4	M5JDM1AA	9M5JDM10	4322035
		NWD-2S(400-98308-4)	J4K170417-4	M5JDM1AC	9M5JDM10	4322036

Certificate of Analysis

December 22, 2014

TestAmerica Pensacola
3355 McLemore Drive
Pensacola, FL 32514

Attention: Noel Savoie

Date Received at Lab	:	November 13, 2014
Project Name/Number	:	Agrico Pensacola/64000434
Sample Type	:	Six (6) Water
Job Number	:	400-98308-1
SDG Number	:	49002

CASE NARRATIVE

I. Introduction

On November 13, 2014, six water samples were received at TestAmerica's Richland laboratory for radiochemical analysis. Upon receipt, the samples were assigned the TestAmerica identification number as described on the cover page of the Analytical Data Package report form. The samples were assigned to Lot Numbers J4K170417.

II. Sample Receipt

The samples were received in good condition and no anomalies were noted upon check-in.

III. Analytical Results/Methodology

The analytical results for this report are presented by laboratory sample ID. Each set of data includes sample identification information; analytical results and the appropriate associated statistical uncertainties.

The analysis requested was:

Gas Proportional Counting

Radium-228 by method RL-RA-001

Alpha Scintillation Counting

Radium-226 by method RL-RA-001

IV. Quality Control

The analytical result for each analysis performed includes a minimum of one laboratory control sample (LCS), and one reagent blank sample analysis. Any exceptions have been noted in the "Comments" section.

V. Comments

Gas Proportional Counting

Radium-228

In initial batch 4322036, the agreement of sample AC-3D and its duplicate exceeded acceptance criteria. The sample and duplicate were remilked and reanalyzed in batch 4345065. Except as noted, the LCS, batch blank, sample duplicate and sample results are within acceptance limits.

In reanalysis batch 4345065 the LCS recovery was below acceptance criteria and the duplicate sample was slightly higher than CRDL due to low, but acceptable tracer yield. The sample results confirm original analysis results. Except as noted, the LCS, batch blank, sample duplicate and sample results are within acceptance limits.

Alpha Scintillation Counting

Radium 226:

The LCS, batch blank, samples and sample duplicate results are within acceptance limits.

I certify that this Certificate of Analysis is in compliance with the SOW and/or NELAC, both technically and for completeness, for other than the conditions detailed above. The Laboratory Manager or a designee, as verified by the following signature has authorized release of the data contained in this hard copy data package.

Reviewed and approved:

Robin Ebert-Mays
Project Manager

Drinking Water Method Cross References

DRINKING WATER ASTM METHOD CROSS REFERENCES		
Referenced Method	Isotope(s)	TestAmerica Richland's SOP No.
EPA 901.1	Cs-134, I-131	RL-GAM-001
EPA 900.0	Alpha & Beta	RL-GPC-001
EPA 00-02	Gross Alpha (Coprecipitation)	RL-GPC-002
EPA 903.0	Total Alpha Radium (Ra-226)	RL-RA-002
EPA 903.1	Ra-226	RL-RA-001
EPA 904.0	Ra-228	RL-RA-001
EPA 905.0	Sr-89/90	RL-GPC-003
ASTM D5174	Uranium	RL-KPA-003
EPA 906.0	Tritium	RL-LSC-005

Results in this report relate only to the sample(s) analyzed.

Uncertainty Estimation

TestAmerica Richland has adopted the internationally accepted approach to estimating uncertainties described in "NIST Technical Note 1297, 1994 Edition". The approach, "Law of Propagation of Errors", involves the identification of all variables in an analytical method which are used to derive a result. These variables are related to the analytical result (R) by some functional relationship, $R = \text{constants} * f(x,y,z,...)$. The components (x,y,z) are evaluated to determine their contribution to the overall method uncertainty. The individual component uncertainties (u_i) are then combined using a statistical model that provides the most probable overall uncertainty value. All component uncertainties are categorized as type A, evaluated by statistical methods, or type B, evaluated by other means. Uncertainties not included in the components, such as sample homogeneity, are combined with the component uncertainty as the square root of the sum-of-the-squares of the individual uncertainties. The uncertainty associated with the derived result is the combined uncertainty (u_c) multiplied by the coverage factor (1,2, or 3).

When three or more sample replicates are used to derive the analytical result, the type A uncertainty is the standard deviation of the mean value ($S/\sqrt{n}$), where S is the standard deviation of the derived results. The type B uncertainties are all other random or non-random components that are not included in the standard deviation.

The derivation of the general "Law of Propagation of Errors" equations and specific example are available on request.

Report Definitions

Action Lev	An agreed upon activity level used to trigger some action when the final result is greater than or equal to the Action Level. Often the Action Level is related to the Decision Limit.
Batch	The QC preparation batch number that relates laboratory samples to QC samples that were prepared and analyzed together.
Bias	Defined by the equation (Result/Expected)-1 as defined by ANSI N13.30.
COC No	Chain of Custody Number assigned by the Client or TestAmerica.
Count Error (#s)	Poisson counting statistics of the gross sample count and background. The uncertainty is absolute and in the same units as the result. For Liquid Scintillation Counting (LSC) the batch blank count is the background.
Total Uncert (#s) <i>u_c - Combined Uncertainty.</i>	All known uncertainties associated with the preparation and analysis of the sample are propagated to give a measure of the uncertainty associated with the result, <i>u_c the combined uncertainty</i> . The uncertainty is absolute and in the same units as the result.
(#s), Coverage Factor	The coverage factor defines the width of the confidence interval, 1, 2 or 3 standard deviations.
CRDL (RL)	Contractual Required Detection Limit as defined in the Client's Statement Of Work or TestAmerica "default" nominal detection limit. Often referred to the reporting level (RL)
Lc	Decision Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume associated with the sample. The Type I error probability is approximately 5%. $Lc = (1.645 * \sqrt{2 * (BkgndCnt / BkgndCntMin) / SCntMin}) * (ConvFct / (Eff * Yld * Abn * Vol) * IngrFct)$. For LSC methods the batch blank is used as a measure of the background variability. Lc cannot be calculated when the background count is zero.
Lot-Sample No	The number assigned by the LIMS software to track samples received on the same day for a given client. The sample number is a sequential number assigned to each sample in the Lot.
MDC MDA	Detection Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume with a Type I and II error probability of approximately 5%. $MDC = (4.65 * \sqrt{(BkgndCnt / BkgndCntMin) / SCntMin}) + 2.71 / SCntMin * (ConvFct / (Eff * Yld * Abn * Vol) * IngrFct)$. For LSC methods the batch blank is used as a measure of the background variability.
Primary Detector	The instrument identifier associated with the analysis of the sample aliquot.
Ratio U-234/U-238	The U-234 result divided by the U-238 result. The U-234/U-238 ratio for natural uranium in NIST SRM 4321C is 1.038.
Rst/MDC	Ratio of the Result to the MDC. A value greater than 1 may indicate activity above background at a high level of confidence. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Rst/TotUcert	Ratio of the Result to the Total Uncertainty. If the uncertainty has a coverage factor of 2 a value greater than 1 may indicate activity above background at approximately the 95% level of confidence assuming a two-sided confidence interval. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Report DB No	Sample Identifier used by the report system. The number is based upon the first five digits of the Work Order Number.
RER	The equation Replicate Error Ratio = $(S-D) / [\sqrt{TPUs^2 + TPUD^2}]$ as defined by ICPT BOA where S is the original sample result, D is the result of the duplicate, TPUs is the total uncertainty of the original sample and TPUD is the total uncertainty of the duplicate sample.
SDG	Sample Delivery Group Number assigned by the Client or assigned by TestAmerica upon sample receipt.
Sum Rpt Alpha Spec Rst(s)	The sum of the reported alpha spec results for tests derived from the same sample excluding duplicate result where the results are in the same units.
Work Order	The LIMS software assign test specific identifier.
Yield	The recovery of the tracer added to the sample such as Pu-242 used to trace a Pu-239/40 method.

Sample Results Summary

Date: 22-Dec-14

TestAmerica Inc TARL

Ordered by Method, Batch No., Client Sample ID.

Report No. : 63980

SDG No: 49002

Batch	Client Id Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	MDL	CRDL	RER2
4322035	RL-RA-001								
	AC-23D(400-98308-3)								
	M5JDL1AA Ra-226		2.51E+00 +- 6.2E-01		pCi/L	98%	1.93E-01	1.00E+00	
	AC-3D(400-98308-1)								
	M5JDJ1AA Ra-226		9.02E-01 +- 2.6E-01	J	pCi/L	99%	1.12E-01	1.00E+00	
	AC-3D(400-98308-1) DUP								
	M5JDJ1AD Ra-226		5.07E-01 +- 2.1E-01	J	pCi/L	83%	1.91E-01	1.00E+00	2.4
	AC-3S(400-98308-2)								
	M5JDK1AA Ra-226		3.00E-02 +- 8.2E-02	U	pCi/L	89%	1.64E-01	1.00E+00	
	DUP-3(400-98308-6)								
	M5JDP1AA Ra-226		1.24E-01 +- 8.4E-02	J	pCi/L	100%	1.20E-01	1.00E+00	
	NWD-2D(400-98308-5)								
	M5JDN1AA Ra-226		8.13E-01 +- 2.5E-01	J	pCi/L	95%	2.12E-01	1.00E+00	
	NWD-2S(400-98308-4)								
	M5JDM1AA Ra-226		3.39E-01 +- 1.6E-01	J	pCi/L	96%	1.85E-01	1.00E+00	
4322036	RL-RA-001								
	AC-23D(400-98308-3)								
	M5JDL1AC Ra-228		3.63E+00 +- 6.6E-01		pCi/L	86%	7.46E-01	1.00E+00	
	AC-3S(400-98308-2)								
	M5JDK1AC Ra-228		1.59E-01 +- 3.8E-01	U	pCi/L	85%	8.43E-01	1.00E+00	
	DUP-3(400-98308-6)								
	M5JDP1AC Ra-228		2.57E-01 +- 2.2E-01	U	pCi/L	95%	4.67E-01	1.00E+00	
	NWD-2D(400-98308-5)								
	M5JDN1AC Ra-228		9.66E-01 +- 3.2E-01	J	pCi/L	89%	5.04E-01	1.00E+00	
	NWD-2S(400-98308-4)								
	M5JDM1AC Ra-228		8.75E-01 +- 3.3E-01	J	pCi/L	87%	5.44E-01	1.00E+00	
4345065	RL-RA-001								
	AC-3D(400-98308-1)								
	M5JDJ2AC Ra-228		1.10E+01 +- 1.5E+00		pCi/L	73%	9.39E-01	1.00E+00	
	AC-3D(400-98308-1) DUP								
	M5JDJ2AE Ra-228		8.70E+00 +- 1.4E+00		pCi/L	53%	1.10E+00	1.00E+00	2.2
No. of Results: 14									

TestAmerica Inc
rptTALRchSaSum
mary2 V5.3.6.1
A2002

RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPUs)+sq(TPUD))] as defined by ICPT BOA.

J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

QC Results Summary
TestAmerica Inc TARL
 Ordered by Method, Batch No, QC Type,.

Date: 22-Dec-14

Report No. : 63980

SDG No.: 49002

Batch	Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	LCS Recovery	Bias	MDL
RL-RA-001									
4322035 BLANK QC,									
	M5JQ61AA	Ra-226	7.54E-03 +- 5.7E-02	U	pCi/L	88%			1.26E-01
4322035 LCS,									
	M5JQ61AC	Ra-226	1.06E+01 +- 2.5E+00		pCi/L	80%	106%	0.1	2.15E-01
RL-RA-001									
4322036 BLANK QC,									
	M5JQ71AA	Ra-228	2.35E-01 +- 2.5E-01	U	pCi/L	80%			5.36E-01
4322036 LCS,									
	M5JQ71AC	Ra-228	8.22E+00 +- 1.2E+00		pCi/L	74%	83%	-0.2	5.75E-01
RL-RA-001									
4345065 BLANK QC,									
	M5JQ72AA	Ra-228	3.48E-01 +- 4.0E-01	U	pCi/L	75%			8.67E-01
4345065 LCS,									
	M5JQ72AC	Ra-228	5.78E+00 +- 8.8E-01		pCi/L	89%	55%	-0.4	7.01E-01
No. of Results: 6									

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49002 Collection Date: 11/11/2014 1:00:00 PM
Lot-Sample No.: J4K170417-3 Report No.: 63980 Received Date: 11/13/2014 10:40:00 AM
Client Sample ID: AC-23D(400-98308-3) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4322035 RL-RA-001 2.51E+00 3.1E-01 6.2E-01 Work Order: M5JDL1AA Report DB ID: 9M5JDL10												
Ra-226					1.93E-01	pCi/L	98%	(13.)	12/8/14 05:44 p		0.9469	ASCGMB
						8.51E-02	1.00E+00	(8.1)			L	
Batch: 4322036 RL-RA-001 3.63E+00 5.1E-01 6.6E-01 Work Order: M5JDL1AC Report DB ID: 9M5JDL10												
Ra-228					7.46E-01	pCi/L	86%	(4.9)	12/11/14 12:16 p		0.9469	GPC1D
						3.47E-01	1.00E+00	(11.)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
V5.3.6.1 A2002

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 49002

Collection Date: 11/11/2014 9:38:00 AM

Lot-Sample No.: J4K1170417-1

Report No.: 63980

Received Date: 11/13/2014 10:40:00 AM

Client Sample ID: AC-3D(400-98308-1)

COC No.:

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4322035 RL-RA-001												
Work Order: M5JDJ1AA Report DB ID: 9M5JDJ10												
Ra-226	9.02E-01	J	1.7E-01	2.6E-01	1.12E-01	pCi/L	99%	(8.)	12/8/14 05:44 p		0.9204	ASC3MA
						4.69E-02	1.00E+00	(7.)			L	
Batch: 4345065 RL-RA-001												
Work Order: M5JDJ2AC Report DB ID: 9M5JDJ20												
Ra-228	1.10E+01		8.8E-01	1.5E+00	9.39E-01	pCi/L	73%	(11.7)	12/18/14 01:16 p		0.9204	GPC1A
						4.37E-01	1.00E+00	(14.6)			L	

No. of Results: 2

Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 49002

Collection Date: 11/11/2014 10:54:00 AM

Lot-Sample No.: J4K170417-2

Report No.: 63980

Received Date: 11/13/2014 10:40:00 AM

Client Sample ID: AC-3S(400-98308-2)

COC No.:

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4322035 RL-RA-001												
Work Order: M5JDK1AA Report DB ID: 9M5JDK10												
Ra-226	3.00E-02	U	8.1E-02	8.2E-02	1.64E-01	pCi/L	89%	0.18	12/8/14 05:44 p		0.942	ASCFRM
						7.18E-02	1.00E+00	0.73			L	
Batch: 4322036 RL-RA-001												
Work Order: M5JDK1AC Report DB ID: 9M5JDK10												
Ra-228	1.59E-01	U	3.3E-01	3.8E-01	8.43E-01	pCi/L	85%	0.19	12/11/14 12:16 p		0.942	GPC1C
						3.94E-01	1.00E+00	0.84			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 49002

Collection Date: 11/11/2014

Lot-Sample No.: J4K170417-6

Report No.: 63980

Received Date: 11/13/2014 10:40:00 AM

Client Sample ID: DUP-3(400-98308-6)

COC No.:

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4322035 RL-RA-001												
Work Order: M5JDP1AA Report DB ID: 9M5JDP10												
Ra-226	1.24E-01	J	7.9E-02	8.4E-02	1.20E-01	pCi/L	100%	(1.)	12/8/14 05:44 p		0.9455	ASCKMD
						5.07E-02	1.00E+00	(3.)			L	
Batch: 4322036 RL-RA-001												
Work Order: M5JDP1AC Report DB ID: 9M5JDP10												
Ra-228	2.57E-01	U	2.2E-01	2.2E-01	4.67E-01	pCi/L	95%	0.55	12/11/14 12:16 p		0.9455	GPC2C
						2.04E-01	1.00E+00	(2.3)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 49002

Collection Date: 11/11/2014 3:41:00 PM

Lot-Sample No.: J4K170417-5

Report No. : 63980

Received Date: 11/13/2014 10:40:00 AM

Client Sample ID: NWD-2D(400-98308-5)

COC No. :

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4322035 RL-RA-001												
Ra-226	8.13E-01	J	1.9E-01	2.5E-01	2.12E-01	pCi/L	95%	(3.8)	12/8/14 05:44 p		0.9292	ASCJMB
						9.46E-02	1.00E+00	(6.5)			L	
Batch: 4322036 RL-RA-001												
Ra-228	9.66E-01	J	3.0E-01	3.2E-01	5.04E-01	pCi/L	89%	(1.9)	12/11/14 12:16 p		0.9292	GPC2B
						2.21E-01	1.00E+00	(6.)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K170417-4
Client Sample ID: NWD-2S(400-98308-4)

SDG: 49002
Report No.: 63980
COC No.:
Collection Date: 11/11/2014 3:10:00 PM
Received Date: 11/13/2014 10:40:00 AM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4322035 RL-RA-001												
Work Order: M5JDM1AA Report DB ID: 9M5JDM10												
Ra-226	3.39E-01	J	1.4E-01	1.6E-01	1.85E-01	pCi/L	96%	(1.8)	12/8/14 05:45 p		0.9521	ASCHSB
						8.15E-02	1.00E+00	(4.3)			L	
Batch: 4322036 RL-RA-001												
Work Order: M5JDM1AC Report DB ID: 9M5JDM10												
Ra-228	8.75E-01	J	3.1E-01	3.3E-01	5.44E-01	pCi/L	87%	(1.6)	12/11/14 12:16 p		0.9521	GPC2A
						2.40E-01	1.00E+00	(5.3)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM II

Date: 22-Dec-14

DUPLICATE RESULTS

Lab Name: TestAmerica Inc SDG: 49002 Collection Date: 11/11/2014 9:38:00 AM
Lot-Sample No.: J4K170417-1 Report No.: 63980 Received Date: 11/13/2014 10:40:00 AM
Client Sample ID: AC-3D(400-98308-1) DUP COC No.: Matrix: WATER

Parameter	Result, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4322035 RL-RA-001 Work Order: M5JDJ1AD Report DB ID: M5JDJ1DR Orig Sa DB ID: 9M5JDJ10												
Ra-226	5.07E-01	J	1.6E-01	2.1E-01	1.91E-01	pCi/L	83%	(2.7)	12/8/14 05:44 p		0.9217	ASC9RA
	9.02E-01	J	RER2 2.4			1.00E+00		(4.9)			L	
Batch: 4345065 RL-RA-001 Work Order: M5JDJ2AE Report DB ID: M5JDJ2ER Orig Sa DB ID: 9M5JDJ20												
Ra-228	8.70E+00		9.3E-01	1.4E+00	1.10E+00	pCi/L	53%	(7.9)	12/18/14 01:16 p		0.9217	GPC1B
	1.10E+01		RER2 2.2			1.00E+00		(12.9)			L	

No. of Results: 2 Comments:

TestAmerica Inc RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPU_s+sq(TPU_d))] as defined by ICPT BOA.
MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.

FORM II
BLANK RESULTS

Date: 22-Dec-14

Lab Name: TestAmerica Inc SDG: 49002 Report No. : 63980
Matrix: WATER

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Lc	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4322035												
Ra-226	7.54E-03	U	5.7E-02	5.7E-02	1.26E-01	pCi/L	88%	0.06	12/8/14 05:53 p		1.0	ASCLMB
					5.26E-02	1.00E+00		0.26			L	
Batch: 4322036												
Ra-228	2.35E-01	U	2.4E-01	2.5E-01	5.36E-01	pCi/L	80%	0.44	12/11/14 12:16 p		1.0	GPC2D
					2.35E-01	1.00E+00		(1.9)			L	
Batch: 4345065												
Ra-228	3.48E-01	U	3.7E-01	4.0E-01	8.67E-01	pCi/L	75%	0.4	12/18/14 01:16 p		0.942	GPC1C
					4.03E-01	1.00E+00		(1.7)			L	
No. of Results: 3 Comments:												

TestAmerica Inc MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

UptSTLRchBlank
V5.3.6.1 A2002


FORM II
LCS RESULTS

Date: 22-Dec-14

Lab Name: TestAmerica Inc SDG: 49002
Matrix: WATER Report No.: 63980

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL	Report Unit	Yield	Expected	Expected Uncert	Recovery, Bias	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4322035 RL-RA-001 Work Order: M5JQ61AC Report DB ID: M5JQ61CS													
Ra-226	1.06E+01		6.0E-01	2.5E+00	2.15E-01	pCi/L	80%	9.97E+00	1.12E-01	106%	12/8/14 05:52 p	1.0021	ASCMAC
							Rec Limits:	75	125	0.1			
Batch: 4322036 RL-RA-001 Work Order: M5JQ71AC Report DB ID: M5JQ71CS													
Ra-228	8.22E+00		7.3E-01	1.2E+00	5.75E-01	pCi/L	74%	9.86E+00	1.13E-01	83%	12/11/14 12:11 p	1.0021	GPC3A
							Rec Limits:	75	125	-0.2			
Batch: 4345065 RL-RA-001 Work Order: M5JQ72AC Report DB ID: M5JQ72CS													
Ra-228	5.78E+00		5.8E-01	8.8E-01	7.01E-01	pCi/L	89%	1.05E+01	1.20E-01	55%	12/18/14 01:16 p	0.9469	GPC1D
							Rec Limits:	75	125	-0.4			
No. of Results: 3 Comments:													

Chain of Custody Record



Client Information (Sub Contract Lab)		Sampler:		Lab PWT: Saviole, Noel		Carrier Tracking No(s):		COC No: 400-65159-1	
Client Contact:		Phone:		E-Mail: noel.saviole@testamericainc.com		Page: Page 1 of 1		Job #: 400-98308-1	
Shipping/Receiving		Company:		TestAmerica Laboratories, Inc.		Analysis Requested		Preservation Codes:	
Address:		Due Date Requested:		11/25/2014		TAT Requested (days):		A - HCL M - Hexane N - None O - AsNaO2 P - Na2O4S Q - Na2SO3 R - Na2S2SO3 S - H2SO4 T - TSP Dodecahydrate U - Acetone V - MCAA W - ph 4-6 Z - other (specify)	
City:		PO #:		WO #:		Project #:		Total Number of Containers	
State, Zip:		509-375-3131(Tel) 509-375-5590(Fax)		64000434		SSOW#:		Special Instructions/Note:	
Phone:		Project Name:		Agrico Pensacola		Site:			
Email:		Sample Date		Sample Time		Sample Type (C=Comp, G=grab)		Matrix (W=water, S=solid, O=waste, BT=Tissue, A=Air)	
Sample Identification - Client ID (Lab ID)		Sample Date		Sample Time		Sample Type (C=Comp, G=grab)		Matrix (W=water, S=solid, O=waste, BT=Tissue, A=Air)	
AC-3D (400-98308-1)	11/11/14	09:38	Central	Water	X	X	X	3	M5JDJ
AC-3S (400-98308-2)	11/11/14	10:54	Central	Water	X	X	X	3	M5JDK
AC-23D (400-98308-3)	11/11/14	13:00	Central	Water	X	X	X	3	M5JDL
NWD-2S (400-98308-4)	11/11/14	15:10	Central	Water	X	X	X	3	M5JDM
NWD-2D (400-98308-5)	11/11/14	15:41	Central	Water	X	X	X	3	M5JDN
DUP-3 (400-98308-6)	11/11/14		Central	Water	X	X	X	3	M5JDP
Possible Hazard Identification									
Unconfirmed									
Deliverable Requested: I, II, III, IV, Other (specify)									
Sample Disposal (A fee may be assessed if samples are retained longer than 1 month)									
Return To Client									
Disposal By Lab									
Special Instructions/QC Requirements:									
Empty Kit Relinquished by:		Date:		Time:		Method of Shipment:			
Relinquished by: DCC		11-12-14		1600		Company: TH		Date/Time: 11/13/14	
Relinquished by:		Date/Time:				Company:		Date/Time:	
Relinquished by:		Date/Time:				Company:		Date/Time:	
Custody Seals Intact		Custody Seal No.:				Cooler Temperature(s) °C and Other Remarks:		J4K170417	

Sample Check-in List

Date/Time Received: 11/13/14 1040 Container GM Screen Result: (Airlock) 40 cpm Initials [J]
 Sample GM Screen Result (Sample Receiving) 40 cpm Initials [J]
 Client: STP SDG #: 49002 SAF #: _____ NA [J]
 Lot Number: J4K170417
 Chain of Custody # N/A

Shipping Container ID or Air Bill Number : _____ NA [J]

Samples received inside shipping container/cooler/box Yes [J] Continue with 1 through 4. Initial appropriate response.
 No [] Go to 5, add comment to #16.

1. Custody Seals on shipping container intact? Yes [J] No [] No Custody Seal []
2. Custody Seals dated and signed? Yes [J] No [] No Custody Seal []
3. Cooler temperature: _____ °C NA [J]
4. Vermiculite/packing materials is NA [J] Wet [] Dry []

Item 5 through 16 for samples. Initial appropriate response.

5. Chain of Custody record present? Yes [J] No []
6. Number of samples received (Each sample may contain multiple bottles): 6
7. Containers received: 27x1p 18x1p
JF 11/13/14
8. Sample holding times exceeded? NA [] Yes [] No [J]
9. Samples have: _____ tape _____ hazard labels _____ custody seals J appropriate sample labels
10. Matrix: _____ A (FLT, Wipe, Solid, Soil) J I (Water) _____ S (Air, Niosh 7400) _____ T (Biological, Ni-63)
11. Samples:
J are in good condition _____ are leaking _____ are broken
 _____ have air bubbles (Only for samples requiring no head space) _____ Other _____
12. Sample pH appropriate for analysis requested Yes [J] No [] NA []
 (If acidification is necessary go to pH area & document sample ID, initial pH, amount of HNO₃ added and pH after addition on table)
13. Were any anomalies identified in sample receipt? Yes [] No [J]
14. Description of anomalies (include sample numbers): NA [J] _____
15. Sample Location, Sample Collector Listed on COC? * Yes [] No [J]
 *For documentation only. No corrective action needed.
16. Additional Information: N/A

[] Client/Courier denied temperature check.

[] Client/Courier unpack cooler.

Sample Check-in List completed by Sample Custodian:

Signature: _____ Date: 11/13/14

Client Notification needed? Yes [] No [] Date: _____

By: _____

Person contacted: _____

[] No action necessary; process as is

Project Manager: J. Mayes

Date: 11/18/14

TestAmerica
A Division of TestAmerica, Inc.

1	2	3	4	5	6	7	8	9	10	11

TestAmerica

THE LEADER IN ENVIRONMENTAL TESTING

ANALYTICAL REPORT

TestAmerica Laboratories, Inc.

TestAmerica Pensacola

3355 McLemore Drive

Pensacola, FL 32514

Tel: (850)474-1001

TestAmerica Job ID: 400-98371-1

Client Project/Site: Agrico Pensacola

For:

URS Corporation

1625 Summit Lake Drive

Suite 200

Tallahassee, Florida 32317

Attn: Mr. Jeff Wagner



Authorized for release by:

12/17/2014 4:42:08 PM

Noel Savoie, Project Manager I

(850)878-3994

noel.savoie@testamericainc.com

LINKS

Review your project
results through

TotalAccess

Have a Question?



Visit us at:

www.testamericainc.com

The test results in this report meet all 2003 NELAC and 2009 TNI requirements for accredited parameters, exceptions are noted in this report. This report may not be reproduced except in full, and with written approval from the laboratory. For questions please contact the Project Manager at the e-mail address or telephone number listed on this page.

This report has been electronically signed and authorized by the signatory. Electronic signature is intended to be the legally binding equivalent of a traditionally handwritten signature.

Results relate only to the items tested and the sample(s) as received by the laboratory.

Table of Contents

Cover Page	1
Table of Contents	2
Definitions	3
Case Narrative	4
Sample Summary	5
Client Sample Results	6
QC Sample Results	8
Chronicle	12
Method Summary	14
Subcontract Data	15
Chain of Custody	33



Definitions/Glossary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Glossary

Abbreviation	These commonly used abbreviations may or may not be present in this report.
□	Listed under the "D" column to designate that the result is reported on a dry weight basis
%R	Percent Recovery
CFL	Contains Free Liquid
CNF	Contains no Free Liquid
DER	Duplicate error ratio (normalized absolute difference)
Dil Fac	Dilution Factor
DL, RA, RE, IN	Indicates a Dilution, Re-analysis, Re-extraction, or additional Initial metals/anion analysis of the sample
DLC	Decision level concentration
MDA	Minimum detectable activity
EDL	Estimated Detection Limit
MDC	Minimum detectable concentration
MDL	Method Detection Limit
ML	Minimum Level (Dioxin)
NC	Not Calculated
ND	Not detected at the reporting limit (or MDL or EDL if shown)
PQL	Practical Quantitation Limit
QC	Quality Control
RER	Relative error ratio
RL	Reporting Limit or Requested Limit (Radiochemistry)
RPD	Relative Percent Difference, a measure of the relative difference between two points
TEF	Toxicity Equivalent Factor (Dioxin)
TEQ	Toxicity Equivalent Quotient (Dioxin)

Case Narrative

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Job ID: 400-98371-1

Laboratory: TestAmerica Pensacola

Narrative

Job Narrative 400-98371-1

Comments

No additional comments.

Receipt

The samples were received on 11/12/2014 5:25 PM; the samples arrived in good condition, properly preserved and, where required, on ice. The temperatures of the 2 coolers at receipt time were 4.3° C and 5.2° C.

Except:

The following samples were submitted for analysis; however, it was not listed on the Chain-of-Custody (COC): ACB-31S (400-98371-5) and EQ-1 (400-98371-6). Client requested we proceed with analyses.

HPLC/IC

Method 300.0: The following sample was diluted to bring the concentration of target analytes within the calibration range: AC-2S (400-98371-3). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Metals

No analytical or quality issues were noted, other than those described in the Definitions/Glossary page.

General Chemistry

Method 353.2: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-5D (400-98371-1), AC-5S (400-98371-2), AC-2S (400-98371-3), AC-2D (400-98371-4), and ACB-31S (400-98371-5). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Subcontract Work

Methods Radium 226 by EPA Method 903.1, Radium 228 by EPA Method 904.0: These methods were subcontracted to TestAmerica Richland. Report attached.

Sample Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Lab Sample ID	Client Sample ID	Matrix	Collected	Received
400-98371-1	AC-5D	Water	11/12/14 09:39	11/12/14 17:25
400-98371-2	AC-5S	Water	11/12/14 10:09	11/12/14 17:25
400-98371-3	AC-2S	Water	11/12/14 13:23	11/12/14 17:25
400-98371-4	AC-2D	Water	11/12/14 14:18	11/12/14 17:25
400-98371-5	ACB-31S	Water	11/12/14 16:34	11/12/14 17:25
400-98371-6	EQ-1	Water	11/12/14 11:30	11/12/14 17:25

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Client Sample ID: AC-5D

Date Collected: 11/12/14 09:39

Date Received: 11/12/14 17:25

Lab Sample ID: 400-98371-1

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	7.0		1.0		mg/L			11/25/14 19:59	1
Sulfate	1.4		1.0		mg/L			11/25/14 19:59	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/19/14 16:44	1
Nitrate Nitrite as N	2.8		0.25		mg/L			11/21/14 13:43	5
Nitrate as N	2.8		0.050		mg/L			11/21/14 13:43	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 08:44	1

Client Sample ID: AC-5S

Date Collected: 11/12/14 10:09

Date Received: 11/12/14 17:25

Lab Sample ID: 400-98371-2

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	9.0		1.0		mg/L			11/25/14 20:22	1
Sulfate	24		1.0		mg/L			11/25/14 20:22	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/19/14 16:54	1
Nitrate Nitrite as N	4.5		0.25		mg/L			11/21/14 13:49	5
Nitrate as N	4.5		0.050		mg/L			11/21/14 13:49	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 08:44	1

Client Sample ID: AC-2S

Date Collected: 11/12/14 13:23

Date Received: 11/12/14 17:25

Lab Sample ID: 400-98371-3

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	4.2		1.0		mg/L			11/25/14 20:45	1
Sulfate	73		5.0		mg/L			11/26/14 14:25	5

Method: 6010C - Metals (ICP) - Total Recoverable

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Arsenic	0.020		0.0050		mg/L		11/14/14 09:32	11/14/14 19:24	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	34		0.50		mg/L			11/19/14 17:08	5
Nitrate Nitrite as N	3.1		0.10		mg/L			11/24/14 10:08	2
Nitrate as N	3.1		0.050		mg/L			11/24/14 10:08	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 08:44	1

TestAmerica Pensacola

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Client Sample ID: AC-2D

Lab Sample ID: 400-98371-4

Date Collected: 11/12/14 14:18

Matrix: Water

Date Received: 11/12/14 17:25

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	6.8		1.0		mg/L			11/25/14 21:54	1
Sulfate	16		1.0		mg/L			11/25/14 21:54	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	2.2		0.10		mg/L			11/19/14 17:01	1
Nitrate Nitrite as N	2.0		0.10		mg/L			11/24/14 10:09	2
Nitrate as N	2.0		0.050		mg/L			11/24/14 10:09	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 08:44	1

Client Sample ID: ACB-31S

Lab Sample ID: 400-98371-5

Date Collected: 11/12/14 16:34

Matrix: Water

Date Received: 11/12/14 17:25

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	2.1		1.0		mg/L			11/25/14 22:16	1
Sulfate	37		1.0		mg/L			11/25/14 22:16	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/19/14 17:11	1
Nitrate Nitrite as N	2.4		0.10		mg/L			11/24/14 10:10	2
Nitrate as N	2.4		0.050		mg/L			11/24/14 10:10	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 08:44	1

Client Sample ID: EQ-1

Lab Sample ID: 400-98371-6

Date Collected: 11/12/14 11:30

Matrix: Water

Date Received: 11/12/14 17:25

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			11/26/14 09:27	1
Sulfate	<1.0		1.0		mg/L			11/26/14 09:27	1

Method: 6010C - Metals (ICP) - Total Recoverable

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Arsenic	<0.0050		0.0050		mg/L		11/14/14 09:32	11/14/14 19:27	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/19/14 17:14	1
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/24/14 10:11	1
Nitrate as N	<0.050		0.050		mg/L			11/24/14 10:11	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 08:44	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Method: 300.0 - Anions, Ion Chromatography

Lab Sample ID: MB 400-237963/4

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			11/25/14 12:44	1
Sulfate	<1.0		1.0		mg/L			11/25/14 12:44	1

Lab Sample ID: MB 400-237963/45

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Sulfate	<1.0		1.0		mg/L			11/26/14 13:16	1

Lab Sample ID: LCS 400-237963/46

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Sulfate	10.0	9.67		mg/L		97	90 - 110

Lab Sample ID: LCS 400-237963/5

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	10.5		mg/L		105	90 - 110
Sulfate	10.0	9.32		mg/L		93	90 - 110

Lab Sample ID: LCSD 400-237963/47

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Sulfate	10.0	9.54		mg/L		95	90 - 110	1	15

Lab Sample ID: LCSD 400-237963/6

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	10.6		mg/L		106	90 - 110	1	15
Sulfate	10.0	9.29		mg/L		93	90 - 110	0	15

Method: 6010C - Metals (ICP)

Lab Sample ID: MB 400-236712/1-A

Matrix: Water

Analysis Batch: 236976

Client Sample ID: Method Blank

Prep Type: Total Recoverable

Prep Batch: 236712

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Arsenic	<0.0050		0.0050		mg/L		11/14/14 09:32	11/14/14 18:12	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Method: 6010C - Metals (ICP) (Continued)

Lab Sample ID: LCS 400-236712/2-A

Matrix: Water

Analysis Batch: 236976

Client Sample ID: Lab Control Sample

Prep Type: Total Recoverable

Prep Batch: 236712

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Arsenic	1.00	1.06		mg/L		106	80 - 120

Lab Sample ID: 400-98371-6 MS

Matrix: Water

Analysis Batch: 236976

Client Sample ID: EQ-1

Prep Type: Total Recoverable

Prep Batch: 236712

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Arsenic	<0.0050		1.00	1.00		mg/L		100	75 - 125

Method: 340.2 - Fluoride

Lab Sample ID: MB 400-237352/3

Matrix: Water

Analysis Batch: 237352

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/19/14 16:02	1

Lab Sample ID: LCS 400-237352/4

Matrix: Water

Analysis Batch: 237352

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.30		mg/L		108	90 - 110

Lab Sample ID: 400-98371-1 DU

Matrix: Water

Analysis Batch: 237352

Client Sample ID: AC-5D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	DU Result	DU Qualifier	Unit	D	RPD	Limit
Fluoride	<0.10		<0.10		mg/L		NC	4

Method: 353.2 - Nitrogen, Nitrate-Nitrite

Lab Sample ID: MB 400-237601/46

Matrix: Water

Analysis Batch: 237601

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/21/14 13:18	1

Lab Sample ID: LCS 400-237601/47

Matrix: Water

Analysis Batch: 237601

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.530		mg/L		106	90 - 110

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Method: 353.2 - Nitrogen, Nitrate-Nitrite (Continued)

Lab Sample ID: MRL 400-237601/12

Matrix: Water

Analysis Batch: 237601

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	<0.050		mg/L		87	50 - 150

Lab Sample ID: MB 400-237769/14

Matrix: Water

Analysis Batch: 237769

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/24/14 09:52	1

Lab Sample ID: MB 400-237769/48

Matrix: Water

Analysis Batch: 237769

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/24/14 10:36	1

Lab Sample ID: LCS 400-237769/15

Matrix: Water

Analysis Batch: 237769

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.469		mg/L		94	90 - 110

Lab Sample ID: LCS 400-237769/49

Matrix: Water

Analysis Batch: 237769

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.531		mg/L		106	90 - 110

Lab Sample ID: MRL 400-237769/12

Matrix: Water

Analysis Batch: 237769

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	<0.050		mg/L		87	50 - 150

Method: SM 4500 NO2 B - Nitrogen, Nitrite

Lab Sample ID: MB 400-236885/6

Matrix: Water

Analysis Batch: 236885

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/13/14 08:06	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Method: SM 4500 NO2 B - Nitrogen, Nitrite (Continued)

Lab Sample ID: MB 400-236885/66

Matrix: Water

Analysis Batch: 236885

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/13/14 15:01	1

Lab Sample ID: LCS 400-236885/7

Matrix: Water

Analysis Batch: 236885

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.278		mg/L		93	90 - 110

Lab Sample ID: LCS 400-236885/81

Matrix: Water

Analysis Batch: 236885

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.279		mg/L		93	90 - 110

Lab Sample ID: MRL 400-236885/3

Matrix: Water

Analysis Batch: 236885

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.100	<0.10		mg/L		97	50 - 150

Lab Sample ID: 400-98371-1 MS

Matrix: Water

Analysis Batch: 236885

Client Sample ID: AC-5D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	<0.10		0.100	<0.10		mg/L		99	80 - 118

Lab Sample ID: 400-98371-1 MSD

Matrix: Water

Analysis Batch: 236885

Client Sample ID: AC-5D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Nitrite as N	<0.10		0.100	<0.10		mg/L		98	80 - 118	1	9

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Client Sample ID: AC-5D

Date Collected: 11/12/14 09:39

Date Received: 11/12/14 17:25

Lab Sample ID: 400-98371-1

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/25/14 19:59	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 16:44	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237601	11/21/14 13:43	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237608	11/21/14 13:43	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 08:44	LSS	TAL PEN

Client Sample ID: AC-5S

Date Collected: 11/12/14 10:09

Date Received: 11/12/14 17:25

Lab Sample ID: 400-98371-2

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/25/14 20:22	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 16:54	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237601	11/21/14 13:49	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237608	11/21/14 13:49	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 08:44	LSS	TAL PEN

Client Sample ID: AC-2S

Date Collected: 11/12/14 13:23

Date Received: 11/12/14 17:25

Lab Sample ID: 400-98371-3

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/25/14 20:45	TAJ	TAL PEN
Total/NA	Analysis	300.0		5	237963	11/26/14 14:25	TAJ	TAL PEN
Total Recoverable	Prep	3005A			236712	11/14/14 09:32	DN1	TAL PEN
Total Recoverable	Analysis	6010C		1	236976	11/14/14 19:24	SLM	TAL PEN
Total/NA	Analysis	340.2		5	237352	11/19/14 17:08	SLT	TAL PEN
Total/NA	Analysis	353.2		2	237769	11/24/14 10:08	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:08	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 08:44	LSS	TAL PEN

Client Sample ID: AC-2D

Date Collected: 11/12/14 14:18

Date Received: 11/12/14 17:25

Lab Sample ID: 400-98371-4

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/25/14 21:54	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 17:01	SLT	TAL PEN
Total/NA	Analysis	353.2		2	237769	11/24/14 10:09	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:09	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 08:44	LSS	TAL PEN

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Client Sample ID: ACB-31S

Date Collected: 11/12/14 16:34

Date Received: 11/12/14 17:25

Lab Sample ID: 400-98371-5

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/25/14 22:16	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 17:11	SLT	TAL PEN
Total/NA	Analysis	353.2		2	237769	11/24/14 10:10	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:10	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 08:44	LSS	TAL PEN

Client Sample ID: EQ-1

Date Collected: 11/12/14 11:30

Date Received: 11/12/14 17:25

Lab Sample ID: 400-98371-6

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/26/14 09:27	TAJ	TAL PEN
Total Recoverable	Prep	3005A			236712	11/14/14 09:32	DN1	TAL PEN
Total Recoverable	Analysis	6010C		1	236976	11/14/14 19:27	SLM	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 17:14	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237769	11/24/14 10:11	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:11	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 08:44	LSS	TAL PEN

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Method Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98371-1

Method	Method Description	Protocol	Laboratory
300.0	Anions, Ion Chromatography	MCAWW	TAL PEN
6010C	Metals (ICP)	SW846	TAL PEN
340.2	Fluoride	MCAWW	TAL PEN
353.2	Nitrogen, Nitrate-Nitrite	MCAWW	TAL PEN
Nitrate by calc	Nitrogen, Nitrate	SM	TAL PEN
SM 4500 NO2 B	Nitrogen, Nitrite	SM	TAL PEN
Rad 226-Method 903.1 (Richland)	RAD-226 (RCH)	NONE	TAL RCH
Rad 228-Method 904.0 (Richland)	RAD-228 (RCH)	NONE	TAL RCH

Protocol References:

MCAWW = "Methods For Chemical Analysis Of Water And Wastes", EPA-600/4-79-020, March 1983 And Subsequent Revisions.

NONE = NONE

SM = "Standard Methods For The Examination Of Water And Wastewater",

SW846 = "Test Methods For Evaluating Solid Waste, Physical/Chemical Methods", Third Edition, November 1986 And Its Updates.

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Analytical Data Package Prepared For

TestAmerica Pensacola

Radiochemical Analysis By

TestAmerica Inc

2800 G.W. Way, Richland Wa, 99354, (509)-375-3131.

Assigned Laboratory Code: TARL

Data Package Contains _____ Pages

Report No.: 63866

Results in this report relate only to the sample(s) analyzed.

SDG No.	Order No.	Client Sample ID (List Order)	Lot-Sa No.	Work Order	Report DB ID	Batch No.
48996		AC-2D(400-98371-4)	J4K140427-4	M5H4W1AA	9M5H4W10	4321032
		AC-2D(400-98371-4)	J4K140427-4	M5H4W1AC	9M5H4W10	4321033
		AC-2S(400-98371-3)	J4K140427-3	M5H4V1AA	9M5H4V10	4321032
		AC-2S(400-98371-3)	J4K140427-3	M5H4V1AC	9M5H4V10	4321033
		AC-5D(400-98371-1)	J4K140427-1	M5H4R1AA	9M5H4R10	4321032
		AC-5D(400-98371-1)	J4K140427-1	M5H4R1AC	9M5H4R10	4321033
		AC-5S(400-98371-2)	J4K140427-2	M5H4T1AA	9M5H4T10	4321032
		AC-5S(400-98371-2)	J4K140427-2	M5H4T1AC	9M5H4T10	4321033
		ACB-31S(400-98371-5)	J4K140427-5	M5H4X1AA	9M5H4X10	4321032
		ACB-31S(400-98371-5)	J4K140427-5	M5H4X1AC	9M5H4X10	4321033
		EQ-1(400-98371-6)	J4K140427-6	M5H401AA	9M5H4010	4321032
		EQ-1(400-98371-6)	J4K140427-6	M5H401AC	9M5H4010	4321033

Certificate of Analysis

December 12, 2014

TestAmerica Pensacola
3355 McLemore Drive
Pensacola, FL 32514

Attention: Noel Savoie

Date Received at Lab	:	November 14, 2014
Project Name/Number	:	Agrico Pensacola/64000434
Sample Type	:	Six (6) Water
Job Number	:	400-98371-1
SDG Number	:	48996

CASE NARRATIVE

I. Introduction

On November 14, 2014, six water samples were received at TestAmerica's Richland laboratory for radiochemical analysis. Upon receipt, the samples were assigned the TestAmerica identification number as described on the cover page of the Analytical Data Package report form. The samples were assigned to Lot Numbers J4K140427.

II. Sample Receipt

The samples were received in good condition and no anomalies were noted upon check-in.

III. Analytical Results/Methodology

The analytical results for this report are presented by laboratory sample ID. Each set of data includes sample identification information; analytical results and the appropriate associated statistical uncertainties.

The analysis requested was:

Gas Proportional Counting

Radium-228 by method RL-RA-001

Alpha Scintillation Counting

Radium-226 by method RL-RA-001

IV. Quality Control

The analytical result for each analysis performed includes a minimum of one laboratory control sample (LCS), and one reagent blank sample analysis. Any exceptions have been noted in the Comments” section.

V. Comments

Gas Proportional Counting

Radium-228

The LCS, batch blank, sample duplicate and sample results are within acceptance limits.

Alpha Scintillation Counting

Radium 226:

The LCS, batch blank, samples and sample duplicate results are within acceptance limits.

I certify that this Certificate of Analysis is in compliance with the SOW and/or NELAC, both technically and for completeness, for other than the conditions detailed above. The Laboratory Manager or a designee, as verified by the following signature has authorized release of the data contained in this hard copy data package.

Reviewed and approved:

Robin Ebert-Mays
Project Manager

Drinking Water Method Cross References

DRINKING WATER ASTM METHOD CROSS REFERENCES		
Referenced Method	Isotope(s)	TestAmerica Richland's SOP No.
EPA 901.1	Cs-134, I-131	RL-GAM-001
EPA 900.0	Alpha & Beta	RL-GPC-001
EPA 00-02	Gross Alpha (Coprecipitation)	RL-GPC-002
EPA 903.0	Total Alpha Radium (Ra-226)	RL-RA-002
EPA 903.1	Ra-226	RL-RA-001
EPA 904.0	Ra-228	RL-RA-001
EPA 905.0	Sr-89/90	RL-GPC-003
ASTM D5174	Uranium	RL-KPA-003
EPA 906.0	Tritium	RL-LSC-005

Results in this report relate only to the sample(s) analyzed.

Uncertainty Estimation

TestAmerica Richland has adopted the internationally accepted approach to estimating uncertainties described in "NIST Technical Note 1297, 1994 Edition". The approach, "Law of Propagation of Errors", involves the identification of all variables in an analytical method which are used to derive a result. These variables are related to the analytical result (R) by some functional relationship, $R = \text{constants} * f(x,y,z,...)$. The components (x,y,z) are evaluated to determine their contribution to the overall method uncertainty. The individual component uncertainties (u_i) are then combined using a statistical model that provides the most probable overall uncertainty value. All component uncertainties are categorized as type A, evaluated by statistical methods, or type B, evaluated by other means. Uncertainties not included in the components, such as sample homogeneity, are combined with the component uncertainty as the square root of the sum-of-the-squares of the individual uncertainties. The uncertainty associated with the derived result is the combined uncertainty (u_c) multiplied by the coverage factor (1,2, or 3).

When three or more sample replicates are used to derive the analytical result, the type A uncertainty is the standard deviation of the mean value ($S/\sqrt{n}$), where S is the standard deviation of the derived results. The type B uncertainties are all other random or non-random components that are not included in the standard deviation.

The derivation of the general "Law of Propagation of Errors" equations and specific example are available on request.

Report Definitions

Action Lev	An agreed upon activity level used to trigger some action when the final result is greater than or equal to the Action Level. Often the Action Level is related to the Decision Limit.
Batch	The QC preparation batch number that relates laboratory samples to QC samples that were prepared and analyzed together.
Bias	Defined by the equation (Result/Expected)-1 as defined by ANSI N13.30.
COC No	Chain of Custody Number assigned by the Client or TestAmerica.
Count Error (#s)	Poisson counting statistics of the gross sample count and background. The uncertainty is absolute and in the same units as the result. For Liquid Scintillation Counting (LSC) the batch blank count is the background.
Total Uncert (#s) <i>u_c - Combined Uncertainty.</i>	All known uncertainties associated with the preparation and analysis of the sample are propagated to give a measure of the uncertainty associated with the result, <i>u_c the combined uncertainty</i> . The uncertainty is absolute and in the same units as the result.
(#s), Coverage Factor	The coverage factor defines the width of the confidence interval, 1, 2 or 3 standard deviations.
CRDL (RL)	Contractual Required Detection Limit as defined in the Client's Statement Of Work or TestAmerica "default" nominal detection limit. Often referred to the reporting level (RL)
Lc	Decision Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume associated with the sample. The Type I error probability is approximately 5%. $Lc = (1.645 * \sqrt{2 * (BkgndCnt / BkgndCntMin) / SCntMin}) * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability. Lc cannot be calculated when the background count is zero.
Lot-Sample No	The number assigned by the LIMS software to track samples received on the same day for a given client. The sample number is a sequential number assigned to each sample in the Lot.
MDC MDA	Detection Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume with a Type I and II error probability of approximately 5%. $MDC = (4.65 * \sqrt{(BkgndCnt / BkgndCntMin) / SCntMin}) + 2.71 / SCntMin * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability.
Primary Detector	The instrument identifier associated with the analysis of the sample aliquot.
Ratio U-234/U-238	The U-234 result divided by the U-238 result. The U-234/U-238 ratio for natural uranium in NIST SRM 4321C is 1.038.
Rst/MDC	Ratio of the Result to the MDC. A value greater than 1 may indicate activity above background at a high level of confidence. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Rst/TotUcert	Ratio of the Result to the Total Uncertainty. If the uncertainty has a coverage factor of 2 a value greater than 1 may indicate activity above background at approximately the 95% level of confidence assuming a two-sided confidence interval. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Report DB No	Sample Identifier used by the report system. The number is based upon the first five digits of the Work Order Number.
RER	The equation Replicate Error Ratio = $(S-D) / [\sqrt{TPUs^2 + TPUD^2}]$ as defined by ICPT BOA where S is the original sample result, D is the result of the duplicate, TPUs is the total uncertainty of the original sample and TPUD is the total uncertainty of the duplicate sample.
SDG	Sample Delivery Group Number assigned by the Client or assigned by TestAmerica upon sample receipt.
Sum Rpt Alpha Spec Rst(s)	The sum of the reported alpha spec results for tests derived from the same sample excluding duplicate result where the results are in the same units.
Work Order	The LIMS software assign test specific identifier.
Yield	The recovery of the tracer added to the sample such as Pu-242 used to trace a Pu-239/40 method.

Sample Results Summary

Date: 12-Dec-14

TestAmerica Inc TARL

Ordered by Method, Batch No., Client Sample ID.

Report No. : 63866

SDG No: 48996

Batch	Client Id Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	MDL	CRDL	RER2
4321032	RL-RA-001								
	AC-2D(400-98371-4)								
	M5H4W1AA Ra-226		9.11E-01 +- 2.5E-01	J	pCi/L	96%	1.88E-01	1.00E+00	
	AC-2S(400-98371-3)								
	M5H4V1AA Ra-226		9.51E-02 +- 1.0E-01	U	pCi/L	91%	1.89E-01	1.00E+00	
	AC-5D(400-98371-1)								
	M5H4R1AA Ra-226		6.60E-01 +- 1.9E-01	J	pCi/L	100%	1.54E-01	1.00E+00	
	AC-5S(400-98371-2)								
	M5H4T1AA Ra-226		5.96E-01 +- 2.1E-01	J	pCi/L	82%	1.80E-01	1.00E+00	
	AC-8D(400-98418-1) DUP								
	M5H411AD Ra-226		7.27E-01 +- 2.3E-01	J	pCi/L	98%	1.62E-01	1.00E+00	4.0
	ACB-31S(400-98371-5)								
	M5H4X1AA Ra-226		4.30E-01 +- 1.7E-01	J	pCi/L	95%	2.10E-01	1.00E+00	
	EQ-1(400-98371-6)								
	M5H401AA Ra-226		-5.78E-02 +- 8.0E-02	U	pCi/L	85%	1.91E-01	1.00E+00	
4321033	RL-RA-001								
	AC-2D(400-98371-4)								
	M5H4W1AC Ra-228		1.31E+00 +- 4.5E-01		pCi/L	81%	7.92E-01	1.00E+00	
	AC-2S(400-98371-3)								
	M5H4V1AC Ra-228		3.09E-01 +- 4.0E-01	U	pCi/L	83%	8.68E-01	1.00E+00	
	AC-5D(400-98371-1)								
	M5H4R1AC Ra-228		1.44E+00 +- 5.0E-01		pCi/L	74%	8.84E-01	1.00E+00	
	AC-5S(400-98371-2)								
	M5H4T1AC Ra-228		1.32E+00 +- 4.8E-01		pCi/L	71%	8.58E-01	1.00E+00	
	AC-8D(400-98418-1) DUP								
	M5H411AE Ra-228		1.28E+00 +- 3.8E-01		pCi/L	87%	5.34E-01	1.00E+00	0.5
	ACB-31S(400-98371-5)								
	M5H4X1AC Ra-228		4.59E+00 +- 7.9E-01		pCi/L	79%	6.12E-01	1.00E+00	
	EQ-1(400-98371-6)								
	M5H401AC Ra-228		6.36E-02 +- 2.6E-01	U	pCi/L	76%	6.07E-01	1.00E+00	
No. of Results: 14									

TestAmerica Inc
rptTALRchSaSum
mary2 V5.3.6.1
A2002

RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPUs)+sq(TPUD))] as defined by ICPT BOA.

J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

QC Results Summary
TestAmerica Inc TARL
 Ordered by Method, Batch No, QC Type,.

Date: 12-Dec-14

Report No. : 63866

SDG No.: 48996

Batch	Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	LCS Recovery	Bias	MDL
RL-RA-001									
4321032 BLANK QC,									
	M5JDW1AA	Ra-226	6.84E-02 +- 9.1E-02	U	pCi/L	75%			1.66E-01
4321032 LCS,									
	M5JDW1AC	Ra-226	1.13E+01 +- 2.3E+00		pCi/L	86%	113%	0.1	1.62E-01
RL-RA-001									
4321033 BLANK QC,									
	M5JDX1AA	Ra-228	3.32E-02 +- 2.8E-01	U	pCi/L	70%			6.78E-01
4321033 LCS,									
	M5JDX1AC	Ra-228	1.10E+01 +- 1.4E+00		pCi/L	81%	111%	0.1	8.07E-01
No. of Results: 4									

FORM I

Date: 12-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 48996 Collection Date: 11/12/2014 2:18:00 PM
Lot-Sample No.: J4K140427-4 Report No.: 63866 Received Date: 11/14/2014 11:00:00 AM
Client Sample ID: AC-2D(400-98371-4) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001 9.11E-01 J 1.7E-01 2.5E-01 M5H4W1AA 8.61E-02 96% (4.9) 12/9/14 07:09 p 0.9492 ASC5HA												
Work Order: M5H4W1AA Report DB ID: 9M5H4W10 1.00E+00 (7.3)												
Batch: 4321033 RL-RA-001 1.31E+00 4.2E-01 4.5E-01 7.92E-01 pCi/L 81% (1.7) 12/11/14 03:48 p 0.9492 GPC1D												
Work Order: M5H4W1AC Report DB ID: 9M5H4W10 1.00E+00 (5.8)												
3.68E-01 1.00E+00 (5.8)												

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 12-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 48996

Collection Date: 11/12/2014 1:23:00 PM

Lot-Sample No.: J4K140427-3

Report No.: 63866

Received Date: 11/14/2014 11:00:00 AM

Client Sample ID: AC-2S(400-98371-3)

COC No.:

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001												
Work Order: M5H4V1AA Report DB ID: 9M5H4V10												
Ra-226	9.51E-02	U	1.0E-01	1.0E-01	1.89E-01	pCi/L	91%	0.5	12/9/14 07:09 p		0.9405	ASC4UA
						8.56E-02	1.00E+00	(1.8)			L	
Batch: 4321033 RL-RA-001												
Work Order: M5H4V1AC Report DB ID: 9M5H4V10												
Ra-228	3.09E-01	U	3.7E-01	4.0E-01	8.68E-01	pCi/L	83%	0.36	12/11/14 03:48 p		0.9405	GPC1C
						4.06E-01	1.00E+00	(1.5)			L	

No. of Results: 2

Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 12-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 48996

Collection Date: 11/12/2014 9:39:00 AM

Lot-Sample No.: J4K140427-1

Report No.: 63866

Received Date: 11/14/2014 11:00:00 AM

Client Sample ID: AC-5D(400-98371-1)

COC No.:

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001												
Ra-226	6.60E-01	J	1.4E-01	1.9E-01	1.54E-01	pCi/L	100%	(4.3)	12/9/14 07:09 p		0.946	ASC1RH
							Report DB ID: 9M5H4R10				L	
Batch: 4321033 RL-RA-001												
Ra-228	1.44E+00		4.7E-01	5.0E-01	8.84E-01	pCi/L	74%	(1.6)	12/11/14 03:48 p		0.946	GPC1A
							Report DB ID: 9M5H4R10				L	

No. of Results: 2

Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 12-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 48996

Collection Date: 11/12/2014 10:09:00 AM

Lot-Sample No.: J4K140427-2

Report No.: 63866

Received Date: 11/14/2014 11:00:00 AM

Client Sample ID: AC-5S(400-98371-2)

COC No.:

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001												
Work Order: M5H4T1AA Report DB ID: 9M5H4T10												
Ra-226	5.96E-01	J	1.7E-01	2.1E-01	1.80E-01	pCi/L	82%	(3.3)	12/9/14 07:09 p		0.9346	ASC3RA
						7.77E-02	1.00E+00	(5.7)			L	
Batch: 4321033 RL-RA-001												
Work Order: M5H4T1AC Report DB ID: 9M5H4T10												
Ra-228	1.32E+00		4.5E-01	4.8E-01	8.58E-01	pCi/L	71%	(1.5)	12/11/14 03:48 p		0.9346	GPC1B
						3.97E-01	1.00E+00	(5.5)			L	
No. of Results: 2 Comments:												

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 12-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K140427-5
Client Sample ID: ACB-31S(400-98371-5)

SDG: 48996
Report No.: 63866
COC No.:
Collection Date: 11/12/2014 4:34:00 PM
Received Date: 11/14/2014 11:00:00 AM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001												
Work Order: M5H4X1AA Report DB ID: 9M5H4X10												
Ra-226	4.30E-01	J	1.5E-01	1.7E-01	2.10E-01	pCi/L	95%	(2.)	12/9/14 07:09 p		0.938	ASC7RH
						9.45E-02	1.00E+00	(4.9)			L	
Batch: 4321033 RL-RA-001												
Work Order: M5H4X1AC Report DB ID: 9M5H4X10												
Ra-228	4.59E+00		5.8E-01	7.9E-01	6.12E-01	pCi/L	79%	(7.5)	12/11/14 03:48 p		0.938	GPC2A
						2.70E-01	1.00E+00	(11.6)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 12-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 48996

Collection Date: 11/12/2014 11:30:00 AM

Lot-Sample No.: J4K140427-6

Report No.: 63866

Received Date: 11/14/2014 11:00:00 AM

Client Sample ID: EQ-1(400-98371-6)

COC No.:

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001												
Work Order: M5H401AA Report DB ID: 9M5H4010												
Ra-226	-5.78E-02	U	7.9E-02	8.0E-02	1.91E-01	pCi/L	85%	-0.3	12/9/14 07:00 p		0.9038	ASC8HD
						8.50E-02	1.00E+00	-(1.4)			L	
Batch: 4321033 RL-RA-001												
Work Order: M5H401AC Report DB ID: 9M5H4010												
Ra-228	6.36E-02	U	1.9E-01	2.6E-01	6.07E-01	pCi/L	76%	0.1	12/11/14 03:48 p		0.9038	GPC2B
						2.66E-01	1.00E+00	0.49			L	

No. of Results: 2

Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM II

Date: 12-Dec-14

DUPLICATE RESULTS

Lab Name: TestAmerica Inc SDG: 48997 Collection Date: 11/13/2014 8:20:00 AM
 Lot-Sample No.: J4K140428-1 Report No.: 63866 Received Date: 11/14/2014 11:00:00 AM
 Client Sample ID: AC-8D(400-98418-1) DUP COC No.: Matrix: WATER

Parameter	Result, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001 Work Order: M5H411AD Report DB ID: M5H411DR Orig Sa DB ID: 9M5H4110												
Ra-226	7.27E-01	J	1.6E-01	2.3E-01	1.62E-01	pCi/L	98%	(4.5)	12/9/14 07:08 p	0.9291	L	ASCASC
	2.07E-01	J	RER2 4.0			1.00E+00		(6.2)				
Batch: 4321033 RL-RA-001 Work Order: M5H411AE Report DB ID: M5H411ER Orig Sa DB ID: 9M5H4110												
Ra-228	1.28E+00		3.4E-01	3.8E-01	5.34E-01	pCi/L	87%	(2.4)	12/11/14 03:48 p	0.9291	L	GPC2D
	1.14E+00		RER2 0.5			1.00E+00		(6.8)				

No. of Results: 2 Comments:

TestAmerica Inc RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPU_s)+sq(TPU_d))] as defined by ICPT BOA.
 rptSTLRchDupV5. MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
 3.6.1 A2002 J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.



Date: 12-Dec-14

SDG: 48996
Report No.: 63866

No. of Results:	2	Comments:

FORM II
LCS RESULTS

Date: 12-Dec-14

Lab Name: TestAmerica Inc SDG: 48996
Matrix: WATER Report No.: 63866

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL	Report Unit	Yield	Expected	Expected Uncert	Recovery, Bias	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001 Work Order: M5JDW1AC Report DB ID: M5JDW1CS													
Ra-226	1.13E+01		6.0E-01	2.3E+00	1.62E-01	pCi/L	86%	9.98E+00	1.13E-01	113%	12/9/14 07:35 p	1.0004	ASCPMA
							Rec Limits:	75	125	0.1			
Batch: 4321033 RL-RA-001 Work Order: M5JDX1AC Report DB ID: M5JDX1CS													
Ra-228	1.10E+01		7.8E-01	1.4E+00	8.07E-01	pCi/L	81%	9.87E+00	1.13E-01	111%	12/11/14 03:49 p	1.0004	GPC6B
							Rec Limits:	75	125	0.1			

No. of Results: 2 Comments:

TestAmerica Pensacola
3355 McLenore Drive
Pensacola, FL 32514
Phone (850) 474-1001 Fax (850) 478-2671

Chain of Custody Record

TestAmerica

THE LEADER IN ENVIRONMENTAL TESTING

Client Information (Sub Contract Lab)		Lab PM: Savoie, Noel		Carrier Tracking No(s):		COC No: 400-65251.1	
Client Contact: Shipping/Receiving		Phone: noel.savoie@testamericainc.com		E-Mail: noel.savoie@testamericainc.com		Page: Page 1 of 1	
Company: TestAmerica Laboratories, Inc.		Due Date Requested: 11/26/2014		Analysis Requested		Job #: 400-98371-1	
Address: 2800 George Washington Way, City: Richland, State, Zip: WA, 98352		TAT Requested (days):		PO #:		Preservation Codes:	
Phone: 509-375-3131(Tel) 509-375-5590(Fax)		WO #:		Project #: 64000434		M - Hexane N - None O - AsNaO2 P - Na2O4S Q - Na2SO3 R - Na2S2O3 S - H2SO4 T - TSP Dodecahydrate U - Acetone V - MCAA W - pH 4-5 X - EDTA Z - other (specify)	
Email:		SSOW#:		Project Name: Agrico Pensacola		Other:	
Site:		Sample Date		Sample Time		Sample Type (C=Comp, G=grab)	
Sample Identification - Client ID (Lab ID)		Matrix (W=water, S=solid, O=waste/oil, BT=Tissue, A=Air)		Field Filtered Sample (Yes or No)		Sub (Radium 228 by EPA Method 904.0/ Rad 226-Method 904.0 (Richland) Sub (Radium 228 by EPA Method 903.1/ Rad 226-Method 903.1 (Richland)	
AC-5D (400-98371-1)	M5H4R	11/12/14	09:39 Central			X	X
AC-5S (400-98371-2)	M5H4T	11/12/14	10:09 Central			X	X
AC-2S (400-98371-3)	M5H4V	11/12/14	13:23 Central			X	X
AC-2D (400-98371-4)	M5H4W	11/12/14	14:18 Central			X	X
ACB-31S (400-98371-5)	M5H4X	11/12/14	16:34 Central			X	X
EQ-1 (400-98371-6)	M5H40	11/12/14	11:30 Central			X	X
Possible Hazard Identification		Unconfirmed		Deliverable Requested: I, II, III, IV, Other (specify)		Special Instructions/Note: D.I.E.F.	
Empty Kit Relinquished by: SCALAN		Date/Time: 11-13-14 1600		Date: 11-13-14		Sample Disposal (A fee may be assessed if samples are retained longer than 1 month)	
Relinquished by: SCALAN		Date/Time:		Date:		Return To Client ☐ Disposal By Lab ☐ Archive For Months	
Relinquished by:		Date/Time:		Date:		Special Instructions/QC Requirements:	
Relinquished by:		Date/Time:		Date:		Method of Shipment:	
Custody Seal No.:		Custody Seal Intact: ☐ Yes ☐ No		Cooler Temperature(s) °C and Other Remarks:		Company: J4K140427	

Sample Check-in List

Date/Time Received: 11/14/14 1100 Container GM Screen Result: (Airlock) 40 cpm Initials JF
Sample GM Screen Result (Sample Receiving) 20 cpm Initials JF

Client: STP SDG #: 48996 SAF #: _____ NA JF

Lot Number: J4KTT* J4K140427

Chain of Custody # N/A

Shipping Container ID or Air Bill Number : _____ NA JF

Samples received inside shipping container/cooler/box Yes JF Continue with 1 through 4. Initial appropriate response.
No [] Go to 5, add comment to #16.

1. Custody Seals on shipping container intact? Yes [] No [] No Custody Seal [JF]
2. Custody Seals dated and signed? Yes [] No [] No Custody Seal [JF]
3. Cooler temperature: _____ °C NA [JF]
4. Vermiculite/packing materials is NA [] Wet [] Dry [JF]

Item 5 through 16 for samples. Initial appropriate response.

5. Chain of Custody record present? Yes JF No []
6. Number of samples received (Each sample may contain multiple bottles): 6
7. Containers received: 18x1p

8. Sample holding times exceeded? NA [] Yes [] No [JF]
9. Samples have: _____ tape _____ hazard labels _____ custody seals JF appropriate sample labels
10. Matrix: _____ A (FLT, Wipe, Solid, Soil) JF (Water) _____ S (Air, Niosh 7400) _____ T (Biological, Ni-63)
11. Samples:
_____ are in good condition _____ are leaking _____ are broken
_____ have air bubbles (Only for samples requiring no head space) _____ Other _____
12. Sample pH appropriate for analysis requested Yes JF No [] NA []
(If acidification is necessary go to pH area & document sample ID, initial pH, amount of HNO₃ added and pH after addition on table)
13. Were any anomalies identified in sample receipt? Yes [] No [JF]
14. Description of anomalies (include sample numbers): NA [JF] _____

15. Sample Location, Sample Collector Listed on COC? * Yes [] No [JF]
*For documentation only. No corrective action needed.

16. Additional Information: N/A

[] Client/Courier denied temperature check.

[] Client/Courier unpack cooler.

Sample Check-in List completed by Sample Custodian:

Signature: _____ Date: 11/14/14

Client Notification needed? Yes [] No [] Date: _____

By: _____

Person contacted: _____

[] No action necessary; process as is

Project Manager ELMayer

Date 11/17/14

TestAmerica Tallahassee
2846 Industrial Plaza Drive
Tallahassee, FL 32301
Phone (850) 878-3994 Fax (850) 878-9504

Chain of Custody Record

TestAmerica
THE LEADER IN ENVIRONMENTAL TESTING

08371

Client Information		Samples: <u>Dechlorination, J. Plethron</u>		Lab PM: <u>Savoie, Noel</u>		Carrier Tracking No(s):		COC No: <u>640-48009-12359.3</u>						
Client Contact: <u>Mr. Jeff Wagner</u>		Phone: <u>850-528-8095</u>		E-Mail: <u>noel.savoie@testamericainc.com</u>				Page: <u>3 of 5</u>						
Company: <u>URS Corporation</u>								Job #:						
Address: <u>1625 Summit Lake Drive Suite 200</u>		Due Date Requested:		Analysis Requested		Total Number of containers		Preservation Codes:						
City: <u>Tallahassee</u>		TAT Requested (days):						A - HCL B - NaOH C - Zn Acetate D - Nitric Acid E - NaHSO4 F - MeOH G - Amchlor H - Ascorbic Acid I - Ice J - DI Water K - EDTA L - EDA Z - other (specify)						
State, Zip: <u>FL, 32317</u>		PO #: <u>308649 US</u>						M - Hexane N - None O - AsNaO2 P - Na2OAS Q - Na2SO3 R - Na2S2SO3 S - H2SO4 T - TSP Dodecalhydrate U - Acetone V - MCAA W - pH 4-5 X - EDTA						
Phone: <u>850-402-6409(Tel)</u>		WO #: <u>12806620.00000 Vendor #1427536</u>						Other:						
Email: <u>jeffrey_wagner@urscorp.com</u>		Project #: <u>64000434</u>												
Site: <u>AgriCo Pensacola</u>		SSOW#:												
Sample Identification		Sample Date	Sample Time	Sample Type (C=Comp, G=grab)	Matrix (W=water, S=solid, O=waste/soil, ST=Tissue, A=Air)	Field Filtered Sample (Yes or No)	Perform MS/MSD (Yes or No)	353.2 Pres - Nitrate Nitrite as N	340.2 SM4500 NO2-B	SUBCONTRACT - Rad 228-Method 903.1 (Richland)	SUBCONTRACT - Rad 228-Method 904.0 (Richland)	300 ORGM 28D - Chloride and Sulfate	6010B - Arsenic	Special Instructions/Note:
AC-SD	11/12/14	0839	G	W										
AC-SS	11/12/14	1009	G	W										
AC-ZS	11/12/14	1323	G	W										
AC-2D	11/12/14	1418	G	W										
Possible Hazard Identification ☒ Non-Hazard ☐ Flammable ☐ Skin Irritant ☐ Poison B ☐ Unknown ☐ Radiological														
Deliverable Requested: I, II, III, IV, Other (specify)														
Empty Kit Relinquished by: <u>Jeffrey Wagner</u> Date: <u>11/15/14</u> Time: <u>1500</u>														
Relinquished by: <u>Jeffrey Wagner</u> Date: <u>11/14</u> Time: <u>1725</u>														
Relinquished by: <u>Jeffrey Wagner</u> Date: <u>11/14</u> Time: <u>1725</u>														
Custody Seals Intact: <u>Yes</u> ☐ No ☐														
Custody Seal No.: <u>5.864306 IR-2</u>														

TestAmerica

THE LEADER IN ENVIRONMENTAL TESTING

ANALYTICAL REPORT

TestAmerica Laboratories, Inc.

TestAmerica Pensacola

3355 McLemore Drive

Pensacola, FL 32514

Tel: (850)474-1001

TestAmerica Job ID: 400-98418-1

Client Project/Site: Agrico Pensacola

Revision: 1

For:

URS Corporation

1625 Summit Lake Drive

Suite 200

Tallahassee, Florida 32317

Attn: Mr. Jeff Wagner



Authorized for release by:

12/22/2014 2:42:30 PM

Noel Savoie, Project Manager I

(850)878-3994

noel.savoie@testamericainc.com

LINKS

Review your project
results through

TotalAccess

Have a Question?



Visit us at:

www.testamericainc.com

The test results in this report meet all 2003 NELAC and 2009 TNI requirements for accredited parameters, exceptions are noted in this report. This report may not be reproduced except in full, and with written approval from the laboratory. For questions please contact the Project Manager at the e-mail address or telephone number listed on this page.

This report has been electronically signed and authorized by the signatory. Electronic signature is intended to be the legally binding equivalent of a traditionally handwritten signature.

Results relate only to the items tested and the sample(s) as received by the laboratory.

1

2

3

4

5

6

7

8

9

10

11

Table of Contents

Cover Page	1
Table of Contents	2
Definitions	3
Case Narrative	4
Sample Summary	5
Client Sample Results	6
QC Sample Results	9
Chronicle	13
Method Summary	16
Subcontract Data	17
Chain of Custody	37



Definitions/Glossary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Glossary

Abbreviation	These commonly used abbreviations may or may not be present in this report.
□	Listed under the "D" column to designate that the result is reported on a dry weight basis
%R	Percent Recovery
CFL	Contains Free Liquid
CNF	Contains no Free Liquid
DER	Duplicate error ratio (normalized absolute difference)
Dil Fac	Dilution Factor
DL, RA, RE, IN	Indicates a Dilution, Re-analysis, Re-extraction, or additional Initial metals/anion analysis of the sample
DLC	Decision level concentration
MDA	Minimum detectable activity
EDL	Estimated Detection Limit
MDC	Minimum detectable concentration
MDL	Method Detection Limit
ML	Minimum Level (Dioxin)
NC	Not Calculated
ND	Not detected at the reporting limit (or MDL or EDL if shown)
PQL	Practical Quantitation Limit
QC	Quality Control
RER	Relative error ratio
RL	Reporting Limit or Requested Limit (Radiochemistry)
RPD	Relative Percent Difference, a measure of the relative difference between two points
TEF	Toxicity Equivalent Factor (Dioxin)
TEQ	Toxicity Equivalent Quotient (Dioxin)

Case Narrative

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Job ID: 400-98418-1

Laboratory: TestAmerica Pensacola

Narrative

Job Narrative 400-98418-1

Comments

Revision created to correct sample ID in Richland's report.

Receipt

The samples were received on 11/13/2014 1:45 PM; the samples arrived in good condition, properly preserved and, where required, on ice. The temperatures of the 3 coolers at receipt time were 0.1° C, 0.4° C and 1.0° C.

Except:

The following sample was submitted for analysis; however, it was not listed on the Chain-of-Custody (COC): DUP-1 (OU-1) (400-98418-8)

HPLC/IC

No analytical or quality issues were noted, other than those described in the Definitions/Glossary page.

General Chemistry

Method 353.2: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-34S (400-98418-3), AC-8D (400-98418-1), DUP-1 (OU-1) (400-98418-8), and DUP-2 (400-98418-6). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Subcontract Work

Methods Radium 226 by EPA Method 903.1, Radium 228 by EPA Method 904.0: These methods were subcontracted to TestAmerica Richland. Report attached.

Sample Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Lab Sample ID	Client Sample ID	Matrix	Collected	Received
400-98418-1	AC-8D	Water	11/13/14 08:20	11/13/14 13:45
400-98418-2	ACB-32S	Water	11/13/14 09:21	11/13/14 13:45
400-98418-3	AC-34S	Water	11/13/14 10:23	11/13/14 13:45
400-98418-4	AC-7SR	Water	11/13/14 11:41	11/13/14 13:45
400-98418-5	AC-33S	Water	11/13/14 12:49	11/13/14 13:45
400-98418-6	DUP-2	Water	11/13/14 00:00	11/13/14 13:45
400-98418-7	DUP-4	Water	11/13/14 00:00	11/13/14 13:45
400-98418-8	DUP-1 (OU-1)	Water	11/13/14 00:00	11/13/14 13:45

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Client Sample ID: AC-8D

Date Collected: 11/13/14 08:20

Date Received: 11/13/14 13:45

Lab Sample ID: 400-98418-1

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	13		1.0		mg/L			11/26/14 09:50	1
Sulfate	4.8		1.0		mg/L			11/26/14 09:50	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/19/14 16:12	1
Nitrate Nitrite as N	5.3		0.25		mg/L			11/24/14 10:41	5
Nitrate as N	5.3		0.050		mg/L			11/24/14 10:41	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 15:01	1

Client Sample ID: ACB-32S

Date Collected: 11/13/14 09:21

Date Received: 11/13/14 13:45

Lab Sample ID: 400-98418-2

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	1.4		1.0		mg/L			11/26/14 14:48	1
Sulfate	13		1.0		mg/L			11/26/14 14:48	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	0.12		0.10		mg/L			11/19/14 16:30	1
Nitrate Nitrite as N	0.55		0.050		mg/L			11/24/14 10:42	1
Nitrate as N	0.55		0.050		mg/L			11/24/14 10:42	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 15:01	1

Client Sample ID: AC-34S

Date Collected: 11/13/14 10:23

Date Received: 11/13/14 13:45

Lab Sample ID: 400-98418-3

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	3.2		1.0		mg/L			11/26/14 15:11	1
Sulfate	39		1.0		mg/L			11/26/14 15:11	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	1.2		0.10		mg/L			11/19/14 16:33	1
Nitrate Nitrite as N	2.6		0.10		mg/L			11/24/14 10:43	2
Nitrate as N	2.6		0.050		mg/L			11/24/14 10:43	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 15:01	1

Client Sample ID: AC-7SR

Date Collected: 11/13/14 11:41

Date Received: 11/13/14 13:45

Lab Sample ID: 400-98418-4

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	3.3		1.0		mg/L			11/26/14 15:34	1
Sulfate	28		1.0		mg/L			11/26/14 15:34	1

TestAmerica Pensacola

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Client Sample ID: AC-7SR

Lab Sample ID: 400-98418-4

Date Collected: 11/13/14 11:41

Matrix: Water

Date Received: 11/13/14 13:45

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	1.8		0.10		mg/L			11/19/14 16:35	1
Nitrate Nitrite as N	1.2		0.050		mg/L			11/24/14 10:45	1
Nitrate as N	1.2		0.050		mg/L			11/24/14 10:45	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 15:01	1

Client Sample ID: AC-33S

Lab Sample ID: 400-98418-5

Date Collected: 11/13/14 12:49

Matrix: Water

Date Received: 11/13/14 13:45

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	3.4		1.0		mg/L			11/26/14 15:57	1
Sulfate	28		1.0		mg/L			11/26/14 15:57	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	0.63		0.10		mg/L			11/19/14 16:38	1
Nitrate Nitrite as N	0.18		0.050		mg/L			11/24/14 10:46	1
Nitrate as N	0.18		0.050		mg/L			11/24/14 10:46	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 15:01	1

Client Sample ID: DUP-2

Lab Sample ID: 400-98418-6

Date Collected: 11/13/14 00:00

Matrix: Water

Date Received: 11/13/14 13:45

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	13		1.0		mg/L			11/26/14 16:19	1
Sulfate	4.4		1.0		mg/L			11/26/14 16:19	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 09:31	1
Nitrate Nitrite as N	5.4		0.25		mg/L			11/24/14 10:52	5
Nitrate as N	5.4		0.050		mg/L			11/24/14 10:52	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 15:01	1

Client Sample ID: DUP-4

Lab Sample ID: 400-98418-7

Date Collected: 11/13/14 00:00

Matrix: Water

Date Received: 11/13/14 13:45

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	3.3		1.0		mg/L			11/26/14 16:42	1
Sulfate	27		1.0		mg/L			11/26/14 16:42	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	0.63		0.10		mg/L			11/24/14 09:35	1
Nitrate Nitrite as N	0.19		0.050		mg/L			11/24/14 10:53	1
Nitrate as N	0.19		0.050		mg/L			11/24/14 10:53	1

TestAmerica Pensacola

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Client Sample ID: DUP-4

Date Collected: 11/13/14 00:00

Date Received: 11/13/14 13:45

Lab Sample ID: 400-98418-7

Matrix: Water

General Chemistry (Continued)

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/13/14 15:04	1

Client Sample ID: DUP-1 (OU-1)

Date Collected: 11/13/14 00:00

Date Received: 11/13/14 13:45

Lab Sample ID: 400-98418-8

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	3.1		1.0		mg/L			11/26/14 17:51	1
Sulfate	39		1.0		mg/L			11/26/14 17:51	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	1.2		0.10		mg/L			11/24/14 09:37	1
Nitrate Nitrite as N	2.7		0.10		mg/L			11/24/14 10:54	2
Nitrate as N	2.7		0.050		mg/L			11/24/14 10:54	1
Nitrite as N	<0.10		0.10		mg/L			11/13/14 15:04	1

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Method: 300.0 - Anions, Ion Chromatography

Lab Sample ID: MB 400-237963/4

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			11/25/14 12:44	1
Sulfate	<1.0		1.0		mg/L			11/25/14 12:44	1

Lab Sample ID: MB 400-237963/45

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			11/26/14 13:16	1
Sulfate	<1.0		1.0		mg/L			11/26/14 13:16	1

Lab Sample ID: LCS 400-237963/46

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	10.7		mg/L		107	90 - 110
Sulfate	10.0	9.67		mg/L		97	90 - 110

Lab Sample ID: LCS 400-237963/5

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	10.5		mg/L		105	90 - 110
Sulfate	10.0	9.32		mg/L		93	90 - 110

Lab Sample ID: LCSD 400-237963/47

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	10.7		mg/L		107	90 - 110	0	15
Sulfate	10.0	9.54		mg/L		95	90 - 110	1	15

Lab Sample ID: LCSD 400-237963/6

Matrix: Water

Analysis Batch: 237963

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	10.6		mg/L		106	90 - 110	1	15
Sulfate	10.0	9.29		mg/L		93	90 - 110	0	15

Lab Sample ID: 400-98418-1 MS

Matrix: Water

Analysis Batch: 237963

Client Sample ID: AC-8D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	13		10.0	24.0		mg/L		108	80 - 120

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Method: 300.0 - Anions, Ion Chromatography (Continued)

Lab Sample ID: 400-98418-1 MS

Matrix: Water

Analysis Batch: 237963

Client Sample ID: AC-8D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Sulfate	4.8		10.0	14.5		mg/L		97	80 - 120

Lab Sample ID: 400-98418-1 MSD

Matrix: Water

Analysis Batch: 237963

Client Sample ID: AC-8D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	13		10.0	23.8		mg/L		106	80 - 120	1	20
Sulfate	4.8		10.0	14.3		mg/L		95	80 - 120	1	20

Method: 340.2 - Fluoride

Lab Sample ID: MB 400-237352/3

Matrix: Water

Analysis Batch: 237352

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/19/14 16:02	1

Lab Sample ID: LCS 400-237352/4

Matrix: Water

Analysis Batch: 237352

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.30		mg/L		108	90 - 110

Lab Sample ID: 400-98418-1 MS

Matrix: Water

Analysis Batch: 237352

Client Sample ID: AC-8D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	<0.10		1.00	1.08		mg/L		108	74 - 125

Lab Sample ID: 400-98418-1 MSD

Matrix: Water

Analysis Batch: 237352

Client Sample ID: AC-8D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Fluoride	<0.10		1.00	1.08		mg/L		108	74 - 125	0	4

Lab Sample ID: MB 400-237758/3

Matrix: Water

Analysis Batch: 237758

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 09:06	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Method: 340.2 - Fluoride (Continued)

Lab Sample ID: LCS 400-237758/4

Matrix: Water

Analysis Batch: 237758

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.30		mg/L		108	90 - 110

Method: 353.2 - Nitrogen, Nitrate-Nitrite

Lab Sample ID: MB 400-237769/48

Matrix: Water

Analysis Batch: 237769

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/24/14 10:36	1

Lab Sample ID: LCS 400-237769/49

Matrix: Water

Analysis Batch: 237769

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.531		mg/L		106	90 - 110

Lab Sample ID: MRL 400-237769/12

Matrix: Water

Analysis Batch: 237769

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	<0.050		mg/L		87	50 - 150

Method: SM 4500 NO2 B - Nitrogen, Nitrite

Lab Sample ID: MB 400-236885/6

Matrix: Water

Analysis Batch: 236885

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/13/14 08:06	1

Lab Sample ID: MB 400-236885/66

Matrix: Water

Analysis Batch: 236885

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/13/14 15:01	1

Lab Sample ID: LCS 400-236885/7

Matrix: Water

Analysis Batch: 236885

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.278		mg/L		93	90 - 110

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Method: SM 4500 NO2 B - Nitrogen, Nitrite (Continued)

Lab Sample ID: LCS 400-236885/81

Matrix: Water

Analysis Batch: 236885

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.279		mg/L		93	90 - 110

Lab Sample ID: MRL 400-236885/3

Matrix: Water

Analysis Batch: 236885

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.100	<0.10		mg/L		97	50 - 150

Lab Sample ID: 400-98418-5 MS

Matrix: Water

Analysis Batch: 236885

Client Sample ID: AC-33S

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	<0.10		0.100	<0.10		mg/L		94	80 - 118

Lab Sample ID: 400-98418-5 MSD

Matrix: Water

Analysis Batch: 236885

Client Sample ID: AC-33S

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Nitrite as N	<0.10		0.100	<0.10		mg/L		96	80 - 118	2	9

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Client Sample ID: AC-8D

Date Collected: 11/13/14 08:20

Date Received: 11/13/14 13:45

Lab Sample ID: 400-98418-1

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/26/14 09:50	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 16:12	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237769	11/24/14 10:41	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:41	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 15:01	LSS	TAL PEN

Client Sample ID: ACB-32S

Date Collected: 11/13/14 09:21

Date Received: 11/13/14 13:45

Lab Sample ID: 400-98418-2

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/26/14 14:48	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 16:30	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237769	11/24/14 10:42	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:42	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 15:01	LSS	TAL PEN

Client Sample ID: AC-34S

Date Collected: 11/13/14 10:23

Date Received: 11/13/14 13:45

Lab Sample ID: 400-98418-3

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/26/14 15:11	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 16:33	SLT	TAL PEN
Total/NA	Analysis	353.2		2	237769	11/24/14 10:43	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:43	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 15:01	LSS	TAL PEN

Client Sample ID: AC-7SR

Date Collected: 11/13/14 11:41

Date Received: 11/13/14 13:45

Lab Sample ID: 400-98418-4

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/26/14 15:34	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 16:35	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237769	11/24/14 10:45	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:45	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 15:01	LSS	TAL PEN

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Client Sample ID: AC-33S

Lab Sample ID: 400-98418-5

Date Collected: 11/13/14 12:49

Matrix: Water

Date Received: 11/13/14 13:45

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/26/14 15:57	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237352	11/19/14 16:38	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237769	11/24/14 10:46	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:46	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 15:01	LSS	TAL PEN

Client Sample ID: DUP-2

Lab Sample ID: 400-98418-6

Date Collected: 11/13/14 00:00

Matrix: Water

Date Received: 11/13/14 13:45

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/26/14 16:19	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237758	11/24/14 09:31	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237769	11/24/14 10:52	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:52	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 15:01	LSS	TAL PEN

Client Sample ID: DUP-4

Lab Sample ID: 400-98418-7

Date Collected: 11/13/14 00:00

Matrix: Water

Date Received: 11/13/14 13:45

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/26/14 16:42	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237758	11/24/14 09:35	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237769	11/24/14 10:53	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:53	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 15:04	LSS	TAL PEN

Client Sample ID: DUP-1 (OU-1)

Lab Sample ID: 400-98418-8

Date Collected: 11/13/14 00:00

Matrix: Water

Date Received: 11/13/14 13:45

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	237963	11/26/14 17:51	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237758	11/24/14 09:37	SLT	TAL PEN
Total/NA	Analysis	353.2		2	237769	11/24/14 10:54	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237955	11/24/14 10:54	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236885	11/13/14 15:04	LSS	TAL PEN

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001
TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131



Method Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98418-1

Method	Method Description	Protocol	Laboratory
300.0	Anions, Ion Chromatography	MCAWW	TAL PEN
340.2	Fluoride	MCAWW	TAL PEN
353.2	Nitrogen, Nitrate-Nitrite	MCAWW	TAL PEN
Nitrate by calc	Nitrogen, Nitrate	SM	TAL PEN
SM 4500 NO2 B	Nitrogen, Nitrite	SM	TAL PEN
Rad 226-Method 903.1 (Richland)	RAD-226 (RCH)	NONE	TAL RCH
Rad 228-Method 904.0 (Richland)	RAD-228 (RCH)	NONE	TAL RCH

Protocol References:

MCAWW = "Methods For Chemical Analysis Of Water And Wastes", EPA-600/4-79-020, March 1983 And Subsequent Revisions.

NONE = NONE

SM = "Standard Methods For The Examination Of Water And Wastewater",

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Analytical Data Package Prepared For

TestAmerica Pensacola

Radiochemical Analysis By

TestAmerica Inc

2800 G.W. Way, Richland Wa, 99354, (509)-375-3131.

Assigned Laboratory Code: TARL

Data Package Contains _____ Pages

Report No.: 63983

Results in this report relate only to the sample(s) analyzed.

SDG No.	Order No.	Client Sample ID (List Order)	Lot-Sa No.	Work Order	Report DB ID	Batch No.
48997		AC-33S(400-98418-5)	J4K140428-5	M5H451AA	9M5H4510	4321032
		AC-33S(400-98418-5)	J4K140428-5	M5H451AC	9M5H4510	4321033
		AC-34S(400-98418-3)	J4K140428-3	M5H431AA	9M5H4310	4321032
		AC-34S(400-98418-3)	J4K140428-3	M5H431AC	9M5H4310	4321033
		AC-7SR(400-98418-4)	J4K140428-4	M5H441AA	9M5H4410	4321032
		AC-7SR(400-98418-4)	J4K140428-4	M5H441AC	9M5H4410	4321033
		AC-8D(400-98418-1)	J4K140428-1	M5H411AA	9M5H4110	4321032
		AC-8D(400-98418-1)	J4K140428-1	M5H411AC	9M5H4110	4321033
		ACB-32S(400-98418-2)	J4K140428-2	M5H421AA	9M5H4210	4321032
		ACB-32S(400-98418-2)	J4K140428-2	M5H421AC	9M5H4210	4321033
		DUP-1(OU-1)(400-98418-8)	J4K140428-8	M5H481AA	9M5H4810	4321032
		DUP-1(OU-1)(400-98418-8)	J4K140428-8	M5H481AC	9M5H4810	4321033
		DUP-2(400-98418-6)	J4K140428-6	M5H461AA	9M5H4610	4321032
		DUP-2(400-98418-6)	J4K140428-6	M5H461AC	9M5H4610	4321033
		DUP-4(400-98418-7)	J4K140428-7	M5H471AA	9M5H4710	4321032
		DUP-4(400-98418-7)	J4K140428-7	M5H471AC	9M5H4710	4321033



Certificate of Analysis

December 12, 2014

Revised Date December 22, 2014

TestAmerica Pensacola
3355 McLemore Drive
Pensacola, FL 32514

Attention: Noel Savoie

Date Received at Lab	:	November 14, 2014
Project Name/Number	:	Agrico Pensacola/64000434
Sample Type	:	Eight (8) Water
Job Number	:	400-98418-1
SDG Number	:	48997

CASE NARRATIVE

This report has been revised to correct sample ID.

All changes to this narrative have been bolded, underlined and are italicized.

I. Introduction

On November 14, 2014, eight water samples were received at TestAmerica's Richland laboratory for radiochemical analysis. Upon receipt, the samples were assigned the TestAmerica identification number as described on the cover page of the Analytical Data Package report form. The samples were assigned to Lot Numbers J4K140428.

II. Sample Receipt

The samples were received in good condition and no anomalies were noted upon check-in.

III. Analytical Results/Methodology

The analytical results for this report are presented by laboratory sample ID. Each set of data includes sample identification information; analytical results and the appropriate associated statistical uncertainties.

The analysis requested was:

Gas Proportional Counting

Radium-228 by method RL-RA-001

Alpha Scintillation Counting

Radium-226 by method RL-RA-001

TestAmerica Pensacola
December 12, 2014
Revised Date: December 22, 2014

IV. Quality Control

The analytical result for each analysis performed includes a minimum of one laboratory control sample (LCS), and one reagent blank sample analysis. Any exceptions have been noted in the Comments” section.

V. Comments

Gas Proportional Counting

Radium-228

The LCS, batch blank, sample duplicate and sample results are within acceptance limits.

Alpha Scintillation Counting

Radium 226:

The LCS, batch blank, samples and sample duplicate results are within acceptance limits.

I certify that this Certificate of Analysis is in compliance with the SOW and/or NELAC, both technically and for completeness, for other than the conditions detailed above. The Laboratory Manager or a designee, as verified by the following signature has authorized release of the data contained in this hard copy data package.

Reviewed and approved:

Robin Ebert-Mays
Project Manager

Drinking Water Method Cross References

DRINKING WATER ASTM METHOD CROSS REFERENCES		
Referenced Method	Isotope(s)	TestAmerica Richland's SOP No.
EPA 901.1	Cs-134, I-131	RL-GAM-001
EPA 900.0	Alpha & Beta	RL-GPC-001
EPA 00-02	Gross Alpha (Coprecipitation)	RL-GPC-002
EPA 903.0	Total Alpha Radium (Ra-226)	RL-RA-002
EPA 903.1	Ra-226	RL-RA-001
EPA 904.0	Ra-228	RL-RA-001
EPA 905.0	Sr-89/90	RL-GPC-003
ASTM D5174	Uranium	RL-KPA-003
EPA 906.0	Tritium	RL-LSC-005

Results in this report relate only to the sample(s) analyzed.

Uncertainty Estimation

TestAmerica Richland has adopted the internationally accepted approach to estimating uncertainties described in "NIST Technical Note 1297, 1994 Edition". The approach, "Law of Propagation of Errors", involves the identification of all variables in an analytical method which are used to derive a result. These variables are related to the analytical result (R) by some functional relationship, $R = \text{constants} * f(x,y,z,...)$. The components (x,y,z) are evaluated to determine their contribution to the overall method uncertainty. The individual component uncertainties (u_i) are then combined using a statistical model that provides the most probable overall uncertainty value. All component uncertainties are categorized as type A, evaluated by statistical methods, or type B, evaluated by other means. Uncertainties not included in the components, such as sample homogeneity, are combined with the component uncertainty as the square root of the sum-of-the-squares of the individual uncertainties. The uncertainty associated with the derived result is the combined uncertainty (u_c) multiplied by the coverage factor (1,2, or 3).

When three or more sample replicates are used to derive the analytical result, the type A uncertainty is the standard deviation of the mean value ($S/\sqrt{n}$), where S is the standard deviation of the derived results. The type B uncertainties are all other random or non-random components that are not included in the standard deviation.

The derivation of the general "Law of Propagation of Errors" equations and specific example are available on request.

Report Definitions

Action Lev	An agreed upon activity level used to trigger some action when the final result is greater than or equal to the Action Level. Often the Action Level is related to the Decision Limit.
Batch	The QC preparation batch number that relates laboratory samples to QC samples that were prepared and analyzed together.
Bias	Defined by the equation (Result/Expected)-1 as defined by ANSI N13.30.
COC No	Chain of Custody Number assigned by the Client or TestAmerica.
Count Error (#s)	Poisson counting statistics of the gross sample count and background. The uncertainty is absolute and in the same units as the result. For Liquid Scintillation Counting (LSC) the batch blank count is the background.
Total Uncert (#s) u_c - Combined Uncertainty.	All known uncertainties associated with the preparation and analysis of the sample are propagated to give a measure of the uncertainty associated with the result, u_c the combined uncertainty. The uncertainty is absolute and in the same units as the result.
(#s), Coverage Factor	The coverage factor defines the width of the confidence interval, 1, 2 or 3 standard deviations.
CRDL (RL)	Contractual Required Detection Limit as defined in the Client's Statement Of Work or TestAmerica "default" nominal detection limit. Often referred to the reporting level (RL)
Lc	Decision Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume associated with the sample. The Type I error probability is approximately 5%. $Lc = (1.645 * \sqrt{2 * (BkgndCnt / BkgndCntMin) / SCntMin}) * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability. Lc cannot be calculated when the background count is zero.
Lot-Sample No	The number assigned by the LIMS software to track samples received on the same day for a given client. The sample number is a sequential number assigned to each sample in the Lot.
MDC MDA	Detection Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume with a Type I and II error probability of approximately 5%. $MDC = (4.65 * \sqrt{(BkgndCnt / BkgndCntMin) / SCntMin}) + 2.71 / SCntMin * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability.
Primary Detector	The instrument identifier associated with the analysis of the sample aliquot.
Ratio U-234/U-238	The U-234 result divided by the U-238 result. The U-234/U-238 ratio for natural uranium in NIST SRM 4321C is 1.038.
Rst/MDC	Ratio of the Result to the MDC. A value greater than 1 may indicate activity above background at a high level of confidence. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Rst/TotUcert	Ratio of the Result to the Total Uncertainty. If the uncertainty has a coverage factor of 2 a value greater than 1 may indicate activity above background at approximately the 95% level of confidence assuming a two-sided confidence interval. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Report DB No	Sample Identifier used by the report system. The number is based upon the first five digits of the Work Order Number.
RER	The equation Replicate Error Ratio = $(S-D) / [\sqrt{TPUs^2 + TPUD^2}]$ as defined by ICPT BOA where S is the original sample result, D is the result of the duplicate, TPUs is the total uncertainty of the original sample and TPUD is the total uncertainty of the duplicate sample.
SDG	Sample Delivery Group Number assigned by the Client or assigned by TestAmerica upon sample receipt.
Sum Rpt Alpha Spec Rst(s)	The sum of the reported alpha spec results for tests derived from the same sample excluding duplicate result where the results are in the same units.
Work Order	The LIMS software assign test specific identifier.
Yield	The recovery of the tracer added to the sample such as Pu-242 used to trace a Pu-239/40 method.

Sample Results Summary

Date: 22-Dec-14

TestAmerica Inc TARL

Ordered by Method, Batch No., Client Sample ID.

Report No. : 63983

SDG No: 48997

Batch	Client Id Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	MDL	CRDL	RER2
4321032	RL-RA-001								
	AC-33S(400-98418-5)								
	M5H451AA Ra-226		4.35E-01 +- 1.5E-01	J	pCi/L	93%	1.63E-01	1.00E+00	
	AC-34S(400-98418-3)								
	M5H431AA Ra-226		4.55E-02 +- 8.4E-02	U	pCi/L	100%	1.62E-01	1.00E+00	
	AC-7SR(400-98418-4)								
	M5H441AA Ra-226		3.24E-01 +- 1.2E-01	J	pCi/L	100%	1.21E-01	1.00E+00	
	AC-8D(400-98418-1)								
	M5H411AA Ra-226		2.07E-01 +- 1.1E-01	J	pCi/L	98%	1.50E-01	1.00E+00	
	AC-8D(400-98418-1) DUP								
	M5H411AD Ra-226		7.27E-01 +- 2.3E-01	J	pCi/L	98%	1.62E-01	1.00E+00	4.0
	ACB-32S(400-98418-2)								
	M5H421AA Ra-226		1.94E-01 +- 1.1E-01	J	pCi/L	85%	1.38E-01	1.00E+00	
	DUP-1(OU-1)(400-98418-8)								
	M5H481AA Ra-226		1.50E-01 +- 1.1E-01	U	pCi/L	92%	1.54E-01	1.00E+00	
	DUP-2(400-98418-6)								
	M5H461AA Ra-226		9.09E-01 +- 2.8E-01	J	pCi/L	84%	1.74E-01	1.00E+00	
	DUP-4(400-98418-7)								
	M5H471AA Ra-226		4.44E-01 +- 1.5E-01	J	pCi/L	97%	1.12E-01	1.00E+00	
4321033	RL-RA-001								
	AC-33S(400-98418-5)								
	M5H451AC Ra-228		2.47E+00 +- 5.0E-01		pCi/L	87%	5.21E-01	1.00E+00	
	AC-34S(400-98418-3)								
	M5H431AC Ra-228		5.93E-01 +- 2.8E-01	J	pCi/L	86%	5.14E-01	1.00E+00	
	AC-7SR(400-98418-4)								
	M5H441AC Ra-228		8.77E-01 +- 3.0E-01	J	pCi/L	91%	4.71E-01	1.00E+00	
	AC-8D(400-98418-1)								
	M5H411AC Ra-228		1.14E+00 +- 3.5E-01		pCi/L	91%	5.14E-01	1.00E+00	
	AC-8D(400-98418-1) DUP								
	M5H411AE Ra-228		1.28E+00 +- 3.8E-01		pCi/L	87%	5.34E-01	1.00E+00	0.5
	ACB-32S(400-98418-2)								
	M5H421AC Ra-228		6.63E-01 +- 3.2E-01	J	pCi/L	77%	5.90E-01	1.00E+00	
	DUP-1(OU-1)(400-98418-8)								
	M5H481AC Ra-228		1.58E-02 +- 3.4E-01	U	pCi/L	77%	8.04E-01	1.00E+00	
	DUP-2(400-98418-6)								
	M5H461AC Ra-228		1.39E+00 +- 4.3E-01		pCi/L	75%	6.66E-01	1.00E+00	
	DUP-4(400-98418-7)								
	M5H471AC Ra-228		2.10E+00 +- 4.9E-01		pCi/L	83%	5.78E-01	1.00E+00	
No. of Results: 18									

TestAmerica Inc
rptTALRchSaSum
mary2 V5.3.6.1
A2002

RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPUs)+sq(TPUD))] as defined by ICPT BOA.

J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

QC Results Summary
TestAmerica Inc TARL
 Ordered by Method, Batch No, QC Type,.

Report No. : 63983

SDG No.: 48996

Batch	Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	LCS Recovery	Bias	MDL
RL-RA-001									
4321032	BLANK QC,								
	M5JDW1AA	Ra-226	6.84E-02 +- 9.1E-02	U	pCi/L	75%			1.66E-01
4321032	LCS,								
	M5JDW1AC	Ra-226	1.13E+01 +- 2.3E+00		pCi/L	86%	113%	0.1	1.62E-01
RL-RA-001									
4321033	BLANK QC,								
	M5JDX1AA	Ra-228	3.32E-02 +- 2.8E-01	U	pCi/L	70%			6.78E-01
4321033	LCS,								
	M5JDX1AC	Ra-228	1.10E+01 +- 1.4E+00		pCi/L	81%	111%	0.1	8.07E-01
No. of Results: 4									

TestAmerica Inc Bias - (Result/Expected)-1 as defined by ANSI N13.30.

rptSTLRchQcSummary V5.3.6.1
 A2002

U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 48997

Collection Date: 11/13/2014 12:49:00 PM

Lot-Sample No.: J4K140428-5

Report No. : 63983

Received Date: 11/14/2014 11:00:00 AM

Client Sample ID: AC-33S(400-98418-5)

COC No. :

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001												
Work Order: M5H451AA Report DB ID: 9M5H4510												
Ra-226	4.35E-01	J	1.3E-01	1.5E-01	1.63E-01	pCi/L	93%	(2.7)	12/9/14 07:24 p		0.9512	ASCGMA
							7.37E-02	1.00E+00	(5.7)	L		
Batch: 4321033 RL-RA-001												
Work Order: M5H451AC Report DB ID: 9M5H4510												
Ra-228	2.47E+00		4.1E-01	5.0E-01	5.21E-01	pCi/L	87%	(4.7)	12/11/14 03:48 p		0.9512	GPC3D
							2.31E-01	1.00E+00	(9.8)	L		

No. of Results: 2 Comments:

TestAmerica Inc

MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.

J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.

U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K140428-3
Client Sample ID: AC-34S(400-98418-3)

SDG: 48997
Report No. : 63983
COC No. :
Collection Date: 11/13/2014 10:23:00 AM
Received Date: 11/14/2014 11:00:00 AM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001												
Work Order: M5H431AA Report DB ID: 9M5H4310												
Ra-226	4.55E-02	U	8.3E-02	8.4E-02	1.62E-01	pCi/L	100%	0.28	12/9/14 07:25 p		0.9262	ASCDMC
						7.26E-02	1.00E+00	(1.1)			L	
Batch: 4321033 RL-RA-001												
Work Order: M5H431AC Report DB ID: 9M5H4310												
Ra-228	5.93E-01	J	2.7E-01	2.8E-01	5.14E-01	pCi/L	86%	(1.2)	12/11/14 03:48 p		0.9262	GPC3B
						2.26E-01	1.00E+00	(4.2)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K140428-4
Client Sample ID: AC-7SR(400-98418-4)

SDG: 48997
Report No. : 63983
COC No. :
Collection Date: 11/13/2014 11:41:00 AM
Received Date: 11/14/2014 11:00:00 AM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001												
Work Order: M5H441AA Report DB ID: 9M5H4410												
Ra-226	3.24E-01	J	1.0E-01	1.2E-01	1.21E-01	pCi/L	100%	(2.7)	12/9/14 07:25 p		0.9086	ASCEHB
							5.30E-02	1.00E+00	(5.4)	L		
Batch: 4321033 RL-RA-001												
Work Order: M5H441AC Report DB ID: 9M5H4410												
Ra-228	8.77E-01	J	2.8E-01	3.0E-01	4.71E-01	pCi/L	91%	(1.9)	12/11/14 03:48 p		0.9086	GPC3C
							2.06E-01	1.00E+00	(5.8)	L		

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K140428-1
Client Sample ID: AC-8D(400-98418-1)

SDG: 48997
Report No. : 63983
COC No. :
Collection Date: 11/13/2014 8:20:00 AM
Received Date: 11/14/2014 11:00:00 AM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001												
Work Order: M5H411AA Report DB ID: 9M5H4110												
Ra-226	2.07E-01	J	1.0E-01	1.1E-01	1.50E-01	pCi/L	98%	(1.4)	12/9/14 07:09 p		0.9025	ASC9MA
							6.68E-02	1.00E+00	(3.7)	L		
Batch: 4321033 RL-RA-001												
Work Order: M5H411AC Report DB ID: 9M5H4110												
Ra-228	1.14E+00		3.3E-01	3.5E-01	5.14E-01	pCi/L	91%	(2.2)	12/11/14 03:48 p		0.9025	GPC2C
							2.25E-01	1.00E+00	(6.4)	L		

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 48997 Collection Date: 11/13/2014 9:21:00 AM
Lot-Sample No.: J4K140428-2 Report No.: 63983 Received Date: 11/14/2014 11:00:00 AM
Client Sample ID: ACB-32S(400-98418-2) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001 Work Order: M5H421AA Report DB ID: 9M5H4210												
Ra-226	1.94E-01	J	9.6E-02	1.1E-01	1.38E-01	pCi/L	85%	(1.4)	12/9/14 07:25 p		0.9439	ASCBMB
						6.02E-02	1.00E+00	(3.6)			L	
Batch: 4321033 RL-RA-001 Work Order: M5H421AC Report DB ID: 9M5H4210												
Ra-228	6.63E-01	J	3.1E-01	3.2E-01	5.90E-01	pCi/L	77%	(1.1)	12/11/14 03:48 p		0.9439	GPC3A
						2.60E-01	1.00E+00	(4.1)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 48997 Collection Date: 11/13/2014
Lot-Sample No.: J4K140428-8 Report No.: 63983 Received Date: 11/14/2014 11:00:00 AM
Client Sample ID: DUP-1(OU-1)(400-98418-8) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001 Work Order: M5H481AA Report DB ID: 9M5H4810												
Ra-226	1.50E-01	U	9.8E-02	1.1E-01	1.54E-01	pCi/L	92%	0.98	12/9/14 07:35 p		0.9218	ASCMRA
						6.64E-02	1.00E+00	(2.9)			L	
Batch: 4321033 RL-RA-001 Work Order: M5H481AC Report DB ID: 9M5H4810												
Ra-228	1.58E-02	U	1.8E-01	3.4E-01	8.04E-01	pCi/L	77%	0.02	12/11/14 03:49 p		0.9218	GPC4C
						3.66E-01	1.00E+00	0.09			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 48997 Collection Date: 11/13/2014
Lot-Sample No.: J4K140428-6 Report No.: 63983 Received Date: 11/14/2014 11:00:00 AM
Client Sample ID: DUP-2(400-98418-6) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001 9.09E-01 J 2.0E-01 2.8E-01 Work Order: M5H461AA Report DB ID: 9M5H4610												
Ra-226					1.74E-01	pCi/L	84%	(5.2)	12/9/14 07:35 p		0.9257	ASCJMC
						7.48E-02	1.00E+00	(6.5)			L	
Batch: 4321033 RL-RA-001 1.39E+00 J 4.0E-01 4.3E-01 Work Order: M5H461AC Report DB ID: 9M5H4610												
Ra-228					6.66E-01	pCi/L	75%	(2.1)	12/11/14 03:49 p		0.9257	GPC4A
						2.96E-01	1.00E+00	(6.4)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 22-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K140428-7
Client Sample ID: DUP-4(400-98418-7)

SDG: 48997
Report No.: 63983
COC No.:
Collection Date: 11/13/2014
Received Date: 11/14/2014 11:00:00 AM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001												
Ra-226	4.44E-01	J	1.1E-01	1.5E-01	1.12E-01	pCi/L	97%	(4.)	12/9/14 07:24 p		0.9432	ASCKAB
							4.84E-02	1.00E+00	(6.)	L		
Batch: 4321033 RL-RA-001												
Ra-228	2.10E+00		4.2E-01	4.9E-01	5.78E-01	pCi/L	83%	(3.6)	12/11/14 03:49 p		0.9432	GPC4B
							2.56E-01	1.00E+00	(8.6)	L		

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM II

Date: 22-Dec-14

DUPLICATE RESULTS

Lab Name: TestAmerica Inc SDG: 48997 Collection Date: 11/13/2014 8:20:00 AM
Lot-Sample No.: J4K140428-1 Report No.: 63983 Received Date: 11/14/2014 11:00:00 AM
Client Sample ID: AC-8D(400-98418-1) DUP COC No.: Matrix: WATER

Parameter	Result, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001 Work Order: M5H411AD Report DB ID: M5H411DR Orig Sa DB ID: 9M5H4110												
Ra-226	7.27E-01	J	1.6E-01	2.3E-01	1.62E-01	pCi/L	98%	(4.5)	12/9/14 07:08 p	0.9291	L	ASCASC
	2.07E-01	J	RER2 4.0			1.00E+00		(6.2)				
Batch: 4321033 RL-RA-001 Work Order: M5H411AE Report DB ID: M5H411ER Orig Sa DB ID: 9M5H4110												
Ra-228	1.28E+00		3.4E-01	3.8E-01	5.34E-01	pCi/L	87%	(2.4)	12/11/14 03:48 p	0.9291	L	GPC2D
	1.14E+00		RER2 0.5			1.00E+00		(6.8)				

No. of Results: 2 Comments:

TestAmerica Inc RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPU)s+sq(TPUd))] as defined by ICPT BOA.
MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.

FORM II
BLANK RESULTS

Date: 22-Dec-14

Lab Name: TestAmerica Inc SDG: 48996
Matrix: WATER Report No. : 63983

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Lc	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4321032												
				Work Order: M5JDW1AA								
Ra-226	6.84E-02	U	8.9E-02	9.1E-02	1.66E-01	pCi/L	75%	0.41	12/9/14 07:35 p		1.0024	ASCNMA
					7.29E-02	1.00E+00		(1.5)			L	
Batch: 4321033												
				Work Order: M5JDX1AA								
Ra-228	3.32E-02	U	2.4E-01	2.8E-01	6.78E-01	pCi/L	70%	0.05	12/11/14 03:49 p		1.0024	GPC4D
					3.02E-01	1.00E+00		0.23			L	

No. of Results: 2 Comments:

FORM II
LCS RESULTS

Date: 22-Dec-14


Lab Name: TestAmerica Inc
Matrix: WATER

SDG: 48996
Report No.: 63983

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL	Report Unit	Yield	Expected	Expected Uncert	Recovery, Bias	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4321032 RL-RA-001													
Ra-226	1.13E+01		6.0E-01	2.3E+00	1.62E-01	pCi/L	86%	9.98E+00	1.13E-01	113%	12/9/14 07:35 p	1.0004	ASCPMA
							Rec Limits:	75	125	0.1			
Batch: 4321033 RL-RA-001													
Ra-228	1.10E+01		7.8E-01	1.4E+00	8.07E-01	pCi/L	81%	9.87E+00	1.13E-01	111%	12/11/14 03:49 p	1.0004	GPC6B
							Rec Limits:	75	125	0.1			

No. of Results: 2 Comments:

Chain of Custody Record



Client Information (Sub Contract Lab) Client Contact: Shipping/Receiving: Company: TestAmerica Laboratories, Inc.		Lab PM: E-Mail: Phone: E-Mail:	Carrier Tracking No(s): Page: Job #:	COC No: 400-65283.1							
Address: 2800 George Washington Way, City: State, Zip: PO #: Phone: Email: Project Name: Site:		Due Date Requested: TAT Requested (days): PO #: WO #: Project #: SSOW#:	Analysis Requested	Preservation Codes: A - HCL B - NaOH C - Zn Acetate D - Nitric Acid E - NaHSO4 F - MeOH G - Amchlor H - Ascorbic Acid I - Ice J - DI Water K - EDTA L - EDA M - Hexane N - None O - AsNaO2 P - Na2O4S Q - Na2SO3 R - Na2S2O3 S - H2SO4 T - TSP Dodecahydrate U - Acetone V - MCAA W - ph 4-5 Z - other (specify) Other:							
Sample Identification - Client ID (Lab ID)		Sample Date	Sample Time	Sample Type (C-Comp, G-Grab)	Matrix (W-water, S-solid, O-waste/soil, BT-Tissue, A-Air)	Field/Filtered Sample (Yes or No)	Sub (Radium 228 by EPA Method 904.0) / Rad 228-Method	Sub (Radium 226 by EPA Method 903.1) / Rad 226-Method	Sub (Radium 226 by EPA Method 903.1) / Rad 226-Method	Total Number of Containers	Special Instructions/Note:
AC-8D (400-98418-1)	M5H41	11/13/14	08:20 Central	Water	Water		X	X		3	D.E.F J4K140428 SDG#48997 Due 12/12/14
ACB-32S (400-98418-2)	M5H42	11/13/14	09:21 Central	Water	Water		X	X		3	
AC-34S (400-98418-3)	M5H43	11/13/14	10:23 Central	Water	Water		X	X		3	
AC-75R (400-98418-4) AC-7SR	M5H44	11/13/14	11:41 Central	Water	Water		X	X		3	
AC-33S (400-98418-5)	M5H45	11/13/14	12:49 Central	Water	Water		X	X		3	
DUP-2 (400-98418-6)	M5H46	11/13/14	Central	Water	Water		X	X		3	
DUP-4 (400-98418-7)	M5H47	11/13/14	Central	Water	Water		X	X		3	
DUP-1 (OU-1) (400-98418-8)	M5H48	11/13/14	Central	Water	Water		X	X		3	
Possible Hazard Identification Unconfirmed Deliverable Requested: I, II, III, IV, Other (specify)		Sample Disposal (A fee may be assessed if samples are retained longer than 1 month) ☐ Return To Client ☐ Disposal By Lab ☐ Archive For _____ Months		Special Instructions/QC Requirements:		Revised Report					
Empty Kit Relinquished by:		Date:		Method of Shipment:		Date/Time:					
Relinquished by: Relinquished by: Relinquished by:		Date/Time: Date/Time: Date/Time:		Company Company Company		Received by: Received by: Received by:					
Custody Seal Intact: Δ Yes Δ No		Custody Seal No.:		Cooler Temperature(s) °C and Other Remarks:		Company ny ny					

Sample Check-in List

REVISED REPORT

Date/Time Received: 11/14/14 1100 Container GM Screen Result: (Airlock) 40 cpm Initials [J]
Sample GM Screen Result (Sample Receiving) 20 cpm Initials [J]

Client: STP SDG #: 48997 SAF #: _____ NA [J]

Lot Number: J4K140428

Chain of Custody # N/A

Shipping Container ID or Air Bill Number : _____ NA [J]

Samples received inside shipping container/cooler/box Yes [J] Continue with 1 through 4. Initial appropriate response.
No [] Go to 5, add comment to #16.

1. Custody Seals on shipping container intact? Yes [] No [] No Custody Seal [J]
2. Custody Seals dated and signed? Yes [] No [] No Custody Seal [J]
3. Cooler temperature: _____ °C NA [J]
4. Vermiculite/packing materials is NA [] Wet [] Dry [J]

Item 5 through 16 for samples. Initial appropriate response.

5. Chain of Custody record present? Yes [J] No []
6. Number of samples received (Each sample may contain multiple bottles): 8
7. Containers received: 24xlp
8. Sample holding times exceeded? NA [] Yes [] No [J]
9. Samples have: _____ tape _____ hazard labels _____ custody seals J appropriate sample labels
10. Matrix: _____ A (FLT, Wipe, Solid, Soil) J I (Water) _____ S (Air, Niosh 7400) _____ T (Biological, Ni-63)
11. Samples:
J are in good condition _____ are leaking _____ are broken
_____ have air bubbles (Only for samples requiring no head space) _____ Other _____
12. Sample pH appropriate for analysis requested Yes [J] No [] NA []
(If acidification is necessary go to pH area & document sample ID, initial pH, amount of HNO₃ added and pH after addition on table)
13. Were any anomalies identified in sample receipt? Yes [] No [J]
14. Description of anomalies (include sample numbers): NA [J] _____
15. Sample Location, Sample Collector Listed on COC? * Yes [] No [J]
*For documentation only. No corrective action needed.
16. Additional Information: NM

[] Client/Courier denied temperature check.

[] Client/Courier unpack cooler.

Sample Check-in List completed by Sample Custodian:

Signature: _____ Date: 11/14/14

Client Notification needed? Yes [] No [] Date: _____

By: _____

Person contacted: _____

[J] No action necessary; process as is

Project Manager: [Signature]

Date: 11/17/14

Chain of Custody Record

Client Information		Lab Pmt: Saviole, Noel		Carrier Tracking No(s):		COC No: 640-48009-12359.4	
Client Contact: Mr. Jeff Wagner		E-Mail: noel.saviole@testamericainc.com		Page: Page 4 of 5			
Company: URS Corporation				Job #:			
Address: 1625 Summit Lake Drive Suite 200				Due Date Requested:			
City: Tallahassee				TAT Requested (days):			
State, Zip: FL, 32317							
Phone: 850-402-6409 (Tel)				PO #:			
Email: jeffrey.wagner@urscorp.com				308649 US			
Project Name: Agrico Pensacola				WO #:			
Site:				12806620.00000 Vendor #1427536			
				Project #:			
				64000434			
				SSOW#:			

Sample Identification	Sample Date	Sample Time	Sample Type (C=comp, G=grab)	Matrix (W=water, S=solid, O=wastefoil, BT=Trace, Asap)	Field Filtered Sample (Yes or No)		Performance MS/MSD (Yes or No)		SUBCONTRACT - Rad 226-Method 903.1 (Richland)		SUBCONTRACT - Rad 228-Method 904.0 (Richland)		300_ORGFM_28D - Chloride and Sulfate		6010B - Arsenic		Total Number of Containers	Special Instructions/Notes:
					S	N	S	N	S	N	S	N	S	N	S	N		
AC-8D	11/13/14	0820	G	W					1	1	2	1					6	
ACB-32S	11/13/14	0921	G	W					1	1	2	1					6	
AC-34S	11/13/14	1023	G	W					1	1	2	1					6	
AC-7SR	11/13/14	1141	G	W					1	1	2	1					6	
AC-33S	11/13/14	1249	G	W					1	1	2	1					6	
DUP-2	11/13/14		G	W					1	1	2	1					6	
DUP-4	11/13/14		G	W					1	1	2	1					6	

Possible Hazard Identification		☐ Non-Hazard ☐ Flammable ☐ Skin Irritant ☐ Poison B ☐ Unknown ☐ Radiological	
Deliverable Requested: I, II, III, IV, Other (specify)			
Empty Kit Relinquished by: <i>Jeffrey W.</i>		Date: 11/15/14	
Relinquished by: <i>Jeffrey W.</i>		Date: 11/13/14	
Relinquished by:		Date: 11/13/14	
Relinquished by:		Date: 11/13/14	
Custody Seals Intact: ☐ Yes ☐ No		Custody Seal No.:	

Sample Disposal (A fee may be assessed if samples are retained longer than 1 month)		☐ Return To Client ☒ Disposal By Lab ☐ Archive For _____ Months	
Special Instructions/QC Requirements:			
Time: 1500		Method of Shipment:	
Relinquished by: <i>Jeffrey W.</i>		Date/Time: 11/13-14 1345	
Relinquished by:		Date/Time:	
Relinquished by:		Date/Time:	
Cooler Temperature(s) °C and Other Remarks: 10°C 0.4°C 0.1°C		Company: <i>URS</i>	

TestAmerica

THE LEADER IN ENVIRONMENTAL TESTING

ANALYTICAL REPORT

TestAmerica Laboratories, Inc.

TestAmerica Pensacola

3355 McLemore Drive

Pensacola, FL 32514

Tel: (850)474-1001

TestAmerica Job ID: 400-98478-1

Client Project/Site: Agrico Pensacola

For:

URS Corporation

1625 Summit Lake Drive

Suite 200

Tallahassee, Florida 32317

Attn: Mr. Jeff Wagner



Authorized for release by:

12/19/2014 9:24:59 AM

Noel Savoie, Project Manager I

(850)878-3994

noel.savoie@testamericainc.com

LINKS

Review your project
results through

TotalAccess

Have a Question?



Visit us at:

www.testamericainc.com

The test results in this report meet all 2003 NELAC and 2009 TNI requirements for accredited parameters, exceptions are noted in this report. This report may not be reproduced except in full, and with written approval from the laboratory. For questions please contact the Project Manager at the e-mail address or telephone number listed on this page.

This report has been electronically signed and authorized by the signatory. Electronic signature is intended to be the legally binding equivalent of a traditionally handwritten signature.

Results relate only to the items tested and the sample(s) as received by the laboratory.

Table of Contents

Cover Page	1
Table of Contents	2
Definitions	3
Case Narrative	4
Sample Summary	5
Client Sample Results	6
QC Sample Results	9
Chronicle	14
Method Summary	16
Subcontract Data	17
Chain of Custody	40



Definitions/Glossary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Qualifiers

General Chemistry

Qualifier	Qualifier Description
F1	MS and/or MSD Recovery exceeds the control limits

Glossary

Abbreviation	These commonly used abbreviations may or may not be present in this report.
α	Listed under the "D" column to designate that the result is reported on a dry weight basis
%R	Percent Recovery
CFL	Contains Free Liquid
CNF	Contains no Free Liquid
DER	Duplicate error ratio (normalized absolute difference)
Dil Fac	Dilution Factor
DL, RA, RE, IN	Indicates a Dilution, Re-analysis, Re-extraction, or additional Initial metals/anion analysis of the sample
DLC	Decision level concentration
MDA	Minimum detectable activity
EDL	Estimated Detection Limit
MDC	Minimum detectable concentration
MDL	Method Detection Limit
ML	Minimum Level (Dioxin)
NC	Not Calculated
ND	Not detected at the reporting limit (or MDL or EDL if shown)
PQL	Practical Quantitation Limit
QC	Quality Control
RER	Relative error ratio
RL	Reporting Limit or Requested Limit (Radiochemistry)
RPD	Relative Percent Difference, a measure of the relative difference between two points
TEF	Toxicity Equivalent Factor (Dioxin)
TEQ	Toxicity Equivalent Quotient (Dioxin)

Case Narrative

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Job ID: 400-98478-1

Laboratory: TestAmerica Pensacola

Narrative

Job Narrative 400-98478-1

Comments

No additional comments.

Receipt

The samples were received on 11/14/2014 3:04 PM; the samples arrived in good condition, properly preserved and, where required, on ice. The temperatures of the 2 coolers at receipt time were 4.3° C and 4.9° C.

HPLC/IC

No analytical or quality issues were noted, other than those described in the Definitions/Glossary page.

General Chemistry

Method 353.2: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-27S (400-98478-2) and PIP-D (400-98478-3). Elevated reporting limits (RLs) are provided.

Method 353.2: The matrix spike/matrix spike duplicate (MS/MSD) recoveries for batch 237814 were outside control limits. Sample matrix interference and/or non-homogeneity are suspected because the associated laboratory control sample (LCS) recovery was within acceptance limits.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Subcontract Work

Methods Radium 226 by EPA Method 903.1, Radium 228 by EPA Method 904.0: These methods were subcontracted to TestAmerica Richland. Report attached.

Sample Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Lab Sample ID	Client Sample ID	Matrix	Collected	Received
400-98478-1	AC-27D	Water	11/13/14 16:00	11/14/14 15:04
400-98478-2	AC-27S	Water	11/13/14 16:42	11/14/14 15:04
400-98478-3	PIP-D	Water	11/14/14 08:52	11/14/14 15:04
400-98478-4	NWD-4S	Water	11/14/14 10:38	11/14/14 15:04
400-98478-5	NWD-4D	Water	11/14/14 11:09	11/14/14 15:04
400-98478-6	AC-6D	Water	11/14/14 13:39	11/14/14 15:04
400-98478-7	EQ-2	Water	11/14/14 10:48	11/14/14 15:04

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Client Sample ID: AC-27D

Lab Sample ID: 400-98478-1

Date Collected: 11/13/14 16:00

Matrix: Water

Date Received: 11/14/14 15:04

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	4.0		1.0		mg/L			12/01/14 14:43	1
Sulfate	10		1.0		mg/L			12/01/14 14:43	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	0.10		0.10		mg/L			11/24/14 09:14	1
Nitrate Nitrite as N	0.095		0.050		mg/L			11/24/14 13:17	1
Nitrate as N	0.095		0.050		mg/L			11/24/14 13:17	1
Nitrite as N	<0.10		0.10		mg/L			11/14/14 16:39	1

Client Sample ID: AC-27S

Lab Sample ID: 400-98478-2

Date Collected: 11/13/14 16:42

Matrix: Water

Date Received: 11/14/14 15:04

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	19		1.0		mg/L			12/01/14 15:52	1
Sulfate	4.5		1.0		mg/L			12/01/14 15:52	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 10:01	1
Nitrate Nitrite as N	1.5		0.10		mg/L			11/24/14 13:14	2
Nitrate as N	1.5		0.050		mg/L			11/24/14 13:14	1
Nitrite as N	<0.10		0.10		mg/L			11/14/14 16:39	1

Client Sample ID: PIP-D

Lab Sample ID: 400-98478-3

Date Collected: 11/14/14 08:52

Matrix: Water

Date Received: 11/14/14 15:04

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	9.0		1.0		mg/L			12/01/14 16:15	1
Sulfate	5.6		1.0		mg/L			12/01/14 16:15	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 10:03	1
Nitrate Nitrite as N	3.7		0.25		mg/L			11/24/14 13:15	5
Nitrate as N	3.7		0.050		mg/L			11/24/14 13:15	1
Nitrite as N	<0.10		0.10		mg/L			11/14/14 16:39	1

Client Sample ID: NWD-4S

Lab Sample ID: 400-98478-4

Date Collected: 11/14/14 10:38

Matrix: Water

Date Received: 11/14/14 15:04

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	4.3		1.0		mg/L			12/01/14 16:37	1
Sulfate	4.8		1.0		mg/L			12/01/14 16:37	1

TestAmerica Pensacola

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Client Sample ID: NWD-4S

Date Collected: 11/14/14 10:38

Date Received: 11/14/14 15:04

Lab Sample ID: 400-98478-4

Matrix: Water

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 09:22	1
Nitrate Nitrite as N	0.41		0.050		mg/L			11/24/14 13:42	1
Nitrate as N	0.41		0.050		mg/L			11/24/14 13:42	1
Nitrite as N	<0.10		0.10		mg/L			11/14/14 16:39	1

Client Sample ID: NWD-4D

Date Collected: 11/14/14 11:09

Date Received: 11/14/14 15:04

Lab Sample ID: 400-98478-5

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	10		1.0		mg/L			12/01/14 19:18	1
Sulfate	28		1.0		mg/L			12/01/14 19:18	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 10:05	1
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/24/14 13:21	1
Nitrate as N	<0.050		0.050		mg/L			11/24/14 13:16	1
Nitrite as N	<0.10		0.10		mg/L			11/14/14 16:39	1

Client Sample ID: AC-6D

Date Collected: 11/14/14 13:39

Date Received: 11/14/14 15:04

Lab Sample ID: 400-98478-6

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	7.0		1.0		mg/L			12/01/14 18:55	1
Sulfate	43		1.0		mg/L			12/01/14 18:55	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 10:09	1
Nitrate Nitrite as N	4.7		0.25		mg/L			11/24/14 13:22	5
Nitrate as N	4.7		0.050		mg/L			11/24/14 13:21	1
Nitrite as N	<0.10		0.10		mg/L			11/14/14 16:39	1

Client Sample ID: EQ-2

Date Collected: 11/14/14 10:48

Date Received: 11/14/14 15:04

Lab Sample ID: 400-98478-7

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/01/14 18:32	1
Sulfate	<1.0		1.0		mg/L			12/01/14 18:32	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 11:21	1
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/24/14 13:16	1
Nitrate as N	<0.050		0.050		mg/L			11/24/14 13:22	1

TestAmerica Pensacola

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Client Sample ID: EQ-2

Date Collected: 11/14/14 10:48

Date Received: 11/14/14 15:04

Lab Sample ID: 400-98478-7

Matrix: Water

General Chemistry (Continued)

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/14/14 16:40	1

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Method: 300.0 - Anions, Ion Chromatography

Lab Sample ID: MB 400-238428/4

Matrix: Water

Analysis Batch: 238428

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/01/14 13:34	1
Sulfate	<1.0		1.0		mg/L			12/01/14 13:34	1

Lab Sample ID: LCS 400-238428/5

Matrix: Water

Analysis Batch: 238428

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	10.3		mg/L		103	90 - 110
Sulfate	10.0	10.7		mg/L		107	90 - 110

Lab Sample ID: LCSD 400-238428/6

Matrix: Water

Analysis Batch: 238428

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	10.2		mg/L		102	90 - 110	1	15
Sulfate	10.0	10.5		mg/L		105	90 - 110	1	15

Lab Sample ID: 400-98478-1 MS

Matrix: Water

Analysis Batch: 238428

Client Sample ID: AC-27D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	4.0		10.0	13.6		mg/L		97	80 - 120
Sulfate	10		10.0	20.6		mg/L		104	80 - 120

Lab Sample ID: 400-98478-1 MSD

Matrix: Water

Analysis Batch: 238428

Client Sample ID: AC-27D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	4.0		10.0	13.9		mg/L		99	80 - 120	2	20
Sulfate	10		10.0	21.4		mg/L		112	80 - 120	4	20

Lab Sample ID: 400-98478-4 MS

Matrix: Water

Analysis Batch: 238428

Client Sample ID: NWD-4S

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	4.3		10.0	14.1		mg/L		98	80 - 120
Sulfate	4.8		10.0	15.2		mg/L		104	80 - 120

Lab Sample ID: 400-98478-4 MSD

Matrix: Water

Analysis Batch: 238428

Client Sample ID: NWD-4S

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	4.3		10.0	13.9		mg/L		97	80 - 120	1	20

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Method: 300.0 - Anions, Ion Chromatography (Continued)

Lab Sample ID: 400-98478-4 MSD

Matrix: Water

Analysis Batch: 238428

Client Sample ID: NWD-4S

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Sulfate	4.8		10.0	14.9		mg/L		101	80 - 120	2	20

Method: 340.2 - Fluoride

Lab Sample ID: MB 400-237758/3

Matrix: Water

Analysis Batch: 237758

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 09:06	1

Lab Sample ID: LCS 400-237758/4

Matrix: Water

Analysis Batch: 237758

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.30		mg/L		108	90 - 110

Lab Sample ID: 400-98478-1 MS

Matrix: Water

Analysis Batch: 237758

Client Sample ID: AC-27D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	0.10		1.00	1.21		mg/L		111	74 - 125

Lab Sample ID: 400-98478-1 MSD

Matrix: Water

Analysis Batch: 237758

Client Sample ID: AC-27D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Fluoride	0.10		1.00	1.19		mg/L		109	74 - 125	2	4

Lab Sample ID: 400-98478-4 MS

Matrix: Water

Analysis Batch: 237758

Client Sample ID: NWD-4S

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	<0.10		1.00	1.08		mg/L		108	74 - 125

Lab Sample ID: 400-98478-4 MSD

Matrix: Water

Analysis Batch: 237758

Client Sample ID: NWD-4S

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Fluoride	<0.10		1.00	1.08		mg/L		108	74 - 125	0	4

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Method: 340.2 - Fluoride (Continued)

Lab Sample ID: MB 400-237785/3

Matrix: Water

Analysis Batch: 237785

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 11:11	1

Lab Sample ID: LCS 400-237785/4

Matrix: Water

Analysis Batch: 237785

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.30		mg/L		108	90 - 110

Lab Sample ID: 400-98478-7 MS

Matrix: Water

Analysis Batch: 237785

Client Sample ID: EQ-2

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	<0.10		1.00	1.08		mg/L		108	74 - 125

Lab Sample ID: 400-98478-7 MSD

Matrix: Water

Analysis Batch: 237785

Client Sample ID: EQ-2

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Fluoride	<0.10		1.00	1.08		mg/L		108	74 - 125	0	4

Method: 353.2 - Nitrogen, Nitrate-Nitrite

Lab Sample ID: MB 400-237814/14

Matrix: Water

Analysis Batch: 237814

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/24/14 12:58	1

Lab Sample ID: MB 400-237814/46

Matrix: Water

Analysis Batch: 237814

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/24/14 13:40	1

Lab Sample ID: LCS 400-237814/15

Matrix: Water

Analysis Batch: 237814

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.469		mg/L		94	90 - 110

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Method: 353.2 - Nitrogen, Nitrate-Nitrite (Continued)

Lab Sample ID: LCS 400-237814/47

Matrix: Water

Analysis Batch: 237814

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.502		mg/L		100	90 - 110

Lab Sample ID: MRL 400-237814/12

Matrix: Water

Analysis Batch: 237814

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	<0.050		mg/L		86	50 - 150

Lab Sample ID: 400-98478-1 MS

Matrix: Water

Analysis Batch: 237814

Client Sample ID: AC-27D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.095		0.500	0.530	F1	mg/L		87	90 - 110

Lab Sample ID: 400-98478-1 MSD

Matrix: Water

Analysis Batch: 237814

Client Sample ID: AC-27D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Nitrate Nitrite as N	0.095		0.500	0.529	F1	mg/L		87	90 - 110	0	4

Lab Sample ID: 400-98478-4 MS

Matrix: Water

Analysis Batch: 237814

Client Sample ID: NWD-4S

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.41		0.500	0.886		mg/L		96	90 - 110

Lab Sample ID: 400-98478-4 MSD

Matrix: Water

Analysis Batch: 237814

Client Sample ID: NWD-4S

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Nitrate Nitrite as N	0.41		0.500	0.868		mg/L		92	90 - 110	2	4

Method: SM 4500 NO2 B - Nitrogen, Nitrite

Lab Sample ID: MB 400-236891/6

Matrix: Water

Analysis Batch: 236891

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/14/14 16:15	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Method: SM 4500 NO2 B - Nitrogen, Nitrite (Continued)

Lab Sample ID: LCS 400-236891/7

Matrix: Water

Analysis Batch: 236891

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.276		mg/L		92	90 - 110

Lab Sample ID: MRL 400-236891/3

Matrix: Water

Analysis Batch: 236891

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.100	<0.10		mg/L		97	50 - 150

Lab Sample ID: 400-98478-1 MS

Matrix: Water

Analysis Batch: 236891

Client Sample ID: AC-27D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	<0.10		0.100	<0.10		mg/L		99	80 - 118

Lab Sample ID: 400-98478-1 MSD

Matrix: Water

Analysis Batch: 236891

Client Sample ID: AC-27D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Nitrite as N	<0.10		0.100	<0.10		mg/L		98	80 - 118	0	9

Lab Sample ID: 400-98478-4 MS

Matrix: Water

Analysis Batch: 236891

Client Sample ID: NWD-4S

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	<0.10		0.100	<0.10		mg/L		97	80 - 118

Lab Sample ID: 400-98478-4 MSD

Matrix: Water

Analysis Batch: 236891

Client Sample ID: NWD-4S

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Nitrite as N	<0.10		0.100	<0.10		mg/L		98	80 - 118	1	9

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Client Sample ID: AC-27D

Date Collected: 11/13/14 16:00

Date Received: 11/14/14 15:04

Lab Sample ID: 400-98478-1

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 14:43	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237758	11/24/14 09:14	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237814	11/24/14 13:17	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237952	11/24/14 13:17	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236891	11/14/14 16:39	LSS	TAL PEN

Client Sample ID: AC-27S

Date Collected: 11/13/14 16:42

Date Received: 11/14/14 15:04

Lab Sample ID: 400-98478-2

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 15:52	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237758	11/24/14 10:01	SLT	TAL PEN
Total/NA	Analysis	353.2		2	237814	11/24/14 13:14	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237952	11/24/14 13:14	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236891	11/14/14 16:39	LSS	TAL PEN

Client Sample ID: PIP-D

Date Collected: 11/14/14 08:52

Date Received: 11/14/14 15:04

Lab Sample ID: 400-98478-3

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 16:15	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237758	11/24/14 10:03	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237814	11/24/14 13:15	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237952	11/24/14 13:15	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236891	11/14/14 16:39	LSS	TAL PEN

Client Sample ID: NWD-4S

Date Collected: 11/14/14 10:38

Date Received: 11/14/14 15:04

Lab Sample ID: 400-98478-4

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 16:37	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237758	11/24/14 09:22	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237814	11/24/14 13:42	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237952	11/24/14 13:42	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236891	11/14/14 16:39	LSS	TAL PEN

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Client Sample ID: NWD-4D

Lab Sample ID: 400-98478-5

Date Collected: 11/14/14 11:09

Matrix: Water

Date Received: 11/14/14 15:04

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 19:18	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237758	11/24/14 10:05	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237814	11/24/14 13:21	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237952	11/24/14 13:16	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236891	11/14/14 16:39	LSS	TAL PEN

Client Sample ID: AC-6D

Lab Sample ID: 400-98478-6

Date Collected: 11/14/14 13:39

Matrix: Water

Date Received: 11/14/14 15:04

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 18:55	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237758	11/24/14 10:09	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237814	11/24/14 13:22	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237952	11/24/14 13:21	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236891	11/14/14 16:39	LSS	TAL PEN

Client Sample ID: EQ-2

Lab Sample ID: 400-98478-7

Date Collected: 11/14/14 10:48

Matrix: Water

Date Received: 11/14/14 15:04

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 18:32	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 11:21	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237814	11/24/14 13:16	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237952	11/24/14 13:22	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	236891	11/14/14 16:40	LSS	TAL PEN

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Method Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98478-1

Method	Method Description	Protocol	Laboratory
300.0	Anions, Ion Chromatography	MCAWW	TAL PEN
340.2	Fluoride	MCAWW	TAL PEN
353.2	Nitrogen, Nitrate-Nitrite	MCAWW	TAL PEN
Nitrate by calc	Nitrogen, Nitrate	SM	TAL PEN
SM 4500 NO2 B	Nitrogen, Nitrite	SM	TAL PEN
Rad 226-Method 903.1 (Richland)	RAD-226 (RCH)	NONE	TAL RCH
Rad 228-Method 904.0 (Richland)	RAD-228 (RCH)	NONE	TAL RCH

Protocol References:

MCAWW = "Methods For Chemical Analysis Of Water And Wastes", EPA-600/4-79-020, March 1983 And Subsequent Revisions.

NONE = NONE

SM = "Standard Methods For The Examination Of Water And Wastewater",

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Analytical Data Package Prepared For

TestAmerica Pensacola

Radiochemical Analysis By

TestAmerica Inc

2800 G.W. Way, Richland Wa, 99354, (509)-375-3131.

Assigned Laboratory Code: TARL

Data Package Contains _____ Pages

Report No.: 63912

Results in this report relate only to the sample(s) analyzed.

SDG No.	Order No.	Client Sample ID (List Order)	Lot-Sa No.	Work Order	Report DB ID	Batch No.
49016		AC-27D(400-98478-1)	J4K190425-1	M5J7J1AA	9M5J7J10	4325026
		AC-27D(400-98478-1)	J4K190425-1	M5J7J1AC	9M5J7J10	4325027
		AC-27S(400-98478-2)	J4K190425-2	M5J7K1AA	9M5J7K10	4325026
		AC-27S(400-98478-2)	J4K190425-2	M5J7K1AC	9M5J7K10	4325027
		AC-6D(400-98478-6)	J4K190425-6	M5J7P1AA	9M5J7P10	4325026
		AC-6D(400-98478-6)	J4K190425-6	M5J7P1AC	9M5J7P10	4325027
		EQ-2(400-98478-7)	J4K190425-7	M5J7Q1AA	9M5J7Q10	4325026
		EQ-2(400-98478-7)	J4K190425-7	M5J7Q1AC	9M5J7Q10	4325027
		NWD-4D(400-98478-5)	J4K190425-5	M5J7N1AA	9M5J7N10	4325026
		NWD-4D(400-98478-5)	J4K190425-5	M5J7N1AC	9M5J7N10	4325027
		NWD-4S(400-98478-4)	J4K190425-4	M5J7M1AA	9M5J7M10	4325026
		NWD-4S(400-98478-4)	J4K190425-4	M5J7M1AC	9M5J7M10	4325027
		PIP-D(400-98478-3)	J4K190425-3	M5J7L1AA	9M5J7L10	4325026
		PIP-D(400-98478-3)	J4K190425-3	M5J7L1AC	9M5J7L10	4325027

Certificate of Analysis

December 17, 2014

TestAmerica Pensacola
3355 McLemore Drive
Pensacola, FL 32514

Attention: Noel Savoie

Date Received at Lab	:	November 15, 2014
Project Name/Number	:	Agrico Pensacola/64000434
Sample Type	:	Seven (7) Water
Job Number	:	400-98478-1
SDG Number	:	49016

CASE NARRATIVE

I. Introduction

On November 15, 2014, seven water samples were received at TestAmerica's Richland laboratory for radiochemical analysis. Upon receipt, the samples were assigned the TestAmerica identification number as described on the cover page of the Analytical Data Package report form. The samples were assigned to Lot Numbers J4K190425.

II. Sample Receipt

The samples were received in good condition and no anomalies were noted upon check-in.

III. Analytical Results/Methodology

The analytical results for this report are presented by laboratory sample ID. Each set of data includes sample identification information; analytical results and the appropriate associated statistical uncertainties.

The analysis requested was:

Gas Proportional Counting

Radium-228 by method RL-RA-001

Alpha Scintillation Counting

Radium-226 by method RL-RA-001

IV. Quality Control

The analytical result for each analysis performed includes a minimum of one laboratory control sample (LCS), and one reagent blank sample analysis. Any exceptions have been noted in the "Comments" section.

V. Comments

Gas Proportional Counting

Radium-228

The LCS, batch blank, sample duplicate and sample results are within acceptance limits.

Alpha Scintillation Counting

Radium 226:

The LCS, batch blank, samples and sample duplicate results are within acceptance limits.

I certify that this Certificate of Analysis is in compliance with the SOW and/or NELAC, both technically and for completeness, for other than the conditions detailed above. The Laboratory Manager or a designee, as verified by the following signature has authorized release of the data contained in this hard copy data package.

Reviewed and approved:

Robin Ebert-Mays
Project Manager

Drinking Water Method Cross References

DRINKING WATER ASTM METHOD CROSS REFERENCES		
Referenced Method	Isotope(s)	TestAmerica Richland's SOP No.
EPA 901.1	Cs-134, I-131	RL-GAM-001
EPA 900.0	Alpha & Beta	RL-GPC-001
EPA 00-02	Gross Alpha (Coprecipitation)	RL-GPC-002
EPA 903.0	Total Alpha Radium (Ra-226)	RL-RA-002
EPA 903.1	Ra-226	RL-RA-001
EPA 904.0	Ra-228	RL-RA-001
EPA 905.0	Sr-89/90	RL-GPC-003
ASTM D5174	Uranium	RL-KPA-003
EPA 906.0	Tritium	RL-LSC-005

Results in this report relate only to the sample(s) analyzed.

Uncertainty Estimation

TestAmerica Richland has adopted the internationally accepted approach to estimating uncertainties described in "NIST Technical Note 1297, 1994 Edition". The approach, "Law of Propagation of Errors", involves the identification of all variables in an analytical method which are used to derive a result. These variables are related to the analytical result (R) by some functional relationship, $R = \text{constants} * f(x,y,z,...)$. The components (x,y,z) are evaluated to determine their contribution to the overall method uncertainty. The individual component uncertainties (u_i) are then combined using a statistical model that provides the most probable overall uncertainty value. All component uncertainties are categorized as type A, evaluated by statistical methods, or type B, evaluated by other means. Uncertainties not included in the components, such as sample homogeneity, are combined with the component uncertainty as the square root of the sum-of-the-squares of the individual uncertainties. The uncertainty associated with the derived result is the combined uncertainty (u_c) multiplied by the coverage factor (1,2, or 3).

When three or more sample replicates are used to derive the analytical result, the type A uncertainty is the standard deviation of the mean value ($S/\sqrt{n}$), where S is the standard deviation of the derived results. The type B uncertainties are all other random or non-random components that are not included in the standard deviation.

The derivation of the general "Law of Propagation of Errors" equations and specific example are available on request.

Report Definitions

Action Lev	An agreed upon activity level used to trigger some action when the final result is greater than or equal to the Action Level. Often the Action Level is related to the Decision Limit.
Batch	The QC preparation batch number that relates laboratory samples to QC samples that were prepared and analyzed together.
Bias	Defined by the equation (Result/Expected)-1 as defined by ANSI N13.30.
COC No	Chain of Custody Number assigned by the Client or TestAmerica.
Count Error (#s)	Poisson counting statistics of the gross sample count and background. The uncertainty is absolute and in the same units as the result. For Liquid Scintillation Counting (LSC) the batch blank count is the background.
Total Uncert (#s) <i>u_c - Combined Uncertainty.</i>	All known uncertainties associated with the preparation and analysis of the sample are propagated to give a measure of the uncertainty associated with the result, <i>u_c the combined uncertainty</i> . The uncertainty is absolute and in the same units as the result.
(#s), Coverage Factor	The coverage factor defines the width of the confidence interval, 1, 2 or 3 standard deviations.
CRDL (RL)	Contractual Required Detection Limit as defined in the Client's Statement Of Work or TestAmerica "default" nominal detection limit. Often referred to the reporting level (RL)
Lc	Decision Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume associated with the sample. The Type I error probability is approximately 5%. $Lc = (1.645 * \sqrt{2 * (BkgndCnt / BkgndCntMin) / SCntMin}) * (ConvFct / (Eff * Yld * Abn * Vol) * IngrFct)$. For LSC methods the batch blank is used as a measure of the background variability. Lc cannot be calculated when the background count is zero.
Lot-Sample No	The number assigned by the LIMS software to track samples received on the same day for a given client. The sample number is a sequential number assigned to each sample in the Lot.
MDC MDA	Detection Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume with a Type I and II error probability of approximately 5%. $MDC = (4.65 * \sqrt{(BkgndCnt / BkgndCntMin) / SCntMin}) + 2.71 / SCntMin * (ConvFct / (Eff * Yld * Abn * Vol) * IngrFct)$. For LSC methods the batch blank is used as a measure of the background variability.
Primary Detector	The instrument identifier associated with the analysis of the sample aliquot.
Ratio U-234/U-238	The U-234 result divided by the U-238 result. The U-234/U-238 ratio for natural uranium in NIST SRM 4321C is 1.038.
Rst/MDC	Ratio of the Result to the MDC. A value greater than 1 may indicate activity above background at a high level of confidence. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Rst/TotUcert	Ratio of the Result to the Total Uncertainty. If the uncertainty has a coverage factor of 2 a value greater than 1 may indicate activity above background at approximately the 95% level of confidence assuming a two-sided confidence interval. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Report DB No	Sample Identifier used by the report system. The number is based upon the first five digits of the Work Order Number.
RER	The equation Replicate Error Ratio = $(S-D) / [\sqrt{TPUs^2 + TPUD^2}]$ as defined by ICPT BOA where S is the original sample result, D is the result of the duplicate, TPUs is the total uncertainty of the original sample and TPUD is the total uncertainty of the duplicate sample.
SDG	Sample Delivery Group Number assigned by the Client or assigned by TestAmerica upon sample receipt.
Sum Rpt Alpha Spec Rst(s)	The sum of the reported alpha spec results for tests derived from the same sample excluding duplicate result where the results are in the same units.
Work Order	The LIMS software assign test specific identifier.
Yield	The recovery of the tracer added to the sample such as Pu-242 used to trace a Pu-239/40 method.

Sample Results Summary

Date: 17-Dec-14

TestAmerica Inc TARL

Ordered by Method, Batch No., Client Sample ID.

Report No. : 63912

SDG No: 49016

Batch	Client Id Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	MDL	CRDL	RER2
4325026	RL-RA-001								
	AC-27D(400-98478-1)								
	M5J7J1AA Ra-226		1.36E-01 +- 9.6E-02	U	pCi/L	96%	1.44E-01	1.00E+00	
	AC-27S(400-98478-2)								
	M5J7K1AA Ra-226		7.85E-01 +- 2.5E-01	J	pCi/L	100%	2.39E-01	1.00E+00	
	AC-27S(400-98478-2) DUP								
	M5J7K1AE Ra-226		7.42E-01 +- 3.2E-01	J	pCi/L	64%	3.79E-01	1.00E+00	0.2
	AC-6D(400-98478-6)								
	M5J7P1AA Ra-226		3.41E+00 +- 9.5E-01		pCi/L	77%	2.36E-01	1.00E+00	
	EQ-2(400-98478-7)								
	M5J7Q1AA Ra-226		9.94E-03 +- 9.3E-02	U	pCi/L	100%	2.00E-01	1.00E+00	
	NWD-4D(400-98478-5)								
	M5J7N1AA Ra-226		1.85E+00 +- 5.7E-01		pCi/L	100%	2.38E-01	1.00E+00	
	NWD-4S(400-98478-4)								
	M5J7M1AA Ra-226		5.15E-01 +- 2.2E-01	J	pCi/L	89%	2.37E-01	1.00E+00	
	PIP-D(400-98478-3)								
	M5J7L1AA Ra-226		1.39E+00 +- 4.2E-01		pCi/L	100%	2.91E-01	1.00E+00	
4325027	RL-RA-001								
	AC-27D(400-98478-1)								
	M5J7J1AC Ra-228		5.82E-01 +- 3.6E-01	U	pCi/L	86%	7.30E-01	1.00E+00	
	AC-27S(400-98478-2)								
	M5J7K1AC Ra-228		2.11E+00 +- 4.8E-01		pCi/L	93%	6.69E-01	1.00E+00	
	AC-27S(400-98478-2) DUP								
	M5J7K1AD Ra-228		2.64E+00 +- 6.2E-01		pCi/L	59%	7.17E-01	1.00E+00	1.4
	AC-6D(400-98478-6)								
	M5J7P1AC Ra-228		2.26E+00 +- 5.4E-01		pCi/L	70%	6.56E-01	1.00E+00	
	EQ-2(400-98478-7)								
	M5J7Q1AC Ra-228		2.13E-01 +- 2.3E-01	U	pCi/L	91%	4.92E-01	1.00E+00	
	NWD-4D(400-98478-5)								
	M5J7N1AC Ra-228		4.22E+00 +- 6.9E-01		pCi/L	92%	4.99E-01	1.00E+00	
	NWD-4S(400-98478-4)								
	M5J7M1AC Ra-228		1.17E+00 +- 3.7E-01		pCi/L	82%	5.28E-01	1.00E+00	
	PIP-D(400-98478-3)								
	M5J7L1AC Ra-228		1.86E+00 +- 4.1E-01		pCi/L	92%	4.43E-01	1.00E+00	
No. of Results: 16									

TestAmerica Inc
rptTALRchSaSum
mary2 V5.3.6.1
A2002

RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPUs)+sq(TPUD))] as defined by ICPT BOA.

J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

QC Results Summary
TestAmerica Inc TARL
 Ordered by Method, Batch No, QC Type,.

Date: 17-Dec-14

Report No. : 63912

SDG No.: 49016

Batch	Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	LCS Recovery	Bias	MDL
RL-RA-001									
4325026 MATRIX SPIKE, AC-27D(400-98478-1)									
	M5J7J1AJ	Ra-226	1.02E+01 +- 2.1E+00		pCi/L	100%	97%	0.0	2.43E-01
	M5J7J1AH	Ra-226	1.11E+01 +- 2.5E+00		pCi/L	94%	105%	0.0	1.76E-01
4325026 BLANK QC,									
	M5KNM1AA	Ra-226	3.92E-02 +- 8.7E-02	U	pCi/L	99%			1.73E-01
4325026 LCS,									
	M5KNM1AC	Ra-226	1.18E+01 +- 2.4E+00		pCi/L	96%	119%	0.2	2.21E-01
4325026 MATRIX SPIKE, NWD-4S(400-98478-4)									
	M5J7M1AG	Ra-226	1.12E+01 +- 2.9E+00		pCi/L	100%	107%	0.1	2.36E-01
	M5J7M1AF	Ra-226	1.46E+01 +- 3.2E+00		pCi/L	91%	139%	0.4	2.80E-01
RL-RA-001									
4325027 MATRIX SPIKE, AC-27D(400-98478-1)									
	M5J7J1AG	Ra-228	9.12E+00 +- 1.3E+00		pCi/L	93%	87%	-0.1	7.20E-01
	M5J7J1AF	Ra-228	1.04E+01 +- 1.5E+00		pCi/L	85%	99%	0.0	6.92E-01
4325027 BLANK QC,									
	M5KNP1AA	Ra-228	3.80E-01 +- 2.5E-01	U	pCi/L	91%			4.88E-01
4325027 LCS,									
	M5KNP1AC	Ra-228	9.81E+00 +- 1.4E+00		pCi/L	88%	100%	0.0	5.09E-01
4325027 MATRIX SPIKE, NWD-4S(400-98478-4)									
	M5J7M1AE	Ra-228	9.50E+00 +- 1.5E+00		pCi/L	92%	91%	-0.1	4.16E-01
	M5J7M1AD	Ra-228	7.50E+00 +- 1.3E+00		pCi/L	73%	72%	-0.3	5.96E-01

No. of Results: 12

FORM I

Date: 17-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49016 Collection Date: 11/13/2014 4:00:00 PM
Lot-Sample No.: J4K190425-1 Report No.: 63912 Received Date: 11/15/2014 11:00:00 AM
Client Sample ID: AC-27D(400-98478-1) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325026 RL-RA-001 Work Order: M5J7J1AA Report DB ID: 9M5J7J10												
Ra-226	1.36E-01	U	9.2E-02	9.6E-02	1.44E-01	pCi/L	96%	0.95	12/12/14 09:50 p		0.9416	ASC1MB
						6.15E-02	1.00E+00	(2.8)			L	
Batch: 4325027 RL-RA-001 Work Order: M5J7J1AC Report DB ID: 9M5J7J10												
Ra-228	5.82E-01	U	3.5E-01	3.6E-01	7.30E-01	pCi/L	86%	0.8	12/16/14 12:36 p		0.9416	GPC1A
						3.38E-01	1.00E+00	(3.2)			L	
No. of Results: 2 Comments:												

FORM I

Date: 17-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 49016

Collection Date: 11/13/2014 4:42:00 PM

Lot-Sample No.: J4K190425-2

Report No. : 63912

Received Date: 11/15/2014 11:00:00 AM

Client Sample ID: AC-27S(400-98478-2)

COC No. :

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325026 RL-RA-001												
Ra-226	7.85E-01	J	2.0E-01	2.5E-01	2.39E-01	pCi/L	100%	(3.3)	12/12/14 09:51 p		0.9073	ASC5HA
						1.09E-01	1.00E+00	(6.3)			L	
Batch: 4325027 RL-RA-001												
Ra-228	2.11E+00		4.1E-01	4.8E-01	6.69E-01	pCi/L	93%	(3.2)	12/16/14 12:36 p		0.9073	GPC1D
						3.09E-01	1.00E+00	(8.8)			L	

No. of Results: 2

Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mdal/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 17-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 49016

Collection Date: 11/14/2014 1:39:00 PM

Lot-Sample No.: J4K190425-6

Report No. : 63912

Received Date: 11/15/2014 11:00:00 AM

Client Sample ID: AC-6D(400-98478-6)

COC No. :

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325026 RL-RA-001												
Ra-226	3.41E+00		3.9E-01	9.5E-01	2.36E-01	pCi/L	77%	(14.4)	12/12/14 10:04 p		0.9096	ASCFRM
						1.04E-01	1.00E+00	(7.2)			L	
Batch: 4325027 RL-RA-001												
Ra-228	2.26E+00		4.7E-01	5.4E-01	6.56E-01	pCi/L	70%	(3.4)	12/16/14 12:31 p		0.9096	GPC3C
						2.90E-01	1.00E+00	(8.4)			L	

No. of Results: 2

Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 17-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49016 Collection Date: 11/14/2014 10:48:00 AM
Lot-Sample No.: J4K190425-7 Report No.: 63912 Received Date: 11/15/2014 11:00:00 AM
Client Sample ID: EQ-2(400-98478-7) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325026 RL-RA-001												
Ra-226	9.94E-03	U	9.3E-02	9.3E-02	2.00E-01	pCi/L	100%	0.05	12/12/14 10:05 p		0.9052	ASCGMB
							Report DB ID: 9M5J7Q1AA	Report DB ID: 9M5J7Q10				
							8.65E-02	1.00E+00				
								0.21				
Batch: 4325027 RL-RA-001												
Ra-228	2.13E-01	U	2.1E-01	2.3E-01	4.92E-01	pCi/L	91%	0.43	12/16/14 12:31 p		0.9052	GPC3D
							Report DB ID: 9M5J7Q1AC	Report DB ID: 9M5J7Q10				
							2.16E-01	1.00E+00	(1.9)			

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 17-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K190425-5
Client Sample ID: NWD-4D(400-98478-5)

SDG: 49016
Report No.: 63912
COC No.:

Collection Date: 11/14/2014 11:09:00 AM
Received Date: 11/15/2014 11:00:00 AM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325026 RL-RA-001												
Ra-226	1.85E+00		2.8E-01	5.7E-01	2.38E-01	pCi/L	100%	(7.8)	12/12/14 10:05 p		0.8668	ASCEHA
						1.07E-01	1.00E+00	(6.5)			L	
Batch: 4325027 RL-RA-001												
Ra-228	4.22E+00		5.0E-01	6.9E-01	4.99E-01	pCi/L	92%	(8.4)	12/16/14 12:31 p		0.8868	GPC3B
						2.20E-01	1.00E+00	(12.2)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I
SAMPLE RESULTS

Date: 17-Dec-14

Lab Name: TestAmerica Inc SDG: 49016 Collection Date: 11/14/2014 10:38:00 AM
Lot-Sample No.: J4K190425-4 Report No.: 63912 Received Date: 11/15/2014 11:00:00 AM
Client Sample ID: NWD-4S(400-98478-4) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325026 RL-RA-001 5.15E-01 J 1.8E-01 2.2E-01 2.37E-01 pCi/L Report DB ID: 9M5J7M10 89% (2.2) 12/12/14 09:52 p 0.9336 ASC9RA												
Ra-226 1.05E-01 1.00E+00 (4.6)												
Batch: 4325027 RL-RA-001 1.17E+00 3.4E-01 3.7E-01 5.28E-01 pCi/L Report DB ID: 9M5J7M10 82% (2.2) 12/16/14 12:36 p 0.9336 GPC2C												
Ra-228 2.30E-01 1.00E+00 (6.4)												

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.



FORM I

Date: 17-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 49016

Collection Date: 11/14/2014 8:52:00 AM

Lot-Sample No.: J4K190425-3

Report No. : 63912

Received Date: 11/15/2014 11:00:00 AM

Client Sample ID: PIP-D(400-98478-3)

COC No. :

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325026 RL-RA-001												
Work Order: M5J7L1AA Report DB ID: 9M5J7L10												
Ra-226	1.39E+00		2.6E-01	4.2E-01	2.91E-01	pCi/L	100%	(4.8)	12/12/14 09:52 p		0.9436	ASC8HA
						1.34E-01	1.00E+00	(6.6)			L	
Batch: 4325027 RL-RA-001												
Work Order: M5J7L1AC Report DB ID: 9M5J7L10												
Ra-228	1.86E+00		3.5E-01	4.1E-01	4.43E-01	pCi/L	92%	(4.2)	12/16/14 12:36 p		0.9436	GPC2B
						1.92E-01	1.00E+00	(9.)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM II

Date: 17-Dec-14

DUPLICATE RESULTS

Lab Name: TestAmerica Inc

SDG: 49016

Collection Date: 11/13/2014 4:42:00 PM

Lot-Sample No.: J4K190425-2

Report No. : 63912

Received Date: 11/15/2014 11:00:00 AM

Client Sample ID: AC-27S(400-98478-2) DUP

COC No. :

Matrix: WATER

Parameter	Result, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325026												
RL-RA-001												
Work Order: M5J7K1AE												
Ra-226	7.42E-01	J	2.8E-01	3.2E-01	3.79E-01	pCi/L	64%	(2.)	12/12/14 09:51 p	0.9506	L	ASC7RH
	7.85E-01	J	RER2 0.2			1.00E+00		(4.7)				
Batch: 4325027												
RL-RA-001												
Work Order: M5J7K1AD												
Ra-228	2.64E+00		5.4E-01	6.2E-01	7.17E-01	pCi/L	59%	(3.7)	12/16/14 12:36 p	0.9506	L	GPC2A
	2.11E+00		RER2 1.4			1.00E+00		(8.5)				

No. of Results: 2

Comments:

TestAmerica Inc RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPU_s)+sq(TPU_d))] as defined by ICPT BOA.
MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.

FORM II

Date: 17-Dec-14

BLANK RESULTS

Lab Name: TestAmerica Inc

SDG: 49016

Matrix: WATER

Report No. : 63912

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Lc	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUncert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325026												
	RL-RA-001				Work Order: M5KNM1AA							
Ra-226	3.92E-02	U	8.7E-02	8.7E-02	1.73E-01	pCi/L	99%	0.23	12/12/14 10:05 p		1.0	ASCHSB
					7.45E-02	1.00E+00		0.9			L	
Batch: 4325027												
	RL-RA-001				Work Order: M5KNP1AA							
Ra-228	3.80E-01	U	2.4E-01	2.5E-01	4.88E-01	pCi/L	91%	0.78	12/16/14 12:31 p		1.0	GPC4A
					2.17E-01	1.00E+00		(3.1)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

UptSTLRchBlank
V5.3.6.1 A2002



FORM II
LCS RESULTS

Date: 17-Dec-14

Lab Name: TestAmerica Inc

SDG: 49016

Matrix: WATER

Report No.: 63912

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL	Report Unit	Yield	Expected	Expected Uncert	Recovery, Bias	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4325026													
RL-RA-001													
Ra-226	1.18E+01		6.8E-01	2.4E+00	2.21E-01	pCi/L	96%	9.89E+00	1.12E-01	119%	12/13/14 10:13 a	1.0011	ASCJMB
							Rec Limits:	75	125	0.2			
Batch: 4325027													
RL-RA-001													
Ra-228	9.81E+00		7.3E-01	1.4E+00	5.09E-01	pCi/L	88%	9.86E+00	1.13E-01	100%	12/16/14 12:31 p	1.0011	GPC4B
							Rec Limits:	75	125	0.0			

No. of Results: 2 Comments:

FORM II
MATRIX SPIKE RESULTS

Date: 17-Dec-14

Lab Name: TestAmerica Inc SDG: 49016
Lot-Sample No.: J4K190425-1, AC-27D(400-98478-1) Report No.: 63912 Matrix: WATER

Parameter	SpikeResult, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDC MDA	Rpt Unit	Yield	Rec- overy	Expected, Uncert	Analysis, Prep Date	Aliquot Size	Analy Method, Primary Detector
Batch: 4325026												
Ra-226	Work Order: M5J7J1AH			Report DB ID: M5J7J1HW		Orig Sa DB ID: 9M5J7J10						
	1.11E+01		6.1E-01	2.5E+00	1.76E-01 pCi/L	94%	104.91%	1.06E+01	12/12/14 09:50 p	0.9394	L	RL-RA-001
	1.36E-01							1.19E-01				ASC3MA
Batch: 4325026												
Ra-226	Work Order: M5J7J1AJ			Report DB ID: M5J7J1JW		Orig Sa DB ID: 9M5J7J10						
	1.02E+01		6.0E-01	2.1E+00	2.43E-01 pCi/L	100%	96.83%	1.05E+01	12/12/14 09:50 p	0.9425	L	RL-RA-001
	1.36E-01							1.19E-01				ASC4UA
Batch: 4325027												
Ra-228	Work Order: M5J7J1AF			Report DB ID: M5J7J1FW		Orig Sa DB ID: 9M5J7J10						
	1.04E+01		7.7E-01	1.5E+00	6.92E-01 pCi/L	85%	99.36%	1.05E+01	12/16/14 12:36 p	0.9394	L	RL-RA-001
	5.82E-01							1.20E-01				GPC1B
Batch: 4325027												
Ra-228	Work Order: M5J7J1AG			Report DB ID: M5J7J1GW		Orig Sa DB ID: 9M5J7J10						
	9.12E+00		7.1E-01	1.3E+00	7.20E-01 pCi/L	93%	87.46%	1.04E+01	12/16/14 12:36 p	0.9425	L	RL-RA-001
	5.82E-01							1.19E-01				GPC1C

Number of Results: 4

Comments:



FORM II
MATRIX SPIKE RESULTS

Date: 17-Dec-14

Lab Name: TestAmerica Inc SDG: 49016
Lot-Sample No.: J4K190425-4, NWD-4S(400-98478-4) Report No.: 63912 Matrix: WATER

Parameter	SpikeResult, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDC MDA	Rpt Unit	Yield	Rec- overy	Expected, Uncert	Analysis, Prep Date	Aliquot Size	Analy Method, Primary Detector
Batch: 4325026												
Ra-226	1.46E+01		8.5E-01	3.2E+00	2.80E-01	pCi/L	91%	138.70%	1.05E+01	12/12/14 09:50 p	0.9435	RL-RA-001
	5.15E-01								1.18E-01		L	ASCASB
Batch: 4325026												
Ra-226	1.12E+01		6.3E-01	2.9E+00	2.36E-01	pCi/L	100%	107.07%	1.05E+01	12/12/14 10:04 p	0.9455	RL-RA-001
	5.15E-01								1.18E-01		L	ASCDMC
Batch: 4325027												
Ra-228	7.50E+00		7.9E-01	1.3E+00	5.96E-01	pCi/L	73%	71.58%	1.05E+01	12/16/14 12:36 p	0.9435	RL-RA-001
	1.17E+00								1.20E-01		L	GPC2D
Batch: 4325027												
Ra-228	9.50E+00		7.4E-01	1.5E+00	4.16E-01	pCi/L	92%	90.92%	1.05E+01	12/16/14 12:31 p	0.9455	RL-RA-001
	1.17E+00								1.20E-01		L	GPC3A

Number of Results: 4

Comments:



FORM II

Date: 17-Dec-14

MATRIX SPIKE DUPLICATE RESULTS

Lab Name: TestAmerica Inc SDG: 49016 Matrix: WATER
Lot-Sample No.: J4K190425-1, AC-27D(400-98478-1) Report No.: 63912

Parameter	SpikeResult, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDC MDA	Rpt Unit	Yield	Rec-covery	Expected, Uncert	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4325026 RL-RA-001 Work Order: M5J7J1AH Report DB ID: M5J7J1HW Orig Sa DB ID: M5J7J1JW												
Ra-226	1.11E+01		6.1E-01	2.5E+00	1.76E-01	pCi/L	94%	104.91%	1.06E+01	12/12/14 09:50 p	0.9394	ASC3MA
	1.02E+01	RER2	0.5						1.19E-01		L	
Batch: 4325026 RL-RA-001 Work Order: M5J7J1AJ Report DB ID: M5J7J1JW Orig Sa DB ID: M5J7J1HW												
Ra-226	1.02E+01		6.0E-01	2.1E+00	2.43E-01	pCi/L	100%	96.83%	1.05E+01	12/12/14 09:50 p	0.9425	ASC4UA
	1.11E+01	RER2	0.5						1.19E-01		L	
Batch: 4325027 RL-RA-001 Work Order: M5J7J1AF Report DB ID: M5J7J1FW Orig Sa DB ID: M5J7J1GW												
Ra-228	1.04E+01		7.7E-01	1.5E+00	6.92E-01	pCi/L	85%	99.36%	1.05E+01	12/16/14 12:36 p	0.9394	GPC1B
	9.12E+00	RER2	1.3						1.20E-01		L	
Batch: 4325027 RL-RA-001 Work Order: M5J7J1AG Report DB ID: M5J7J1GW Orig Sa DB ID: M5J7J1FW												
Ra-228	9.12E+00		7.1E-01	1.3E+00	7.20E-01	pCi/L	93%	87.46%	1.04E+01	12/16/14 12:36 p	0.9425	GPC1C
	1.04E+01	RER2	1.3						1.19E-01		L	
No. of Results: 4 Comments:												



FORM II

Date: 17-Dec-14

MATRIX SPIKE DUPLICATE RESULTS

Lab Name: TestAmerica Inc SDG: 49016 Matrix: WATER

Lot-Sample No.: J4K190425-4, NWD-4S(400-98478-4) Report No.: 63912

Parameter	SpikeResult, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDC MDA	Rpt Unit	Yield	Rec- overy	Expected, Uncert	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4325026 RL-RA-001 Work Order: M5J7M1AF Report DB ID: M5J7M1FW Orig Sa DB ID: M5J7M1GW												
Ra-226	1.46E+01		8.5E-01	3.2E+00	2.80E-01	pCi/L	91%	138.70%	1.05E+01	12/12/14 09:50 p	0.9435	ASCASB
	1.12E+01	RER2	1.5						1.18E-01		L	
Batch: 4325026 RL-RA-001 Work Order: M5J7M1AG Report DB ID: M5J7M1GW Orig Sa DB ID: M5J7M1FW												
Ra-226	1.12E+01		6.3E-01	2.9E+00	2.36E-01	pCi/L	100%	107.07%	1.05E+01	12/12/14 10:04 p	0.9455	ASCDMC
	1.46E+01	RER2	1.5						1.18E-01		L	
Batch: 4325027 RL-RA-001 Work Order: M5J7M1AD Report DB ID: M5J7M1DW Orig Sa DB ID: M5J7M1EW												
Ra-228	7.50E+00		7.9E-01	1.3E+00	5.96E-01	pCi/L	73%	71.58%	1.05E+01	12/16/14 12:36 p	0.9435	GPC2D
	9.50E+00	RER2	2.0						1.20E-01		L	
Batch: 4325027 RL-RA-001 Work Order: M5J7M1AE Report DB ID: M5J7M1EW Orig Sa DB ID: M5J7M1DW												
Ra-228	9.50E+00		7.4E-01	1.5E+00	4.16E-01	pCi/L	92%	90.92%	1.05E+01	12/16/14 12:31 p	0.9455	GPC3A
	7.50E+00	RER2	2.0						1.20E-01		L	
No. of Results: 4 Comments:												

Chain of Custody Record



Client Information (Sub Contract Lab)		Lab PWT: Savoie, Noel		Carrier Tracking No(s):		COC No: 400-65451.1	
Client Contact: Shipping/Receiving		E-Mail: noel.savoie@testamericainc.com		Page: Page 1 of 1		Job #: 400-98478-1	
Company: TestAmerica Laboratories, Inc.		Analysis Requested					
Address: 2800 George Washington Way, Richmond, WA, 99352		Due Date Requested: 12/1/2014		TAT Requested (days):		Preservation Codes: M - Hexane, N - None, O - AsNaO2, P - Na2O4S, Q - NaHSO4, R - Na2SO3, S - H2SO4, T - TSP Dodecahydrate, U - Acetone, V - MCAA, W - ph 4-5, L - EDA, Z - other (specify)	
Phone: 509-375-3131 (Tel) 509-375-5590 (Fax)		PO #:		WO #:		Other:	
Project Name: Agrico Pensacola		Project #: 64000434		SSOW#:		Special Instructions/Note:	
Site:		Sample Date		Sample Time		Sample Type (C=Comp, G=grab)	
Sample Identification - Client ID (Lab ID)		Sample Date		Sample Time		Matrix (W=water, S=solid, O=wastewater, BT=Tissue, A=Air)	
AC-27D (400-98478-1)		11/13/14		16:00 Central		Water	
AC-27D (400-98478-1MS)		11/13/14		16:00 Central		MS	
AC-27D (400-98478-1MSD)		11/13/14		16:00 Central		MSD	
AC-27S (400-98478-2)		11/13/14		16:42 Central		Water	
PIP-D (400-98478-3)		11/14/14		08:52 Central		Water	
NWD-4S (400-98478-4)		11/14/14		10:38 Central		Water	
NWD-4S (400-98478-4MS)		11/14/14		10:38 Central		Water	
NWD-4S (400-98478-4MSD)		11/14/14		10:38 Central		Water	
NWD-4D (400-98478-5)		11/14/14		11:09 Central		Water	
AC-6D (400-98478-6)		11/14/14		13:39 Central		Water	
EQ-2 (400-98478-7)		11/14/14		10:48 Central		Water	
Possible Hazard Identification		Unconfirmed		Deliverable Requested: I, II, III, IV, Other (specify)		Special Instructions/Note: JTK190425, SDG# 49016, Due 12/12/14	
Empty Kit Relinquished by:		Date: 11-14-14		Time: 16:00		Company: TA	
Relinquished by:		Date/Time: 11/15/14		Time: 11:00		Company: JF	
Relinquished by:		Date/Time: 11/17/14		Time: 11:17		Company: JF	
Relinquished by:		Date/Time:		Time:		Company:	
Custody Seal No.: A Yes A No		Custody Seal No.: A Yes A No		Custody Seal No.: A Yes A No		Custody Seal No.: A Yes A No	

Sample Check-in List

Date/Time Received: 11/15/14 1100 Container GM Screen Result: (Airlock) NA cpm Initials J
JF 11/17/14 Sample GM Screen Result (Sample Receiving) 20 cpm Initials J
 Client: STP SDG #: 49016 SAF #: + NA J
JF 11/19/14
 Lot Number: J4K190425
 Chain of Custody # N/A

Shipping Container ID or Air Bill Number : _____ NA J

Samples received inside shipping container/cooler/box Yes J Continue with 1 through 4. Initial appropriate response.
 No J Go to 5, add comment to #16.

1. Custody Seals on shipping container intact? Yes J No J No Custody Seal J
2. Custody Seals dated and signed? Yes J No J No Custody Seal J
3. Cooler temperature: _____ °C NA J
4. Vermiculite/packing materials is NA J Wet J Dry J

Item 5 through 16 for samples. Initial appropriate response.

5. Chain of Custody record present? Yes J No J
6. Number of samples received (Each sample may contain multiple bottles): 7
7. Containers received: 21xlp

8. Sample holding times exceeded? NA J Yes J No J
9. Samples have: _____ tape _____ hazard labels _____ custody seals J appropriate sample labels
10. Matrix: _____ A (FLT, Wipe, Solid, Soil) J I (Water) _____ S (Air, Niosh 7400) _____ T (Biological, Ni-63)

11. Samples:
J are in good condition _____ are leaking _____ are broken
J have air bubbles (Only for samples requiring no head space) _____ Other _____

12. Sample pH appropriate for analysis requested Yes J No J NA J
 (If acidification is necessary go to pH area & document sample ID, initial pH, amount of HNO₃ added and pH after addition on table)
13. Were any anomalies identified in sample receipt? Yes J No J
14. Description of anomalies (include sample numbers): NA J

15. Sample Location, Sample Collector Listed on COC? * Yes J No J
 *For documentation only. No corrective action needed.

16. Additional Information: ALL Samples AC-27D (MS & MSD) and NWIS-45 (MS & MSD) did not arrive w/ shipment. Total of 7 samples rec'd.
J Client/Courier denied temperature check. J Client/Courier unpack cooler.

Sample Check-in List completed by Sample Custodian:

Signature: [Signature] Date: 11/17/14

Client Notification needed? Yes J No J Date: _____

By: _____

Person contacted: _____

J No action necessary; process as is

Project Manager [Signature]

Date 11/20/14

Chain of Custody Record



Client Information Client Contact: Mr. Jeff Wagner Company: URS Corporation Address: 1625 Summit Lake Drive Suite 200 City: Tallahassee State: FL 32317 Phone: 850-402-6409 (Tel) Email: jeffry_wagner@urscorp.com Project Name: Agricola Pensacola Site:		Sample: <u>DCH 1000, 01212001</u> Photo: <u>850-528-8995</u> Lab PM: Saviole, Noel E-Mail: noel.saviole@testamericainc.com		Car: 400-98478 COC Page 5 of 5 Job #:	
Due Date Requested: TAT Requested (days):		Analysis Requested			
PO #: 308649.US WO #: 12806620.00000 Vendor #1427536 Project #: 64000434 SSOW#:		SUBCONTRACT - Rad 228-Method 904.0 (Richland) SUBCONTRACT - Rad 228-Method 903.1 (Richland) SUBCONTRACT - Rad 228-Method 904.0 (Richland) 300_ORGFM_28D - Chloride and Sulfate 6010B - Arsenic			
Sample Identification AC-27D AC-27S PIP-D NWD-4S NWD-4D AC-6D EQ-2		Sample Date 11.13.14 11.13.14 11.14.14 11.14.14 11.14.14 11.14.14 11.14.14	Sample Time 1600 1642 0852 1038 1109 1339 1048	Sample Type (C=Comp, G=grab) G G G G G G G	Matrix (W=water, S=solid, O=oil, A=air) W W W W W W W
Field Filtered Sample (Yes or No) Perform MS/MSD (Yes or No)		353.2 Pres - Nitrate Nitrite as N 340.2 SM4500_NO2_B SUBCONTRACT - Rad 228-Method 903.1 (Richland) SUBCONTRACT - Rad 228-Method 904.0 (Richland) 300_ORGFM_28D - Chloride and Sulfate 6010B - Arsenic		Total Number of Containers 6 6 6 6 6 6 6	
Preservation Codes: A - HCL B - NaOH C - Zn Acetate D - Nitric Acid E - NaHSO4 F - MeOH G - Amchlor H - Ascorbic Acid I - Ice J - DI Water K - EDTA L - EDA Other:		Special Instructions/Note: MS/MSD MS/MSD			
Possible Hazard Identification ☒ Non-Hazard ☐ Flammable ☐ Skin Irritant ☐ Poison B ☐ Unknown ☐ Radiological Deliverable Requested: I, II, III, IV, Other (specify)					
Sample Disposal (A fee may be assessed if samples are retained longer than 1 month) ☐ Return To Client ☒ Disposal By Lab ☐ Archive For _____ Months					
Special Instructions/QC Requirements:					
Empty Kit Relinquished by: <u>Jeffrey Wagner</u> Date: <u>11/15/14</u> Time: <u>1500</u>		Method of Shipment:			
Relinquished by: <u>Jeffrey Wagner</u> Date/Time: <u>11/14/14 1504</u> Company: <u>URS</u>		Relinquished by: <u>Jeffrey Wagner</u> Date/Time: <u>11/14/14 1504</u> Company: <u>URS</u>			
Relinquished by: <u>Jeffrey Wagner</u> Date/Time: <u>11/14/14 1504</u> Company: <u>URS</u>		Relinquished by: <u>Jeffrey Wagner</u> Date/Time: <u>11/14/14 1504</u> Company: <u>URS</u>			
Custody Seals Intact: <u>Yes</u>		Cooler Temperature(s) °C and Other Remarks: <u>4.90C 4.90C 10.2</u>			

ANALYTICAL REPORT

TestAmerica Laboratories, Inc.

TestAmerica Pensacola

3355 McLemore Drive

Pensacola, FL 32514

Tel: (850)474-1001

TestAmerica Job ID: 400-98525-1

Client Project/Site: Agrico Pensacola

For:

URS Corporation

1625 Summit Lake Drive

Suite 200

Tallahassee, Florida 32317

Attn: Mr. Jeff Wagner



Authorized for release by:

12/19/2014 9:38:07 AM

Noel Savoie, Project Manager I

(850)878-3994

noel.savoie@testamericainc.com

LINKS

Review your project
results through

TotalAccess

Have a Question?



Visit us at:

www.testamericainc.com

The test results in this report meet all 2003 NELAC and 2009 TNI requirements for accredited parameters, exceptions are noted in this report. This report may not be reproduced except in full, and with written approval from the laboratory. For questions please contact the Project Manager at the e-mail address or telephone number listed on this page.

This report has been electronically signed and authorized by the signatory. Electronic signature is intended to be the legally binding equivalent of a traditionally handwritten signature.

Results relate only to the items tested and the sample(s) as received by the laboratory.

Table of Contents

Cover Page	1
Table of Contents	2
Definitions	3
Case Narrative	4
Sample Summary	5
Client Sample Results	6
QC Sample Results	7
Chronicle	10
Method Summary	11
Subcontract Data	12
Chain of Custody	27



Definitions/Glossary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98525-1

Glossary

Abbreviation	These commonly used abbreviations may or may not be present in this report.
□	Listed under the "D" column to designate that the result is reported on a dry weight basis
%R	Percent Recovery
CFL	Contains Free Liquid
CNF	Contains no Free Liquid
DER	Duplicate error ratio (normalized absolute difference)
Dil Fac	Dilution Factor
DL, RA, RE, IN	Indicates a Dilution, Re-analysis, Re-extraction, or additional Initial metals/anion analysis of the sample
DLC	Decision level concentration
MDA	Minimum detectable activity
EDL	Estimated Detection Limit
MDC	Minimum detectable concentration
MDL	Method Detection Limit
ML	Minimum Level (Dioxin)
NC	Not Calculated
ND	Not detected at the reporting limit (or MDL or EDL if shown)
PQL	Practical Quantitation Limit
QC	Quality Control
RER	Relative error ratio
RL	Reporting Limit or Requested Limit (Radiochemistry)
RPD	Relative Percent Difference, a measure of the relative difference between two points
TEF	Toxicity Equivalent Factor (Dioxin)
TEQ	Toxicity Equivalent Quotient (Dioxin)

Case Narrative

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98525-1

Job ID: 400-98525-1

Laboratory: TestAmerica Pensacola

Narrative

Job Narrative 400-98525-1

Comments

No additional comments.

Receipt

The samples were received on 11/17/2014 4:23 PM; the samples arrived in good condition, properly preserved and, where required, on ice. The temperature of the cooler at receipt was 3.8° C.

HPLC/IC

Method 300.0: The following sample was diluted to bring the concentration of target analytes within the calibration range: AC-6S (400-98525-3). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

General Chemistry

Method 353.2: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-21D (400-98525-1), AC-6S (400-98525-2), and AC-29D (400-98525-3). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Subcontract Work

Methods Radium 226 by EPA Method 903.1, Radium 228 by EPA Method 904.0: These methods were subcontracted to TestAmerica Richland. Report attached.

Sample Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98525-1

Lab Sample ID	Client Sample ID	Matrix	Collected	Received
400-98525-1	AC-21D	Water	11/17/14 11:30	11/17/14 16:23
400-98525-2	AC-6S	Water	11/17/14 13:32	11/17/14 16:23
400-98525-3	AC-29D	Water	11/17/14 15:41	11/17/14 16:23

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98525-1

Client Sample ID: AC-21D

Lab Sample ID: 400-98525-1

Date Collected: 11/17/14 11:30

Matrix: Water

Date Received: 11/17/14 16:23

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	7.5		1.0		mg/L			12/01/14 22:43	1
Sulfate	9.8		1.0		mg/L			12/01/14 22:43	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 11:28	1
Nitrate Nitrite as N	3.1		0.10		mg/L			11/24/14 13:59	2
Nitrate as N	3.1		0.050		mg/L			11/24/14 13:59	1
Nitrite as N	<0.10		0.10		mg/L			11/17/14 17:06	1

Client Sample ID: AC-6S

Lab Sample ID: 400-98525-2

Date Collected: 11/17/14 13:32

Matrix: Water

Date Received: 11/17/14 16:23

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	11		1.0		mg/L			12/01/14 23:06	1
Sulfate	38		1.0		mg/L			12/01/14 23:06	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	0.48		0.10		mg/L			11/24/14 11:32	1
Nitrate Nitrite as N	5.7		0.25		mg/L			11/24/14 14:38	5
Nitrate as N	5.7		0.050		mg/L			11/24/14 13:46	1
Nitrite as N	<0.10		0.10		mg/L			11/17/14 17:06	1

Client Sample ID: AC-29D

Lab Sample ID: 400-98525-3

Date Collected: 11/17/14 15:41

Matrix: Water

Date Received: 11/17/14 16:23

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	39		1.0		mg/L			12/01/14 23:29	1
Sulfate	74		25		mg/L			12/03/14 00:19	25

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	30		0.50		mg/L			11/24/14 11:49	5
Nitrate Nitrite as N	8.3		0.25		mg/L			11/24/14 14:03	5
Nitrate as N	8.3		0.050		mg/L			11/24/14 14:03	1
Nitrite as N	<0.10		0.10		mg/L			11/17/14 17:06	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98525-1

Method: 300.0 - Anions, Ion Chromatography

Lab Sample ID: MB 400-238428/4

Matrix: Water

Analysis Batch: 238428

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/01/14 13:34	1
Sulfate	<1.0		1.0		mg/L			12/01/14 13:34	1

Lab Sample ID: LCS 400-238428/5

Matrix: Water

Analysis Batch: 238428

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	10.3		mg/L		103	90 - 110
Sulfate	10.0	10.7		mg/L		107	90 - 110

Lab Sample ID: LCSD 400-238428/6

Matrix: Water

Analysis Batch: 238428

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	10.2		mg/L		102	90 - 110	1	15
Sulfate	10.0	10.5		mg/L		105	90 - 110	1	15

Lab Sample ID: MB 400-238563/4

Matrix: Water

Analysis Batch: 238563

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/02/14 14:25	1
Sulfate	<1.0		1.0		mg/L			12/02/14 14:25	1

Lab Sample ID: LCS 400-238563/5

Matrix: Water

Analysis Batch: 238563

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	9.79		mg/L		98	90 - 110
Sulfate	10.0	9.94		mg/L		99	90 - 110

Lab Sample ID: LCSD 400-238563/6

Matrix: Water

Analysis Batch: 238563

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	9.76		mg/L		98	90 - 110	0	15
Sulfate	10.0	9.75		mg/L		97	90 - 110	2	15

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98525-1

Method: 340.2 - Fluoride

Lab Sample ID: MB 400-237785/3
Matrix: Water
Analysis Batch: 237785

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 11:11	1

Lab Sample ID: LCS 400-237785/4
Matrix: Water
Analysis Batch: 237785

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.30		mg/L		108	90 - 110

Method: 353.2 - Nitrogen, Nitrate-Nitrite

Lab Sample ID: MB 400-237814/46
Matrix: Water
Analysis Batch: 237814

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/24/14 13:40	1

Lab Sample ID: LCS 400-237814/47
Matrix: Water
Analysis Batch: 237814

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.502		mg/L		100	90 - 110

Lab Sample ID: MRL 400-237814/12
Matrix: Water
Analysis Batch: 237814

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	<0.050		mg/L		86	50 - 150

Method: SM 4500 NO2 B - Nitrogen, Nitrite

Lab Sample ID: MB 400-237151/6
Matrix: Water
Analysis Batch: 237151

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/17/14 13:56	1

Lab Sample ID: LCS 400-237151/7
Matrix: Water
Analysis Batch: 237151

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.275		mg/L		92	90 - 110

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98525-1

Method: SM 4500 NO2 B - Nitrogen, Nitrite (Continued)

Lab Sample ID: MRL 400-237151/3

Matrix: Water

Analysis Batch: 237151

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.100	<0.10		mg/L		98	50 - 150

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98525-1

Client Sample ID: AC-21D

Date Collected: 11/17/14 11:30

Date Received: 11/17/14 16:23

Lab Sample ID: 400-98525-1

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 22:43	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 11:28	SLT	TAL PEN
Total/NA	Analysis	353.2		2	237814	11/24/14 13:59	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237952	11/24/14 13:59	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237151	11/17/14 17:06	LSS	TAL PEN

Client Sample ID: AC-6S

Date Collected: 11/17/14 13:32

Date Received: 11/17/14 16:23

Lab Sample ID: 400-98525-2

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 23:06	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 11:32	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237814	11/24/14 14:38	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237952	11/24/14 13:46	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237151	11/17/14 17:06	LSS	TAL PEN

Client Sample ID: AC-29D

Date Collected: 11/17/14 15:41

Date Received: 11/17/14 16:23

Lab Sample ID: 400-98525-3

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 23:29	TAJ	TAL PEN
Total/NA	Analysis	300.0		25	238563	12/03/14 00:19	TAJ	TAL PEN
Total/NA	Analysis	340.2		5	237785	11/24/14 11:49	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237814	11/24/14 14:03	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	237952	11/24/14 14:03	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237151	11/17/14 17:06	LSS	TAL PEN

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

TestAmerica Pensacola

Method Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98525-1

Method	Method Description	Protocol	Laboratory
300.0	Anions, Ion Chromatography	MCAWW	TAL PEN
340.2	Fluoride	MCAWW	TAL PEN
353.2	Nitrogen, Nitrate-Nitrite	MCAWW	TAL PEN
Nitrate by calc	Nitrogen, Nitrate	SM	TAL PEN
SM 4500 NO2 B	Nitrogen, Nitrite	SM	TAL PEN
Rad 226-Method 903.1 (Richland)	RAD-226 (RCH)	NONE	TAL RCH
Rad 228-Method 904.0 (Richland)	RAD-228 (RCH)	NONE	TAL RCH

Protocol References:

MCAWW = "Methods For Chemical Analysis Of Water And Wastes", EPA-600/4-79-020, March 1983 And Subsequent Revisions.

NONE = NONE

SM = "Standard Methods For The Examination Of Water And Wastewater",

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Analytical Data Package Prepared For

TestAmerica Pensacola

Radiochemical Analysis By

TestAmerica Inc

2800 G.W. Way, Richland Wa, 99354, (509)-375-3131.

Assigned Laboratory Code: TARL

Data Package Contains _____ Pages

Report No.: 63915

Results in this report relate only to the sample(s) analyzed.

SDG No.	Order No.	Client Sample ID (List Order)	Lot-Sa No.	Work Order	Report DB ID	Batch No.
49023		AC-21D(400-98525-1)	J4K200411-1	M5KDW1AA	9M5KDW10	4325023
		AC-21D(400-98525-1)	J4K200411-1	M5KDW1AC	9M5KDW10	4325024
		AC-29D(400-98525-3)	J4K200411-3	M5KD01AA	9M5KD010	4325023
		AC-29D(400-98525-3)	J4K200411-3	M5KD01AC	9M5KD010	4325024
		AC-6S(400-98525-2)	J4K200411-2	M5KDX1AA	9M5KDX10	4325023
		AC-6S(400-98525-2)	J4K200411-2	M5KDX1AC	9M5KDX10	4325024

Certificate of Analysis

December 17, 2014

TestAmerica Pensacola
3355 McLemore Drive
Pensacola, FL 32514

Attention: Noel Savoie

Date Received at Lab	:	November 19, 2014
Project Name/Number	:	Agrico Pensacola/64000434
Sample Type	:	Three (3) Water
Job Number	:	400-98525-1
SDG Number	:	49023

CASE NARRATIVE

I. Introduction

On November 19, 2014, two water samples were received at TestAmerica's Richland laboratory for radiochemical analysis. Upon receipt, the samples were assigned the TestAmerica identification number as described on the cover page of the Analytical Data Package report form. The samples were assigned to Lot Numbers J4K200411.

II. Sample Receipt

The samples were received in good condition and no anomalies were noted upon check-in.

III. Analytical Results/Methodology

The analytical results for this report are presented by laboratory sample ID. Each set of data includes sample identification information; analytical results and the appropriate associated statistical uncertainties.

The analysis requested was:

Gas Proportional Counting

Radium-228 by method RL-RA-001

Alpha Scintillation Counting

Radium-226 by method RL-RA-001

IV. Quality Control

The analytical result for each analysis performed includes a minimum of one laboratory control sample (LCS), and one reagent blank sample analysis. Any exceptions have been noted in the Comments” section.

V. Comments

Gas Proportional Counting

Radium-228

The LCS, batch blank, sample duplicate and sample results are within acceptance limits.

Alpha Scintillation Counting

Radium 226:

The LCS, batch blank, samples and sample duplicate results are within acceptance limits.

I certify that this Certificate of Analysis is in compliance with the SOW and/or NELAC, both technically and for completeness, for other than the conditions detailed above. The Laboratory Manager or a designee, as verified by the following signature has authorized release of the data contained in this hard copy data package.

Reviewed and approved:

Robin Ebert-Mays
Project Manager

Drinking Water Method Cross References

DRINKING WATER ASTM METHOD CROSS REFERENCES		
Referenced Method	Isotope(s)	TestAmerica Richland's SOP No.
EPA 901.1	Cs-134, I-131	RL-GAM-001
EPA 900.0	Alpha & Beta	RL-GPC-001
EPA 00-02	Gross Alpha (Coprecipitation)	RL-GPC-002
EPA 903.0	Total Alpha Radium (Ra-226)	RL-RA-002
EPA 903.1	Ra-226	RL-RA-001
EPA 904.0	Ra-228	RL-RA-001
EPA 905.0	Sr-89/90	RL-GPC-003
ASTM D5174	Uranium	RL-KPA-003
EPA 906.0	Tritium	RL-LSC-005

Results in this report relate only to the sample(s) analyzed.

Uncertainty Estimation

TestAmerica Richland has adopted the internationally accepted approach to estimating uncertainties described in "NIST Technical Note 1297, 1994 Edition". The approach, "Law of Propagation of Errors", involves the identification of all variables in an analytical method which are used to derive a result. These variables are related to the analytical result (R) by some functional relationship, $R = \text{constants} * f(x,y,z,...)$. The components (x,y,z) are evaluated to determine their contribution to the overall method uncertainty. The individual component uncertainties (u_i) are then combined using a statistical model that provides the most probable overall uncertainty value. All component uncertainties are categorized as type A, evaluated by statistical methods, or type B, evaluated by other means. Uncertainties not included in the components, such as sample homogeneity, are combined with the component uncertainty as the square root of the sum-of-the-squares of the individual uncertainties. The uncertainty associated with the derived result is the combined uncertainty (u_c) multiplied by the coverage factor (1,2, or 3).

When three or more sample replicates are used to derive the analytical result, the type A uncertainty is the standard deviation of the mean value ($S/\sqrt{n}$), where S is the standard deviation of the derived results. The type B uncertainties are all other random or non-random components that are not included in the standard deviation.

The derivation of the general "Law of Propagation of Errors" equations and specific example are available on request.

Report Definitions

Action Lev	An agreed upon activity level used to trigger some action when the final result is greater than or equal to the Action Level. Often the Action Level is related to the Decision Limit.
Batch	The QC preparation batch number that relates laboratory samples to QC samples that were prepared and analyzed together.
Bias	Defined by the equation (Result/Expected)-1 as defined by ANSI N13.30.
COC No	Chain of Custody Number assigned by the Client or TestAmerica.
Count Error (#s)	Poisson counting statistics of the gross sample count and background. The uncertainty is absolute and in the same units as the result. For Liquid Scintillation Counting (LSC) the batch blank count is the background.
Total Uncert (#s) <i>u_c - Combined Uncertainty.</i>	All known uncertainties associated with the preparation and analysis of the sample are propagated to give a measure of the uncertainty associated with the result, <i>u_c the combined uncertainty</i> . The uncertainty is absolute and in the same units as the result.
(#s), Coverage Factor	The coverage factor defines the width of the confidence interval, 1, 2 or 3 standard deviations.
CRDL (RL)	Contractual Required Detection Limit as defined in the Client's Statement Of Work or TestAmerica "default" nominal detection limit. Often referred to the reporting level (RL)
Lc	Decision Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume associated with the sample. The Type I error probability is approximately 5%. $Lc = (1.645 * \sqrt{2 * (BkgndCnt / BkgndCntMin) / SCntMin}) * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability. Lc cannot be calculated when the background count is zero.
Lot-Sample No	The number assigned by the LIMS software to track samples received on the same day for a given client. The sample number is a sequential number assigned to each sample in the Lot.
MDC MDA	Detection Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume with a Type I and II error probability of approximately 5%. $MDC = (4.65 * \sqrt{(BkgndCnt / BkgndCntMin) / SCntMin}) + 2.71 / SCntMin * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability.
Primary Detector	The instrument identifier associated with the analysis of the sample aliquot.
Ratio U-234/U-238	The U-234 result divided by the U-238 result. The U-234/U-238 ratio for natural uranium in NIST SRM 4321C is 1.038.
Rst/MDC	Ratio of the Result to the MDC. A value greater than 1 may indicate activity above background at a high level of confidence. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Rst/TotUcert	Ratio of the Result to the Total Uncertainty. If the uncertainty has a coverage factor of 2 a value greater than 1 may indicate activity above background at approximately the 95% level of confidence assuming a two-sided confidence interval. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Report DB No	Sample Identifier used by the report system. The number is based upon the first five digits of the Work Order Number.
RER	The equation Replicate Error Ratio = $(S-D) / [\sqrt{TPUs^2 + TPUD^2}]$ as defined by ICPT BOA where S is the original sample result, D is the result of the duplicate, TPUs is the total uncertainty of the original sample and TPUD is the total uncertainty of the duplicate sample.
SDG	Sample Delivery Group Number assigned by the Client or assigned by TestAmerica upon sample receipt.
Sum Rpt Alpha Spec Rst(s)	The sum of the reported alpha spec results for tests derived from the same sample excluding duplicate result where the results are in the same units.
Work Order	The LIMS software assign test specific identifier.
Yield	The recovery of the tracer added to the sample such as Pu-242 used to trace a Pu-239/40 method.

Sample Results Summary

Date: 17-Dec-14

TestAmerica Inc TARL

Ordered by Method, Batch No., Client Sample ID.

Report No. : 63915

SDG No: 49023

Batch	Client Id Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	MDL	CRDL	RER2
4325023	RL-RA-001								
	AC-21D(400-98525-1)								
	M5KDW1AA Ra-226		1.69E+00 +- 3.9E-01		pCi/L	94%	1.57E-01	1.00E+00	
	AC-21D(400-98525-1) DUP								
	M5KDW1AD Ra-226		1.58E+00 +- 4.1E-01		pCi/L	89%	1.88E-01	1.00E+00	0.4
	AC-29D(400-98525-3)								
	M5KD01AA Ra-226		1.53E+00 +- 4.7E-01		pCi/L	89%	2.22E-01	1.00E+00	
	AC-6S(400-98525-2)								
	M5KDX1AA Ra-226		9.37E-01 +- 3.2E-01	J	pCi/L	81%	1.76E-01	1.00E+00	
4325024	RL-RA-001								
	AC-21D(400-98525-1)								
	M5KDW1AC Ra-228		2.30E+00 +- 5.2E-01		pCi/L	83%	5.99E-01	1.00E+00	
	AC-21D(400-98525-1) DUP								
	M5KDW1AE Ra-228		2.39E+00 +- 5.3E-01		pCi/L	81%	5.86E-01	1.00E+00	0.2
	AC-29D(400-98525-3)								
	M5KD01AC Ra-228		1.52E+01 +- 2.0E+00		pCi/L	82%	7.33E-01	1.00E+00	
	AC-6S(400-98525-2)								
	M5KDX1AC Ra-228		2.04E+00 +- 5.8E-01		pCi/L	69%	8.96E-01	1.00E+00	
	No. of Results:	8							

TestAmerica Inc RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPUs)+sq(TPUD))] as defined by ICPT BOA.

rptTALRchSaSum J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.

mary2 V5.3.6.1

A2002

QC Results Summary
TestAmerica Inc TARL
 Ordered by Method, Batch No, QC Type,.

Date: 17-Dec-14

Report No. : 63915

SDG No.: 49023

Batch	Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	LCS Recovery	Bias	MDL
RL-RA-001									
4325023 BLANK QC,									
	M5KNH1AA	Ra-226	2.15E-02 +- 1.2E-01	U	pCi/L	77%			2.53E-01
4325023 LCS,									
	M5KNH1AC	Ra-226	9.97E+00 +- 2.5E+00		pCi/L	100%	101%	0.0	1.11E-01
RL-RA-001									
4325024 BLANK QC,									
	M5KNJ1AA	Ra-228	1.43E-01 +- 3.9E-01	U	pCi/L	70%			8.73E-01
4325024 LCS,									
	M5KNJ1AC	Ra-228	8.62E+00 +- 1.1E+00		pCi/L	93%	87%	-0.1	5.92E-01
No. of Results: 4									

FORM I

Date: 17-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc **SDG:** 49023 **Collection Date:** 11/17/2014 11:30:00 AM
Lot-Sample No.: J4K200411-1 **Report No.:** 63915 **Received Date:** 11/19/2014 12:05:00 PM
Client Sample ID: AC-21D(400-98525-1) **COC No.:** **Matrix:** WATER
 Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325023 RL-RA-001												
Ra-226	1.69E+00		2.1E-01	3.9E-01	1.57E-01	pCi/L	94%	(10.8)	12/15/14 09:21 p		0.9291	ASC1RH
						7.06E-02	1.00E+00	(8.7)			L	
Batch: 4325024 RL-RA-001												
Ra-228	2.30E+00		4.4E-01	5.2E-01	5.99E-01	pCi/L	83%	(3.8)	12/17/14 12:47 p		0.9291	GPC4A
						2.66E-01	1.00E+00	(8.9)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
 rptSTLRchSample U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
 V5.3.6.1 A2002



FORM I

Date: 17-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49023 Collection Date: 11/17/2014 3:41:00 PM
Lot-Sample No.: J4K200411-3 Report No.: 63915 Received Date: 11/19/2014 12:05:00 PM
Client Sample ID: AC-29D(400-98525-3) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325023 RL-RA-001 1.53E+00 2.6E-01 4.7E-01 M5KD01AA 2.22E-01 pCi/L 89% (6.9) 12/15/14 09:22 p 0.8523 ASC7UA												
Work Order: M5KD01AA Report DB ID: 9M5KD010 9.87E-02 1.00E+00 (6.5)												
Batch: 4325024 RL-RA-001 1.52E+01 1.0E+00 2.0E+00 M5KD01AC 7.33E-01 pCi/L 82% (20.7) 12/17/14 12:47 p 0.8523 GPC4D												
Work Order: M5KD01AC Report DB ID: 9M5KD010 3.29E-01 1.00E+00 (15.1)												

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
V5.3.6.1 A2002

FORM I

Date: 17-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 49023

Collection Date: 11/17/2014 1:32:00 PM

Lot-Sample No.: J4K200411-2

Report No.: 63915

Received Date: 11/19/2014 12:05:00 PM

Client Sample ID: AC-6S(400-98525-2)

COC No.:

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325023 RL-RA-001												
Ra-226	9.37E-01	J	1.8E-01	3.2E-01	1.76E-01	pCi/L	81%	(5.3)	12/15/14 09:22 p		0.9389	ASCMMA
						7.81E-02	1.00E+00	(5.9)			L	
Batch: 4325024 RL-RA-001												
Ra-228	2.04E+00		5.3E-01	5.8E-01	8.96E-01	pCi/L	69%	(2.3)	12/17/14 12:47 p		0.9389	GPC4C
						4.09E-01	1.00E+00	(7.)			L	

No. of Results: 2

Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM II

Date: 17-Dec-14

DUPLICATE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K200411-1
Client Sample ID: AC-21D(400-98525-1) DUP

SDG: 49023
Report No.: 63915
COC No.:
Collection Date: 11/17/2014 11:30:00 AM
Received Date: 11/19/2014 12:05:00 PM
Matrix: WATER

Parameter	Result, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325023												
RL-RA-001												
Work Order: M5KDW1AD												
Ra-226	1.58E+00		2.4E-01	4.1E-01	1.88E-01	pCi/L	89%	(8.4)	12/15/14 09:21 p	9M5KDW10	0.9315	ASC5UC
	1.69E+00		RER2 0.4			1.00E+00		(7.7)			L	
Batch: 4325024												
RL-RA-001												
Work Order: M5KDW1AE												
Ra-228	2.39E+00		4.5E-01	5.3E-01	5.86E-01	pCi/L	81%	(4.1)	12/17/14 12:47 p	9M5KDW10	0.9315	GPC4B
	2.30E+00		RER2 0.2			1.00E+00		(9.)			L	

No. of Results: 2 Comments:

TestAmerica Inc RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPU_s)+sq(TPU_d))] as defined by ICPT BOA.
MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.

3.6.1 A2002

FORM II

BLANK RESULTS

Date: 17-Dec-14

Lab Name: TestAmerica Inc
Matrix: WATER

SDG: 49023
Report No. : 63915

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Lc	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4325023												
Work Order: M5KNH1AA						Report DB ID: M5KNH1AB						
Ra-226	2.15E-02	U	1.2E-01	1.2E-01	2.53E-01	pCi/L	77%	0.09	12/15/14 09:22 p		1.0011	ASC8RE
					1.12E-01	1.00E+00		0.35			L	
Batch: 4325024												
Work Order: M5KNJ1AA						Report DB ID: M5KNJ1AB						
Ra-228	1.43E-01	U	3.9E-01	3.9E-01	8.73E-01	pCi/L	70%	0.16	12/17/14 12:48 p		1.0011	GPC6B
					4.07E-01	1.00E+00		0.73			L	

No. of Results: 2 Comments:

FORM II
LCS RESULTS

Date: 17-Dec-14

Lab Name: TestAmerica Inc SDG: 49023
Matrix: WATER Report No.: 63915

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL	Report Unit	Yield	Expected	Expected Uncert	Recovery, Bias	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4325023 RL-RA-001 Work Order: M5KNH1AC Report DB ID: M5KNH1CS													
Ra-226	9.97E+00		4.6E-01	2.5E+00	1.11E-01	pCi/L	100%	9.90E+00	1.12E-01	101%	12/15/14 09:22 p	1.0003	ASCBMB
							Rec Limits:	75	125	0.0			
Batch: 4325024 RL-RA-001 Work Order: M5KNJ1AC Report DB ID: M5KNJ1CS													
Ra-228	8.62E+00		6.3E-01	1.1E+00	5.92E-01	pCi/L	93%	9.86E+00	1.13E-01	87%	12/17/14 12:48 p	1.0003	GPC6C
							Rec Limits:	75	125	-0.1			

No. of Results: 2 Comments:

Chain of Custody Record

Client Information (Sub Contract Lab) Client Contact: Carrier Tracking No(s): Shipping/Receiving: Page: 1 of 1			Lab P/N: COC No: 400-65628.1 E-Mail: Savoie, Noel noel.savoie@testamericainc.com	
Company: TestAmerica Laboratories, Inc. Address: 2800 George Washington Way, City: Richland State, Zip: WA, 99352 Phone: 509-375-3131(Tel) 509-375-5590(Fax) Email:			Job #: 400-98525-1 Preservation Codes: M - Hexane N - None O - AsNaO2 P - Na2O4S Q - Na2SO3 R - Na2S2O3 S - H2SO4 T - TSP Dodecathylate H - Ascorbic Acid I - Ice J - DI Water K - EDTA L - EDA Z - other (specify) Other:	
Analysis Requested			Special Instructions/Note:	
Due Date Requested: 12/2/2014 TAT Requested (days): PO #: WO #: Project #: 64000434 SSOW#:			Total Number of containers:	
Sample Identification - Client ID (Lab ID)			Special Instructions/Note:	
AC-21D (400-98525-1)			M5KDW	
AC-6S (400-98525-2)			M5KDX	
AC-29D (400-98525-3)			M5KDO	
J4K200411			J4K200411	
SDG# 49023			SDG# 49023	
Due 12/17/14			Due 12/17/14	
Sample Disposal (A fee may be assessed if samples are retained longer than 1 month) ☐ Return To Client ☐ Disposal By Lab ☐ Archive For _____ Months			Special Instructions/QC Requirements:	
Date: Time:			Date: Time:	
Date/Time: 12-18-14 6:00 Date/Time: Date/Time:			Date/Time: 11/19/14 12:05 Date/Time: Date/Time:	
Relinquished by: Relinquished by: Relinquished by:			Relinquished by: Relinquished by: Relinquished by:	
Empty Kit Relinquished by: Relinquished by: Relinquished by:			Empty Kit Relinquished by: Relinquished by: Relinquished by:	
Custody Seals Intact: A Yes A No			Custody Seal No.: J4K200411	

Sample Check-in List

Date/Time Received: 11/19/14 1205 Container GM Screen Result: (Airlock) 20 cpm Initials [F]
 Sample GM Screen Result (Sample Receiving) 20 cpm Initials [F]
 Client: STP SDG #: 49023 SAF #: _____ NA [B]
 Lot Number: J4K200411
 Chain of Custody # 400-65628.1

Shipping Container ID or Air Bill Number : _____ NA [B]

Samples received inside shipping container/cooler/box Yes [B] Continue with 1 through 4. Initial appropriate response.
 No [] Go to 5, add comment to #16.

1. Custody Seals on shipping container intact? Yes [F] No [] No Custody Seal []
2. Custody Seals dated and signed? Yes [F] No [] No Custody Seal []
3. Cooler temperature: _____ °C NA [B]
4. Vermiculite/packing materials is NA [] Wet [] Dry [B]

Item 5 through 16 for samples. Initial appropriate response.

5. Chain of Custody record present? Yes [B] No []
6. Number of samples received (Each sample may contain multiple bottles): 3
7. Containers received: 9 x 4p (3 ea.)

8. Sample holding times exceeded? NA [] Yes [] No [B]
9. Samples have: _____ tape _____ hazard labels _____ custody seals [B] appropriate sample labels
10. Matrix: _____ A (FLT, Wipe, Solid, Soil) [B] I (Water) _____ S (Air, Niosh 7400) _____ T (Biological, Ni-63)
11. Samples: [B] are in good condition _____ are leaking _____ are broken
 _____ have air bubbles (Only for samples requiring no head space) Other _____
12. Sample pH appropriate for analysis requested Yes [B] No [] NA []
 (If acidification is necessary go to pH area & document sample ID, initial pH, amount of HNO₃ added and pH after addition on table)
13. Were any anomalies identified in sample receipt? Yes [] No [B]
14. Description of anomalies (include sample numbers): NA [B] _____
15. Sample Location, Sample Collector Listed on COC? * Yes [] No [B]
 *For documentation only. No corrective action needed.
16. Additional Information: NA

[] Client/Courier denied temperature check.

[] Client/Courier unpack cooler.

Sample Check-in List completed by Sample Custodian:

Signature: [Signature] Date: 11-19-14

Client Notification needed? Yes [] No [X] Date: _____

By: _____

Person contacted: _____

[] No action necessary; process as is

Project Manager: [Signature]

Date: 11-20-14

FOR ROBIN EBERT-MAYS

Client Information Client Contact: Mr. Jeff Wagner Company: URS Corporation		Lab PM: Savoie, Noel E-Mail: noel.savoie@testamericainc.com		Carrier Tracking No(s): 640-48009-12359.1		Page: Page 1 of 5 Job #:		
Address: 1625 Summit Lake Drive Suite 200 City: Tallahassee State, Zip: FL, 32317 Phone: 850-402-6409(Tel) Email: jeffry_wagner@urscorp.com Project Name: Agrico Pensacola Site:		Due Date Requested: TAT Requested (days): PO #: 308649 US WO #: 12806620.00000 Vendor #1427536 Project #: 64000434 SSOW#:		Analysis Requested SUBCONTRACT - Rad 226-Method 903.1 (Richland) SUBCONTRACT - Rad 228-Method 904.0 (Richland) SUBCONTRACT - Rad 228-Method 904.0 (Richland) 300_ORGFM_28D - Chloride and Sulfate 6010B - Arsenic 400-98525 COC		Preservation Codes: A - HCL B - NaOH M - Hexane N - None O - AsNaO2 P - Na2O4S Q - Na2SO3 R - Na2S2SO3 S - H2SO4 G - Ascorbic Acid H - Anchlor T - TSP Dodecahydrate U - Acetone J - DI Water K - EDTA V - MCAA W - ph 4-5 L - EDA Z - other (specify) Other:		
Sample Identification AC-21D AC-6S AC-29D		Sample Date 11/17/14 11/17/14 11/17/14	Sample Time 1130 1332 1541	Sample Type G=Comp G=grab G G G	Matrix (W=water, S=solid, O=wasteoil, BT=Tissue, A=air) W W W	Field Filtered Sample (Yes or No) Perform MS/MSD (Yes or No) 553.2_Pres - Nitrate Nitrite as N 340.2_SM4500_NO2_B SUBCONTRACT - Rad 226-Method 903.1 (Richland) SUBCONTRACT - Rad 228-Method 904.0 (Richland) SUBCONTRACT - Rad 228-Method 904.0 (Richland) 300_ORGFM_28D - Chloride and Sulfate 6010B - Arsenic	Total Number of Containers 6 6 6	Special Instructions/Note: 400-98525 COC
Possible Hazard Identification ☐ Non-Hazard ☐ Flammable ☐ Skin Irritant ☐ Poison B ☐ Unknown ☐ Radiological Deliverable Requested: I, II, III, IV, Other (specify)								
Relinquished by: <i>[Signature]</i> Date: 11/17/14		Relinquished by: <i>[Signature]</i> Date: 11/17/14		Relinquished by: <i>[Signature]</i> Date: 11/17/14		Relinquished by: <i>[Signature]</i> Date: 11/17/14		
Empty Kit Relinquished by: <i>[Signature]</i> Date: 11/17/14		Empty Kit Relinquished by: <i>[Signature]</i> Date: 11/17/14		Empty Kit Relinquished by: <i>[Signature]</i> Date: 11/17/14		Empty Kit Relinquished by: <i>[Signature]</i> Date: 11/17/14		
Custody Seals Intact: ☐ Yes ☐ No		Custody Seal No.:		Cooler Temperature(s) °C and Other Remarks: 38°C		Method of Shipment:		

TestAmerica

THE LEADER IN ENVIRONMENTAL TESTING

ANALYTICAL REPORT

TestAmerica Laboratories, Inc.

TestAmerica Pensacola

3355 McLemore Drive

Pensacola, FL 32514

Tel: (850)474-1001

TestAmerica Job ID: 400-98593-1

Client Project/Site: Agrico Pensacola

For:

URS Corporation

1625 Summit Lake Drive

Suite 200

Tallahassee, Florida 32317

Attn: Mr. Jeff Wagner



Authorized for release by:

12/19/2014 3:13:18 PM

Noel Savoie, Project Manager I

(850)878-3994

noel.savoie@testamericainc.com

LINKS

Review your project
results through

TotalAccess

Have a Question?



Visit us at:

www.testamericainc.com

The test results in this report meet all 2003 NELAC and 2009 TNI requirements for accredited parameters, exceptions are noted in this report. This report may not be reproduced except in full, and with written approval from the laboratory. For questions please contact the Project Manager at the e-mail address or telephone number listed on this page.

This report has been electronically signed and authorized by the signatory. Electronic signature is intended to be the legally binding equivalent of a traditionally handwritten signature.

Results relate only to the items tested and the sample(s) as received by the laboratory.

Table of Contents

Cover Page	1
Table of Contents	2
Definitions	3
Case Narrative	4
Sample Summary	5
Client Sample Results	6
QC Sample Results	8
Chronicle	11
Method Summary	13
Subcontract Data	14
Chain of Custody	30



Definitions/Glossary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98593-1

Glossary

Abbreviation	These commonly used abbreviations may or may not be present in this report.
□	Listed under the "D" column to designate that the result is reported on a dry weight basis
%R	Percent Recovery
CFL	Contains Free Liquid
CNF	Contains no Free Liquid
DER	Duplicate error ratio (normalized absolute difference)
Dil Fac	Dilution Factor
DL, RA, RE, IN	Indicates a Dilution, Re-analysis, Re-extraction, or additional Initial metals/anion analysis of the sample
DLC	Decision level concentration
MDA	Minimum detectable activity
EDL	Estimated Detection Limit
MDC	Minimum detectable concentration
MDL	Method Detection Limit
ML	Minimum Level (Dioxin)
NC	Not Calculated
ND	Not detected at the reporting limit (or MDL or EDL if shown)
PQL	Practical Quantitation Limit
QC	Quality Control
RER	Relative error ratio
RL	Reporting Limit or Requested Limit (Radiochemistry)
RPD	Relative Percent Difference, a measure of the relative difference between two points
TEF	Toxicity Equivalent Factor (Dioxin)
TEQ	Toxicity Equivalent Quotient (Dioxin)

Case Narrative

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98593-1

Job ID: 400-98593-1

Laboratory: TestAmerica Pensacola

Narrative

Job Narrative 400-98593-1

Comments

No additional comments.

Receipt

The samples were received on 11/18/2014 4:25 PM; the samples arrived in good condition, properly preserved and, where required, on ice. The temperature of the cooler at receipt was 3.1° C.

HPLC/IC

No analytical or quality issues were noted, other than those described in the Definitions/Glossary page.

General Chemistry

Method 353.2: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-22D (400-98593-1), AC-36D (400-98593-2), AC-11D (400-98593-3), and AC-10D (400-98593-4). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Subcontract Work

Methods Radium 226 by EPA Method 903.1, Radium 228 by EPA Method 904.0: These methods were subcontracted to TestAmerica Richland. Report attached.

Sample Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98593-1

Lab Sample ID	Client Sample ID	Matrix	Collected	Received
400-98593-1	AC-22D	Water	11/18/14 08:24	11/18/14 16:25
400-98593-2	AC-36D	Water	11/18/14 09:49	11/18/14 16:25
400-98593-3	AC-11D	Water	11/18/14 12:39	11/18/14 16:25
400-98593-4	AC-10D	Water	11/18/14 15:24	11/18/14 16:25

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98593-1

Client Sample ID: AC-22D

Date Collected: 11/18/14 08:24

Date Received: 11/18/14 16:25

Lab Sample ID: 400-98593-1

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	12		1.0		mg/L			12/01/14 19:40	1
Sulfate	13		1.0		mg/L			12/01/14 19:40	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	5.0		0.10		mg/L			11/24/14 11:39	1
Nitrate Nitrite as N	4.4		0.25		mg/L			11/25/14 11:24	5
Nitrate as N	4.4		0.050		mg/L			11/25/14 11:24	1
Nitrite as N	<0.10		0.10		mg/L			11/18/14 16:59	1

Client Sample ID: AC-36D

Date Collected: 11/18/14 09:49

Date Received: 11/18/14 16:25

Lab Sample ID: 400-98593-2

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	10		1.0		mg/L			12/01/14 20:03	1
Sulfate	21		1.0		mg/L			12/01/14 20:03	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 11:42	1
Nitrate Nitrite as N	5.0		0.25		mg/L			11/25/14 11:25	5
Nitrate as N	5.0		0.050		mg/L			11/25/14 11:25	1
Nitrite as N	<0.10		0.10		mg/L			11/18/14 16:59	1

Client Sample ID: AC-11D

Date Collected: 11/18/14 12:39

Date Received: 11/18/14 16:25

Lab Sample ID: 400-98593-3

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	8.9		1.0		mg/L			12/01/14 20:26	1
Sulfate	1.4		1.0		mg/L			12/01/14 20:26	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 11:53	1
Nitrate Nitrite as N	2.3		0.10		mg/L			11/25/14 12:07	2
Nitrate as N	2.3		0.050		mg/L			11/25/14 12:07	1
Nitrite as N	<0.10		0.10		mg/L			11/18/14 16:59	1

Client Sample ID: AC-10D

Date Collected: 11/18/14 15:24

Date Received: 11/18/14 16:25

Lab Sample ID: 400-98593-4

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	11		1.0		mg/L			12/01/14 20:49	1
Sulfate	22		1.0		mg/L			12/01/14 20:49	1

TestAmerica Pensacola

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98593-1

Client Sample ID: AC-10D

Lab Sample ID: 400-98593-4

Date Collected: 11/18/14 15:24

Matrix: Water

Date Received: 11/18/14 16:25

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 11:56	1
Nitrate Nitrite as N	5.0		0.25		mg/L			11/25/14 12:20	5
Nitrate as N	5.0		0.050		mg/L			11/25/14 12:20	1
Nitrite as N	<0.10		0.10		mg/L			11/18/14 16:59	1

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98593-1

Method: 300.0 - Anions, Ion Chromatography

Lab Sample ID: MB 400-238428/4

Matrix: Water

Analysis Batch: 238428

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/01/14 13:34	1
Sulfate	<1.0		1.0		mg/L			12/01/14 13:34	1

Lab Sample ID: LCS 400-238428/5

Matrix: Water

Analysis Batch: 238428

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	10.3		mg/L		103	90 - 110
Sulfate	10.0	10.7		mg/L		107	90 - 110

Lab Sample ID: LCSD 400-238428/6

Matrix: Water

Analysis Batch: 238428

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	10.2		mg/L		102	90 - 110	1	15
Sulfate	10.0	10.5		mg/L		105	90 - 110	1	15

Method: 340.2 - Fluoride

Lab Sample ID: MB 400-237785/3

Matrix: Water

Analysis Batch: 237785

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 11:11	1

Lab Sample ID: LCS 400-237785/4

Matrix: Water

Analysis Batch: 237785

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.30		mg/L		108	90 - 110

Method: 353.2 - Nitrogen, Nitrate-Nitrite

Lab Sample ID: MB 400-237957/14

Matrix: Water

Analysis Batch: 237957

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/25/14 11:06	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98593-1

Method: 353.2 - Nitrogen, Nitrate-Nitrite (Continued)

Lab Sample ID: MB 400-237957/46

Matrix: Water

Analysis Batch: 237957

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/25/14 11:48	1

Lab Sample ID: LCS 400-237957/15

Matrix: Water

Analysis Batch: 237957

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.460		mg/L		92	90 - 110

Lab Sample ID: LCS 400-237957/47

Matrix: Water

Analysis Batch: 237957

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.534		mg/L		107	90 - 110

Lab Sample ID: MRL 400-237957/12

Matrix: Water

Analysis Batch: 237957

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	<0.050		mg/L		92	50 - 150

Method: Nitrate by calc - Nitrogen, Nitrate

Lab Sample ID: MB 400-238018/14

Matrix: Water

Analysis Batch: 238018

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate as N	N/A		0.050		mg/L			11/25/14 11:06	1

Lab Sample ID: MB 400-238018/46

Matrix: Water

Analysis Batch: 238018

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate as N	N/A		0.050		mg/L			11/25/14 11:48	1

Method: SM 4500 NO2 B - Nitrogen, Nitrite

Lab Sample ID: MB 400-237404/5

Matrix: Water

Analysis Batch: 237404

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/18/14 12:55	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98593-1

Method: SM 4500 NO2 B - Nitrogen, Nitrite (Continued)

Lab Sample ID: LCS 400-237404/19
Matrix: Water
Analysis Batch: 237404

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.293		mg/L		98	90 - 110

Lab Sample ID: MRL 400-237404/3
Matrix: Water
Analysis Batch: 237404

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.100	<0.10		mg/L		92	50 - 150

Lab Sample ID: 400-98593-4 DU
Matrix: Water
Analysis Batch: 237404

Client Sample ID: AC-10D
Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	DU Result	DU Qualifier	Unit	D	RPD	Limit
Nitrite as N	<0.10		<0.10		mg/L		NC	9

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98593-1

Client Sample ID: AC-22D

Date Collected: 11/18/14 08:24

Date Received: 11/18/14 16:25

Lab Sample ID: 400-98593-1

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 19:40	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 11:39	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237957	11/25/14 11:24	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238018	11/25/14 11:24	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237404	11/18/14 16:59	LSS	TAL PEN

Client Sample ID: AC-36D

Date Collected: 11/18/14 09:49

Date Received: 11/18/14 16:25

Lab Sample ID: 400-98593-2

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 20:03	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 11:42	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237957	11/25/14 11:25	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238018	11/25/14 11:25	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237404	11/18/14 16:59	LSS	TAL PEN

Client Sample ID: AC-11D

Date Collected: 11/18/14 12:39

Date Received: 11/18/14 16:25

Lab Sample ID: 400-98593-3

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 20:26	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 11:53	SLT	TAL PEN
Total/NA	Analysis	353.2		2	237957	11/25/14 12:07	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238018	11/25/14 12:07	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237404	11/18/14 16:59	LSS	TAL PEN

Client Sample ID: AC-10D

Date Collected: 11/18/14 15:24

Date Received: 11/18/14 16:25

Lab Sample ID: 400-98593-4

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238428	12/01/14 20:49	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 11:56	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237957	11/25/14 12:20	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238018	11/25/14 12:20	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237404	11/18/14 16:59	LSS	TAL PEN

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98593-1

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001
TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131



Method Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98593-1

Method	Method Description	Protocol	Laboratory
300.0	Anions, Ion Chromatography	MCAWW	TAL PEN
340.2	Fluoride	MCAWW	TAL PEN
353.2	Nitrogen, Nitrate-Nitrite	MCAWW	TAL PEN
Nitrate by calc	Nitrogen, Nitrate	SM	TAL PEN
SM 4500 NO2 B	Nitrogen, Nitrite	SM	TAL PEN
Rad 226-Method 903.1 (Richland)	RAD-226 (RCH)	NONE	TAL RCH
Rad 228-Method 904.0 (Richland)	RAD-228 (RCH)	NONE	TAL RCH

Protocol References:

MCAWW = "Methods For Chemical Analysis Of Water And Wastes", EPA-600/4-79-020, March 1983 And Subsequent Revisions.

NONE = NONE

SM = "Standard Methods For The Examination Of Water And Wastewater",

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Analytical Data Package Prepared For

TestAmerica Pensacola

Radiochemical Analysis By

TestAmerica Inc

2800 G.W. Way, Richland Wa, 99354, (509)-375-3131.

Assigned Laboratory Code: TARL

Data Package Contains _____ Pages

Report No.: 63933

Results in this report relate only to the sample(s) analyzed.

SDG No.	Order No.	Client Sample ID (List Order)	Lot-Sa No.	Work Order	Report DB ID	Batch No.
49040		AC-10D(400-98593-4)	J4K240405-4	M5K611AA	9M5K6110	4329024
		AC-10D(400-98593-4)	J4K240405-4	M5K611AC	9M5K6110	4329025
		AC-11D(400-98593-3)	J4K240405-3	M5K601AA	9M5K6010	4329024
		AC-11D(400-98593-3)	J4K240405-3	M5K601AC	9M5K6010	4329025
		AC-22D(400-98593-1)	J4K240405-1	M5K6W1AA	9M5K6W10	4329024
		AC-22D(400-98593-1)	J4K240405-1	M5K6W1AC	9M5K6W10	4329025
		AC-36D(400-98593-2)	J4K240405-2	M5K6X1AA	9M5K6X10	4329024
		AC-36D(400-98593-2)	J4K240405-2	M5K6X1AC	9M5K6X10	4329025

Certificate of Analysis

December 18, 2014

TestAmerica Pensacola
3355 McLemore Drive
Pensacola, FL 32514

Attention: Noel Savoie

Date Received at Lab	:	November 20, 2014
Project Name/Number	:	Agrico Pensacola/64000434
Sample Type	:	Four (4) Water
Job Number	:	400-98593-1
SDG Number	:	49040

CASE NARRATIVE

I. Introduction

On November 20, 2014, four water samples were received at TestAmerica's Richland laboratory for radiochemical analysis. Upon receipt, the samples were assigned the TestAmerica identification number as described on the cover page of the Analytical Data Package report form. The samples were assigned to Lot Numbers J4K240405.

II. Sample Receipt

The samples were received in good condition and no anomalies were noted upon check-in.

III. Analytical Results/Methodology

The analytical results for this report are presented by laboratory sample ID. Each set of data includes sample identification information; analytical results and the appropriate associated statistical uncertainties.

The analysis requested was:

Gas Proportional Counting

Radium-228 by method RL-RA-001

Alpha Scintillation Counting

Radium-226 by method RL-RA-001

IV. Quality Control

The analytical result for each analysis performed includes a minimum of one laboratory control sample (LCS), and one reagent blank sample analysis. Any exceptions have been noted in the "Comments" section.

V. Comments

Gas Proportional Counting

Radium-228

The LCS, batch blank, sample duplicate and sample results are within acceptance limits.

Alpha Scintillation Counting

Radium 226:

The LCS, batch blank, samples and sample duplicate results are within acceptance limits.

I certify that this Certificate of Analysis is in compliance with the SOW and/or NELAC, both technically and for completeness, for other than the conditions detailed above. The Laboratory Manager or a designee, as verified by the following signature has authorized release of the data contained in this hard copy data package.

Reviewed and approved:

Robin Ebert-Mays
Project Manager

Drinking Water Method Cross References

DRINKING WATER ASTM METHOD CROSS REFERENCES		
Referenced Method	Isotope(s)	TestAmerica Richland's SOP No.
EPA 901.1	Cs-134, I-131	RL-GAM-001
EPA 900.0	Alpha & Beta	RL-GPC-001
EPA 00-02	Gross Alpha (Coprecipitation)	RL-GPC-002
EPA 903.0	Total Alpha Radium (Ra-226)	RL-RA-002
EPA 903.1	Ra-226	RL-RA-001
EPA 904.0	Ra-228	RL-RA-001
EPA 905.0	Sr-89/90	RL-GPC-003
ASTM D5174	Uranium	RL-KPA-003
EPA 906.0	Tritium	RL-LSC-005

Results in this report relate only to the sample(s) analyzed.

Uncertainty Estimation

TestAmerica Richland has adopted the internationally accepted approach to estimating uncertainties described in "NIST Technical Note 1297, 1994 Edition". The approach, "Law of Propagation of Errors", involves the identification of all variables in an analytical method which are used to derive a result. These variables are related to the analytical result (R) by some functional relationship, $R = \text{constants} * f(x,y,z,...)$. The components (x,y,z) are evaluated to determine their contribution to the overall method uncertainty. The individual component uncertainties (u_i) are then combined using a statistical model that provides the most probable overall uncertainty value. All component uncertainties are categorized as type A, evaluated by statistical methods, or type B, evaluated by other means. Uncertainties not included in the components, such as sample homogeneity, are combined with the component uncertainty as the square root of the sum-of-the-squares of the individual uncertainties. The uncertainty associated with the derived result is the combined uncertainty (u_c) multiplied by the coverage factor (1,2, or 3).

When three or more sample replicates are used to derive the analytical result, the type A uncertainty is the standard deviation of the mean value ($S/\sqrt{n}$), where S is the standard deviation of the derived results. The type B uncertainties are all other random or non-random components that are not included in the standard deviation.

The derivation of the general "Law of Propagation of Errors" equations and specific example are available on request.

Report Definitions

Action Lev	An agreed upon activity level used to trigger some action when the final result is greater than or equal to the Action Level. Often the Action Level is related to the Decision Limit.
Batch	The QC preparation batch number that relates laboratory samples to QC samples that were prepared and analyzed together.
Bias	Defined by the equation (Result/Expected)-1 as defined by ANSI N13.30.
COC No	Chain of Custody Number assigned by the Client or TestAmerica.
Count Error (#s)	Poisson counting statistics of the gross sample count and background. The uncertainty is absolute and in the same units as the result. For Liquid Scintillation Counting (LSC) the batch blank count is the background.
Total Uncert (#s) <i>u_c - Combined Uncertainty.</i>	All known uncertainties associated with the preparation and analysis of the sample are propagated to give a measure of the uncertainty associated with the result, <i>u_c the combined uncertainty</i> . The uncertainty is absolute and in the same units as the result.
(#s), Coverage Factor	The coverage factor defines the width of the confidence interval, 1, 2 or 3 standard deviations.
CRDL (RL)	Contractual Required Detection Limit as defined in the Client's Statement Of Work or TestAmerica "default" nominal detection limit. Often referred to the reporting level (RL)
Lc	Decision Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume associated with the sample. The Type I error probability is approximately 5%. $Lc = (1.645 * \sqrt{2 * (BkgndCnt / BkgndCntMin) / SCntMin}) * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability. Lc cannot be calculated when the background count is zero.
Lot-Sample No	The number assigned by the LIMS software to track samples received on the same day for a given client. The sample number is a sequential number assigned to each sample in the Lot.
MDC MDA	Detection Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume with a Type I and II error probability of approximately 5%. $MDC = (4.65 * \sqrt{(BkgndCnt / BkgndCntMin) / SCntMin}) + 2.71 / SCntMin * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability.
Primary Detector	The instrument identifier associated with the analysis of the sample aliquot.
Ratio U-234/U-238	The U-234 result divided by the U-238 result. The U-234/U-238 ratio for natural uranium in NIST SRM 4321C is 1.038.
Rst/MDC	Ratio of the Result to the MDC. A value greater than 1 may indicate activity above background at a high level of confidence. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Rst/TotUcert	Ratio of the Result to the Total Uncertainty. If the uncertainty has a coverage factor of 2 a value greater than 1 may indicate activity above background at approximately the 95% level of confidence assuming a two-sided confidence interval. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Report DB No	Sample Identifier used by the report system. The number is based upon the first five digits of the Work Order Number.
RER	The equation Replicate Error Ratio = $(S-D) / [\sqrt{TPUs^2 + TPUD^2}]$ as defined by ICPT BOA where S is the original sample result, D is the result of the duplicate, TPUs is the total uncertainty of the original sample and TPUD is the total uncertainty of the duplicate sample.
SDG	Sample Delivery Group Number assigned by the Client or assigned by TestAmerica upon sample receipt.
Sum Rpt Alpha Spec Rst(s)	The sum of the reported alpha spec results for tests derived from the same sample excluding duplicate result where the results are in the same units.
Work Order	The LIMS software assign test specific identifier.
Yield	The recovery of the tracer added to the sample such as Pu-242 used to trace a Pu-239/40 method.

Sample Results Summary

Date: 18-Dec-14

TestAmerica Inc TARL

Ordered by Method, Batch No., Client Sample ID.

Report No. : 63933

SDG No: 49040

Batch	Client Id Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	MDL	CRDL	RER2
4329024	RL-RA-001								
	AC-10D(400-98593-4)								
	M5K611AA Ra-226		1.02E+00 +- 2.9E-01		pCi/L	100%	2.07E-01	1.00E+00	
	AC-11D(400-98593-3)								
	M5K601AA Ra-226		8.51E-01 +- 2.5E-01	J	pCi/L	100%	1.92E-01	1.00E+00	
	AC-22D(400-98593-1)								
	M5K6W1AA Ra-226		1.11E+00 +- 3.0E-01		pCi/L	100%	2.23E-01	1.00E+00	
	AC-22D(400-98593-1) DUP								
	M5K6W1AD Ra-226		1.47E+00 +- 4.7E-01		pCi/L	86%	3.42E-01	1.00E+00	1.3
	AC-36D(400-98593-2)								
	M5K6X1AA Ra-226		1.48E+00 +- 4.7E-01		pCi/L	90%	2.73E-01	1.00E+00	
4329025	RL-RA-001								
	AC-10D(400-98593-4)								
	M5K611AC Ra-228		2.17E+00 +- 5.1E-01		pCi/L	88%	5.99E-01	1.00E+00	
	AC-11D(400-98593-3)								
	M5K601AC Ra-228		1.63E+00 +- 4.6E-01		pCi/L	92%	7.34E-01	1.00E+00	
	AC-22D(400-98593-1)								
	M5K6W1AC Ra-228		2.59E+00 +- 5.6E-01		pCi/L	89%	7.77E-01	1.00E+00	
	AC-22D(400-98593-1) DUP								
	M5K6W1AE Ra-228		3.80E+00 +- 7.3E-01		pCi/L	74%	8.53E-01	1.00E+00	2.6
	AC-36D(400-98593-2)								
	M5K6X1AC Ra-228		2.33E+00 +- 6.0E-01		pCi/L	80%	9.34E-01	1.00E+00	
No. of Results: 10									

TestAmerica Inc RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPUs)+sq(TPUD))] as defined by ICPT BOA.
 rptTALRchSaSum J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
 mary2 V5.3.6.1
 A2002

QC Results Summary
TestAmerica Inc TARL
 Ordered by Method, Batch No, QC Type,.

Date: 18-Dec-14

Report No. : 63933

SDG No.: 49040

Batch	Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	LCS Recovery	Bias	MDL
RL-RA-001									
4329024 BLANK QC,									
	M5LG61AA	Ra-226	1.98E-02 +- 7.8E-02	U	pCi/L	100%			1.62E-01
4329024 LCS,									
	M5LG61AC	Ra-226	8.15E+00 +- 1.8E+00		pCi/L	99%	82%	-0.2	2.32E-01
RL-RA-001									
4329025 BLANK QC,									
	M5LG71AA	Ra-228	2.86E-02 +- 2.0E-01	U	pCi/L	89%			4.84E-01
4329025 LCS,									
	M5LG71AC	Ra-228	8.23E+00 +- 1.1E+00		pCi/L	86%	85%	-0.2	5.00E-01
No. of Results: 4									

FORM I

Date: 18-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49040 Collection Date: 11/18/2014 3:24:00 PM
Lot-Sample No.: J4K240405-4 Report No.: 63933 Received Date: 11/20/2014 1:00:00 PM
Client Sample ID: AC-10D(400-98593-4) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024 RL-RA-001 1.02E+00 2.1E-01 2.9E-01 2.07E-01 pCi/L 100% (4.9) 12/15/14 03:38 p 0.8757 L ASCEHB												
Work Order: M5K611AA Report DB ID: 9M5K6110 9.25E-02 1.00E+00 (7.)												
Batch: 4329025 RL-RA-001 2.17E+00 4.3E-01 5.1E-01 5.99E-01 pCi/L 88% (3.6) 12/17/14 12:47 p 0.8757 L GPC2A												
Work Order: M5K611AC Report DB ID: 9M5K6110 2.65E-01 1.00E+00 (8.5)												

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
V5.3.6.1 A2002

FORM I

Date: 18-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49040 Collection Date: 11/18/2014 12:39:00 PM
Lot-Sample No.: J4K240405-3 Report No.: 63933 Received Date: 11/20/2014 1:00:00 PM
Client Sample ID: AC-11D(400-98593-3) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024 RL-RA-001 Work Order: M5K601AA Report DB ID: 9M5K6010												
Ra-226	8.51E-01	J	1.9E-01	2.5E-01	1.92E-01	pCi/L	100%	(4.4)	12/15/14 03:39 p		0.8804	ASCDMB
						8.50E-02	1.00E+00	(6.8)			L	
Batch: 4329025 RL-RA-001 Work Order: M5K601AC Report DB ID: 9M5K6010												
Ra-228	1.63E+00		4.1E-01	4.6E-01	7.34E-01	pCi/L	92%	(2.2)	12/17/14 12:47 p		0.8804	GPC1D
						3.40E-01	1.00E+00	(7.1)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 18-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K240405-1
Client Sample ID: AC-22D(400-98593-1)

SDG: 49040
Report No.: 63933
COC No.:
Collection Date: 11/18/2014 8:24:00 AM
Received Date: 11/20/2014 1:00:00 PM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024 RL-RA-001												
Ra-226	1.11E+00		2.1E-01	3.0E-01	2.23E-01	pCi/L	100%	(5.)	12/15/14 03:38 p		0.9282	ASC1HB
						1.01E-01	1.00E+00	(7.4)			L	
Batch: 4329025 RL-RA-001												
Ra-228	2.59E+00		4.7E-01	5.6E-01	7.77E-01	pCi/L	89%	(3.3)	12/17/14 12:47 p		0.9282	GPC1A
						3.62E-01	1.00E+00	(9.2)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 18-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K240405-2
Client Sample ID: AC-36D(400-98593-2)

SDG: 49040
Report No.: 63933
COC No.:
Collection Date: 11/18/2014 9:49:00 AM
Received Date: 11/20/2014 1:00:00 PM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024 RL-RA-001												
Ra-226	1.48E+00		2.9E-01	4.7E-01	M5K6X1AA 2.73E-01	pCi/L 1.22E-01	90% 1.00E+00	(5.4) (6.3)	12/15/14 03:38 p		0.8629 L	ASC8HD
Batch: 4329025 RL-RA-001												
Ra-228	2.33E+00		5.2E-01	6.0E-01	M5K6X1AC 9.34E-01	pCi/L 4.35E-01	80% 1.00E+00	(2.5) (7.7)	12/17/14 12:47 p		0.8629 L	GPC1C

No. of Results: 2 Comments:

TestAmerica Inc MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM II

Date: 18-Dec-14

DUPLICATE RESULTS

Lab Name: TestAmerica Inc SDG: 49040 Collection Date: 11/18/2014 8:24:00 AM
Lot-Sample No.: J4K240405-1 Report No.: 63933 Received Date: 11/20/2014 1:00:00 PM
Client Sample ID: AC-22D(400-98593-1) DUP COC No.: Matrix: WATER

Parameter	Result, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024 RL-RA-001 Work Order: M5K6W1AD Report DB ID: M5K6W1DR Orig Sa DB ID: 9M5K6W10												
Ra-226	1.47E+00		3.0E-01	4.7E-01	3.42E-01	pCi/L	86%	(4.3)	12/15/14 03:39 p		0.8838	ASC7HB
	1.11E+00		RER2 1.3			1.00E+00		(6.3)			L	
Batch: 4329025 RL-RA-001 Work Order: M5K6W1AE Report DB ID: M5K6W1ER Orig Sa DB ID: 9M5K6W10												
Ra-228	3.80E+00		5.8E-01	7.3E-01	8.53E-01	pCi/L	74%	(4.5)	12/17/14 12:47 p		0.8838	GPC1B
	2.59E+00		RER2 2.6			1.00E+00		(10.4)			L	

No. of Results: 2 Comments:

TestAmerica Inc RER2 - Replicate Error Ratio = $(S-D)/[\sqrt{(sq(TPU_s)+sq(TPU_d))}]$ as defined by ICPT BOA.
MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.

3.6.1 A2002

Date: 18-Dec-14

SDG: 49040

Report No.: 63933

No. of Results:	2	Comments:

FORM II
LCS RESULTS

Date: 18-Dec-14

Lab Name: TestAmerica Inc
Matrix: WATER

SDG: 49040
Report No.: 63933

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL	Report Unit	Yield	Expected	Expected Uncert	Recovery, Bias	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4329024													
RL-RA-001	8.15E+00		5.9E-01	1.8E+00	2.32E-01	pCi/L	99%	9.93E+00	1.12E-01	82%	12/15/14 03:50 p	1.0009	ASC3RA
Ra-226							Rec Limits:	75	125	-0.2		L	
Batch: 4329025													
RL-RA-001	8.23E+00		6.7E-01	1.1E+00	5.00E-01	pCi/L	86%	9.75E+00	1.11E-01	85%	12/17/14 12:47 p	1.0009	GPC3D
Ra-228							Rec Limits:	75	125	-0.2		L	

No. of Results: 2 Comments:

Chain of Custody Record



Client Information (Sub Contract Lab)		Sampler:	Lab PW:	Carrier Tracking No(s):	GOC No:							
		Savoie, Noel	Savoie, Noel		400-65688.1							
Client Contact: Shipping/Receiving		Phone:	E-Mail:	Page:	Page 1 of 1							
Company: TestAmerica Laboratories, Inc.		Due Date Requested:		Job #:	400-98593-1							
Address: 2800 George Washington Way, City: Richland State, Zip: WA, 99352		TAT Requested (days): PO #: WO #: Project #: 64000434 Site:		Preservation Codes: A - HCL M - Hexane B - NaOH N - None C - Zn Acetate O - AsNaO2 D - Nitric Acid P - Na2O4S E - NaHSO4 Q - Na2SO3 F - MeOH R - Na2S2O3 G - Amchlor S - H2SO4 H - Ascorbic Acid I - Ice J - DI Water K - EDTA L - EDA W - pH 4-5 Z - other (specify) Other:								
Sample Identification - Client ID (Lab ID)		Sample Date	Sample Time	Sample Type (G=Comp, C=grab) BT=Tissue, A=Air	Matrix (W=water, S=solid, O=waste/oil)	Field Filtered Sample (Yes or No)	Perform MS/MSD (Yes or No)	SUB (Radium 226 by EPA Method 903.1) Rad 226-Method	SUB (Radium 228 by EPA Method 904.0) Rad 228-Method	904.0 (Radon)	Total Number of Containers	Special Instructions/Note:
AC-22D (400-98593-1)	11/18/14	08:24 Central	Water	X	X	X	X	3	M5K6W			
AC-36D (400-98593-2)	11/18/14	09:49 Central	Water	X	X	X	X	3	M5K6X			
AC-11D (400-98593-3)	11/18/14	12:39 Central	Water	X	X	X	X	3	M5K6O			
AC-10D (400-98593-4)	11/18/14	15:24 Central	Water	X	X	X	X	3	M5K6I			
Possible Hazard Identification		Sample Disposal (A fee may be assessed if samples are retained longer than 1 month)										
Unconfirmed		☐ Return To Client ☐ Disposal By Lab ☐ Archive For _____ Months										
Deliverable Requested: I, II, IV, Other (specify)		Special Instructions/QC Requirements:										
Empty Kit Relinquished by:		Date:	Time:	Method of Shipment:								
Relinquished by:		Date/Time:	Company:	Received by:								
Relinquished by:		Date/Time:	Company:	Received by:								
Relinquished by:		Date/Time:	Company:	Received by:								
Custody Seal No.:		Cooler Temperature(s) °C and Other Remarks:										

Sample Check-in List

Date/Time Received: 11-20-14/1300 Container GM Screen Result: (Airlock) 20 cpm Initials B
Sample GM Screen Result (Sample Receiving) 20 cpm Initials B

Client: STP SDG #: 49040 SAF #: _____ NA B

Lot Number: J4K240405

Chain of Custody # N/A

Shipping Container ID or Air Bill Number : _____ NA B

Samples received inside shipping container/cooler/box Yes B] Continue with 1 through 4. Initial appropriate response.
No [] Go to 5, add comment to #16.

1. Custody Seals on shipping container intact? Yes B] No [] No Custody Seal []
2. Custody Seals dated and signed? Yes B] No [] No Custody Seal []
3. Cooler temperature: _____ °C NA B]
4. Vermiculite/packing materials is NA [] Wet [] Dry B]

Item 5 through 16 for samples. Initial appropriate response.

5. Chain of Custody record present? Yes B] No []
6. Number of samples received (Each sample may contain multiple bottles): 4
7. Containers received: 12 x 4

8. Sample holding times exceeded? NA [] Yes [] No B]
9. Samples have: _____ tape _____ hazard labels _____ custody seals B appropriate sample labels
10. Matrix: _____ A (FLT, Wipe, Solid, Soil) B I (Water) _____ S (Air, Niosh 7400) _____ T (Biological, Ni-63)

11. Samples: B are in good condition _____ are leaking _____ are broken
_____ have air bubbles (Only for samples requiring no head space) _____ Other _____

12. Sample pH appropriate for analysis requested Yes B] No [] NA []
(If acidification is necessary go to pH area & document sample ID, initial pH, amount of HNO₃ added and pH after addition on table)
13. Were any anomalies identified in sample receipt? Yes [] No B]
14. Description of anomalies (include sample numbers): NA B]

15. Sample Location, Sample Collector Listed on COC? * Yes [] No B]
*For documentation only. No corrective action needed.

16. Additional Information: N/A

[] Client/Courier denied temperature check. [] Client/Courier unpack cooler.

Sample Check-in List completed by Sample Custodian:

Signature: [Signature] Date: 11-23-14

Client Notification needed? Yes [] No [] Date: _____

By: _____

Person contacted: _____

[Signature] No action necessary; process as is

Project Manager [Signature]

Date 11/24/14

12/19/2014

TestAmerica

THE LEADER IN ENVIRONMENTAL TESTING

ANALYTICAL REPORT

TestAmerica Laboratories, Inc.

TestAmerica Pensacola

3355 McLemore Drive

Pensacola, FL 32514

Tel: (850)474-1001

TestAmerica Job ID: 400-98663-1

Client Project/Site: Agrico Pensacola

For:

URS Corporation

1625 Summit Lake Drive

Suite 200

Tallahassee, Florida 32317

Attn: Mr. Jeff Wagner



Authorized for release by:

12/19/2014 3:17:57 PM

Noel Savoie, Project Manager I

(850)878-3994

noel.savoie@testamericainc.com

LINKS

Review your project
results through

TotalAccess

Have a Question?



Visit us at:

www.testamericainc.com

The test results in this report meet all 2003 NELAC and 2009 TNI requirements for accredited parameters, exceptions are noted in this report. This report may not be reproduced except in full, and with written approval from the laboratory. For questions please contact the Project Manager at the e-mail address or telephone number listed on this page.

This report has been electronically signed and authorized by the signatory. Electronic signature is intended to be the legally binding equivalent of a traditionally handwritten signature.

Results relate only to the items tested and the sample(s) as received by the laboratory.

Table of Contents

Cover Page	1
Table of Contents	2
Definitions	3
Case Narrative	4
Sample Summary	5
Client Sample Results	6
QC Sample Results	8
Chronicle	12
Method Summary	14
Subcontract Data	15
Chain of Custody	32



Definitions/Glossary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Qualifiers

General Chemistry

Qualifier	Qualifier Description
F2	MS/MSD RPD exceeds control limits

Glossary

Abbreviation	These commonly used abbreviations may or may not be present in this report.
α	Listed under the "D" column to designate that the result is reported on a dry weight basis
%R	Percent Recovery
CFL	Contains Free Liquid
CNF	Contains no Free Liquid
DER	Duplicate error ratio (normalized absolute difference)
Dil Fac	Dilution Factor
DL, RA, RE, IN	Indicates a Dilution, Re-analysis, Re-extraction, or additional Initial metals/anion analysis of the sample
DLC	Decision level concentration
MDA	Minimum detectable activity
EDL	Estimated Detection Limit
MDC	Minimum detectable concentration
MDL	Method Detection Limit
ML	Minimum Level (Dioxin)
NC	Not Calculated
ND	Not detected at the reporting limit (or MDL or EDL if shown)
PQL	Practical Quantitation Limit
QC	Quality Control
RER	Relative error ratio
RL	Reporting Limit or Requested Limit (Radiochemistry)
RPD	Relative Percent Difference, a measure of the relative difference between two points
TEF	Toxicity Equivalent Factor (Dioxin)
TEQ	Toxicity Equivalent Quotient (Dioxin)

Case Narrative

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Job ID: 400-98663-1

Laboratory: TestAmerica Pensacola

Narrative

Job Narrative 400-98663-1

Comments

No additional comments.

Receipt

The samples were received on 11/19/2014 4:33 PM; the samples arrived in good condition, properly preserved and, where required, on ice. The temperature of the cooler at receipt was 3.1° C.

Except:

The container label for the following sample did not match the information listed on the Chain-of-Custody (COC). The container labels list AC-26S, while the COC lists AC-26C. Per client AC-26S is the correct sample ID.

HPLC/IC

Method 300.0: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-13D (400-98663-2) and DUP-1 (400-98663-5). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

General Chemistry

Method 353.2: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-14D (400-98663-1), AC-13D (400-98663-2), and DUP-1 (400-98663-5). Elevated reporting limits (RLs) are provided.

Method 353.2: The sample duplicate precision for the following sample associated with batch 237957 was outside control limits: AC-26D (400-98663-4 MSD).

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Subcontract Work

Methods Radium 226 by EPA Method 903.1, Radium 228 by EPA Method 904.0: These methods were subcontracted to TestAmerica Richland. Report attached.

Sample Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Lab Sample ID	Client Sample ID	Matrix	Collected	Received
400-98663-1	AC-14D	Water	11/19/14 09:47	11/19/14 16:33
400-98663-2	AC-13D	Water	11/19/14 11:50	11/19/14 16:33
400-98663-3	AC-26C	Water	11/19/14 14:24	11/19/14 16:33
400-98663-4	AC-26D	Water	11/19/14 15:35	11/19/14 16:33
400-98663-5	DUP-1	Water	11/19/14 00:00	11/19/14 16:33

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Client Sample ID: AC-14D

Lab Sample ID: 400-98663-1

Date Collected: 11/19/14 09:47

Matrix: Water

Date Received: 11/19/14 16:33

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	11		1.0		mg/L			12/02/14 16:42	1
Sulfate	26		1.0		mg/L			12/02/14 16:42	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 11:59	1
Nitrate Nitrite as N	5.3		0.25		mg/L			11/25/14 11:40	5
Nitrate as N	5.3		0.050		mg/L			11/25/14 11:40	1
Nitrite as N	<0.10		0.10		mg/L			11/20/14 10:37	1

Client Sample ID: AC-13D

Lab Sample ID: 400-98663-2

Date Collected: 11/19/14 11:50

Matrix: Water

Date Received: 11/19/14 16:33

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	21		1.0		mg/L			12/02/14 17:05	1
Sulfate	250		20		mg/L			12/03/14 19:59	20

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	12		0.20		mg/L			11/24/14 12:17	2
Nitrate Nitrite as N	11		0.50		mg/L			12/01/14 17:42	10
Nitrate as N	11		0.050		mg/L			12/01/14 17:42	1
Nitrite as N	<0.10		0.10		mg/L			11/20/14 10:37	1

Client Sample ID: AC-26C

Lab Sample ID: 400-98663-3

Date Collected: 11/19/14 14:24

Matrix: Water

Date Received: 11/19/14 16:33

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	7.3		1.0		mg/L			12/02/14 17:28	1
Sulfate	13		1.0		mg/L			12/02/14 17:28	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 12:08	1
Nitrate Nitrite as N	1.0		0.050		mg/L			11/25/14 11:42	1
Nitrate as N	1.0		0.050		mg/L			11/25/14 11:42	1
Nitrite as N	<0.10		0.10		mg/L			11/20/14 10:37	1

Client Sample ID: AC-26D

Lab Sample ID: 400-98663-4

Date Collected: 11/19/14 15:35

Matrix: Water

Date Received: 11/19/14 16:33

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	2.8		1.0		mg/L			12/02/14 17:50	1
Sulfate	7.5		1.0		mg/L			12/02/14 17:50	1

TestAmerica Pensacola

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Client Sample ID: AC-26D

Date Collected: 11/19/14 15:35

Date Received: 11/19/14 16:33

Lab Sample ID: 400-98663-4

Matrix: Water

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 12:19	1
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/25/14 11:50	1
Nitrate as N	<0.050		0.050		mg/L			11/25/14 11:50	1
Nitrite as N	<0.10		0.10		mg/L			11/20/14 10:37	1

Client Sample ID: DUP-1

Date Collected: 11/19/14 00:00

Date Received: 11/19/14 16:33

Lab Sample ID: 400-98663-5

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	21		1.0		mg/L			12/02/14 18:59	1
Sulfate	250		20		mg/L			12/03/14 20:22	20

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	12		0.20		mg/L			11/24/14 12:28	2
Nitrate Nitrite as N	11		0.50		mg/L			11/25/14 11:53	10
Nitrate as N	11		0.050		mg/L			11/25/14 11:53	1
Nitrite as N	<0.10		0.10		mg/L			11/20/14 10:37	1

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Method: 300.0 - Anions, Ion Chromatography

Lab Sample ID: MB 400-238563/4

Matrix: Water

Analysis Batch: 238563

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/02/14 14:25	1
Sulfate	<1.0		1.0		mg/L			12/02/14 14:25	1

Lab Sample ID: LCS 400-238563/5

Matrix: Water

Analysis Batch: 238563

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	9.79		mg/L		98	90 - 110
Sulfate	10.0	9.94		mg/L		99	90 - 110

Lab Sample ID: LCSD 400-238563/6

Matrix: Water

Analysis Batch: 238563

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	9.76		mg/L		98	90 - 110	0	15
Sulfate	10.0	9.75		mg/L		97	90 - 110	2	15

Lab Sample ID: MB 400-238692/4

Matrix: Water

Analysis Batch: 238692

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/03/14 13:30	1
Sulfate	<1.0		1.0		mg/L			12/03/14 13:30	1

Lab Sample ID: LCS 400-238692/5

Matrix: Water

Analysis Batch: 238692

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	9.78		mg/L		98	90 - 110
Sulfate	10.0	10.0		mg/L		100	90 - 110

Lab Sample ID: LCSD 400-238692/6

Matrix: Water

Analysis Batch: 238692

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	9.65		mg/L		96	90 - 110	1	15
Sulfate	10.0	9.77		mg/L		98	90 - 110	2	15

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Method: 340.2 - Fluoride

Lab Sample ID: MB 400-237785/3
Matrix: Water
Analysis Batch: 237785

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 11:11	1

Lab Sample ID: LCS 400-237785/4
Matrix: Water
Analysis Batch: 237785

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.30		mg/L		108	90 - 110

Lab Sample ID: 400-98663-3 DU
Matrix: Water
Analysis Batch: 237785

Client Sample ID: AC-26C
Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	DU Result	DU Qualifier	Unit	D	RPD	Limit
Fluoride	<0.10		<0.10		mg/L		NC	4

Method: 353.2 - Nitrogen, Nitrate-Nitrite

Lab Sample ID: MB 400-237957/14
Matrix: Water
Analysis Batch: 237957

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/25/14 11:06	1

Lab Sample ID: MB 400-237957/46
Matrix: Water
Analysis Batch: 237957

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/25/14 11:48	1

Lab Sample ID: LCS 400-237957/15
Matrix: Water
Analysis Batch: 237957

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.460		mg/L		92	90 - 110

Lab Sample ID: LCS 400-237957/47
Matrix: Water
Analysis Batch: 237957

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.534		mg/L		107	90 - 110

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Method: 353.2 - Nitrogen, Nitrate-Nitrite (Continued)

Lab Sample ID: MRL 400-237957/12

Matrix: Water

Analysis Batch: 237957

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	<0.050		mg/L		92	50 - 150

Lab Sample ID: 400-98663-4 MS

Matrix: Water

Analysis Batch: 237957

Client Sample ID: AC-26D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	<0.050		0.500	0.532		mg/L		101	90 - 110

Lab Sample ID: 400-98663-4 MSD

Matrix: Water

Analysis Batch: 237957

Client Sample ID: AC-26D

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Nitrate Nitrite as N	<0.050		0.500	0.478	F2	mg/L		90	90 - 110	11	4

Lab Sample ID: MB 400-238443/14

Matrix: Water

Analysis Batch: 238443

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			12/01/14 17:07	1

Lab Sample ID: LCS 400-238443/15

Matrix: Water

Analysis Batch: 238443

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.488		mg/L		97	90 - 110

Lab Sample ID: MRL 400-238443/12

Matrix: Water

Analysis Batch: 238443

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	<0.050		mg/L		98	50 - 150

Method: Nitrate by calc - Nitrogen, Nitrate

Lab Sample ID: MB 400-238018/14

Matrix: Water

Analysis Batch: 238018

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate as N	N/A		0.050		mg/L			11/25/14 11:06	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Method: Nitrate by calc - Nitrogen, Nitrate (Continued)

Lab Sample ID: MB 400-238018/46

Matrix: Water

Analysis Batch: 238018

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate as N	N/A		0.050		mg/L			11/25/14 11:48	1

Lab Sample ID: MB 400-238494/46

Matrix: Water

Analysis Batch: 238494

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate as N	N/A		0.050		mg/L			12/01/14 17:49	1

Method: SM 4500 NO2 B - Nitrogen, Nitrite

Lab Sample ID: MB 400-237496/9

Matrix: Water

Analysis Batch: 237496

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/20/14 09:38	1

Lab Sample ID: LCS 400-237496/20

Matrix: Water

Analysis Batch: 237496

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.299		mg/L		100	90 - 110

Lab Sample ID: MRL 400-237496/7

Matrix: Water

Analysis Batch: 237496

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.100	<0.10		mg/L		96	50 - 150

Lab Sample ID: 400-98663-5 DU

Matrix: Water

Analysis Batch: 237496

Client Sample ID: DUP-1

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	DU Result	DU Qualifier	Unit	D	RPD	RPD Limit
Nitrite as N	<0.10		<0.10		mg/L		NC	9

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Client Sample ID: AC-14D

Date Collected: 11/19/14 09:47

Date Received: 11/19/14 16:33

Lab Sample ID: 400-98663-1

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238563	12/02/14 16:42	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 11:59	SLT	TAL PEN
Total/NA	Analysis	353.2		5	237957	11/25/14 11:40	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238018	11/25/14 11:40	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237496	11/20/14 10:37	LSS	TAL PEN

Client Sample ID: AC-13D

Date Collected: 11/19/14 11:50

Date Received: 11/19/14 16:33

Lab Sample ID: 400-98663-2

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238563	12/02/14 17:05	TAJ	TAL PEN
Total/NA	Analysis	300.0		20	238692	12/03/14 19:59	TAJ	TAL PEN
Total/NA	Analysis	340.2		2	237785	11/24/14 12:17	SLT	TAL PEN
Total/NA	Analysis	353.2		10	238443	12/01/14 17:42	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238494	12/01/14 17:42	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237496	11/20/14 10:37	LSS	TAL PEN

Client Sample ID: AC-26C

Date Collected: 11/19/14 14:24

Date Received: 11/19/14 16:33

Lab Sample ID: 400-98663-3

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238563	12/02/14 17:28	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 12:08	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237957	11/25/14 11:42	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238018	11/25/14 11:42	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237496	11/20/14 10:37	LSS	TAL PEN

Client Sample ID: AC-26D

Date Collected: 11/19/14 15:35

Date Received: 11/19/14 16:33

Lab Sample ID: 400-98663-4

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238563	12/02/14 17:50	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 12:19	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237957	11/25/14 11:50	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238018	11/25/14 11:50	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237496	11/20/14 10:37	LSS	TAL PEN

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Client Sample ID: DUP-1

Date Collected: 11/19/14 00:00

Date Received: 11/19/14 16:33

Lab Sample ID: 400-98663-5

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238563	12/02/14 18:59	TAJ	TAL PEN
Total/NA	Analysis	300.0		20	238692	12/03/14 20:22	TAJ	TAL PEN
Total/NA	Analysis	340.2		2	237785	11/24/14 12:28	SLT	TAL PEN
Total/NA	Analysis	353.2		10	237957	11/25/14 11:53	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238018	11/25/14 11:53	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237496	11/20/14 10:37	LSS	TAL PEN

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLeMure Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Method Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98663-1

Method	Method Description	Protocol	Laboratory
300.0	Anions, Ion Chromatography	MCAWW	TAL PEN
340.2	Fluoride	MCAWW	TAL PEN
353.2	Nitrogen, Nitrate-Nitrite	MCAWW	TAL PEN
Nitrate by calc	Nitrogen, Nitrate	SM	TAL PEN
SM 4500 NO2 B	Nitrogen, Nitrite	SM	TAL PEN
Rad 226-Method 903.1 (Richland)	RAD-226 (RCH)	NONE	TAL RCH
Rad 228-Method 904.0 (Richland)	RAD-228 (RCH)	NONE	TAL RCH

Protocol References:

MCAWW = "Methods For Chemical Analysis Of Water And Wastes", EPA-600/4-79-020, March 1983 And Subsequent Revisions.

NONE = NONE

SM = "Standard Methods For The Examination Of Water And Wastewater",

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Analytical Data Package Prepared For

TestAmerica Pensacola

Radiochemical Analysis By

TestAmerica Inc

2800 G.W. Way, Richland Wa, 99354, (509)-375-3131.

Assigned Laboratory Code: TARL

Data Package Contains _____ Pages

Report No.: 63936

Results in this report relate only to the sample(s) analyzed.

SDG No.	Order No.	Client Sample ID (List Order)	Lot-Sa No.	Work Order	Report DB ID	Batch No.
49041		AC-13D(400-98663-2)	J4K240407-2	M5K641AA	9M5K6410	4329024
		AC-13D(400-98663-2)	J4K240407-2	M5K641AC	9M5K6410	4329025
		AC-14D(400-98663-1)	J4K240407-1	M5K631AA	9M5K6310	4329024
		AC-14D(400-98663-1)	J4K240407-1	M5K631AC	9M5K6310	4329025
		AC-26D(400-98663-4)	J4K240407-4	M5K661AA	9M5K6610	4329024
		AC-26D(400-98663-4)	J4K240407-4	M5K661AC	9M5K6610	4329025
		AC-26S(400-98663-3)	J4K240407-3	M5K651AA	9M5K6510	4329024
		AC-26S(400-98663-3)	J4K240407-3	M5K651AC	9M5K6510	4329025
		DUP-1(400-98663-5)	J4K240407-5	M5K671AA	9M5K6710	4329024
		DUP-1(400-98663-5)	J4K240407-5	M5K671AC	9M5K6710	4329025

Certificate of Analysis

December 18, 2014

TestAmerica Pensacola
3355 McLemore Drive
Pensacola, FL 32514

Attention: Noel Savoie

Date Received at Lab	:	November 21, 2014
Project Name/Number	:	Agrico Pensacola/64000434
Sample Type	:	Five (5) Water
Job Number	:	400-98663-1
SDG Number	:	49041

CASE NARRATIVE

I. Introduction

On November 20, 2014, five water samples were received at TestAmerica's Richland laboratory for radiochemical analysis. Upon receipt, the samples were assigned the TestAmerica identification number as described on the cover page of the Analytical Data Package report form. The samples were assigned to Lot Numbers J4K240407.

II. Sample Receipt

The samples were received in good condition and no anomalies were noted upon check-in.

III. Analytical Results/Methodology

The analytical results for this report are presented by laboratory sample ID. Each set of data includes sample identification information; analytical results and the appropriate associated statistical uncertainties.

The analysis requested was:

Gas Proportional Counting

Radium-228 by method RL-RA-001

Alpha Scintillation Counting

Radium-226 by method RL-RA-001

IV. Quality Control

The analytical result for each analysis performed includes a minimum of one laboratory control sample (LCS), and one reagent blank sample analysis. Any exceptions have been noted in the Comments” section.

V. Comments

Gas Proportional Counting

Radium-228

The LCS, batch blank, sample duplicate and sample results are within acceptance limits.

Alpha Scintillation Counting

Radium 226:

The LCS, batch blank, samples and sample duplicate results are within acceptance limits.

I certify that this Certificate of Analysis is in compliance with the SOW and/or NELAC, both technically and for completeness, for other than the conditions detailed above. The Laboratory Manager or a designee, as verified by the following signature has authorized release of the data contained in this hard copy data package.

Reviewed and approved:

Robin Ebert-Mays
Project Manager

Drinking Water Method Cross References

DRINKING WATER ASTM METHOD CROSS REFERENCES		
Referenced Method	Isotope(s)	TestAmerica Richland's SOP No.
EPA 901.1	Cs-134, I-131	RL-GAM-001
EPA 900.0	Alpha & Beta	RL-GPC-001
EPA 00-02	Gross Alpha (Coprecipitation)	RL-GPC-002
EPA 903.0	Total Alpha Radium (Ra-226)	RL-RA-002
EPA 903.1	Ra-226	RL-RA-001
EPA 904.0	Ra-228	RL-RA-001
EPA 905.0	Sr-89/90	RL-GPC-003
ASTM D5174	Uranium	RL-KPA-003
EPA 906.0	Tritium	RL-LSC-005

Results in this report relate only to the sample(s) analyzed.

Uncertainty Estimation

TestAmerica Richland has adopted the internationally accepted approach to estimating uncertainties described in "NIST Technical Note 1297, 1994 Edition". The approach, "Law of Propagation of Errors", involves the identification of all variables in an analytical method which are used to derive a result. These variables are related to the analytical result (R) by some functional relationship, $R = \text{constants} * f(x,y,z,...)$. The components (x,y,z) are evaluated to determine their contribution to the overall method uncertainty. The individual component uncertainties (u_i) are then combined using a statistical model that provides the most probable overall uncertainty value. All component uncertainties are categorized as type A, evaluated by statistical methods, or type B, evaluated by other means. Uncertainties not included in the components, such as sample homogeneity, are combined with the component uncertainty as the square root of the sum-of-the-squares of the individual uncertainties. The uncertainty associated with the derived result is the combined uncertainty (u_c) multiplied by the coverage factor (1,2, or 3).

When three or more sample replicates are used to derive the analytical result, the type A uncertainty is the standard deviation of the mean value ($S/\sqrt{n}$), where S is the standard deviation of the derived results. The type B uncertainties are all other random or non-random components that are not included in the standard deviation.

The derivation of the general "Law of Propagation of Errors" equations and specific example are available on request.

Report Definitions

Action Lev	An agreed upon activity level used to trigger some action when the final result is greater than or equal to the Action Level. Often the Action Level is related to the Decision Limit.
Batch	The QC preparation batch number that relates laboratory samples to QC samples that were prepared and analyzed together.
Bias	Defined by the equation (Result/Expected)-1 as defined by ANSI N13.30.
COC No	Chain of Custody Number assigned by the Client or TestAmerica.
Count Error (#s)	Poisson counting statistics of the gross sample count and background. The uncertainty is absolute and in the same units as the result. For Liquid Scintillation Counting (LSC) the batch blank count is the background.
Total Uncert (#s) <i>u_c - Combined Uncertainty.</i>	All known uncertainties associated with the preparation and analysis of the sample are propagated to give a measure of the uncertainty associated with the result, <i>u_c the combined uncertainty</i> . The uncertainty is absolute and in the same units as the result.
(#s), Coverage Factor	The coverage factor defines the width of the confidence interval, 1, 2 or 3 standard deviations.
CRDL (RL)	Contractual Required Detection Limit as defined in the Client's Statement Of Work or TestAmerica "default" nominal detection limit. Often referred to the reporting level (RL)
Lc	Decision Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume associated with the sample. The Type I error probability is approximately 5%. $Lc = (1.645 * \sqrt{2 * (BkgndCnt / BkgndCntMin) / SCntMin}) * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability. Lc cannot be calculated when the background count is zero.
Lot-Sample No	The number assigned by the LIMS software to track samples received on the same day for a given client. The sample number is a sequential number assigned to each sample in the Lot.
MDC MDA	Detection Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume with a Type I and II error probability of approximately 5%. $MDC = (4.65 * \sqrt{(BkgndCnt / BkgndCntMin) / SCntMin}) + 2.71 / SCntMin * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability.
Primary Detector	The instrument identifier associated with the analysis of the sample aliquot.
Ratio U-234/U-238	The U-234 result divided by the U-238 result. The U-234/U-238 ratio for natural uranium in NIST SRM 4321C is 1.038.
Rst/MDC	Ratio of the Result to the MDC. A value greater than 1 may indicate activity above background at a high level of confidence. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Rst/TotUcert	Ratio of the Result to the Total Uncertainty. If the uncertainty has a coverage factor of 2 a value greater than 1 may indicate activity above background at approximately the 95% level of confidence assuming a two-sided confidence interval. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Report DB No	Sample Identifier used by the report system. The number is based upon the first five digits of the Work Order Number.
RER	The equation Replicate Error Ratio = $(S-D) / [\sqrt{TPUs^2 + TPUD^2}]$ as defined by ICPT BOA where S is the original sample result, D is the result of the duplicate, TPUs is the total uncertainty of the original sample and TPUD is the total uncertainty of the duplicate sample.
SDG	Sample Delivery Group Number assigned by the Client or assigned by TestAmerica upon sample receipt.
Sum Rpt Alpha Spec Rst(s)	The sum of the reported alpha spec results for tests derived from the same sample excluding duplicate result where the results are in the same units.
Work Order	The LIMS software assign test specific identifier.
Yield	The recovery of the tracer added to the sample such as Pu-242 used to trace a Pu-239/40 method.

Sample Results Summary

Date: 18-Dec-14

TestAmerica Inc TARL

Ordered by Method, Batch No., Client Sample ID.

Report No. : 63936

SDG No: 49041

Batch	Client Id Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	MDL	CRDL	RER2
4329024 RL-RA-001									
AC-13D(400-98663-2)									
	M5K641AA	Ra-226	1.23E+00 +- 3.9E-01		pCi/L	68%	2.45E-01	1.00E+00	
AC-14D(400-98663-1)									
	M5K631AA	Ra-226	1.41E+00 +- 3.9E-01		pCi/L	83%	2.46E-01	1.00E+00	
AC-22D(400-98593-1) DUP									
	M5K6W1AD	Ra-226	1.47E+00 +- 4.7E-01		pCi/L	86%	3.42E-01	1.00E+00	1.3
AC-26D(400-98663-4)									
	M5K661AA	Ra-226	3.22E-02 +- 1.1E-01	U	pCi/L	100%	2.14E-01	1.00E+00	
AC-26S(400-98663-3)									
	M5K651AA	Ra-226	8.21E-02 +- 1.1E-01	U	pCi/L	94%	1.96E-01	1.00E+00	
DUP-1(400-98663-5)									
	M5K671AA	Ra-226	1.45E+00 +- 4.0E-01		pCi/L	83%	2.51E-01	1.00E+00	
4329025 RL-RA-001									
AC-13D(400-98663-2)									
	M5K641AC	Ra-228	8.24E+00 +- 1.3E+00		pCi/L	61%	8.28E-01	1.00E+00	
AC-14D(400-98663-1)									
	M5K631AC	Ra-228	1.82E+00 +- 4.7E-01		pCi/L	73%	5.74E-01	1.00E+00	
AC-22D(400-98593-1) DUP									
	M5K6W1AE	Ra-228	3.80E+00 +- 7.3E-01		pCi/L	74%	8.53E-01	1.00E+00	2.6
AC-26D(400-98663-4)									
	M5K661AC	Ra-228	1.22E-01 +- 2.4E-01	U	pCi/L	91%	5.38E-01	1.00E+00	
AC-26S(400-98663-3)									
	M5K651AC	Ra-228	6.34E-01 +- 3.3E-01	J	pCi/L	84%	6.16E-01	1.00E+00	
DUP-1(400-98663-5)									
	M5K671AC	Ra-228	7.04E+00 +- 1.1E+00		pCi/L	73%	6.79E-01	1.00E+00	
No. of Results: 12									

TestAmerica Inc
rptTALRchSaSum
mary2 V5.3.6.1
A2002

RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPUs)+sq(TPUD))] as defined by ICPT BOA.

J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

QC Results Summary
TestAmerica Inc TARL
 Ordered by Method, Batch No, QC Type,.

Date: 18-Dec-14

Report No. : 63936

SDG No.: 49040

Batch	Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	LCS Recovery	Bias	MDL
RL-RA-001									
4329024 BLANK QC,									
	M5LG61AA	Ra-226	1.98E-02 +- 7.8E-02	U	pCi/L	100%			1.62E-01
4329024 LCS,									
	M5LG61AC	Ra-226	8.15E+00 +- 1.8E+00		pCi/L	99%	82%	-0.2	2.32E-01
RL-RA-001									
4329025 BLANK QC,									
	M5LG71AA	Ra-228	2.86E-02 +- 2.0E-01	U	pCi/L	89%			4.84E-01
4329025 LCS,									
	M5LG71AC	Ra-228	8.23E+00 +- 1.1E+00		pCi/L	86%	85%	-0.2	5.00E-01
No. of Results: 4									

FORM I

Date: 18-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49041 Collection Date: 11/19/2014 11:50:00 AM
Lot-Sample No.: J4K240407-2 Report No.: 63936 Received Date: 11/21/2014 10:50:00 AM
Client Sample ID: AC-13D(400-98663-2) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024 RL-RA-001 1.23E+00 2.7E-01 3.9E-01 M5K641AA 2.45E-01 pCi/L 68% (5.) 12/15/14 03:38 p 0.9105 ASCKMD												
Work Order: M5K641AA Report DB ID: 9M5K6410 1.06E-01 1.00E+00 (6.3)												
Batch: 4329025 RL-RA-001 8.24E+00 8.9E-01 1.3E+00 M5K641AC 8.28E-01 pCi/L 61% (10.) 12/17/14 12:47 p 0.9105 GPC2C												
Work Order: M5K641AC Report DB ID: 9M5K6410 3.66E-01 1.00E+00 (12.7)												

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
V5.3.6.1 A2002

FORM I

Date: 18-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K240407-1
Client Sample ID: AC-14D(400-98663-1)
SDG: 49041
Report No. : 63936
COC No. :
Collection Date: 11/19/2014 9:47:00 AM
Received Date: 11/21/2014 10:50:00 AM
Matrix: WATER
 Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024 RL-RA-001												
Ra-226	1.41E+00		2.7E-01	3.9E-01	2.46E-01	pCi/L	83%	(5.7)	12/15/14 03:39 p		0.8634	ASCHAD
						1.08E-01	1.00E+00	(7.3)			L	
Batch: 4329025 RL-RA-001												
Ra-228	1.82E+00		4.1E-01	4.7E-01	5.74E-01	pCi/L	73%	(3.2)	12/17/14 12:47 p		0.8834	GPC2B
						2.47E-01	1.00E+00	(7.7)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
 rptSTLRchSample U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
 V5.3.6.1 A2002

FORM I

Date: 18-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K240407-4
Client Sample ID: AC-26D(400-98663-4)

SDG: 49041
Report No.: 63936
COC No.:
Collection Date: 11/19/2014 3:35:00 PM
Received Date: 11/21/2014 10:50:00 AM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024 RL-RA-001												
Work Order: M5K661AA						Report DB ID: 9M5K6610						
Ra-226	3.22E-02	U	1.1E-01	1.1E-01	2.14E-01	pCi/L	100%	0.15	12/15/14 03:49 p		0.85	ASCMAC
						9.44E-02	1.00E+00	0.61			L	
Batch: 4329025 RL-RA-001												
Work Order: M5K661AC						Report DB ID: 9M5K6610						
Ra-228	1.22E-01	U	2.2E-01	2.4E-01	5.38E-01	pCi/L	91%	0.23	12/17/14 12:47 p		0.85	GPC3A
						2.36E-01	1.00E+00	(1.)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
V5.3.6.1 A2002

FORM I

Date: 18-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K240407-3
Client Sample ID: AC-26S(400-98663-3)

SDG: 49041
Report No.: 63936
COC No.:
Collection Date: 11/19/2014 2:24:00 PM
Received Date: 11/21/2014 10:50:00 AM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024 RL-RA-001												
Ra-226	8.21E-02	U	1.1E-01	1.1E-01	1.96E-01	pCi/L	94%	0.42	12/15/14 03:48 p		0.8601	ASCLMD
						8.65E-02	1.00E+00	(1.5)			L	
Batch: 4329025 RL-RA-001												
Ra-228	6.34E-01	J	3.1E-01	3.3E-01	6.16E-01	pCi/L	84%	(1.)	12/17/14 12:47 p		0.8601	GPC2D
						2.71E-01	1.00E+00	(3.8)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM I

Date: 18-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc

SDG: 49041

Collection Date: 11/19/2014

Lot-Sample No.: J4K240407-5

Report No.: 63936

Received Date: 11/21/2014 10:50:00 AM

Client Sample ID: DUP-1(400-98663-5)

COC No.:

Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024 RL-RA-001												
Ra-226	1.45E+00		2.7E-01	4.0E-01	2.51E-01	pCi/L	83%	(5.8)	12/15/14 03:48 p		0.8857	ASCNMD
						1.11E-01	1.00E+00	(7.3)			L	
Batch: 4329025 RL-RA-001												
Ra-228	7.04E+00		7.3E-01	1.1E+00	6.79E-01	pCi/L	73%	(10.4)	12/17/14 12:47 p		0.8857	GPC3B
						3.01E-01	1.00E+00	(13.)			L	

No. of Results: 2

Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM II

Date: 18-Dec-14

DUPLICATE RESULTS

Lab Name: TestAmerica Inc

SDG: 49040

Collection Date: 11/18/2014 8:24:00 AM

Lot-Sample No.: J4K240405-1

Report No.: 63936

Received Date: 11/20/2014 1:00:00 PM

Client Sample ID: AC-22D(400-98593-1) DUP

COC No.:

Matrix: WATER

Parameter	Result, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024												
RL-RA-001												
Ra-226	1.47E+00		3.0E-01	4.7E-01	3.42E-01	pCi/L	86%	(4.3)	Orig Sa DB ID: 9M5K6W10 12/15/14 03:39 p		0.8838	ASC7HB
	1.11E+00		RER2 1.3			1.00E+00		(6.3)			L	
Batch: 4329025												
RL-RA-001												
Ra-228	3.80E+00		5.8E-01	7.3E-01	8.53E-01	pCi/L	74%	(4.5)	Orig Sa DB ID: 9M5K6W10 12/17/14 12:47 p		0.8838	GPC1B
	2.59E+00		RER2 2.6			1.00E+00		(10.4)			L	

No. of Results: 2 Comments:

FORM II
BLANK RESULTS

Date: 18-Dec-14

Lab Name: TestAmerica Inc
Matrix: WATER

SDG: 49040
Report No. : 63936

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Lc	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4329024												
RL-RA-001					Work Order: M5LG61AA							
Ra-226	1.98E-02	U	7.8E-02	7.8E-02	1.62E-01	pCi/L	100%	0.12	12/15/14 03:50 p	1.0014	L	ASCPMD
					7.01E-02	1.00E+00		0.51				
Batch: 4329025												
RL-RA-001					Work Order: M5LG71AA							
Ra-228	2.86E-02	U	1.6E-01	2.0E-01	4.84E-01	pCi/L	89%	0.06	12/17/14 12:47 p	1.0014	L	GPC3C
					2.14E-01	1.00E+00		0.28				

No. of Results: 2 Comments:

TestAmerica Inc MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

UptSTLRchBlank
V5.3.6.1 A2002

FORM II
LCS RESULTS

Date: 18-Dec-14

Lab Name: TestAmerica Inc SDG: 49040
Matrix: WATER Report No.: 63936

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL	Report Unit	Yield	Expected	Expected Uncert	Recovery, Bias	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4329024													
RL-RA-001	8.15E+00		5.9E-01	1.8E+00	2.32E-01	pCi/L	99%	9.93E+00	1.12E-01	82%	12/15/14 03:50 p	1.0009	ASC3RA
Ra-226							Rec Limits:	75	125	-0.2		L	
Batch: 4329025													
RL-RA-001	8.23E+00		6.7E-01	1.1E+00	5.00E-01	pCi/L	86%	9.75E+00	1.11E-01	85%	12/17/14 12:47 p	1.0009	GPC3D
Ra-228							Rec Limits:	75	125	-0.2		L	

No. of Results: 2 Comments:

Chain of Custody Record



TestAmerica

[illegible]

Sample Check-in List

Date/Time Received: 11-21-14/1050 Container GM Screen Result: (Airlock) 20 cpm Initials B
 Sample GM Screen Result (Sample Receiving) 20 cpm Initials B
 Client: STP SDG #: 40 49041 SAF #: NA B
 Lot Number: J4K240407 JF 11/24/14
 Chain of Custody # N/A

Shipping Container ID or Air Bill Number : NA B

Samples received inside shipping container/cooler/box Yes B] Continue with 1 through 4. Initial appropriate response.
 No []] Go to 5, add comment to #16.

1. Custody Seals on shipping container intact? Yes B] No [] No Custody Seal []
2. Custody Seals dated and signed? Yes B] No [] No Custody Seal []
3. Cooler temperature: B °C NA B]
4. Vermiculite/packing materials is NA [] Wet [] Dry B]

Item 5 through 16 for samples. Initial appropriate response.

5. Chain of Custody record present? Yes B] No []
6. Number of samples received (Each sample may contain multiple bottles): 5
7. Containers received: 15xLP

8. Sample holding times exceeded? NA [] Yes [] No B]
9. Samples have: B tape B hazard labels B custody seals B appropriate sample labels
10. Matrix: B A (FLT, Wipe, Solid, Soil) B I (Water) B S (Air, Niosh 7400) B T (Biological, Ni-63)
11. Samples: B are in good condition B are leaking B are broken
B have air bubbles (Only for samples requiring no head space) B Other B

- (12.) Sample pH appropriate for analysis requested Yes B] No [] NA []
 (If acidification is necessary go to pH area & document sample ID, initial pH, amount of HNO₃ added and pH after addition on table)
13. Were any anomalies identified in sample receipt? Yes [] No B]
14. Description of anomalies (include sample numbers): NA B]

15. Sample Location, Sample Collector Listed on COC? * Yes [] No B]
 *For documentation only. No corrective action needed.
16. Additional Information: N/A

[] Client/Courier denied temperature check. [] Client/Courier unpack cooler.

Sample Check-in List completed by Sample Custodian:

Signature: [Signature] Date: 11-21-14

Client Notification needed? Yes [] No [] Date: _____

By: _____

Person contacted: _____

X [] No action necessary; process as is

Project Manager [Signature]

Date 11/24/14

12/19/2014

ANALYTICAL REPORT

TestAmerica Laboratories, Inc.

TestAmerica Pensacola

3355 McLemore Drive

Pensacola, FL 32514

Tel: (850)474-1001

TestAmerica Job ID: 400-98714-1

Client Project/Site: Agrico Pensacola

Revision: 1

For:

URS Corporation

1625 Summit Lake Drive

Suite 200

Tallahassee, Florida 32317

Attn: Mr. Jeff Wagner



Authorized for release by:

1/9/2015 12:34:37 PM

Noel Savoie, Project Manager I

(850)878-3994

noel.savoie@testamericainc.com

LINKS

Review your project
results through

TotalAccess

Have a Question?



Visit us at:

www.testamericainc.com

The test results in this report meet all 2003 NELAC and 2009 TNI requirements for accredited parameters, exceptions are noted in this report. This report may not be reproduced except in full, and with written approval from the laboratory. For questions please contact the Project Manager at the e-mail address or telephone number listed on this page.

This report has been electronically signed and authorized by the signatory. Electronic signature is intended to be the legally binding equivalent of a traditionally handwritten signature.

Results relate only to the items tested and the sample(s) as received by the laboratory.

Table of Contents

Cover Page	1
Table of Contents	2
Definitions	3
Case Narrative	4
Sample Summary	5
Client Sample Results	6
QC Sample Results	7
Chronicle	11
Method Summary	12
Subcontract Data	13
Chain of Custody	28



Definitions/Glossary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98714-1

Qualifiers

General Chemistry

Qualifier	Qualifier Description
4	MS, MSD: The analyte present in the original sample is greater than 4 times the matrix spike concentration; therefore, control limits are not applicable.
F1	MS and/or MSD Recovery exceeds the control limits
F2	MS/MSD RPD exceeds control limits

Glossary

Abbreviation	These commonly used abbreviations may or may not be present in this report.
□	Listed under the "D" column to designate that the result is reported on a dry weight basis
%R	Percent Recovery
CFL	Contains Free Liquid
CNF	Contains no Free Liquid
DER	Duplicate error ratio (normalized absolute difference)
Dil Fac	Dilution Factor
DL, RA, RE, IN	Indicates a Dilution, Re-analysis, Re-extraction, or additional Initial metals/anion analysis of the sample
DLC	Decision level concentration
MDA	Minimum detectable activity
EDL	Estimated Detection Limit
MDC	Minimum detectable concentration
MDL	Method Detection Limit
ML	Minimum Level (Dioxin)
NC	Not Calculated
ND	Not detected at the reporting limit (or MDL or EDL if shown)
PQL	Practical Quantitation Limit
QC	Quality Control
RER	Relative error ratio
RL	Reporting Limit or Requested Limit (Radiochemistry)
RPD	Relative Percent Difference, a measure of the relative difference between two points
TEF	Toxicity Equivalent Factor (Dioxin)
TEQ	Toxicity Equivalent Quotient (Dioxin)

Case Narrative

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98714-1

Job ID: 400-98714-1

Laboratory: TestAmerica Pensacola

Narrative

Job Narrative 400-98714-1

Comments

Revision created to remove results from a non-site well AC-28D (400-98714-2).

Receipt

The samples were received on 11/20/2014 4:08 PM; the samples arrived in good condition, properly preserved and, where required, on ice.

HPLC/IC

Method 300.0: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-12D (400-98714-1), AC-25D (400-98714-4), and AC-9D2 (400-98714-3). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

General Chemistry

Method 353.2: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-12D (400-98714-1), AC-25D (400-98714-4), and AC-9D2 (400-98714-3). Elevated reporting limits (RLs) are provided.

Method 353.2: The matrix spike/matrix spike duplicate (MS/MSD) and precision recoveries for batch 238721 were outside control limits. Sample matrix interference and/or non-homogeneity are suspected because the associated laboratory control sample (LCS) recovery was within acceptance limits.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Subcontract Work

Methods Radium 226 by EPA Method 903.1, Radium 228 by EPA Method 904.0: These methods were subcontracted to TestAmerica Richland. Report attached.

Sample Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98714-1

Lab Sample ID	Client Sample ID	Matrix	Collected	Received
400-98714-1	AC-12D	Water	11/20/14 08:29	11/20/14 16:08
400-98714-3	AC-9D2	Water	11/20/14 13:12	11/20/14 16:08
400-98714-4	AC-25D	Water	11/20/14 15:10	11/20/14 16:08

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98714-1

Client Sample ID: AC-12D

Date Collected: 11/20/14 08:29

Date Received: 11/20/14 16:08

Lab Sample ID: 400-98714-1

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	16		1.0		mg/L			12/04/14 17:32	1
Sulfate	230		10		mg/L			12/05/14 14:06	10

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	10		0.20		mg/L			12/10/14 16:46	2
Nitrate Nitrite as N	8.6		0.50		mg/L			12/03/14 15:40	10
Nitrate as N	8.6		0.050		mg/L			12/03/14 15:40	1
Nitrite as N	<0.10		0.10		mg/L			11/20/14 18:06	1

Client Sample ID: AC-9D2

Date Collected: 11/20/14 13:12

Date Received: 11/20/14 16:08

Lab Sample ID: 400-98714-3

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	36		1.0		mg/L			12/04/14 18:18	1
Sulfate	240		20		mg/L			12/05/14 14:29	20

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	29		0.50		mg/L			12/10/14 16:39	5
Nitrate Nitrite as N	11		0.50		mg/L			12/03/14 15:41	10
Nitrate as N	11		0.050		mg/L			12/03/14 15:41	1
Nitrite as N	<0.10		0.10		mg/L			11/20/14 18:06	1

Client Sample ID: AC-25D

Date Collected: 11/20/14 15:10

Date Received: 11/20/14 16:08

Lab Sample ID: 400-98714-4

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	320		20		mg/L			12/05/14 14:52	20
Sulfate	91		20		mg/L			12/05/14 14:52	20

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	76		1.0		mg/L			12/10/14 16:42	10
Nitrate Nitrite as N	3.7		0.10		mg/L			12/03/14 15:42	2
Nitrate as N	3.7		0.050		mg/L			12/03/14 15:42	1
Nitrite as N	<0.10		0.10		mg/L			11/20/14 18:06	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98714-1

Method: 300.0 - Anions, Ion Chromatography

Lab Sample ID: MB 400-238918/4

Matrix: Water

Analysis Batch: 238918

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/04/14 12:58	1
Sulfate	<1.0		1.0		mg/L			12/04/14 12:58	1

Lab Sample ID: LCS 400-238918/5

Matrix: Water

Analysis Batch: 238918

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	9.91		mg/L		99	90 - 110
Sulfate	10.0	10.2		mg/L		102	90 - 110

Lab Sample ID: LCSD 400-238918/6

Matrix: Water

Analysis Batch: 238918

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	9.83		mg/L		98	90 - 110	1	15
Sulfate	10.0	9.99		mg/L		100	90 - 110	3	15

Lab Sample ID: MB 400-238997/4

Matrix: Water

Analysis Batch: 238997

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/05/14 12:12	1
Sulfate	<1.0		1.0		mg/L			12/05/14 12:12	1

Lab Sample ID: LCS 400-238997/5

Matrix: Water

Analysis Batch: 238997

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	9.59		mg/L		96	90 - 110
Sulfate	10.0	9.91		mg/L		99	90 - 110

Lab Sample ID: LCSD 400-238997/6

Matrix: Water

Analysis Batch: 238997

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	9.68		mg/L		97	90 - 110	1	15
Sulfate	10.0	9.95		mg/L		100	90 - 110	0	15

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98714-1

Method: 340.2 - Fluoride

Lab Sample ID: MB 400-239545/3
Matrix: Water
Analysis Batch: 239545

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			12/10/14 15:54	1

Lab Sample ID: LCS 400-239545/4
Matrix: Water
Analysis Batch: 239545

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.02		mg/L		101	90 - 110

Lab Sample ID: 400-98714-1 MS
Matrix: Water
Analysis Batch: 239545

Client Sample ID: AC-12D
Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	10		2.00	12.1	4	mg/L		87	74 - 125

Lab Sample ID: 400-98714-1 MSD
Matrix: Water
Analysis Batch: 239545

Client Sample ID: AC-12D
Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Fluoride	10		2.00	12.1	4	mg/L		87	74 - 125	0	4

Method: 353.2 - Nitrogen, Nitrate-Nitrite

Lab Sample ID: MB 400-238721/14
Matrix: Water
Analysis Batch: 238721

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			12/03/14 15:34	1

Lab Sample ID: LCS 400-238721/15
Matrix: Water
Analysis Batch: 238721

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.457		mg/L		91	90 - 110

Lab Sample ID: MRL 400-238721/12
Matrix: Water
Analysis Batch: 238721

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	0.0514		mg/L		103	50 - 150

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98714-1

Method: 353.2 - Nitrogen, Nitrate-Nitrite (Continued)

Lab Sample ID: 400-98714-C-2 MS

Matrix: Water

Analysis Batch: 238721

Client Sample ID: 400-98714-C-2 MS

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MS Result	MS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.66		0.500	1.10	F1	mg/L		89	90 - 110

Lab Sample ID: 400-98714-C-2 MSD

Matrix: Water

Analysis Batch: 238721

Client Sample ID: 400-98714-C-2 MSD

Prep Type: Total/NA

Analyte	Sample Result	Sample Qualifier	Spike Added	MSD Result	MSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Nitrate Nitrite as N	0.66		0.500	1.00	F1 F2	mg/L		69	90 - 110	9	4

Method: Nitrate by calc - Nitrogen, Nitrate

Lab Sample ID: MB 400-238724/14

Matrix: Water

Analysis Batch: 238724

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate as N	N/A		0.050		mg/L			12/03/14 15:34	1

Method: SM 4500 NO2 B - Nitrogen, Nitrite

Lab Sample ID: MB 400-237496/60

Matrix: Water

Analysis Batch: 237496

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/20/14 17:30	1

Lab Sample ID: MB 400-237496/9

Matrix: Water

Analysis Batch: 237496

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/20/14 09:38	1

Lab Sample ID: LCS 400-237496/20

Matrix: Water

Analysis Batch: 237496

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.299		mg/L		100	90 - 110

Lab Sample ID: LCS 400-237496/74

Matrix: Water

Analysis Batch: 237496

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.320		mg/L		107	90 - 110

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98714-1

Method: SM 4500 NO2 B - Nitrogen, Nitrite (Continued)

Lab Sample ID: MRL 400-237496/7

Matrix: Water

Analysis Batch: 237496

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.100	<0.10		mg/L		96	50 - 150

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98714-1

Client Sample ID: AC-12D

Date Collected: 11/20/14 08:29

Date Received: 11/20/14 16:08

Lab Sample ID: 400-98714-1

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238918	12/04/14 17:32	TAJ	TAL PEN
Total/NA	Analysis	300.0		10	238997	12/05/14 14:06	TAJ	TAL PEN
Total/NA	Analysis	340.2		2	239545	12/10/14 16:46	SLT	TAL PEN
Total/NA	Analysis	353.2		10	238721	12/03/14 15:40	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238724	12/03/14 15:40	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237496	11/20/14 18:06	LSS	TAL PEN

Client Sample ID: AC-9D2

Date Collected: 11/20/14 13:12

Date Received: 11/20/14 16:08

Lab Sample ID: 400-98714-3

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238918	12/04/14 18:18	TAJ	TAL PEN
Total/NA	Analysis	300.0		20	238997	12/05/14 14:29	TAJ	TAL PEN
Total/NA	Analysis	340.2		5	239545	12/10/14 16:39	SLT	TAL PEN
Total/NA	Analysis	353.2		10	238721	12/03/14 15:41	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238724	12/03/14 15:41	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237496	11/20/14 18:06	LSS	TAL PEN

Client Sample ID: AC-25D

Date Collected: 11/20/14 15:10

Date Received: 11/20/14 16:08

Lab Sample ID: 400-98714-4

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		20	238997	12/05/14 14:52	TAJ	TAL PEN
Total/NA	Analysis	340.2		10	239545	12/10/14 16:42	SLT	TAL PEN
Total/NA	Analysis	353.2		2	238721	12/03/14 15:42	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238724	12/03/14 15:42	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237496	11/20/14 18:06	LSS	TAL PEN

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Method Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98714-1

Method	Method Description	Protocol	Laboratory
300.0	Anions, Ion Chromatography	MCAWW	TAL PEN
340.2	Fluoride	MCAWW	TAL PEN
353.2	Nitrogen, Nitrate-Nitrite	MCAWW	TAL PEN
Nitrate by calc	Nitrogen, Nitrate	SM	TAL PEN
SM 4500 NO2 B	Nitrogen, Nitrite	SM	TAL PEN
Rad 226-Method 903.1 (Richland)	RAD-226 (RCH)	NONE	TAL RCH
Rad 228-Method 904.0 (Richland)	RAD-228 (RCH)	NONE	TAL RCH

Protocol References:

MCAWW = "Methods For Chemical Analysis Of Water And Wastes", EPA-600/4-79-020, March 1983 And Subsequent Revisions.

NONE = NONE

SM = "Standard Methods For The Examination Of Water And Wastewater",

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Analytical Data Package Prepared For
TestAmerica Pensacola

400-98714-1

Radiochemical Analysis By

TestAmerica Inc

2800 G.W. Way, Richland Wa, 99354, (509)-375-3131.

Assigned Laboratory Code: TARL

Data Package Contains _____ Pages

Report No.: 64029

Results in this report relate only to the sample(s) analyzed.

SDG No.	Order No.	Client Sample ID (List Order)	Lot-Sa No.	Work Order	Report DB ID	Batch No.
49062		AC-12D(400-98714-1)	J4K260413-1	M5L331AA	9M5L3310	4335069
		AC-12D(400-98714-1)	J4K260413-1	M5L331AC	9M5L3310	4335071
		AC-25D(400-98714-4)	J4K260413-4	M5L361AA	9M5L3610	4335069
		AC-25D(400-98714-4)	J4K260413-4	M5L361AC	9M5L3610	4335071
		AC-9D2(400-98714-3)	J4K260413-3	M5L351AA	9M5L3510	4335069
		AC-9D2(400-98714-3)	J4K260413-3	M5L351AC	9M5L3510	4335071



Certificate of Analysis

December 24, 2014

January 8, 2015

TestAmerica Pensacola
3355 McLemore Drive
Pensacola, FL 32514

Attention: Noel Savoie

Date Received at Lab	:	November 25, 2014
Project Name/Number	:	Agrico Pensacola/64000434
Sample Type	:	Four (4) Water
Job Number	:	400-98714-1
SDG Number	:	49062

CASE NARRATIVE

This data report has been amended to exclude results for sample AC-28D per client request. All amendments in the case narrative are bold, italicized and underlined.

I. Introduction

On November 25, 2014, four water samples were received at TestAmerica's Richland laboratory for radiochemical analysis. Upon receipt, the samples were assigned the TestAmerica identification number as described on the cover page of the Analytical Data Package report form. The samples were assigned to Lot Numbers J4K260413.

II. Sample Receipt

Two of the bottles have sample ID AC-28D handwritten on the bottle and AC-25D on the printed label. Except as noted, the samples were received in good condition and no anomalies were noted upon check-in.

III. Analytical Results/Methodology

The analytical results for this report are presented by laboratory sample ID. Each set of data includes sample identification information; analytical results and the appropriate associated statistical uncertainties.

The analysis requested was:

Gas Proportional Counting

Radium-228 by method RL-RA-001

Alpha Scintillation Counting

Radium-226 by method RL-RA-001

TestAmerica Pensacola
December 24, 2014
January 8, 2015

IV. Quality Control

The analytical result for each analysis performed includes a minimum of one laboratory control sample (LCS), and one reagent blank sample analysis. Any exceptions have been noted in the "Comments" section.

V. Comments

Gas Proportional Counting

Radium-228

The LCS, batch blank, sample duplicate and sample results are within acceptance limits.

Alpha Scintillation Counting

Radium 226:

The LCS, batch blank, samples and sample duplicate results are within acceptance limits.

I certify that this Certificate of Analysis is in compliance with the SOW and/or NELAC, both technically and for completeness, for other than the conditions detailed above. The Laboratory Manager or a designee, as verified by the following signature has authorized release of the data contained in this hard copy data package.

Reviewed and approved:

Robin Ebert-Mays
Project Manager

Drinking Water Method Cross References

DRINKING WATER ASTM METHOD CROSS REFERENCES		
Referenced Method	Isotope(s)	TestAmerica Richland's SOP No.
EPA 901.1	Cs-134, I-131	RL-GAM-001
EPA 900.0	Alpha & Beta	RL-GPC-001
EPA 00-02	Gross Alpha (Coprecipitation)	RL-GPC-002
EPA 903.0	Total Alpha Radium (Ra-226)	RL-RA-002
EPA 903.1	Ra-226	RL-RA-001
EPA 904.0	Ra-228	RL-RA-001
EPA 905.0	Sr-89/90	RL-GPC-003
ASTM D5174	Uranium	RL-KPA-003
EPA 906.0	Tritium	RL-LSC-005

Results in this report relate only to the sample(s) analyzed.

Uncertainty Estimation

TestAmerica Richland has adopted the internationally accepted approach to estimating uncertainties described in "NIST Technical Note 1297, 1994 Edition". The approach, "Law of Propagation of Errors", involves the identification of all variables in an analytical method which are used to derive a result. These variables are related to the analytical result (R) by some functional relationship, $R = \text{constants} * f(x,y,z,...)$. The components (x,y,z) are evaluated to determine their contribution to the overall method uncertainty. The individual component uncertainties (u_i) are then combined using a statistical model that provides the most probable overall uncertainty value. All component uncertainties are categorized as type A, evaluated by statistical methods, or type B, evaluated by other means. Uncertainties not included in the components, such as sample homogeneity, are combined with the component uncertainty as the square root of the sum-of-the-squares of the individual uncertainties. The uncertainty associated with the derived result is the combined uncertainty (u_c) multiplied by the coverage factor (1,2, or 3).

When three or more sample replicates are used to derive the analytical result, the type A uncertainty is the standard deviation of the mean value ($S/\sqrt{n}$), where S is the standard deviation of the derived results. The type B uncertainties are all other random or non-random components that are not included in the standard deviation.

The derivation of the general "Law of Propagation of Errors" equations and specific example are available on request.

Report Definitions

Action Lev	An agreed upon activity level used to trigger some action when the final result is greater than or equal to the Action Level. Often the Action Level is related to the Decision Limit.
Batch	The QC preparation batch number that relates laboratory samples to QC samples that were prepared and analyzed together.
Bias	Defined by the equation (Result/Expected)-1 as defined by ANSI N13.30.
COC No	Chain of Custody Number assigned by the Client or TestAmerica.
Count Error (#s)	Poisson counting statistics of the gross sample count and background. The uncertainty is absolute and in the same units as the result. For Liquid Scintillation Counting (LSC) the batch blank count is the background.
Total Uncert (#s) <i>u_c - Combined Uncertainty.</i>	All known uncertainties associated with the preparation and analysis of the sample are propagated to give a measure of the uncertainty associated with the result, <i>u_c the combined uncertainty</i> . The uncertainty is absolute and in the same units as the result.
(#s), Coverage Factor	The coverage factor defines the width of the confidence interval, 1, 2 or 3 standard deviations.
CRDL (RL)	Contractual Required Detection Limit as defined in the Client's Statement Of Work or TestAmerica "default" nominal detection limit. Often referred to the reporting level (RL)
Lc	Decision Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume associated with the sample. The Type I error probability is approximately 5%. $Lc = (1.645 * \sqrt{2 * (BkgndCnt / BkgndCntMin) / SCntMin}) * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability. Lc cannot be calculated when the background count is zero.
Lot-Sample No	The number assigned by the LIMS software to track samples received on the same day for a given client. The sample number is a sequential number assigned to each sample in the Lot.
MDC MDA	Detection Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume with a Type I and II error probability of approximately 5%. $MDC = (4.65 * \sqrt{(BkgndCnt / BkgndCntMin) / SCntMin}) + 2.71 / SCntMin * (ConvFct / (Eff * Yld * Abn * Vol)) * IngrFct$. For LSC methods the batch blank is used as a measure of the background variability.
Primary Detector	The instrument identifier associated with the analysis of the sample aliquot.
Ratio U-234/U-238	The U-234 result divided by the U-238 result. The U-234/U-238 ratio for natural uranium in NIST SRM 4321C is 1.038.
Rst/MDC	Ratio of the Result to the MDC. A value greater than 1 may indicate activity above background at a high level of confidence. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Rst/TotUcert	Ratio of the Result to the Total Uncertainty. If the uncertainty has a coverage factor of 2 a value greater than 1 may indicate activity above background at approximately the 95% level of confidence assuming a two-sided confidence interval. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Report DB No	Sample Identifier used by the report system. The number is based upon the first five digits of the Work Order Number.
RER	The equation Replicate Error Ratio = $(S - D) / [\sqrt{TPUs^2 + TPUD^2}]$ as defined by ICPT BOA where S is the original sample result, D is the result of the duplicate, TPUs is the total uncertainty of the original sample and TPUD is the total uncertainty of the duplicate sample.
SDG	Sample Delivery Group Number assigned by the Client or assigned by TestAmerica upon sample receipt.
Sum Rpt Alpha Spec Rst(s)	The sum of the reported alpha spec results for tests derived from the same sample excluding duplicate result where the results are in the same units.
Work Order	The LIMS software assign test specific identifier.
Yield	The recovery of the tracer added to the sample such as Pu-242 used to trace a Pu-239/40 method.

Sample Results Summary

Date: 08-Jan-15

TestAmerica Inc TARL

Ordered by Method, Batch No., Client Sample ID.

Report No. : 64029

SDG No: 49062

Batch	Client Id Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	MDL	CRDL	RER2
4335069 RL-RA-001									
	AC-12D(400-98714-1)								
	M5L331AA	Ra-226	2.23E+00 +- 5.5E-01		pCi/L	86%	3.11E-01	1.00E+00	
	AC-25D(400-98714-4)								
	M5L361AA	Ra-226	1.70E+00 +- 5.2E-01		pCi/L	96%	2.43E-01	1.00E+00	
	AC-9D2(400-98714-3)								
	M5L351AA	Ra-226	1.86E+00 +- 5.4E-01		pCi/L	100%	3.18E-01	1.00E+00	
	ACSW-1(400-98766-1) DUP								
	M5L311AD	Ra-226	3.14E-01 +- 1.5E-01	J	pCi/L	100%	1.81E-01	1.00E+00	1.7
4335071 RL-RA-001									
	AC-12D(400-98714-1)								
	M5L331AC	Ra-228	8.63E+00 +- 1.2E+00		pCi/L	78%	8.86E-01	1.00E+00	
	AC-25D(400-98714-4)								
	M5L361AC	Ra-228	5.27E+00 +- 8.8E-01		pCi/L	84%	6.14E-01	1.00E+00	
	AC-9D2(400-98714-3)								
	M5L351AC	Ra-228	7.96E+00 +- 1.1E+00		pCi/L	91%	5.30E-01	1.00E+00	
	ACSW-1(400-98766-1) DUP								
	M5L311AE	Ra-228	1.04E+00 +- 4.1E-01		pCi/L	90%	7.37E-01	1.00E+00	0.7
No. of Results: 8									

TestAmerica Inc RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPUs)+sq(TPUD))] as defined by ICPT BOA.
 rptTALRchSaSum J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
 mary2 V5.3.6.4
 A2002

QC Results Summary
TestAmerica Inc TARL
Ordered by Method, Batch No, QC Type,.

Date: 08-Jan-15

Report No. : 64029

SDG No.: 49061

Batch	Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	LCS Recovery	Bias	MDL
RL-RA-001									
4335069 BLANK QC,									
	M5MJV1AA	Ra-226	4.97E-03 +- 1.1E-01	U	pCi/L	92%			2.31E-01
4335069 LCS,									
	M5MJV1AC	Ra-226	8.28E+00 +- 1.7E+00		pCi/L	99%	84%	-0.2	1.76E-01
RL-RA-001									
4335071 BLANK QC,									
	M5MJ01AA	Ra-228	1.33E-01 +- 2.1E-01	U	pCi/L	81%			4.84E-01
4335071 LCS,									
	M5MJ01AC	Ra-228	9.23E+00 +- 1.3E+00		pCi/L	86%	93%	-0.1	5.43E-01
No. of Results: 4									

TestAmerica Inc Bias - (Result/Expected)-1 as defined by ANSI N13.30.
rptSTLRchQcSummary V5.3.6.4 U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
A2002

FORM I
SAMPLE RESULTS

Date: 08-Jan-15

Lab Name: TestAmerica Inc

SDG: 49062

Collection Date: 11/20/2014 8:29:00 AM

Lot-Sample No.: J4K260413-1

Report No. : 64029

Received Date: 11/25/2014 10:55:00 AM

Client Sample ID: AC-12D(400-98714-1)

COC No. : WATER

Matrix: WATER

400-98714-1

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001												
Work Order: M5L331AA Report DB ID: 9M5L3310												
Ra-226	2.23E+00		3.4E-01	5.5E-01	3.11E-01	pCi/L	86%	(7.2)	12/16/14 06:34 p		0.8415	ASC5HA
						1.42E-01	1.00E+00	(8.)			L	
Batch: 4335071 RL-RA-001												
Work Order: M5L331AC Report DB ID: 9M5L3310												
Ra-228	8.63E+00		7.9E-01	1.2E+00	8.86E-01	pCi/L	78%	(9.7)	12/23/14 12:20 p		0.8415	GPC1D
						4.10E-01	1.00E+00	(13.8)			L	

No. of Results: 2 Comments:

FORM I
SAMPLE RESULTS

Date: 08-Jan-15

Lab Name: TestAmerica Inc

SDG: 49062

Collection Date: 11/20/2014 3:10:00 PM

Lot-Sample No.: J4K260413-4

Report No. : 64029

Received Date: 11/25/2014 10:55:00 AM

Client Sample ID: AC-25D(400-98714-4)

COC No. : WATER

Matrix: WATER

400-98714-1

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001												
Work Order: M5L361AA Report DB ID: 9M5L3610												
Ra-226	1.70E+00		2.9E-01	5.2E-01	2.43E-01	pCi/L	96%	(7.)	12/16/14 06:36 p		0.833	ASC9RA
						1.07E-01	1.00E+00	(6.6)			L	
Batch: 4335071 RL-RA-001												
Work Order: M5L361AC Report DB ID: 9M5L3610												
Ra-228	5.27E+00		6.3E-01	8.8E-01	6.14E-01	pCi/L	84%	(8.6)	12/23/14 12:21 p		0.833	GPC2C
						2.69E-01	1.00E+00	(12.)			L	

No. of Results: 2 Comments:

FORM I
SAMPLE RESULTS

Date: 08-Jan-15

Lab Name: TestAmerica Inc

SDG: 49062

Collection Date: 11/20/2014 1:12:00 PM

Lot-Sample No.: J4K260413-3

Report No. : 64029

Received Date: 11/25/2014 10:55:00 AM

Client Sample ID: AC-9D2(400-98714-3)

COC No. : WATER

Matrix: WATER

400-98714-1

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001												
Ra-226	1.86E+00		3.1E-01	5.4E-01	M5L351AA 3.18E-01	pCi/L 1.46E-01	100% 1.00E+00	9M5L3510 (5.9) (6.9)	12/16/14 06:35 p		0.8533 L	ASC8HA
Batch: 4335071 RL-RA-001												
Ra-228	7.96E+00		7.0E-01	1.1E+00	M5L351AC 5.30E-01	pCi/L 2.32E-01	91% 1.00E+00	9M5L3510 (15.) (14.)	12/23/14 12:21 p		0.8533 L	GPC2B

No. of Results: 2 Comments:

FORM II

Date: 08-Jan-15

DUPLICATE RESULTS

Lab Name: TestAmerica Inc SDG: 49061 Collection Date: 11/21/2014 10:15:00 AM
Lot-Sample No.: J4K260412-1 Report No. : 64029 Received Date: 11/25/2014 10:55:00 AM
Client Sample ID: ACSW-1(400-98766-1) DUP COC No. : Matrix: WATER

Parameter	Result, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001 Work Order: M5L311AD Report DB ID: M5L311DR Orig Sa DB ID: 9M5L3110												
Ra-226	3.14E-01	J	1.3E-01	1.5E-01	1.81E-01	pCi/L	100%	(1.7)	12/16/14 06:34 p	0.8668	L	ASC3MA
	1.49E-01	U	RER2 1.7			1.00E+00		(4.2)				
Batch: 4335071 RL-RA-001 Work Order: M5L311AE Report DB ID: M5L311ER Orig Sa DB ID: 9M5L3110												
Ra-228	1.04E+00		3.9E-01	4.1E-01	7.37E-01	pCi/L	90%	(1.4)	12/23/14 12:20 p	0.8668	L	GPC1B
	1.25E+00		RER2 0.7			1.00E+00		(5.1)				

No. of Results: 2 Comments:

TestAmerica Inc RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPU)s+sq(TPUd))] as defined by ICPT BOA.
MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM II
BLANK RESULTS

Date: 08-Jan-15

Lab Name: TestAmerica Inc SDG: 49061 Report No. : 64029
Matrix: WATER

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Lc	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069												
Work Order: M5MJV1AA					Report DB ID: M5MJV1AB							
Ra-226	4.97E-03	U	1.1E-01	1.1E-01	2.31E-01	pCi/L	92%	0.02	12/16/14 06:46 p	1.0001	1.0001	ASCGMB
					1.02E-01	1.00E+00		0.09			L	
Batch: 4335071												
Work Order: M5MJ01AA					Report DB ID: M5MJ01AB							
Ra-228	1.33E-01	U	2.1E-01	2.1E-01	4.84E-01	pCi/L	81%	0.27	12/23/14 12:21 p	1.0001	1.0001	GPC3D
					2.12E-01	1.00E+00		(1.2)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM II
LCS RESULTS

Date: 08-Jan-15

Lab Name: TestAmerica Inc SDG: 49061
Matrix: WATER Report No.: 64029

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL	Report Unit	Yield	Expected	Expected Uncert	Recovery, Bias	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001 Work Order: M5MJV1AC Report DB ID: M5MJV1CS													
Ra-226	8.28E+00		4.9E-01	1.7E+00	1.76E-01	pCi/L	99%	9.85E+00	1.00E-01	84%	12/20/14 06:05 p	1.0006	ASCDMB
							Rec Limits:	75	125	-0.2			
Batch: 4335071 RL-RA-001 Work Order: M5MJ01AC Report DB ID: M5MJ01CS													
Ra-228	9.23E+00		7.2E-01	1.3E+00	5.43E-01	pCi/L	86%	9.95E+00	1.14E-01	93%	12/23/14 12:21 p	1.0006	GPC4A
							Rec Limits:	75	125	-0.1			

No. of Results: 2 Comments:

Phone (850) 474-1001 Fax (850) 478-2671

Chain of Custody Record



TestAmerica
THE LEADER IN ENVIRONMENTAL TESTING

THE LAGER IS SUPERCONDUCTAL TESTED

[illegible]

Date/Time Received: 11-25-14 / 1055 Container GM Screen Result: (Airlock) 20 cpm Initials BSample GM Screen Result (Sample Receiving) 20 cpm Initials BClient: STP SDG #: 49062 SAF #: _____ NA BLot Number: 34260413Chain of Custody # 400-65905.1Shipping Container ID or Air Bill Number : _____ NA B

Samples received inside shipping container/cooler/box

Yes B] Continue with 1 through 4. Initial appropriate response.
No B] Go to 5, add comment to #16.

1. Custody Seals on shipping container intact? Yes B] No [] No Custody Seal []
2. Custody Seals dated and signed? Yes B] No [] No Custody Seal []
3. Cooler temperature: _____ °C NA B
4. Vermiculite/packing materials is NA [] Wet B Dry []

Item 5 through 16 for samples. Initial appropriate response.

5. Chain of Custody record present? Yes B] No []
6. Number of samples received (Each sample may contain multiple bottles): 4
7. Containers received: 12 x 4P

8. Sample holding times exceeded? NA [] Yes [] No B]
9. Samples have: _____ tape _____ hazard labels _____ custody seals B appropriate sample labels
10. Matrix: _____ A (FLT, Wipe, Solid, Soil) B I (Water) _____ S (Air, Niosh 7400) _____ T (Biological, Ni-63)

11. Samples: B are in good condition _____ are leaking _____ are broken
_____ have air bubbles (Only for samples requiring no head space) _____ Other _____

12. Sample pH appropriate for analysis requested Yes B] No [] NA []
(If acidification is necessary go to pH area & document sample ID) initial pH, amount of HNO₃ added and pH after addition on table)

13. Were any anomalies identified in sample receipt? Yes B] No []

14. Description of anomalies (include sample numbers): NA [] 2 of the bottles have the ID AC28 D on the front of bottle (written) and AC-25D on the side (printed pink label)

15. Sample Location, Sample Collector Listed on COC? * Yes [] No B]
*For documentation only. No corrective action needed.

16. Additional Information: NA

[] Client/Courier denied temperature check.

[] Client/Courier unpack cooler.

Sample Check-in List completed by Sample Custodian:

Signature: [Signature] Date: 11-26-14

Client Notification needed? Yes [] No [] Date: _____

By: _____

Person contacted: _____

[] No action necessary; process as is

Project Manager: [Signature]Date: 12/1/14

[illegible]

TestAmerica

THE LEADER IN ENVIRONMENTAL TESTING

ANALYTICAL REPORT

TestAmerica Laboratories, Inc.

TestAmerica Pensacola

3355 McLemore Drive

Pensacola, FL 32514

Tel: (850)474-1001

TestAmerica Job ID: 400-98766-1

Client Project/Site: Agrico Pensacola-Brackish SW

For:

URS Corporation

1625 Summit Lake Drive

Suite 200

Tallahassee, Florida 32317

Attn: Mr. Jeff Wagner

Noël Savoie

Authorized for release by:

12/29/2014 2:40:35 PM

Noel Savoie, Project Manager I

(850)878-3994

noel.savoie@testamericainc.com

LINKS

Review your project
results through

TotalAccess

Have a Question?



Visit us at:

www.testamericainc.com

The test results in this report meet all 2003 NELAC and 2009 TNI requirements for accredited parameters, exceptions are noted in this report. This report may not be reproduced except in full, and with written approval from the laboratory. For questions please contact the Project Manager at the e-mail address or telephone number listed on this page.

This report has been electronically signed and authorized by the signatory. Electronic signature is intended to be the legally binding equivalent of a traditionally handwritten signature.

Results relate only to the items tested and the sample(s) as received by the laboratory.

Table of Contents

Cover Page	1
Table of Contents	2
Definitions	3
Case Narrative	4
Sample Summary	5
Client Sample Results	6
QC Sample Results	7
Chronicle	10
Method Summary	11
Subcontract Data	12
Chain of Custody	26



Definitions/Glossary

Client: URS Corporation
Project/Site: Agrico Pensacola-Brackish SW

TestAmerica Job ID: 400-98766-1

Glossary

Abbreviation	These commonly used abbreviations may or may not be present in this report.
□	Listed under the "D" column to designate that the result is reported on a dry weight basis
%R	Percent Recovery
CFL	Contains Free Liquid
CNF	Contains no Free Liquid
DER	Duplicate error ratio (normalized absolute difference)
Dil Fac	Dilution Factor
DL, RA, RE, IN	Indicates a Dilution, Re-analysis, Re-extraction, or additional Initial metals/anion analysis of the sample
DLC	Decision level concentration
MDA	Minimum detectable activity
EDL	Estimated Detection Limit
MDC	Minimum detectable concentration
MDL	Method Detection Limit
ML	Minimum Level (Dioxin)
NC	Not Calculated
ND	Not detected at the reporting limit (or MDL or EDL if shown)
PQL	Practical Quantitation Limit
QC	Quality Control
RER	Relative error ratio
RL	Reporting Limit or Requested Limit (Radiochemistry)
RPD	Relative Percent Difference, a measure of the relative difference between two points
TEF	Toxicity Equivalent Factor (Dioxin)
TEQ	Toxicity Equivalent Quotient (Dioxin)

Case Narrative

Client: URS Corporation
Project/Site: Agrico Pensacola-Brackish SW

TestAmerica Job ID: 400-98766-1

Job ID: 400-98766-1

Laboratory: TestAmerica Pensacola

Narrative

Job Narrative 400-98766-1

Comments

The Nitrate analysis was canceled for ACSW-2 due to not having the correct containers for method 353.2.

Receipt

The samples were received on 11/21/2014 11:45 AM; the samples arrived in good condition, properly preserved and, where required, on ice. The temperature of the cooler at receipt was 5.6° C.

HPLC/IC

Method 300.0: The following samples were diluted due to high conductivity: ACSW-1 (400-98766-1) and ACSW-2 (400-98766-2). Elevated reporting limits (RL) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

General Chemistry

No analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Subcontract Work

Methods Radium 226 by EPA Method 903.1, Radium 228 by EPA Method 904.0: These methods were subcontracted to TestAmerica Richland. The subcontract laboratory certifications are different from that of the facility issuing the final report.

Sample Summary

Client: URS Corporation

TestAmerica Job ID: 400-98766-1

Project/Site: Agrico Pensacola-Brackish SW

Lab Sample ID	Client Sample ID	Matrix	Collected	Received
400-98766-1	ACSW-1	Water	11/21/14 10:15	11/21/14 11:45
400-98766-2	ACSW-2	Water	11/21/14 09:10	11/21/14 11:45
400-98766-3	BT-02	Water	11/21/14 08:45	11/21/14 11:45
400-98766-4	BT-107	Water	11/21/14 08:20	11/21/14 11:45
400-98766-5	BT-127	Water	11/21/14 08:00	11/21/14 11:45

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola-Brackish SW

TestAmerica Job ID: 400-98766-1

Client Sample ID: ACSW-1

Date Collected: 11/21/14 10:15

Date Received: 11/21/14 11:45

Lab Sample ID: 400-98766-1

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	18000		500		mg/L			12/03/14 20:45	500
Sulfate	1900		100		mg/L			12/02/14 19:22	100

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	1.1		0.10		mg/L			11/24/14 12:30	1
Nitrate Nitrite as N	0.45		0.050		mg/L			11/25/14 11:54	1
Nitrate as N	0.45		0.050		mg/L			11/25/14 11:54	1
Nitrite as N	<0.10		0.10		mg/L			11/21/14 12:57	1

Client Sample ID: ACSW-2

Date Collected: 11/21/14 09:10

Date Received: 11/21/14 11:45

Lab Sample ID: 400-98766-2

Matrix: Water

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	17000		1000		mg/L			11/21/14 17:13	1000
Sulfate	1800		1000		mg/L			11/21/14 17:13	1000

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	0.82		0.10		mg/L			11/24/14 12:32	1

Client Sample ID: BT-02

Date Collected: 11/21/14 08:45

Date Received: 11/21/14 11:45

Lab Sample ID: 400-98766-3

Matrix: Water

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	1.3		0.10		mg/L			11/24/14 12:34	1

Client Sample ID: BT-107

Date Collected: 11/21/14 08:20

Date Received: 11/21/14 11:45

Lab Sample ID: 400-98766-4

Matrix: Water

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	1.3		0.10		mg/L			11/24/14 12:36	1

Client Sample ID: BT-127

Date Collected: 11/21/14 08:00

Date Received: 11/21/14 11:45

Lab Sample ID: 400-98766-5

Matrix: Water

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	1.3		0.10		mg/L			11/24/14 12:39	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola-Brackish SW

TestAmerica Job ID: 400-98766-1

Method: 300.0 - Anions, Ion Chromatography

Lab Sample ID: MB 400-237456/62

Matrix: Water

Analysis Batch: 237456

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			11/21/14 10:08	1
Sulfate	<1.0		1.0		mg/L			11/21/14 10:08	1

Lab Sample ID: LCS 400-237456/63

Matrix: Water

Analysis Batch: 237456

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	10.5		mg/L		105	90 - 110
Sulfate	10.0	9.23		mg/L		92	90 - 110

Lab Sample ID: LCSD 400-237456/64

Matrix: Water

Analysis Batch: 237456

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	10.5		mg/L		105	90 - 110	0	15
Sulfate	10.0	9.22		mg/L		92	90 - 110	0	15

Lab Sample ID: MB 400-238563/4

Matrix: Water

Analysis Batch: 238563

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Sulfate	<1.0		1.0		mg/L			12/02/14 14:25	1

Lab Sample ID: LCS 400-238563/5

Matrix: Water

Analysis Batch: 238563

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Sulfate	10.0	9.94		mg/L		99	90 - 110

Lab Sample ID: LCSD 400-238563/6

Matrix: Water

Analysis Batch: 238563

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Sulfate	10.0	9.75		mg/L		97	90 - 110	2	15

Lab Sample ID: MB 400-238692/4

Matrix: Water

Analysis Batch: 238692

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/03/14 13:30	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola-Brackish SW

TestAmerica Job ID: 400-98766-1

Method: 300.0 - Anions, Ion Chromatography (Continued)

Lab Sample ID: LCS 400-238692/5

Matrix: Water

Analysis Batch: 238692

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	9.78		mg/L		98	90 - 110

Lab Sample ID: LCSD 400-238692/6

Matrix: Water

Analysis Batch: 238692

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	9.65		mg/L		96	90 - 110	1	15

Method: 340.2 - Fluoride

Lab Sample ID: MB 400-237785/3

Matrix: Water

Analysis Batch: 237785

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			11/24/14 11:11	1

Lab Sample ID: LCS 400-237785/4

Matrix: Water

Analysis Batch: 237785

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.30		mg/L		108	90 - 110

Method: 353.2 - Nitrogen, Nitrate-Nitrite

Lab Sample ID: MB 400-237957/46

Matrix: Water

Analysis Batch: 237957

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			11/25/14 11:48	1

Lab Sample ID: LCS 400-237957/47

Matrix: Water

Analysis Batch: 237957

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.534		mg/L		107	90 - 110

Lab Sample ID: MRL 400-237957/12

Matrix: Water

Analysis Batch: 237957

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	<0.050		mg/L		92	50 - 150

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola-Brackish SW

TestAmerica Job ID: 400-98766-1

Method: Nitrate by calc - Nitrogen, Nitrate

Lab Sample ID: MB 400-238018/46

Matrix: Water

Analysis Batch: 238018

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate as N	N/A		0.050		mg/L			11/25/14 11:48	1

Method: SM 4500 NO2 B - Nitrogen, Nitrite

Lab Sample ID: MB 400-237679/6

Matrix: Water

Analysis Batch: 237679

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/21/14 08:26	1

Lab Sample ID: LCS 400-237679/7

Matrix: Water

Analysis Batch: 237679

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.317		mg/L		106	90 - 110

Lab Sample ID: MRL 400-237679/3

Matrix: Water

Analysis Batch: 237679

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.100	<0.10		mg/L		96	50 - 150

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola-Brackish SW

TestAmerica Job ID: 400-98766-1

Client Sample ID: ACSW-1

Date Collected: 11/21/14 10:15

Date Received: 11/21/14 11:45

Lab Sample ID: 400-98766-1

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		100	238563	12/02/14 19:22	TAJ	TAL PEN
Total/NA	Analysis	300.0		500	238692	12/03/14 20:45	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 12:30	SLT	TAL PEN
Total/NA	Analysis	353.2		1	237957	11/25/14 11:54	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238018	11/25/14 11:54	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	237679	11/21/14 12:57	LSS	TAL PEN

Client Sample ID: ACSW-2

Date Collected: 11/21/14 09:10

Date Received: 11/21/14 11:45

Lab Sample ID: 400-98766-2

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1000	237456	11/21/14 17:13	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	237785	11/24/14 12:32	SLT	TAL PEN

Client Sample ID: BT-02

Date Collected: 11/21/14 08:45

Date Received: 11/21/14 11:45

Lab Sample ID: 400-98766-3

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	340.2		1	237785	11/24/14 12:34	SLT	TAL PEN

Client Sample ID: BT-107

Date Collected: 11/21/14 08:20

Date Received: 11/21/14 11:45

Lab Sample ID: 400-98766-4

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	340.2		1	237785	11/24/14 12:36	SLT	TAL PEN

Client Sample ID: BT-127

Date Collected: 11/21/14 08:00

Date Received: 11/21/14 11:45

Lab Sample ID: 400-98766-5

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	340.2		1	237785	11/24/14 12:39	SLT	TAL PEN

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

TestAmerica Pensacola

Method Summary

Client: URS Corporation
Project/Site: Agrico Pensacola-Brackish SW

TestAmerica Job ID: 400-98766-1

Method	Method Description	Protocol	Laboratory
300.0	Anions, Ion Chromatography	MCAWW	TAL PEN
340.2	Fluoride	MCAWW	TAL PEN
353.2	Nitrogen, Nitrate-Nitrite	MCAWW	TAL PEN
Nitrate by calc	Nitrogen, Nitrate	SM	TAL PEN
SM 4500 NO2 B	Nitrogen, Nitrite	SM	TAL PEN
Rad 226-Method 903.1 (Richland)	RAD-226 (RCH)	NONE	TAL RCH
Rad 228-Method 904.0 (Richland)	RAD-228 (RCH)	NONE	TAL RCH

Protocol References:

MCAWW = "Methods For Chemical Analysis Of Water And Wastes", EPA-600/4-79-020, March 1983 And Subsequent Revisions.

NONE = NONE

SM = "Standard Methods For The Examination Of Water And Wastewater",

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Analytical Data Package Prepared For

TestAmerica Pensacola

Radiochemical Analysis By

TestAmerica Inc

2800 G.W. Way, Richland Wa, 99354, (509)-375-3131.

Assigned Laboratory Code: TARL

Data Package Contains _____ Pages

Report No.: 64028

Results in this report relate only to the sample(s) analyzed.

SDG No.	Order No.	Client Sample ID (List Order)	Lot-Sa No.	Work Order	Report DB ID	Batch No.
49061		ACSW-1(400-98766-1)	J4K260412-1	M5L311AA	9M5L3110	4335069
		ACSW-1(400-98766-1)	J4K260412-1	M5L311AC	9M5L3110	4335071
		ACSW-2(400-98766-2)	J4K260412-2	M5L321AA	9M5L3210	4335069
		ACSW-2(400-98766-2)	J4K260412-2	M5L321AC	9M5L3210	4335071

Certificate of Analysis

December 24, 2014

TestAmerica Pensacola
3355 McLemore Drive
Pensacola, FL 32514

Attention: Noel Savoie

Date Received at Lab	:	November 25, 2014
Project Name/Number	:	Agrico Pensacola/64000434
Sample Type	:	Two (2) Water
Job Number	:	400-98766-1
SDG Number	:	49061

CASE NARRATIVE

I. Introduction

On November 25, 2014, two water samples were received at TestAmerica's Richland laboratory for radiochemical analysis. Upon receipt, the samples were assigned the TestAmerica identification number as described on the cover page of the Analytical Data Package report form. The samples were assigned to Lot Numbers J4K260412.

II. Sample Receipt

The samples were received in good condition and no anomalies were noted upon check-in.

III. Analytical Results/Methodology

The analytical results for this report are presented by laboratory sample ID. Each set of data includes sample identification information; analytical results and the appropriate associated statistical uncertainties.

The analysis requested was:

Gas Proportional Counting

Radium-228 by method RL-RA-001

Alpha Scintillation Counting

Radium-226 by method RL-RA-001

IV. Quality Control

The analytical result for each analysis performed includes a minimum of one laboratory control sample (LCS), and one reagent blank sample analysis. Any exceptions have been noted in the Comments” section.

V. Comments

Gas Proportional Counting

Radium-228

The LCS, batch blank, sample duplicate and sample results are within acceptance limits.

Alpha Scintillation Counting

Radium 226:

The LCS, batch blank, samples and sample duplicate results are within acceptance limits.

I certify that this Certificate of Analysis is in compliance with the SOW and/or NELAC, both technically and for completeness, for other than the conditions detailed above. The Laboratory Manager or a designee, as verified by the following signature has authorized release of the data contained in this hard copy data package.

Reviewed and approved:

Robin Ebert-Mays
Project Manager

Drinking Water Method Cross References

DRINKING WATER ASTM METHOD CROSS REFERENCES		
Referenced Method	Isotope(s)	TestAmerica Richland's SOP No.
EPA 901.1	Cs-134, I-131	RL-GAM-001
EPA 900.0	Alpha & Beta	RL-GPC-001
EPA 00-02	Gross Alpha (Coprecipitation)	RL-GPC-002
EPA 903.0	Total Alpha Radium (Ra-226)	RL-RA-002
EPA 903.1	Ra-226	RL-RA-001
EPA 904.0	Ra-228	RL-RA-001
EPA 905.0	Sr-89/90	RL-GPC-003
ASTM D5174	Uranium	RL-KPA-003
EPA 906.0	Tritium	RL-LSC-005

Results in this report relate only to the sample(s) analyzed.

Uncertainty Estimation

TestAmerica Richland has adopted the internationally accepted approach to estimating uncertainties described in "NIST Technical Note 1297, 1994 Edition". The approach, "Law of Propagation of Errors", involves the identification of all variables in an analytical method which are used to derive a result. These variables are related to the analytical result (R) by some functional relationship, $R = \text{constants} * f(x,y,z,...)$. The components (x,y,z) are evaluated to determine their contribution to the overall method uncertainty. The individual component uncertainties (u_i) are then combined using a statistical model that provides the most probable overall uncertainty value. All component uncertainties are categorized as type A, evaluated by statistical methods, or type B, evaluated by other means. Uncertainties not included in the components, such as sample homogeneity, are combined with the component uncertainty as the square root of the sum-of-the-squares of the individual uncertainties. The uncertainty associated with the derived result is the combined uncertainty (u_c) multiplied by the coverage factor (1,2, or 3).

When three or more sample replicates are used to derive the analytical result, the type A uncertainty is the standard deviation of the mean value ($S/\sqrt{n}$), where S is the standard deviation of the derived results. The type B uncertainties are all other random or non-random components that are not included in the standard deviation.

The derivation of the general "Law of Propagation of Errors" equations and specific example are available on request.

Report Definitions

Action Lev	An agreed upon activity level used to trigger some action when the final result is greater than or equal to the Action Level. Often the Action Level is related to the Decision Limit.
Batch	The QC preparation batch number that relates laboratory samples to QC samples that were prepared and analyzed together.
Bias	Defined by the equation (Result/Expected)-1 as defined by ANSI N13.30.
COC No	Chain of Custody Number assigned by the Client or TestAmerica.
Count Error (#s)	Poisson counting statistics of the gross sample count and background. The uncertainty is absolute and in the same units as the result. For Liquid Scintillation Counting (LSC) the batch blank count is the background.
Total Uncert (#s) <i>u_c - Combined Uncertainty.</i>	All known uncertainties associated with the preparation and analysis of the sample are propagated to give a measure of the uncertainty associated with the result, <i>u_c the combined uncertainty</i> . The uncertainty is absolute and in the same units as the result.
(#s), Coverage Factor	The coverage factor defines the width of the confidence interval, 1, 2 or 3 standard deviations.
CRDL (RL)	Contractual Required Detection Limit as defined in the Client's Statement Of Work or TestAmerica "default" nominal detection limit. Often referred to the reporting level (RL)
Lc	Decision Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume associated with the sample. The Type I error probability is approximately 5%. $Lc = (1.645 * \sqrt{2 * (BkgndCnt / BkgndCntMin) / SCntMin}) * (ConvFct / (Eff * Yld * Abn * Vol) * IngrFct)$. For LSC methods the batch blank is used as a measure of the background variability. Lc cannot be calculated when the background count is zero.
Lot-Sample No	The number assigned by the LIMS software to track samples received on the same day for a given client. The sample number is a sequential number assigned to each sample in the Lot.
MDC MDA	Detection Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume with a Type I and II error probability of approximately 5%. $MDC = (4.65 * \sqrt{(BkgndCnt / BkgndCntMin) / SCntMin}) + 2.71 / SCntMin * (ConvFct / (Eff * Yld * Abn * Vol) * IngrFct)$. For LSC methods the batch blank is used as a measure of the background variability.
Primary Detector	The instrument identifier associated with the analysis of the sample aliquot.
Ratio U-234/U-238	The U-234 result divided by the U-238 result. The U-234/U-238 ratio for natural uranium in NIST SRM 4321C is 1.038.
Rst/MDC	Ratio of the Result to the MDC. A value greater than 1 may indicate activity above background at a high level of confidence. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Rst/TotUcert	Ratio of the Result to the Total Uncertainty. If the uncertainty has a coverage factor of 2 a value greater than 1 may indicate activity above background at approximately the 95% level of confidence assuming a two-sided confidence interval. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Report DB No	Sample Identifier used by the report system. The number is based upon the first five digits of the Work Order Number.
RER	The equation Replicate Error Ratio = $(S-D) / [\sqrt{TPUs^2 + TPUD^2}]$ as defined by ICPT BOA where S is the original sample result, D is the result of the duplicate, TPUs is the total uncertainty of the original sample and TPUD is the total uncertainty of the duplicate sample.
SDG	Sample Delivery Group Number assigned by the Client or assigned by TestAmerica upon sample receipt.
Sum Rpt Alpha Spec Rst(s)	The sum of the reported alpha spec results for tests derived from the same sample excluding duplicate result where the results are in the same units.
Work Order	The LIMS software assign test specific identifier.
Yield	The recovery of the tracer added to the sample such as Pu-242 used to trace a Pu-239/40 method.

Sample Results Summary

Date: 24-Dec-14

TestAmerica Inc TARL

Ordered by Method, Batch No., Client Sample ID.

Report No. : 64028

SDG No: 49061

Client Id			Result +/- Uncertainty (2s)	Qual	Units	Tracer Yield	MDL	CRDL	RER2
Batch	Work Order	Parameter							
4335069 RL-RA-001									
ACSW-1(400-98766-1)									
M5L311AA	Ra-226		1.49E-01 +- 1.3E-01	U	pCi/L	97%	2.19E-01	1.00E+00	
ACSW-1(400-98766-1) DUP									
M5L311AD	Ra-226		3.14E-01 +- 1.5E-01	J	pCi/L	100%	1.81E-01	1.00E+00	1.7
ACSW-2(400-98766-2)									
M5L321AA	Ra-226		3.09E-01 +- 1.7E-01	J	pCi/L	98%	2.49E-01	1.00E+00	
4335071 RL-RA-001									
ACSW-1(400-98766-1)									
M5L311AC	Ra-228		1.25E+00 +- 4.4E-01		pCi/L	85%	7.79E-01	1.00E+00	
ACSW-1(400-98766-1) DUP									
M5L311AE	Ra-228		1.04E+00 +- 4.1E-01		pCi/L	90%	7.37E-01	1.00E+00	0.7
ACSW-2(400-98766-2)									
M5L321AC	Ra-228		5.55E-01 +- 3.7E-01	U	pCi/L	89%	7.57E-01	1.00E+00	
No. of Results: 6									

TestAmerica Inc
rptTALRchSaSum
mary2 V5.3.6.2
A2002

RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPUs)+sq(TPUD))] as defined by ICPT BOA.

J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.

U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

QC Results Summary
TestAmerica Inc TARL
 Ordered by Method, Batch No, QC Type,.

Date: 24-Dec-14

Report No. : 64028

SDG No.: 49061

Batch	Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	LCS Recovery	Bias	MDL
RL-RA-001									
4335069 BLANK QC,									
	M5MJV1AA	Ra-226	4.97E-03 +- 1.1E-01	U	pCi/L	92%			2.31E-01
4335069 LCS,									
	M5MJV1AC	Ra-226	8.28E+00 +- 1.7E+00		pCi/L	99%	84%	-0.2	1.76E-01
RL-RA-001									
4335071 BLANK QC,									
	M5MJ01AA	Ra-228	1.33E-01 +- 2.1E-01	U	pCi/L	81%			4.84E-01
4335071 LCS,									
	M5MJ01AC	Ra-228	9.23E+00 +- 1.3E+00		pCi/L	86%	93%	-0.1	5.43E-01
No. of Results: 4									

FORM I

Date: 24-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49061 Collection Date: 11/21/2014 10:15:00 AM
Lot-Sample No.: J4K260412-1 Report No.: 64028 Received Date: 11/25/2014 10:55:00 AM
Client Sample ID: ACSW-1(400-98766-1) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001 1.49E-01 U 1.3E-01 1.3E-01 2.19E-01 pCi/L 97% 0.68 12/16/14 06:33 p 0.891 ASC1MB												
Work Order: M5L311AA Report DB ID: 9M5L3110 9.84E-02 1.00E+00 (2.3)												
Batch: 4335071 RL-RA-001 1.25E+00 4.1E-01 4.4E-01 7.79E-01 pCi/L 85% (1.6) 12/23/14 12:20 p 0.891 GPC1A												
Work Order: M5L311AC Report DB ID: 9M5L3110 3.61E-01 1.00E+00 (5.7)												
No. of Results: 2 Comments:												

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
V5.3.6.2 A2002

FORM I

Date: 24-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49061 Collection Date: 11/21/2014 9:10:00 AM
Lot-Sample No.: J4K260412-2 Report No.: 64028 Received Date: 11/25/2014 10:55:00 AM
Client Sample ID: ACSW-2(400-98766-2) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001 3.09E-01 J 1.6E-01 1.7E-01 2.49E-01 pCi/L 98% (1.2) 12/16/14 06:34 p 0.9131 ASC4UA												
Work Order: M5L321AA Report DB ID: 9M5L3210 1.12E-01 1.00E+00 (3.7)												
Batch: 4335071 RL-RA-001 5.55E-01 U 3.6E-01 3.7E-01 7.57E-01 pCi/L 89% 0.73 12/23/14 12:20 p 0.9131 GPC1C												
Work Order: M5L321AC Report DB ID: 9M5L3210 3.51E-01 1.00E+00 (3.)												
No. of Results: 2 Comments:												

TestAmerica Inc MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

FORM II

Date: 24-Dec-14

DUPLICATE RESULTS

Lab Name: TestAmerica Inc

SDG: 49061

Collection Date: 11/21/2014 10:15:00 AM

Lot-Sample No.: J4K260412-1

Report No. : 64028

Received Date: 11/25/2014 10:55:00 AM

Client Sample ID: ACSW-1(400-98766-1) DUP

COC No. :

Matrix: WATER

Parameter	Result, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001												
Work Order: M5L311AD Report DB ID: M5L311DR Orig Sa DB ID: 9M5L3110												
Ra-226	3.14E-01	J	1.3E-01	1.5E-01	1.81E-01	pCi/L	100%	(1.7)	12/16/14 06:34 p		0.8668	ASC3MA
	1.49E-01	U	RER2	1.7		1.00E+00		(4.2)			L	
Batch: 4335071 RL-RA-001												
Work Order: M5L311AE Report DB ID: M5L311ER Orig Sa DB ID: 9M5L3110												
Ra-228	1.04E+00		3.9E-01	4.1E-01	7.37E-01	pCi/L	90%	(1.4)	12/23/14 12:20 p		0.8668	GPC1B
	1.25E+00		RER2	0.7		1.00E+00		(5.1)			L	

No. of Results: 2 Comments:

TestAmerica Inc RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPU_s)+sq(TPU_d))] as defined by ICPT BOA.
MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

Date: 24-Dec-14

SDG: 49061

Report No.: 64028

No. of Results:	2	Comments:

FORM II
LCS RESULTS

Date: 24-Dec-14

Lab Name: TestAmerica Inc SDG: 49061
Matrix: WATER Report No.: 64028

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL	Report Unit	Yield	Expected	Expected Uncert	Recovery, Bias	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001 Work Order: M5MJV1AC Report DB ID: M5MJV1CS													
Ra-226	8.28E+00		4.9E-01	1.7E+00	1.76E-01	pCi/L	99%	9.85E+00	1.00E-01	84%	12/20/14 06:05 p	1.0006	ASCDMB
							Rec Limits:	75	125	-0.2			
Batch: 4335071 RL-RA-001 Work Order: M5MJ01AC Report DB ID: M5MJ01CS													
Ra-228	9.23E+00		7.2E-01	1.3E+00	5.43E-01	pCi/L	86%	9.95E+00	1.14E-01	93%	12/23/14 12:21 p	1.0006	GPC4A
							Rec Limits:	75	125	-0.1			

No. of Results: 2 Comments:

Phone (850) 474-1001 Fax (850) 478-2671

Chain of Custody Record



TestAmerica
THE LEADER IN ENVIRONMENTAL TESTING

[illegible]

Sample Check-in List

Date/Time Received: 11-25-14 1055 Container GM Screen Result: (Airlock) 20 cpm Initials BS]
 Sample GM Screen Result (Sample Receiving) 20 cpm Initials BS]
 Client: STP SDG #: 49061 SAF #: _____ NA BS]
 Lot Number: 34K260412
 Chain of Custody # 400-65936.1

Shipping Container ID or Air Bill Number : _____ NA BS]

Samples received inside shipping container/cooler/box Yes BS] Continue with 1 through 4. Initial appropriate response.
 No [] Go to 5, add comment to #16.

1. Custody Seals on shipping container intact? Yes BS] No [] No Custody Seal []
2. Custody Seals dated and signed? Yes BS] No [] No Custody Seal []
3. Cooler temperature: _____ °C NA BS]
4. Vermiculite/packing materials is NA [] Wet BS] Dry []

Item 5 through 16 for samples. Initial appropriate response.

5. Chain of Custody record present? Yes BS] No []
6. Number of samples received (Each sample may contain multiple bottles): 2
7. Containers received: 6 x 4P
8. Sample holding times exceeded? NA [] Yes [] No BS]
9. Samples have: _____ tape _____ hazard labels _____ custody seals BS appropriate sample labels
10. Matrix: _____ A (FLT, Wipe, Solid, Soil) BS I (Water) _____ S (Air, Niosh 7400) _____ T (Biological, Ni-63)
11. Samples:
BS are in good condition _____ are leaking _____ are broken
BS have air bubbles (Only for samples requiring no head space) _____ Other _____
12. Sample pH appropriate for analysis requested Yes BS] No [] NA []
 (If acidification is necessary go to pH area & document sample ID, initial pH, amount of HNO₃ added and pH after addition on table)
13. Were any anomalies identified in sample receipt? Yes [] No BS]
14. Description of anomalies (include sample numbers): NA BS] _____
15. Sample Location, Sample Collector Listed on COC? * Yes [] No BS]
 *For documentation only. No corrective action needed.
16. Additional Information: N/A

[] Client/Courier denied temperature check.

[] Client/Courier unpack cooler.

Sample Check-in List completed by Sample Custodian:

Signature: [Signature] Date: 11-26-14

Client Notification needed? Yes [] No [] Date: _____

By: _____

Person contacted: _____

☒ No action necessary; process as is

Project Manager [Signature]

Date 12/1/14

TestAmerica Pensacola

3355 McLeamore Drive
Pensacola, FL 32514
Phone (850) 474-1001 Fax (850) 478-2671

Chain of Custody Record

TestAmerica

THE LEADER IN ENVIRONMENTAL TESTING

Client Information Client Contact: Mr. Jeff Wagner Company: URS Corporation Address: 1625 Summit Lake Drive Suite 200 City: Tallahassee State: FL 32317 Phone: 850-402-6409 (Tel) Email: jeffry_wagner@urscorp.com Project Name: Agrico Pensacola - Brackish Surface Water Site:		Lab Pmt: Saviole, Noel E-Mail: noel.saviole@testamericainc.com Due Date Requested: TAT Requested (days): PO #: 308649 US WO #: 12806620.00000 Vendor #1427536 Project #: 64000434 SSOW#:		Carrier Tracking No(s): COC No: 640-48310-12423.1 Page: Page 1 of 1 Job #:	
Sample ID: 1625 Summit Lake Drive Suite 200 Sample Name: Brackish Surface Water Sample Type: Water		Analysis Requested SUBCONTRACT - Rad 226-Method 903.1 (Richland) SUBCONTRACT - Rad 226-Method 904.0 (Richland) SUBCONTRACT - Rad 226-Method 904.0 (Richland) SUBCONTRACT - Rad 226-Method 904.0 (Richland)		Preservation Codes: A - HCL B - NaOH C - Zn Acetate D - Nitric Acid E - NaHSO4 F - MeOH G - Anchlor H - Ascorbic Acid I - Ice J - DI Water K - EDTA L - EDA Other:	
Sample Identification ACSW-1 ACSW-2 BT-02 BT-107 BT-127		Sample Date 11/21/14 11/21/14 11/21/14 11/21/14 11/21/14		Sample Time 1015 0910 0845 0820 0800	
Matrix (W=water, S=solid, O=waste/soil, BT=Trace, AS=Air)		Sample Type (C=comp, G=grab)		Matrix (W=water, S=solid, O=waste/soil, BT=Trace, AS=Air)	
Total Number of Containers		Total Number of Containers		Special Instructions/Note:	
Sample Disposal (A fee may be assessed if samples are retained longer than 1 month) ☐ Return To Client ☐ Disposal By Lab ☐ Archive For _____ Months		Special Instructions/QC Requirements:		Method of Shipment:	
Empty Kit Relinquished by:		Date:		Date:	
Relinquished by:		Date:		Date:	
Relinquished by:		Date:		Date:	
Relinquished by:		Date:		Date:	
Custody Seals Intact: Δ Yes Δ No		Custody Seal No.:		Cooler Temperature(s) °C and Other Remarks:	

TestAmerica

THE LEADER IN ENVIRONMENTAL TESTING

ANALYTICAL REPORT

TestAmerica Laboratories, Inc.

TestAmerica Pensacola

3355 McLemore Drive

Pensacola, FL 32514

Tel: (850)474-1001

TestAmerica Job ID: 400-98898-1

Client Project/Site: Agrico Pensacola

For:

URS Corporation

1625 Summit Lake Drive

Suite 200

Tallahassee, Florida 32317

Attn: Mr. Jeff Wagner



Authorized for release by:

12/29/2014 2:44:04 PM

Noel Savoie, Project Manager I

(850)878-3994

noel.savoie@testamericainc.com

LINKS

Review your project
results through

TotalAccess

Have a Question?



Visit us at:

www.testamericainc.com

The test results in this report meet all 2003 NELAC and 2009 TNI requirements for accredited parameters, exceptions are noted in this report. This report may not be reproduced except in full, and with written approval from the laboratory. For questions please contact the Project Manager at the e-mail address or telephone number listed on this page.

This report has been electronically signed and authorized by the signatory. Electronic signature is intended to be the legally binding equivalent of a traditionally handwritten signature.

Results relate only to the items tested and the sample(s) as received by the laboratory.

Table of Contents

Cover Page	1
Table of Contents	2
Definitions	3
Case Narrative	4
Sample Summary	5
Client Sample Results	6
QC Sample Results	8
Chronicle	11
Method Summary	13
Subcontract Data	14
Chain of Custody	30



Definitions/Glossary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98898-1

Glossary

Abbreviation	These commonly used abbreviations may or may not be present in this report.
□	Listed under the "D" column to designate that the result is reported on a dry weight basis
%R	Percent Recovery
CFL	Contains Free Liquid
CNF	Contains no Free Liquid
DER	Duplicate error ratio (normalized absolute difference)
Dil Fac	Dilution Factor
DL, RA, RE, IN	Indicates a Dilution, Re-analysis, Re-extraction, or additional Initial metals/anion analysis of the sample
DLC	Decision level concentration
MDA	Minimum detectable activity
EDL	Estimated Detection Limit
MDC	Minimum detectable concentration
MDL	Method Detection Limit
ML	Minimum Level (Dioxin)
NC	Not Calculated
ND	Not detected at the reporting limit (or MDL or EDL if shown)
PQL	Practical Quantitation Limit
QC	Quality Control
RER	Relative error ratio
RL	Reporting Limit or Requested Limit (Radiochemistry)
RPD	Relative Percent Difference, a measure of the relative difference between two points
TEF	Toxicity Equivalent Factor (Dioxin)
TEQ	Toxicity Equivalent Quotient (Dioxin)

Case Narrative

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98898-1

Job ID: 400-98898-1

Laboratory: TestAmerica Pensacola

Narrative

Job Narrative 400-98898-1

Comments

No additional comments.

Receipt

The samples were received on 11/25/2014 11:20 AM; the samples arrived in good condition, properly preserved and, where required, on ice. The temperature of the cooler at receipt was 5.4° C.

HPLC/IC

Method 300.0: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-24D (400-98898-3) and AC-35D (400-98898-1). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

General Chemistry

Method 353.2: The following samples were diluted to bring the concentration of target analytes within the calibration range: AC-24D (400-98898-3), AC-24S (400-98898-2), AC-30D (400-98898-4), and AC-35D (400-98898-1). Elevated reporting limits (RLs) are provided.

No additional analytical or quality issues were noted, other than those described above or in the Definitions/Glossary page.

Subcontract Work

Methods Radium 226 by EPA Method 903.1, Radium 228 by EPA Method 904.0: These methods were subcontracted to TestAmerica Richland. The subcontract laboratory certifications are different from that of the facility issuing the final report.

Sample Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98898-1

Lab Sample ID	Client Sample ID	Matrix	Collected	Received
400-98898-1	AC-35D	Water	11/24/14 11:45	11/25/14 11:20
400-98898-2	AC-24S	Water	11/24/14 13:59	11/25/14 11:20
400-98898-3	AC-24D	Water	11/24/14 15:40	11/25/14 11:20
400-98898-4	AC-30D	Water	11/25/14 10:10	11/25/14 11:20

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98898-1

Client Sample ID: AC-35D

Lab Sample ID: 400-98898-1

Date Collected: 11/24/14 11:45

Matrix: Water

Date Received: 11/25/14 11:20

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	300		20		mg/L			12/05/14 15:15	20
Sulfate	190		20		mg/L			12/05/14 15:15	20

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	110		2.0		mg/L			12/11/14 11:33	20
Nitrate Nitrite as N	9.6		0.50		mg/L			12/01/14 18:21	10
Nitrate as N	9.6		0.050		mg/L			12/01/14 18:21	1
Nitrite as N	<0.10		0.10		mg/L			11/25/14 12:55	1

Client Sample ID: AC-24S

Lab Sample ID: 400-98898-2

Date Collected: 11/24/14 13:59

Matrix: Water

Date Received: 11/25/14 11:20

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	7.6		1.0		mg/L			12/04/14 19:27	1
Sulfate	12		1.0		mg/L			12/04/14 19:27	1

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			12/11/14 11:03	1
Nitrate Nitrite as N	3.6		0.25		mg/L			12/01/14 18:22	5
Nitrate as N	3.6		0.050		mg/L			12/01/14 18:22	1
Nitrite as N	<0.10		0.10		mg/L			11/25/14 13:15	1

Client Sample ID: AC-24D

Lab Sample ID: 400-98898-3

Date Collected: 11/24/14 15:40

Matrix: Water

Date Received: 11/25/14 11:20

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	130		10		mg/L			12/05/14 15:38	10
Sulfate	75		10		mg/L			12/05/14 15:38	10

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	51		1.0		mg/L			12/11/14 11:42	10
Nitrate Nitrite as N	4.2		0.25		mg/L			12/01/14 18:23	5
Nitrate as N	4.2		0.050		mg/L			12/01/14 18:23	1
Nitrite as N	<0.10		0.10		mg/L			11/25/14 13:15	1

Client Sample ID: AC-30D

Lab Sample ID: 400-98898-4

Date Collected: 11/25/14 10:10

Matrix: Water

Date Received: 11/25/14 11:20

Method: 300.0 - Anions, Ion Chromatography

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	13		1.0		mg/L			12/04/14 20:12	1
Sulfate	40		1.0		mg/L			12/04/14 20:12	1

TestAmerica Pensacola

Client Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98898-1

Client Sample ID: AC-30D

Lab Sample ID: 400-98898-4

Date Collected: 11/25/14 10:10

Matrix: Water

Date Received: 11/25/14 11:20

General Chemistry

Analyte	Result	Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	5.0		0.10		mg/L			12/11/14 11:10	1
Nitrate Nitrite as N	3.8		0.25		mg/L			12/01/14 18:24	5
Nitrate as N	3.8		0.050		mg/L			12/01/14 18:24	1
Nitrite as N	<0.10		0.10		mg/L			11/25/14 13:15	1

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98898-1

Method: 300.0 - Anions, Ion Chromatography

Lab Sample ID: MB 400-238918/4

Matrix: Water

Analysis Batch: 238918

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/04/14 12:58	1
Sulfate	<1.0		1.0		mg/L			12/04/14 12:58	1

Lab Sample ID: LCS 400-238918/5

Matrix: Water

Analysis Batch: 238918

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	9.91		mg/L		99	90 - 110
Sulfate	10.0	10.2		mg/L		102	90 - 110

Lab Sample ID: LCSD 400-238918/6

Matrix: Water

Analysis Batch: 238918

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	9.83		mg/L		98	90 - 110	1	15
Sulfate	10.0	9.99		mg/L		100	90 - 110	3	15

Lab Sample ID: MB 400-238997/4

Matrix: Water

Analysis Batch: 238997

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Chloride	<1.0		1.0		mg/L			12/05/14 12:12	1
Sulfate	<1.0		1.0		mg/L			12/05/14 12:12	1

Lab Sample ID: LCS 400-238997/5

Matrix: Water

Analysis Batch: 238997

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Chloride	10.0	9.59		mg/L		96	90 - 110
Sulfate	10.0	9.91		mg/L		99	90 - 110

Lab Sample ID: LCSD 400-238997/6

Matrix: Water

Analysis Batch: 238997

Client Sample ID: Lab Control Sample Dup

Prep Type: Total/NA

Analyte	Spike Added	LCSD Result	LCSD Qualifier	Unit	D	%Rec	%Rec. Limits	RPD	RPD Limit
Chloride	10.0	9.68		mg/L		97	90 - 110	1	15
Sulfate	10.0	9.95		mg/L		100	90 - 110	0	15

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98898-1

Method: 340.2 - Fluoride

Lab Sample ID: MB 400-239629/3
Matrix: Water
Analysis Batch: 239629

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Fluoride	<0.10		0.10		mg/L			12/11/14 10:41	1

Lab Sample ID: LCS 400-239629/4
Matrix: Water
Analysis Batch: 239629

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Fluoride	4.00	4.02		mg/L		101	90 - 110

Method: 353.2 - Nitrogen, Nitrate-Nitrite

Lab Sample ID: MB 400-238443/46
Matrix: Water
Analysis Batch: 238443

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate Nitrite as N	<0.050		0.050		mg/L			12/01/14 17:49	1

Lab Sample ID: LCS 400-238443/47
Matrix: Water
Analysis Batch: 238443

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.500	0.503		mg/L		101	90 - 110

Lab Sample ID: MRL 400-238443/12
Matrix: Water
Analysis Batch: 238443

Client Sample ID: Lab Control Sample
Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrate Nitrite as N	0.0500	<0.050		mg/L		98	50 - 150

Method: Nitrate by calc - Nitrogen, Nitrate

Lab Sample ID: MB 400-238494/14
Matrix: Water
Analysis Batch: 238494

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate as N	N/A		0.050		mg/L			12/01/14 17:07	1

Lab Sample ID: MB 400-238494/46
Matrix: Water
Analysis Batch: 238494

Client Sample ID: Method Blank
Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrate as N	N/A		0.050		mg/L			12/01/14 17:49	1

TestAmerica Pensacola

QC Sample Results

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98898-1

Method: SM 4500 NO2 B - Nitrogen, Nitrite

Lab Sample ID: MB 400-238027/5

Matrix: Water

Analysis Batch: 238027

Client Sample ID: Method Blank

Prep Type: Total/NA

Analyte	MB Result	MB Qualifier	PQL	MDL	Unit	D	Prepared	Analyzed	Dil Fac
Nitrite as N	<0.10		0.10		mg/L			11/25/14 12:06	1

Lab Sample ID: LCS 400-238027/16

Matrix: Water

Analysis Batch: 238027

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	LCS Result	LCS Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.300	0.303		mg/L		101	90 - 110

Lab Sample ID: MRL 400-238027/3

Matrix: Water

Analysis Batch: 238027

Client Sample ID: Lab Control Sample

Prep Type: Total/NA

Analyte	Spike Added	MRL Result	MRL Qualifier	Unit	D	%Rec	%Rec. Limits
Nitrite as N	0.100	<0.10		mg/L		95	50 - 150

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98898-1

Client Sample ID: AC-35D

Date Collected: 11/24/14 11:45

Date Received: 11/25/14 11:20

Lab Sample ID: 400-98898-1

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		20	238997	12/05/14 15:15	TAJ	TAL PEN
Total/NA	Analysis	340.2		20	239629	12/11/14 11:33	SLT	TAL PEN
Total/NA	Analysis	353.2		10	238443	12/01/14 18:21	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238494	12/01/14 18:21	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	238027	11/25/14 12:55	LSS	TAL PEN

Client Sample ID: AC-24S

Date Collected: 11/24/14 13:59

Date Received: 11/25/14 11:20

Lab Sample ID: 400-98898-2

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238918	12/04/14 19:27	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	239629	12/11/14 11:03	SLT	TAL PEN
Total/NA	Analysis	353.2		5	238443	12/01/14 18:22	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238494	12/01/14 18:22	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	238027	11/25/14 13:15	LSS	TAL PEN

Client Sample ID: AC-24D

Date Collected: 11/24/14 15:40

Date Received: 11/25/14 11:20

Lab Sample ID: 400-98898-3

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		10	238997	12/05/14 15:38	TAJ	TAL PEN
Total/NA	Analysis	340.2		10	239629	12/11/14 11:42	SLT	TAL PEN
Total/NA	Analysis	353.2		5	238443	12/01/14 18:23	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238494	12/01/14 18:23	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	238027	11/25/14 13:15	LSS	TAL PEN

Client Sample ID: AC-30D

Date Collected: 11/25/14 10:10

Date Received: 11/25/14 11:20

Lab Sample ID: 400-98898-4

Matrix: Water

Prep Type	Batch Type	Batch Method	Run	Dilution Factor	Batch Number	Prepared or Analyzed	Analyst	Lab
Total/NA	Analysis	300.0		1	238918	12/04/14 20:12	TAJ	TAL PEN
Total/NA	Analysis	340.2		1	239629	12/11/14 11:10	SLT	TAL PEN
Total/NA	Analysis	353.2		5	238443	12/01/14 18:24	JAT	TAL PEN
Total/NA	Analysis	Nitrate by calc		1	238494	12/01/14 18:24	JAT	TAL PEN
Total/NA	Analysis	SM 4500 NO2 B		1	238027	11/25/14 13:15	LSS	TAL PEN

TestAmerica Pensacola

Lab Chronicle

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98898-1

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001
TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131



Method Summary

Client: URS Corporation
Project/Site: Agrico Pensacola

TestAmerica Job ID: 400-98898-1

Method	Method Description	Protocol	Laboratory
300.0	Anions, Ion Chromatography	MCAWW	TAL PEN
340.2	Fluoride	MCAWW	TAL PEN
353.2	Nitrogen, Nitrate-Nitrite	MCAWW	TAL PEN
Nitrate by calc	Nitrogen, Nitrate	SM	TAL PEN
SM 4500 NO2 B	Nitrogen, Nitrite	SM	TAL PEN
Rad 226-Method 903.1 (Richland)	RAD-226 (RCH)	NONE	TAL RCH
Rad 228-Method 904.0 (Richland)	RAD-228 (RCH)	NONE	TAL RCH

Protocol References:

MCAWW = "Methods For Chemical Analysis Of Water And Wastes", EPA-600/4-79-020, March 1983 And Subsequent Revisions.

NONE = NONE

SM = "Standard Methods For The Examination Of Water And Wastewater",

Laboratory References:

TAL PEN = TestAmerica Pensacola, 3355 McLemore Drive, Pensacola, FL 32514, TEL (850)474-1001

TAL RCH = TestAmerica Richland, 2800 George Washington Way, Richland, WA 99352, TEL (509)375-3131

Analytical Data Package Prepared For

TestAmerica Pensacola

Radiochemical Analysis By

TestAmerica Inc

2800 G.W. Way, Richland Wa, 99354, (509)-375-3131.

Assigned Laboratory Code: TARL

Data Package Contains _____ Pages

Report No.: 64030

Results in this report relate only to the sample(s) analyzed.

SDG No.	Order No.	Client Sample ID (List Order)	Lot-Sa No.	Work Order	Report DB ID	Batch No.
49063		AC-24D(400-98898-3)	J4K260415-3	M5L4Q1AA	9M5L4Q10	4335069
		AC-24D(400-98898-3)	J4K260415-3	M5L4Q1AC	9M5L4Q10	4335071
		AC-24S(400-98898-2)	J4K260415-2	M5L4P1AA	9M5L4P10	4335069
		AC-24S(400-98898-2)	J4K260415-2	M5L4P1AC	9M5L4P10	4335071
		AC-30D(400-98898-4)	J4K260415-4	M5L4R1AA	9M5L4R10	4335069
		AC-30D(400-98898-4)	J4K260415-4	M5L4R1AC	9M5L4R10	4335071
		AC-35D(400-98898-1)	J4K260415-1	M5L4N1AA	9M5L4N10	4335069
		AC-35D(400-98898-1)	J4K260415-1	M5L4N1AC	9M5L4N10	4335071

Certificate of Analysis

December 24, 2014

TestAmerica Pensacola
3355 McLemore Drive
Pensacola, FL 32514

Attention: Noel Savoie

Date Received at Lab	:	November 25, 2014
Project Name/Number	:	Agrico Pensacola/64000434
Sample Type	:	Four (4) Water
Job Number	:	400-98898-1
SDG Number	:	49063

CASE NARRATIVE

I. Introduction

On November 26, 2014, four water samples were received at TestAmerica's Richland laboratory for radiochemical analysis. Upon receipt, the samples were assigned the TestAmerica identification number as described on the cover page of the Analytical Data Package report form. The samples were assigned to Lot Numbers J4K260415.

II. Sample Receipt

The samples were received in good condition and no anomalies were noted upon check-in.

III. Analytical Results/Methodology

The analytical results for this report are presented by laboratory sample ID. Each set of data includes sample identification information; analytical results and the appropriate associated statistical uncertainties.

The analysis requested was:

Gas Proportional Counting

Radium-228 by method RL-RA-001

Alpha Scintillation Counting

Radium-226 by method RL-RA-001

IV. Quality Control

The analytical result for each analysis performed includes a minimum of one laboratory control sample (LCS), and one reagent blank sample analysis. Any exceptions have been noted in the "Comments" section.

V. Comments

Gas Proportional Counting

Radium-228

The LCS, batch blank, sample duplicate and sample results are within acceptance limits.

Alpha Scintillation Counting

Radium 226:

The LCS, batch blank, samples and sample duplicate results are within acceptance limits.

I certify that this Certificate of Analysis is in compliance with the SOW and/or NELAC, both technically and for completeness, for other than the conditions detailed above. The Laboratory Manager or a designee, as verified by the following signature has authorized release of the data contained in this hard copy data package.

Reviewed and approved:

Robin Ebert-Mays
Project Manager

Drinking Water Method Cross References

DRINKING WATER ASTM METHOD CROSS REFERENCES		
Referenced Method	Isotope(s)	TestAmerica Richland's SOP No.
EPA 901.1	Cs-134, I-131	RL-GAM-001
EPA 900.0	Alpha & Beta	RL-GPC-001
EPA 00-02	Gross Alpha (Coprecipitation)	RL-GPC-002
EPA 903.0	Total Alpha Radium (Ra-226)	RL-RA-002
EPA 903.1	Ra-226	RL-RA-001
EPA 904.0	Ra-228	RL-RA-001
EPA 905.0	Sr-89/90	RL-GPC-003
ASTM D5174	Uranium	RL-KPA-003
EPA 906.0	Tritium	RL-LSC-005

Results in this report relate only to the sample(s) analyzed.

Uncertainty Estimation

TestAmerica Richland has adopted the internationally accepted approach to estimating uncertainties described in "NIST Technical Note 1297, 1994 Edition". The approach, "Law of Propagation of Errors", involves the identification of all variables in an analytical method which are used to derive a result. These variables are related to the analytical result (R) by some functional relationship, $R = \text{constants} * f(x,y,z,...)$. The components (x,y,z) are evaluated to determine their contribution to the overall method uncertainty. The individual component uncertainties (u_i) are then combined using a statistical model that provides the most probable overall uncertainty value. All component uncertainties are categorized as type A, evaluated by statistical methods, or type B, evaluated by other means. Uncertainties not included in the components, such as sample homogeneity, are combined with the component uncertainty as the square root of the sum-of-the-squares of the individual uncertainties. The uncertainty associated with the derived result is the combined uncertainty (u_c) multiplied by the coverage factor (1,2, or 3).

When three or more sample replicates are used to derive the analytical result, the type A uncertainty is the standard deviation of the mean value ($S/\sqrt{n}$), where S is the standard deviation of the derived results. The type B uncertainties are all other random or non-random components that are not included in the standard deviation.

The derivation of the general "Law of Propagation of Errors" equations and specific example are available on request.

Report Definitions

Action Lev	An agreed upon activity level used to trigger some action when the final result is greater than or equal to the Action Level. Often the Action Level is related to the Decision Limit.
Batch	The QC preparation batch number that relates laboratory samples to QC samples that were prepared and analyzed together.
Bias	Defined by the equation (Result/Expected)-1 as defined by ANSI N13.30.
COC No	Chain of Custody Number assigned by the Client or TestAmerica.
Count Error (#s)	Poisson counting statistics of the gross sample count and background. The uncertainty is absolute and in the same units as the result. For Liquid Scintillation Counting (LSC) the batch blank count is the background.
Total Uncert (#s) <i>u_c - Combined Uncertainty.</i>	All known uncertainties associated with the preparation and analysis of the sample are propagated to give a measure of the uncertainty associated with the result, <i>u_c the combined uncertainty</i> . The uncertainty is absolute and in the same units as the result.
(#s), Coverage Factor	The coverage factor defines the width of the confidence interval, 1, 2 or 3 standard deviations.
CRDL (RL)	Contractual Required Detection Limit as defined in the Client's Statement Of Work or TestAmerica "default" nominal detection limit. Often referred to the reporting level (RL)
Lc	Decision Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume associated with the sample. The Type I error probability is approximately 5%. $Lc = (1.645 * \sqrt{2 * (BkgndCnt / BkgndCntMin) / SCntMin}) * (ConvFct / (Eff * Yld * Abn * Vol) * IngrFct)$. For LSC methods the batch blank is used as a measure of the background variability. Lc cannot be calculated when the background count is zero.
Lot-Sample No	The number assigned by the LIMS software to track samples received on the same day for a given client. The sample number is a sequential number assigned to each sample in the Lot.
MDC MDA	Detection Level based on instrument background or blank, adjusted by the Efficiency, Chemical Yield, and Volume with a Type I and II error probability of approximately 5%. $MDC = (4.65 * \sqrt{(BkgndCnt / BkgndCntMin) / SCntMin}) + 2.71 / SCntMin * (ConvFct / (Eff * Yld * Abn * Vol) * IngrFct)$. For LSC methods the batch blank is used as a measure of the background variability.
Primary Detector	The instrument identifier associated with the analysis of the sample aliquot.
Ratio U-234/U-238	The U-234 result divided by the U-238 result. The U-234/U-238 ratio for natural uranium in NIST SRM 4321C is 1.038.
Rst/MDC	Ratio of the Result to the MDC. A value greater than 1 may indicate activity above background at a high level of confidence. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Rst/TotUcert	Ratio of the Result to the Total Uncertainty. If the uncertainty has a coverage factor of 2 a value greater than 1 may indicate activity above background at approximately the 95% level of confidence assuming a two-sided confidence interval. Caution should be used when applying this factor and it should be used in concert with the qualifiers associated with the result.
Report DB No	Sample Identifier used by the report system. The number is based upon the first five digits of the Work Order Number.
RER	The equation Replicate Error Ratio = $(S-D) / [\sqrt{TPUs^2 + TPUD^2}]$ as defined by ICPT BOA where S is the original sample result, D is the result of the duplicate, TPUs is the total uncertainty of the original sample and TPUD is the total uncertainty of the duplicate sample.
SDG	Sample Delivery Group Number assigned by the Client or assigned by TestAmerica upon sample receipt.
Sum Rpt Alpha Spec Rst(s)	The sum of the reported alpha spec results for tests derived from the same sample excluding duplicate result where the results are in the same units.
Work Order	The LIMS software assign test specific identifier.
Yield	The recovery of the tracer added to the sample such as Pu-242 used to trace a Pu-239/40 method.

Sample Results Summary

Date: 24-Dec-14

TestAmerica Inc TARL

Ordered by Method, Batch No., Client Sample ID.

Report No. : 64030

SDG No: 49063

Client Id		Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	MDL	CRDL	RER2
Batch	Work Order								
4335069 RL-RA-001									
AC-24D(400-98898-3)									
M5L4Q1AA	Ra-226		2.12E+00 +- 6.4E-01		pCi/L	100%	2.54E-01	1.00E+00	
AC-24S(400-98898-2)									
M5L4P1AA	Ra-226		2.63E-01 +- 2.0E-01	U	pCi/L	83%	3.33E-01	1.00E+00	
AC-30D(400-98898-4)									
M5L4R1AA	Ra-226		1.62E+00 +- 4.7E-01		pCi/L	100%	1.62E-01	1.00E+00	
AC-35D(400-98898-1)									
M5L4N1AA	Ra-226		2.59E+00 +- 6.4E-01		pCi/L	100%	2.57E-01	1.00E+00	
ACSW-1(400-98766-1) DUP									
M5L311AD	Ra-226		3.14E-01 +- 1.5E-01	J	pCi/L	100%	1.81E-01	1.00E+00	1.7
4335071 RL-RA-001									
AC-24D(400-98898-3)									
M5L4Q1AC	Ra-228		7.14E+00 +- 1.0E+00		pCi/L	90%	5.47E-01	1.00E+00	
AC-24S(400-98898-2)									
M5L4P1AC	Ra-228		1.96E+00 +- 4.8E-01		pCi/L	75%	5.90E-01	1.00E+00	
AC-30D(400-98898-4)									
M5L4R1AC	Ra-228		6.04E+00 +- 9.2E-01		pCi/L	93%	4.98E-01	1.00E+00	
AC-35D(400-98898-1)									
M5L4N1AC	Ra-228		7.28E+00 +- 1.1E+00		pCi/L	90%	3.98E-01	1.00E+00	
ACSW-1(400-98766-1) DUP									
M5L311AE	Ra-228		1.04E+00 +- 4.1E-01		pCi/L	90%	7.37E-01	1.00E+00	0.7
No. of Results: 10									

QC Results Summary
TestAmerica Inc TARL
 Ordered by Method, Batch No, QC Type,.

Date: 24-Dec-14

Report No. : 64030

SDG No.: 49061

Batch	Work Order	Parameter	Result +- Uncertainty (2s)	Qual	Units	Tracer Yield	LCS Recovery	Bias	MDL
RL-RA-001									
4335069 BLANK QC,									
	M5MJV1AA	Ra-226	4.97E-03 +- 1.1E-01	U	pCi/L	92%			2.31E-01
4335069 LCS,									
	M5MJV1AC	Ra-226	8.28E+00 +- 1.7E+00		pCi/L	99%	84%	-0.2	1.76E-01
RL-RA-001									
4335071 BLANK QC,									
	M5MJ01AA	Ra-228	1.33E-01 +- 2.1E-01	U	pCi/L	81%			4.84E-01
4335071 LCS,									
	M5MJ01AC	Ra-228	9.23E+00 +- 1.3E+00		pCi/L	86%	93%	-0.1	5.43E-01
No. of Results: 4									

FORM I

Date: 24-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49063 Collection Date: 11/24/2014 3:40:00 PM
Lot-Sample No.: J4K260415-3 Report No.: 64030 Received Date: 11/26/2014 1:00:00 PM
Client Sample ID: AC-24D(400-98898-3) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001 2.12E+00 3.0E-01 6.4E-01 Work Order: M5L4Q1AA Report DB ID: 9M5L4Q10												
Ra-226					2.54E-01	pCi/L	100%	(8.4)	12/16/14 06:45 p		0.8809	ASCEHA
						1.15E-01	1.00E+00	(6.6)			L	
Batch: 4335071 RL-RA-001 7.14E+00 6.5E-01 1.0E+00 Work Order: M5L4Q1AC Report DB ID: 9M5L4Q10												
Ra-228					5.47E-01	pCi/L	90%	(13.1)	12/23/14 12:21 p		0.8809	GPC3B
						2.42E-01	1.00E+00	(13.8)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
V5.3.6.2 A2002

FORM I

Date: 24-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49063 Collection Date: 11/24/2014 1:59:00 PM
Lot-Sample No.: J4K260415-2 Report No.: 64030 Received Date: 11/26/2014 1:00:00 PM
Client Sample ID: AC-24S(400-98898-2) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001 2.63E-01 U 1.9E-01 2.0E-01 Work Order: M5L4P1AA Report DB ID: 9M5L4P10												
Ra-226					3.33E-01	pCi/L	83%	0.79	12/16/14 06:44 p		0.9063	ASCDMC
						1.53E-01	1.00E+00	(2.6)			L	
Batch: 4335071 RL-RA-001 1.96E+00 4.2E-01 4.8E-01 Work Order: M5L4P1AC Report DB ID: 9M5L4P10												
Ra-228					5.90E-01	pCi/L	75%	(3.3)	12/23/14 12:21 p		0.9063	GPC3A
						2.57E-01	1.00E+00	(8.1)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
V5.3.6.2 A2002

FORM I

Date: 24-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc SDG: 49063 Collection Date: 11/25/2014 10:10:00 AM
Lot-Sample No.: J4K260415-4 Report No.: 64030 Received Date: 11/26/2014 1:00:00 PM
Client Sample ID: AC-30D(400-98898-4) COC No.: Matrix: WATER
Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001 1.62E+00 2.4E-01 4.7E-01 Work Order: M5L4R1AA Report DB ID: 9M5L4R10												
Ra-226					1.62E-01	pCi/L	100%	(10.)	12/16/14 06:45 p		0.8934	ASCFRM
						7.00E-02	1.00E+00	(6.8)			L	
Batch: 4335071 RL-RA-001 6.04E+00 5.9E-01 9.2E-01 Work Order: M5L4R1AC Report DB ID: 9M5L4R10												
Ra-228					4.98E-01	pCi/L	93%	(12.1)	12/23/14 12:21 p		0.8934	GPC3C
						2.19E-01	1.00E+00	(13.2)			L	

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc\Mda\Mdl, Total Uncert, RDL or not identified by gamma scan software.
V5.3.6.2 A2002

FORM I

Date: 24-Dec-14

SAMPLE RESULTS

Lab Name: TestAmerica Inc
Lot-Sample No.: J4K260415-1
Client Sample ID: AC-35D(400-98898-1)

SDG: 49063
Report No.: 64030
COC No.:

Collection Date: 11/24/2014 11:45:00 AM
Received Date: 11/26/2014 1:00:00 PM
Matrix: WATER

Ordered by Client Sample ID, Batch No.

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, Lc	Yield CRDL(RL)	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001												
Ra-226	2.59E+00		3.6E-01	6.4E-01	M5L4N1IAA 2.57E-01	pCi/L 1.14E-01	100% 1.00E+00	9M5L4N10 (10.1) (8.1)	12/16/14 06:36 p		0.9235 L	ASCASB
Batch: 4335071 RL-RA-001												
Ra-228	7.28E+00		6.5E-01	1.1E+00	M5L4N1IAC 3.98E-01	pCi/L 1.67E-01	90% 1.00E+00	9M5L4N10 (18.3) (13.7)	12/23/14 12:21 p		0.9235 L	GPC2D

No. of Results: 2 Comments:

TestAmerica Inc MDC\MDA\Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.
V5.3.6.2 A2002

FORM II

Date: 24-Dec-14

DUPLICATE RESULTS

Lab Name: TestAmerica Inc SDG: 49061 Collection Date: 11/21/2014 10:15:00 AM
Lot-Sample No.: J4K260412-1 Report No.: 64030 Received Date: 11/25/2014 10:55:00 AM
Client Sample ID: ACSW-1(400-98766-1) DUP COC No.: Matrix: WATER

Parameter	Result, Orig Rst	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL, Action Lev	Rpt Unit, CRDL	Yield	Rst/MDL, Rst/TotUcert	Analysis, Prep Date	Total Sa Size	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001 Work Order: M5L311AD Report DB ID: M5L311DR Orig Sa DB ID: 9M5L3110												
Ra-226	3.14E-01	J	1.3E-01	1.5E-01	1.81E-01	pCi/L	100%	(1.7)	12/16/14 06:34 p	0.8668	L	ASC3MA
	1.49E-01	U	RER2 1.7			1.00E+00		(4.2)				
Batch: 4335071 RL-RA-001 Work Order: M5L311AE Report DB ID: M5L311ER Orig Sa DB ID: 9M5L3110												
Ra-228	1.04E+00		3.9E-01	4.1E-01	7.37E-01	pCi/L	90%	(1.4)	12/23/14 12:20 p	0.8668	L	GPC1B
	1.25E+00		RER2 0.7			1.00E+00		(5.1)				

No. of Results: 2 Comments:

TestAmerica Inc RER2 - Replicate Error Ratio = (S-D)/[sqrt(sq(TPU_s)+sq(TPU_d))] as defined by ICPT BOA.
MDC|MDA,Lc - Detection, Decision Level based on instrument background or blank, adjusted by the sample Efficiency, Yield, and Volume.
J Qual - No U or < qualifier has been assigned and the result is below the Reporting Limit, RL (CRDL) or Report Value is Estimated.
U Qual - Analyzed for but not detected above limiting criteria, Mdc/Mda/Mdl, Total Uncert, RDL or not identified by gamma scan software.

Date: 24-Dec-14

SDG: 49061

Report No.: 64030

No. of Results:	2	Comments:

FORM II
LCS RESULTS

Date: 24-Dec-14

Lab Name: TestAmerica Inc SDG: 49061
Matrix: WATER Report No.: 64030

Parameter	Result	Qual	Count Error (2 s)	Total Uncert(2 s)	MDL	Report Unit	Yield	Expected	Expected Uncert	Recovery, Bias	Analysis, Prep Date	Aliquot Size	Primary Detector
Batch: 4335069 RL-RA-001 Work Order: M5MJV1AC Report DB ID: M5MJV1CS													
Ra-226	8.28E+00		4.9E-01	1.7E+00	1.76E-01	pCi/L	99%	9.85E+00	1.00E-01	84%	12/20/14 06:05 p	1.0006	ASCDMB
							Rec Limits:	75	125	-0.2			
Batch: 4335071 RL-RA-001 Work Order: M5MJ01AC Report DB ID: M5MJ01CS													
Ra-228	9.23E+00		7.2E-01	1.3E+00	5.43E-01	pCi/L	86%	9.95E+00	1.14E-01	93%	12/23/14 12:21 p	1.0006	GPC4A
							Rec Limits:	75	125	-0.1			

No. of Results: 2 Comments:

TestAmerica Pensacola

3355 McLeMere Drive
Pensacola, FL 32514
Phone (850) 474-1001 Fax (850) 478-2671

Chain of Custody Record

TestAmerica
THE LEADER IN ENVIRONMENTAL TESTING



Client Information (Sub Contract Lab) Client Contact: Shipping/Receiving Company: TestAmerica Laboratories, Inc. Address: 2800 George Washington Way, City: Richland State, Zip: WA, 99352 Phone: 509-375-3131(Tel) 509-375-5590(Fax) Email: Project Name: Agrico Pensacola Site:		Sampler: Lab PM: Savoie, Noel E-Mail: noel.savoie@testamericainc.com	Carrier Tracking No(s): COC No: 400-66222-1 Page: Page 1 of 1 Job #: 400-98898-1
Analysis Requested			
Due Date Requested: 12/24/2014 TAT Requested (days): PO #: WO #: Project #: 64000434 SSOW#:		Preservation Codes: A - HCL B - NaOH C - Zn Acetate D - Nitric Acid E - NaHSO4 F - MeOH G - Anchlor H - Ascorbic Acid I - Ice J - DI Water K - EDTA L - EDA Other: M - Hexane N - None O - AsNaO2 P - Na2O4S Q - Na2SO3 R - Na2S2SO3 S - H2SO4 T - TSP Dodecahydrate U - Acetone V - MCAA W - pH 4-5 Z - other (specify)	
Sample Identification - Client ID (Lab ID)		Total Number of Containers	
AC-35D (400-98898-1)	MS5L4N	11/24/14 11:45 Central	3
AC-24S (400-98898-2)	MS5L4P	11/24/14 13:59 Central	3
AC-24D (400-98898-3)	MS5L4Q	11/24/14 15:40 Central	3
AC-30D (400-98898-4)	MS5L4R	11/25/14 10:10 Central	3
J4K260415 SDG-49063 Due 12-5-14		Special Instructions/Note:	
Possible Hazard Identification Unconfirmed Deliverable Requested: I, II, III, IV, Other (specify)			
Sample Disposal (A fee may be assessed if samples are retained longer than 1 month) ☐ Return To Client ☐ Disposal By Lab ☐ Archive For _____ Months			
Special Instructions/QC Requirements:			
Empty Kit Relinquished by:		Method of Shipment:	
Relinquished by:		Date/Time:	
Relinquished by:		Date/Time:	
Relinquished by:		Date/Time:	
Custody Seals Intact: Δ Yes Δ No		Cooler Temperature(s) °C and Other Remarks:	

Sample Check-in List

Date/Time Received: 11-26-14 / 1300 Container GM Screen Result: (Airlock) 20 cpm Initials B]
 Sample GM Screen Result (Sample Receiving) 0 cpm Initials B]
 Client: STR SDG #: 49063 SAF #: _____ NA B]
 Lot Number: J4K260415
 Chain of Custody # 400-66222.1

Shipping Container ID or Air Bill Number: _____ NA B]

Samples received inside shipping container/cooler/box Yes B] Continue with 1 through 4. Initial appropriate response.
 No [] Go to 5, add comment to #16.

1. Custody Seals on shipping container intact? Yes B] No [] No Custody Seal []
2. Custody Seals dated and signed? Yes B] No [] No Custody Seal []
3. Cooler temperature: _____ °C NA B]
4. Vermiculite/packing materials is NA [] Wet B] Dry []

Item 5 through 16 for samples. Initial appropriate response.

5. Chain of Custody record present? Yes B] No []
6. Number of samples received (Each sample may contain multiple bottles): 4
7. Containers received: 12 x 4

8. Sample holding times exceeded? NA [] Yes [] No B]
9. Samples have: _____ tape _____ hazard labels _____ custody seals B appropriate sample labels
10. Matrix: _____ A (FLT, Wipe, Solid, Soil) B I (Water) _____ S (Air, Niosh 7400) _____ T (Biological, Ni-63)
11. Samples: B are in good condition B are leaking _____ are broken
 _____ have air bubbles (Only for samples requiring no head space) _____ Other _____
12. Sample pH appropriate for analysis requested Yes B] No [] NA []
 (If acidification is necessary go to pH area & document sample ID, initial pH, amount of HNO₃ added and pH after addition on table)
13. Were any anomalies identified in sample receipt? Yes [] No B]
14. Description of anomalies (include sample numbers): NA B]

15. Sample Location, Sample Collector Listed on COC? * Yes [] No B]
 *For documentation only. No corrective action needed.
16. Additional Information: Samples leaked a little. CMP-0

[] Client/Courier denied temperature check. [] Client/Courier unpack cooler.

Sample Check-in List completed by Sample Custodian:

Signature: [Signature] Date: 11-26-14

Client Notification needed? Yes [] No [] Date: _____

By: _____

Person contacted: _____

☒ No action necessary, process as is

Project Manager [Signature] Date 12/1/14


Chain of Custody Record

Client Information Client Contact: Mr. Jeff Wagner Company: URS Corporation Address: 1625 Summit Lake Drive Suite 200 City: Tallahassee State, Zip: FL, 32317 Phone: 850-402-6409 (Tel) Email: jeffry_wagner@urscorp.com Project Name: Agrico Pensacola Site:		Sample: <i>11/14/14</i> Phone: <i>850-528-8992</i> Lab PM: Saviole, Noel E-Mail: noel.saviole@testamericainc.com		Carrier Tracking No(s): 640-48009-12359.5 Page: Page 5 of 5 Job #:	
Due Date Requested: TAT Requested (days): PO #: 308649. US WO #: 12806620.00000 Vendor #1427536 Project #: 64000434 SSOW#:		Analysis Requested SUBCONTRACT - Rad 226-Method 903.1 (Richland) SUBCONTRACT - Rad 226-Method 904.0 (Richland) SUBCONTRACT - Rad 228-Method 904.0 (Richland) 300 ORGFM 28D - Chloride and Sulfate 6010B - Arsenic 340.2, SM4500 NO2 B 553.2 Pres - Nitrate Nitrite as N Perform MS/MSD (Yes or No) Field Filtered Sample (Yes or No)			
Matrix (W=water, S=solid, O=waste/soil, BT=Tissue, A=AP) Sample Type (C=comp, G=grab) Sample Time Sample Date		Preservation Codes: A - HCL B - NaOH C - Zn Acetate D - Nitric Acid E - NaHSO4 F - MeOH G - Amchlor H - Ascorbic Acid I - Ice J - DI Water K - EDTA L - EDA Other: M - Hexane N - None O - AsNaO2 P - Na2O4S Q - Na2SO3 R - Na2S2O3 S - H2SO4 T - TSP Dodecahydrate U - Acetone V - MCAA W - ph 4-5 Z - other (specify)			
Sample Identification AC-350 AC-245 AC-24D AC-30D		Total Number of containers Special Instructions/Note:			
Possible Hazard Identification ☐ Non-Hazard ☐ Flammable ☐ Skin Irritant ☐ Poison B ☐ Unknown ☐ Radiological		Sample Disposal (A fee may be assessed if samples are retained longer than 1 month) ☐ Return To Client ☒ Disposal By Lab ☐ Archive For _____ Months			
Empty Kit Relinquished by: <i>Jeffrey Wagner</i> Relinquished by: <i>Jeffrey Wagner</i> Relinquished by:		Special Instructions/QC Requirements: Method of Shipment:			
Date: 11/15/14 Time: 11:25:14 Company: ORS		Date/Time: 11/15/14 11:20 Company:			
Date/Time:		Date/Time:			
Date/Time:		Date/Time:			
Custody Seals Intact: Δ Yes Δ No		Cooler Temperature(s) °C and Other Remarks: <i>54°C FH-2</i>			

APPENDIX B


Groundwater Elevation Trend in Surficial Zone

Agrico Site
Pensacola, FL

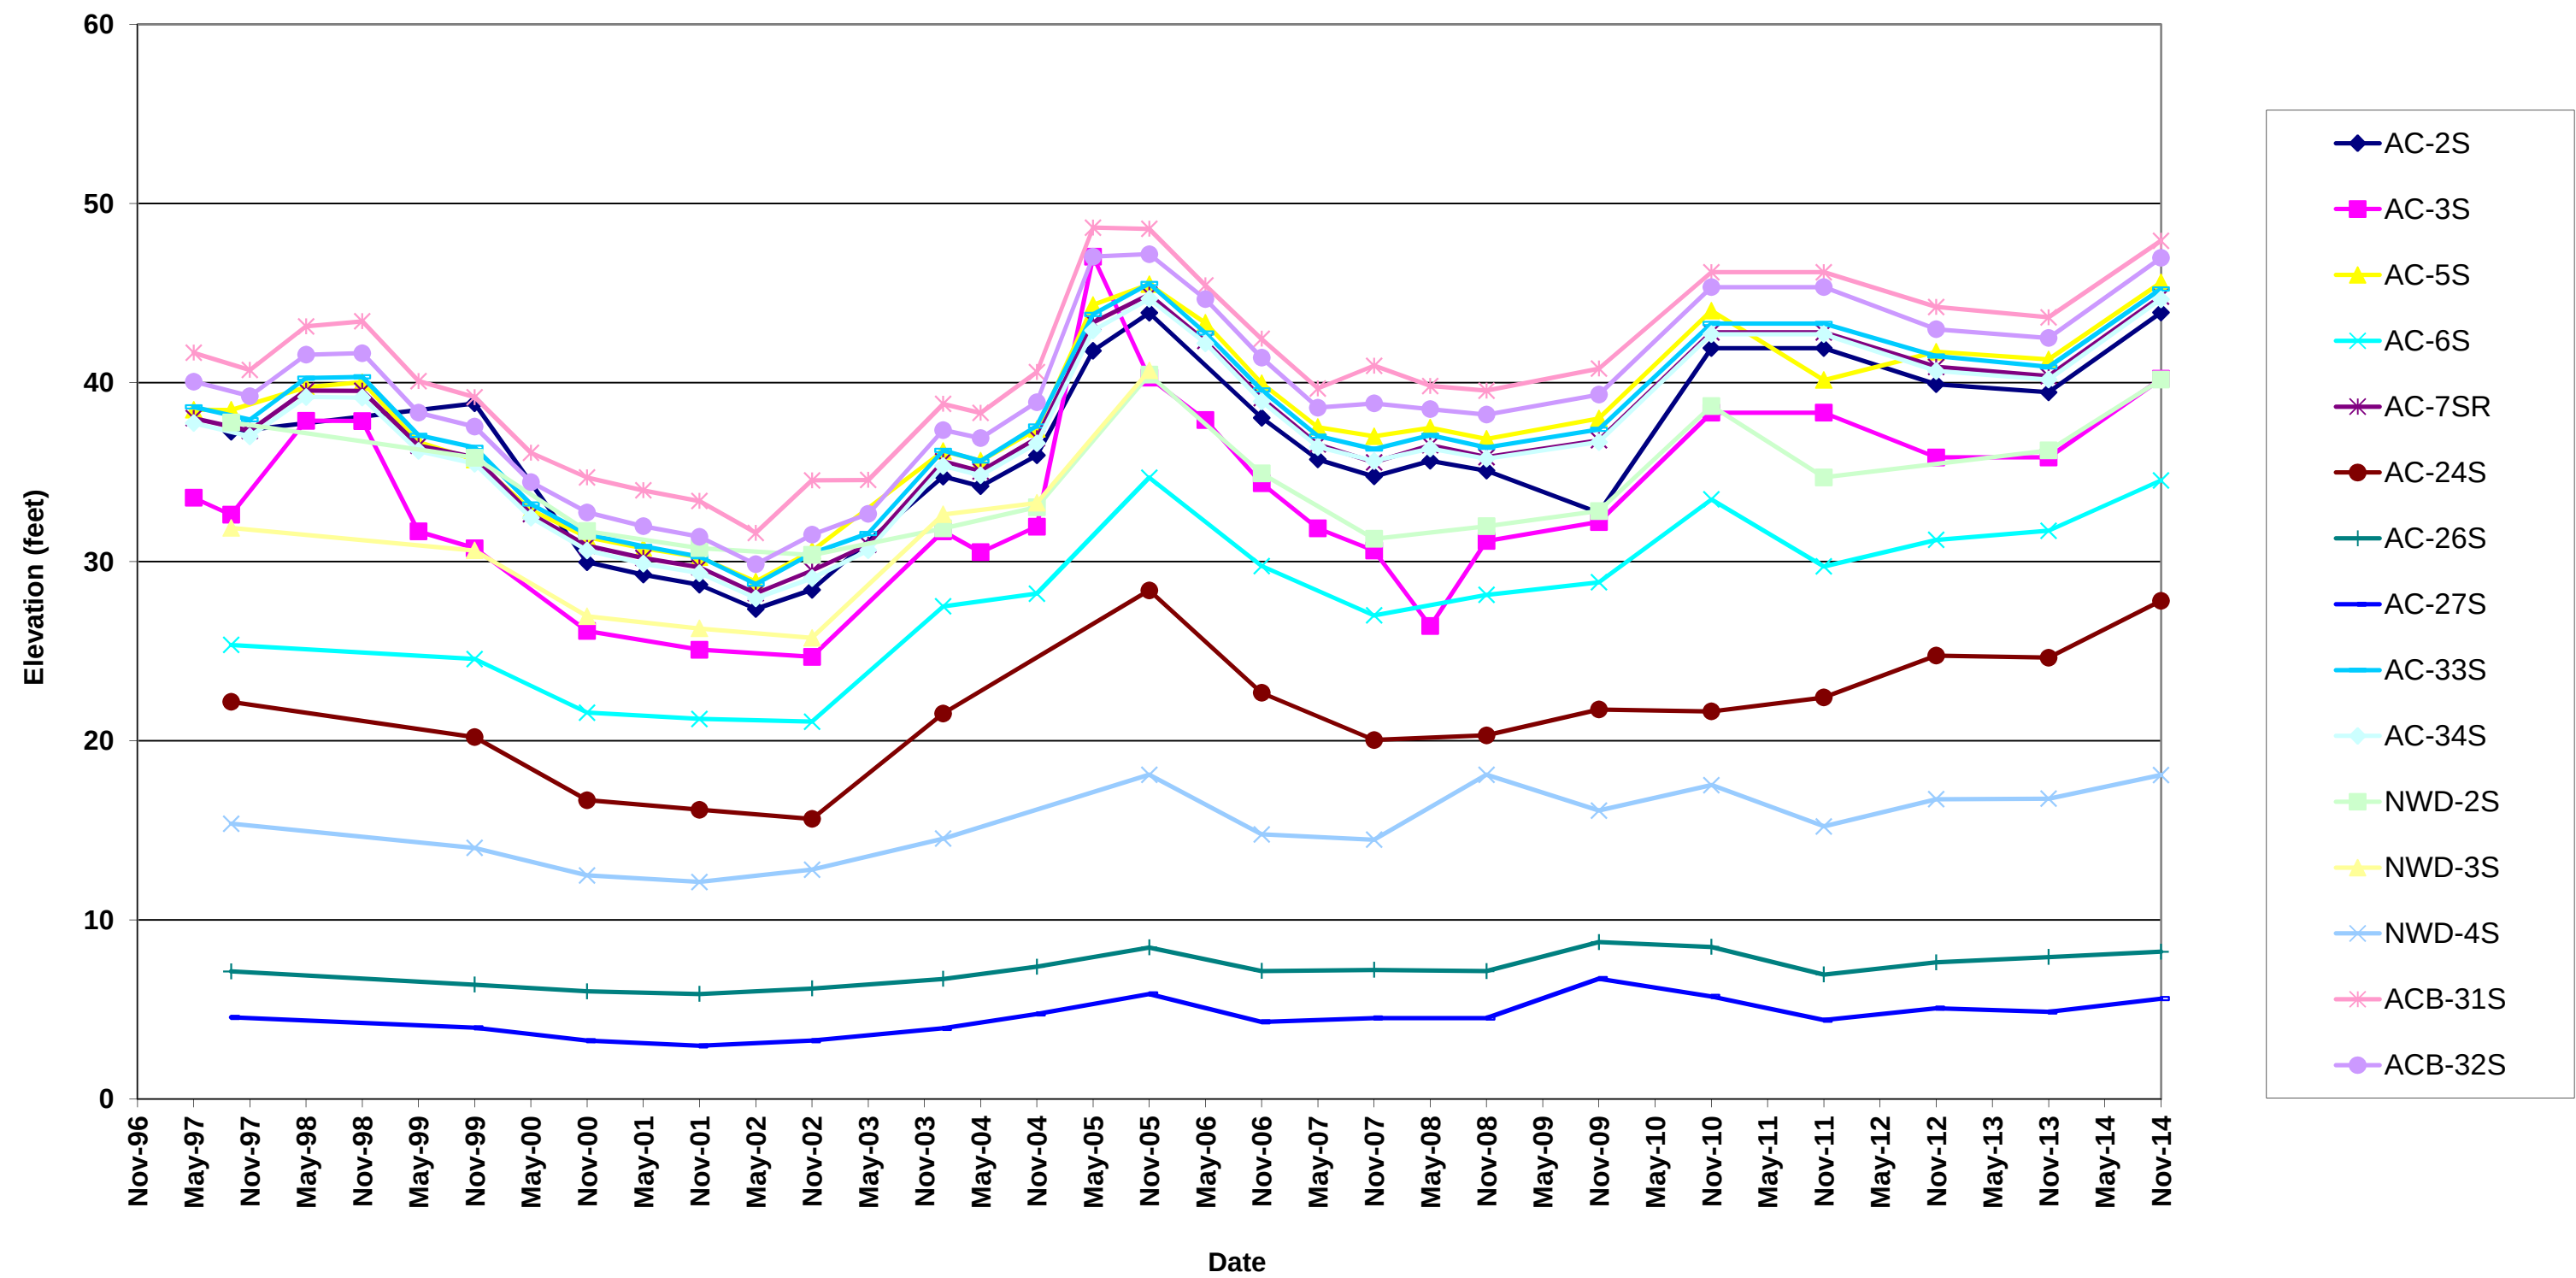

Groundwater Elevation Trend in Main Producing Zone

Agrico Site
Pensacola, FL

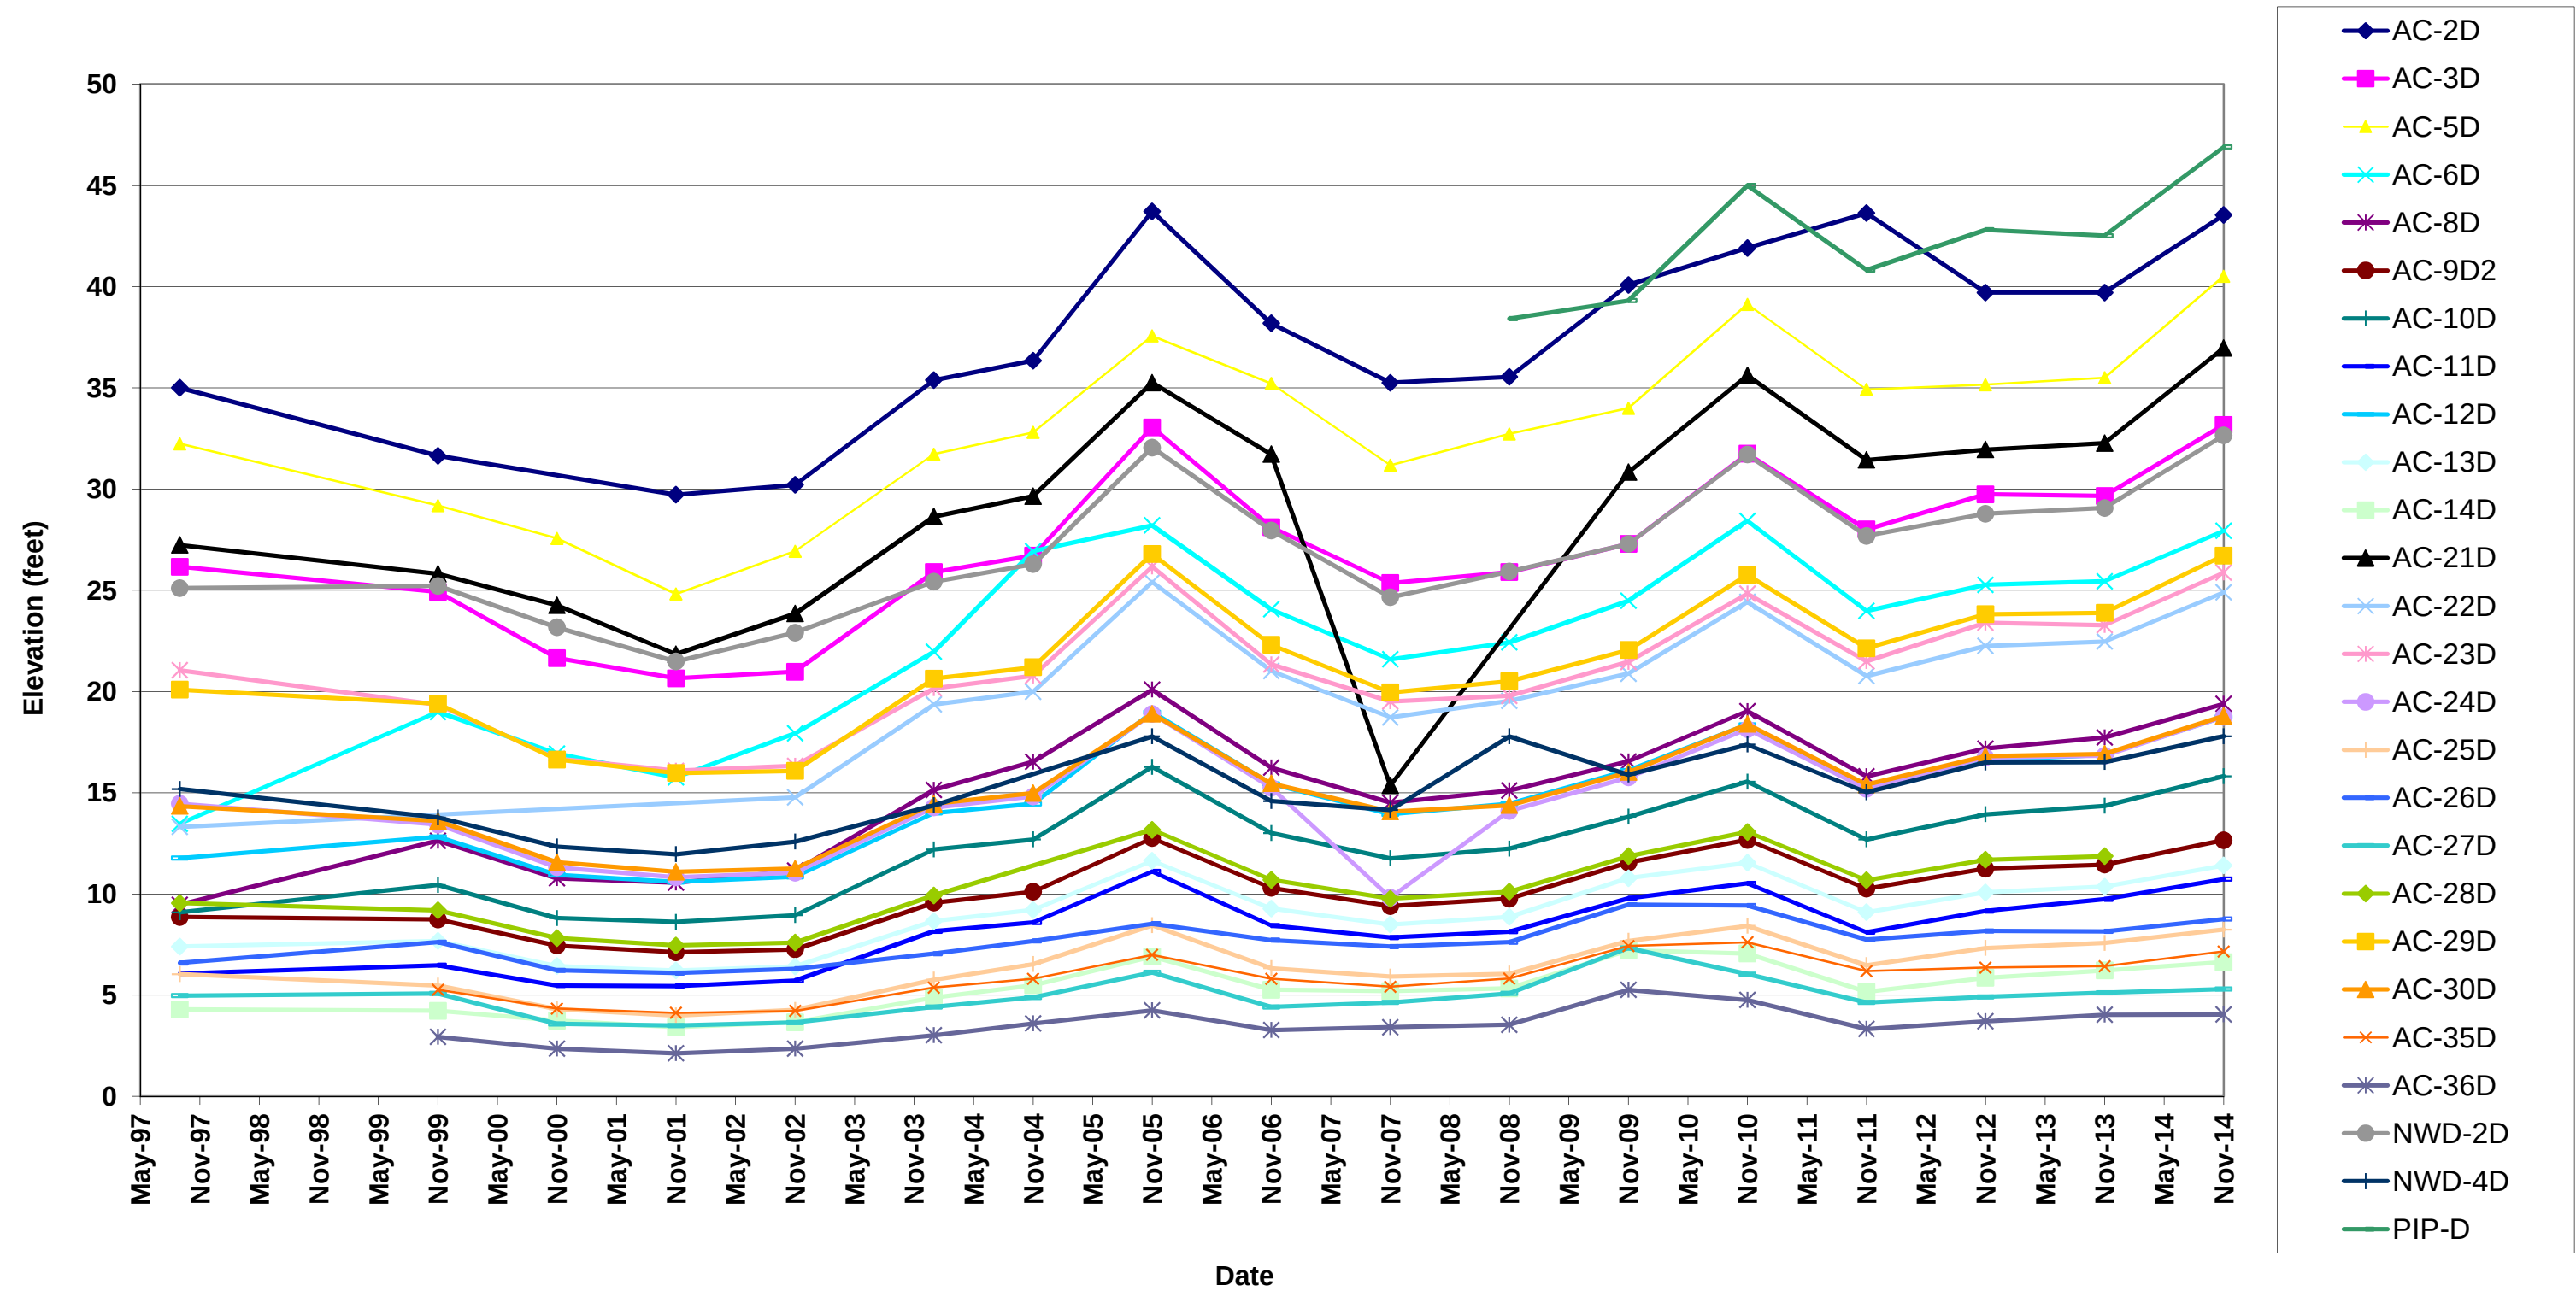

APPENDIX C



MEMORANDUM

To: Alex Webster (FDEP NW District) Walsta Jean-Baptiste (FDEP, Tallahassee) Tim Haag (ECUA) Danny Majors (ECUA) Tom Brown (NFWFMD) Thaddeus Cohen (City of Pensacola) Mark Spitznagel (ECHD) Robert Merritt (ECHD) Keith Wilkins (Escambia County) Alan Hagans (FDOT Chipley)	From: Jeffry R. Wagner, P.G. Office: URS - Tallahassee Date: December 3, 2014

**Subject: Institutional Controls Coordination
Agrico Site, Pensacola, Florida**

As part of the U.S. Environmental Protection Agency (EPA) approved Remedial Action Work Plan for Operating Unit Two (OU-2) (November 1998), periodic communications are planned with the agencies in order to ensure and verify that existing institutional controls remain in place. The purpose of this Memorandum is to solicit, in writing, information on any changes in existing or any proposed new regulatory requirements that may affect the existing institutional controls pertaining to the Agrico Site.

SITE SUMMARY

Monitored Natural Attenuation Results

Statistical MNA evaluations were prepared in 2009 and 2013. The reports that were submitted to EPA and FDEP show that mechanisms for attenuation are in place throughout the OU-2 area. These mechanisms and the OU-1 source remedy are propagating downgradient toward Bayou Texar, as expected. For the plume area, the highest concentrations for each constituent are declining and downgradient peaks are less than historical highs. Increases are still happening for individual wells, but the overall concentrations are still less than the historical highs. It is estimated from statistical evaluation following EPA MNA guidance that much of the groundwater will reach the target concentrations within two to three decades. However, the discharge area near Bayou Texar may take longer. The processes at this discharge boundary are more complex and do not follow the upgradient time line. Additionally, radium declines may lag behind the other constituents and is more dependent on increases in pH as the overall chemical conditions improve upgradient. Initial fate and transport modeling performed for the site in the early 1990s suggested targets would not be reached for at least 70 years. About 20 years has passed since the source controls were implemented. The 50 years remaining is still reasonable and well within the targets estimated with the statistical evaluation.



Distribution List
Institutional Controls Coordination
Agrico Site Operable Unit No. 2 (OU-2)
December 3, 2014
Page 2

Groundwater Sampling Results

Groundwater results for November 2014 continue to compare favorably to past results. Overall concentration trends within the surficial zone are downward and the impact extent is shrinking. Impacts are limited for this zone. This is a direct result of effective source control and the local hydrogeologic conditions.

For the main producing zone, the overall flattening of trends is what has been predicted. This flattening should be expected to continue for some time and eventually evolve into a slowly decreasing trend that accelerates with time.

Slight upward or downward ticks in the trends for the COCs are to be expected over time. It is the long-term trend for each of the COC that is important.

Groundwater Levels

Results of water level measurements collected in November 2014 indicate that groundwater flow remains toward Bayou Texar for both the surficial zone and main producing zone. In 2014, groundwater flow patterns closely followed historical patterns.

Bayou Texar Sampling Results

An assessment of potential impacts downgradient of the Agrico groundwater plume was presented to EPA and FDEP on September 4, 2009 in the report, *“Conceptual Site Model, Ecological Impact Evaluation of Bayou Texar Downgradient of Agrico’s Groundwater Fluoride Plume, September 14, 2009.”* The report concluded that there is no completed exposure pathway between populations of demersal fish and benthic receptors in the Bayou downgradient of the Site, and concentrations of fluoride in pore water and near-bottom surface water that potentially would cause adverse effects to the populations of demersal fish and benthic receptors. The report also concluded that the fluoride solubility in the majority of surface sediments and in all pore waters within the groundwater plume discharge area is controlled by mineral precipitation reactions that are responsible for buffering dissolved concentrations of fluoride. This report was approved by EPA on September 20, 2010. The approval modified the report recommendations to include three additional surface water sampling locations to be added as part of the annual sampling for the site. Sampling continues to show concentrations in the bayou at levels well below the surface water standard (5 mg/L) for fluoride.

Annual groundwater/surface water monitoring was conducted in November 2014 for the Agrico site. Sixteen years of annual monitoring have been conducted since 1999.



Distribution List
Institutional Controls Coordination
Agrico Site Operable Unit No. 2 (OU-2)
December 3, 2014
Page 3

INSTITUTIONAL CONTROLS

Several rules, regulations and policies already exist which control the use of groundwater within the OU-2 area. These serve as institutional controls, and include:

1. Well construction and consumptive use is approved by Northwest Florida Water Management District (NFWFMD). On February 22, 2001 the Northwest Florida Water Management District (NFWFMD) Governing Board passed a well construction moratorium for the area bounded to the north by Hyatt Street, Wynnehurst Street, Kenneth Street, Boxwood Drive and Brookside Place; to the west by the CSX Railroad; to the south by East Cross Street; and to the east by Bayou Texar. This moratorium applies to all new well construction within the designated area except monitoring wells and encompasses both the Agrico and Escambia Treating Company areas. The moratorium remains in effect during 2014. Checking of NFWFMD drilling permits indicates that no well construction permits were issued within the Agrico OU-2 area during 2014.
2. Access is restricted on the Agrico site. The property is secured by a perimeter chain link security fence and locked gates. Restrictive and site information signs are posted advising the public of the on-site conditions, and a contact phone number is also posted for inquiries. The site is routinely inspected by authorized personnel and inspection reports on the site conditions are completed twice a year. Additionally, the site is inspected after each major storm event. Any damages found are repaired. Construction or related activities which would interfere with maintaining the site remedial measures are prohibited by the legal deed restrictions. Any use of the property contrary to the Record of Decision is prohibited, as per covenants filed for the property.
3. The location of the Agrico plume is well characterized and documented. Because this information is submitted to the ECUA and other agencies in an annual report, and because of the NFWFMD well moratorium, it is highly improbable that future municipal wells will be located in the vicinity of the site. It should also be noted that non-Agrico groundwater impacts are present outside of the Agrico plume. To the north of the Agrico site, groundwater impacts have been caused by the Escambia Treating Company (ETC) site. This plume intrudes into the Agrico area to the south. Also south of the Agrico plume, Florida Department of Environmental Protection (FDEP) is assessing a site referred to as Site 348. This site has reportedly contributed to groundwater impacts to the south of the Agrico plume. The Site 348 plume has the potential to intrude into the Agrico area, and Site 348 has similar COCs to those of



Distribution List
Institutional Controls Coordination
Agrico Site Operable Unit No. 2 (OU-2)
December 3, 2014
Page 4

- Agrico. This site is being assessed for possible impacts to ECUA wells, including F& Scott Streets well, No. 9 well, and East Plant well. Groundwater from Site 348 moves easterly and may discharge into Bayou Texar, if not affected by pumping from F & Scott Streets Well. Additionally, other sources of groundwater impacts exist within and in the near proximity of the Agrico plume and include releases from petroleum and dry cleaning related sites as documented by FDEP.
4. The ECUA regularly samples and analyzes water being pumped from public supply wells. ECUA controls the pumpage from these wells. The cause of current impacts to ECUA wells, as noted above, is the subject of an ongoing assessment by FDEP. Pumping of both East Plant and well No.9 has been discontinued. The F& Scott Street well is still active and within a distance from Site 348 impacts that pumping influences could potentially draw the Site 348 plume toward this active well.
 5. In 1997, the Northwest Florida Water Management District (NFWFMD) established 7-year and 20-year capture zones around each ECUA water supply well. These captures zones constitute the wellhead protection area for each well (Richards, Pratt, and Milla, December 1997, Wellhead Protection Area Delineation in Southern Escambia County, Florida; Water Resources Special Report 97-4, NFWFMD). The Agrico plume remains outside of the 20-year capture zone for all supply wells. Site 348 lies within the 20- year capture zone for inactive ECUA Well No. 9. And Site 348 lies in close proximity to the designated capture zone for active ECUA Well F & Scott.
 6. The Designated Area has been established by the FDEP and regulated by Florida Administrative Code, Chapter 62-524, FDEP rules. New potable well permitting requirements must be met in order to install a new potable water well. This designated area is the same as the area defined in item number 1. At this time, the NFWFMD moratorium is a more stringent restriction than that related to the Chapter 62-524 designation.

The 2013 Annual Report is being distributed to you with this memorandum. The 2014 Annual Report is currently in preparation and will not be submitted until at least the second quarter of 2015. This report will be distributed following review and approval by EPA.

Site information is available at the local EPA repository, the West Florida Regional Library. Information includes various project documents. Additionally, a site specific internet web site has been established at: <http://agricopensacola.com>. The web site contains general information and includes all Fact Sheets for the site as well as pertinent documents for the site.



Distribution List
Institutional Controls Coordination
Agrico Site Operable Unit No. 2 (OU-2)
December 3, 2014
Page 5

Three Five-Year Reviews of the Agrico Site have been completed by EPA. Each Review has concluded that the remedy at the Agrico Site is functioning as intended by the Records of Decision for OU-1 and OU-2, and remains protective of human health and the environment. EPA is in the process of conducting the fourth Five-Year Review for the site. The results of the review will be distributed in a report about July 2015.

Please respond in writing concerning any contemplated changes in existing or any proposed new regulatory requirements that may affect the existing institutional controls pertaining to the Agrico Site to Jeffry R. Wagner, URS Corporation, 1625 Summit Lake Drive, Suite 200, Tallahassee, Florida 32317, or send an e-mail to Jeffry.Wagner@urs.com. Your assistance in this cooperative effort is greatly appreciated.

If you have any questions, please contact me at (850) 402--6409.

JRW/lc

cc: Scott Miller, EPA Region 4

Wagner, Jeffry

From: Hagans, Alan <Alan.Hagans@dot.state.fl.us>
Sent: Wednesday, December 03, 2014 11:24 AM
To: Wagner, Jeffry
Cc: Scott Miller
Subject: RE: Agrico Site Pensacola - Annual FDOT Construction Activity Inquiry

Hey Jeff,

Do not see anything upcoming in the 5 year work program that would have impacts.

Thanks,

*Alan Hagans
District Contamination Impacts Coordinator
Department Of Environmental Management (FDOT)
Ph: (850) 330-1511
alan.hagans@dot.state.fl.us*

From: Wagner, Jeffry [<mailto:jeffry.wagner@urs.com>]
Sent: Wednesday, December 03, 2014 9:23 AM
To: Hagans, Alan
Cc: Scott Miller
Subject: Agrico Site Pensacola - Annual FDOT Construction Activity Inquiry

Please see attached file.

Jeff Wagner, PG
Vice President and Principal Hydrogeologist
URS Corporation, IE
1625 Summit Lake Dr
Tallahassee, FL 32317
Direct – 850-402-6409
Cell – 850-251-7208

Note: As of October 17, 2014, URS has become a wholly owned subsidiary of AECOM

Nothing is ever so urgent or important that we can't take the time to do it safely.

This e-mail and any attachments contain URS Corporation confidential information that may be proprietary or privileged. If you receive this message in error or are not the intended recipient, you should not retain, distribute, disclose or use any of this information and you should destroy the e-mail and any attachments or copies.

**Water Well Contractors
Irrigation System Contractors And
Pool Contractors**

Please be advised that additional well construction requirements may be specified for wells constructed in the following localized area of Pensacola, Florida.

- South of Fairfield Drive
- East of Palafox Street
- West of Bayou Texar
- North of Bobe Street

Areas outside of the area described above may also be affected. Please contact the Northwest Florida Water Management District (NFWFMD), the Florida Department of Environmental Protection (FDEP), or the Escambia County Health Department (ECHD) for further information.

Per Chapter 62-524, Florida Administrative Code, New Potable Water Well Permitting in Delineated Areas, and Chapter 40A-3, Florida Administrative Code, Regulation of Wells, water well construction permits issued by the NFWFMD, including wells used for lawn irrigation or filling pools, may have certain specific conditions or limitations attached.

On February 22, 2001 the NFWFMD governing board passed a well construction moratorium that includes the area specified above. This moratorium applies to all wells except monitoring wells. The moratorium is currently in effect and prohibits new wells in the designated area.

For further information contact:

Northwest Florida Water Management District

Tallahassee Office: 850-539-5999

or

Florida Department of Environmental Protection, Northwest District

850-595-8300

or

Escambia County Health Department

850-595-6700

DECLARATION OF COVENANTS, CONDITIONS AND RESTRICTIONS

THIS DECLARATION OF COVENANTS, CONDITIONS AND RESTRICTIONS ("Covenant") is made by CONOCO INC. ("CONOCO"), and shall take effect as of the date set forth below. The purpose of this Covenant is to restrict and prohibit all surface and subsurface uses of the property described herein, in perpetuity, except as specifically set forth herein.

RECITALS

WHEREAS, CONOCO is the owner of real property lying and being in Escambia County, Florida; and

WHEREAS, the intent of CONOCO is that this Covenant apply to and be binding on all property owned by CONOCO as of the date of this document and which lies in the area bounded by North Palafox Street, Brent Lane, North Davis Highway, and Fairfield Drive (the "Property"), as more particularly described on Composite Exhibit "A" consisting of 4 pages, attached and made a part hereof; and

WHEREAS, a RCRA cap is located on the Property containing pollutants in excess of certain standards allowed by federal and state law, as more particularly described in the Record of Decision, Agrico Chemical Superfund Site, September 28, 1992; and

WHEREAS, the Record of Decision described above mandated that CONOCO perform remedial action and impose access and use restrictions on the Property; and

WHEREAS, CONOCO seeks by this Covenant to fully comply with the Record of Decision requirement to restrict access to and use of the Property;

NOW THEREFORE, in consideration of the acceptance by the United States Environmental Protection Agency of the remedial action conditions and limitations stated in the Record of Decision, and acknowledging that the same constituted good and valuable consideration, CONOCO does hereby impose on the Property, in perpetuity, the following reasonable and lawful access and use restrictions.

COVENANTS

1. Access to the Property is restricted (1) to those authorized CONOCO agents and governmental agents or their representatives and officials who must enter the Property to inspect, maintain, or repair fencing or other remedial action measures constructed pursuant to or to be maintained in connection with the Record of Decision, (2) to those persons entitled to exercise the personal servitude of passage

in accordance with and for the limited purposes stated in the Act of Servitude recorded in the Official Records of Escambia County at OR Book 3758, Page 0955, and (3) to those persons who must have access to the Property to service and maintain existing public utilities and electrical power lines.

2. The erection, construction, or placing of any road, parking lot, building, sign, billboard or other advertising, utilities (public or commercial), towers, antennas, or any other structure on or above the ground is prohibited, except (a) as such structures may be required for the purpose of maintaining the remedial measures as required by paragraph 1 herein, or (b) as Conoco, or its agents or assigns, may erect or construct on those portions of the Property on which is not located the RCRA cap and as will not interfere with the maintenance of the remedial measures.

3. Use of the Property for temporary or permanent storage of equipment, inventory, or materials is prohibited, except as the same may be necessary to maintain the remedial measures as required by paragraph 1 herein.

4. The dumping or placing of soil or other substance or material as landfill or the dumping or placing of trash, waste, or unsightly or offensive materials on the Property is prohibited.

5. The removal or harvesting for any commercial purpose of trees, shrubs, or other vegetation is prohibited.

6. The excavation, dredging, or removal of loam, peat, gravel, soil, rock, or other material substance on or under the Property is prohibited, except as may be necessary to maintain the remedial measures as required by paragraph 1 herein.

7. Any drilling, mining, or other removal of soil, water, minerals, gases, or other substances from the surface or subsurface of the Property is prohibited, except as required to comply with the Record of Decision.

8. Any other use of the Property contrary to the Record of Decision is prohibited even though not specifically enumerated herein.

9. The restrictions imposed herein are perpetual restrictions imposed by the lawful owner of the Property and will run with the land and be binding on all successor owners, lessees or other transferees of the Property, as well as all successors and assigns of CONOCO.

10. This Covenant may be enforced by CONOCO, any other Potentially Responsible Party with respect to the Property the United States Environmental Protection Agency or the Florida Department of Environmental Protection, or their successors and assigns.

11. Enforcement of this Covenant shall be by action against any person or persons violating or attempting to violate any provision herein, either in equity or in law.

12. Invalidation of any provision of this Covenant by judgment or court order shall in no way affect any other provision of this Covenant, which shall remain in full force and effect in perpetuity.

IN WITNESS WHEREOF, the Covenantor has executed this Declaration of Covenants, Conditions and Restrictions for the Property described herein, this 11th day of July, 1997.

Signed, sealed and delivered
in the presence of:

ANN LUNDSTROM

Name: Ann Lundstrom

DOROTHY AKERS

Name: Dorothy Akers

STATE OF TEXAS
COUNTY OF HARRIS

The foregoing instrument was acknowledged before me this 11th day of July, 1997, by Dennis R. Parker, as V.P. SHEA of CONOCO INC., a Delaware corporation, and who is personally known to me or who has produced U.S. Passport 131824098 as identification.


COVENANTOR:

CONOCO INC., a Delaware corporation

By: Dennis R. Parker (SEAL)
Dennis R. Parker
Its: Vice President, SHEA

Attest:

[Signature]
Assistant Secretary




[Signature]
Notary Public

Commission No.: _____
My Commission Expires: 9-20-97

This instrument prepared by:

✓ Jesse W. Rigby, of
CLARK, PARTINGTON, HART, LARRY
BOND, STACKHOUSE & STONE
One Pensacola Plaza
125 W. Romana Street, Suite 800
Pensacola, Florida 32501



PARCEL 1:

Commence at the Northwest corner of Section 4, Township 2 South, Range 30 West, Escambia County, Florida; thence North 52°36'16" East along the South line of Section 5, Township 2 South, Range 30 West for a distance of 1194.20 feet to the Easterly R/W line of the Louisville and Nashville Railroad (100' R/W); thence North 24°26'14" West along said Easterly R/W line for a distance of 295.98 feet to the Northerly R/W line of Fairfield Drive (SR #289-A); thence North 52°33'46" East along said Northerly R/W for a distance of 76.08 feet; thence South 37°26'14" East along said R/W for a distance of 90.00 feet; thence North 57°38'32" East along said R/W for a distance of 451.36 feet; thence North 50°39'13" East along said R/W for a distance of 150.08 feet; thence North 37°26'14" West for a distance of 490.00 feet; thence North 52°33'46" East for a distance of 200.00 feet to a point which is the Point of Beginning. From said Point of Beginning, continue North 52°33'46" East for a distance of 200.00 feet; thence South 37°26'14" East for a distance of 400.00 feet to the R/W line of Fairfield Drive (SR #289-A); thence continue South 37°26'14" East along said R/W for a distance of 165.00 feet; thence South 82°26'14" East along said R/W for a distance of 35.36 feet; thence North 52°33'46" East along said R/W for a distance of 177.70 feet to the Westerly R/W line of Interstate Highway 110 (SR #8-A); thence North 16°26'14" West along said Westerly R/W line for a distance of 823.07 feet; thence South 52°39'08" West for a distance of 697.67 feet; thence South 37°26'14" East for a distance of 179.49 feet to the Point of Beginning, containing 7.0 acres, more or less, and lying and being in Section 5, Township 2 South, Range 30 West, Escambia County, Florida, and subject to a 100 foot wide Gulf Power Company Easement. [As recorded in OR Book 3767, Page 0377, Escambia County, Florida.]

PARCEL 2:

Commence at the Northwest corner of Section 4, Township 2 South, Range 30 West, Escambia County, Florida; thence North 52°36'16" East along the South line of Section 5, Township 2 South, Range 30 West for a distance of 1194.20 feet to the Easterly R/W line of the Louisville & Nashville Railroad (100' R/W); thence North 24°26'14" West along said Easterly R/W line for a distance of 295.98 feet to the Northerly R/W line of Fairfield Drive (SR #289-A); thence North 52°33'46" East along said Northerly R/W for a distance of 76.08 feet; thence South 37°26'14" East along said R/W for a distance of 90.00 feet; thence North 57°38'32" East along said R/W for a distance of 451.36 feet; thence North 50°39'13" East along said R/W for a distance of 150.08 feet; thence North 28°20'06" East along said R/W for a distance of 219.32 feet to the Point of Beginning; thence North 52°33'46" East along said R/W for a distance of 200.00 feet; thence North 37°26'14" West for a distance of 400.00 feet; thence South 52°33'46" West for a distance of 200.00 feet; thence South 37°26'14" East for a distance of 400.00 feet to the Point of Beginning, containing 1.84 acres more or less and all lying and being in Section 5, Township 2 South, Range 30 West, Escambia County, Florida. [As recorded in OR Book 3767, Page 0377, Escambia County, Florida.]

PARCEL 3:

A tract being 1,6769 acres in Section 5, Township 2 South, Range 30 West, Escambia County, Florida, being more particularly described as:

Commence at the Northwest Corner of Section 4, Township 2 South, Range 30 West of said Escambia County, Florida; thence North 52°36'16" East along the South line of Section 5, Township 2 South, Range 30 West for 1194.20 feet to the Easterly R/W line of the CSX Railroad (100 foot R/W); thence North 24°26'14" West along said Easterly R/W line for 295.98 feet to the Northerly R/W line of Fairfield Drive (SR #289-A); thence North 52°33'46" East along said Northerly R/W for 25.64 feet; thence North 24°26'14" West for 370.51 feet; thence North 14°47'54" West for 199.93 feet; thence North 52°39'08" East for 970.81 feet; thence North 24°20'24" West for 175.71 feet; thence North 52°38'15" East for 257.88 feet to the Westerly R/W line of a Gulf Power Company Easement (100 feet R/W) as recorded in O.R. Book 298 at Page 512 of the public records of said county and the Point of Beginning; thence along said Westerly R/W line North 18°04'37" West 38.40 feet; thence departing said Westerly R/W line North 75°28'00" East for 93.40 feet; thence South 52°38'15" West for 98.77 feet to the Westerly R/W line of the aforesaid Gulf Power Easement and the Point of Beginning, AND

Commence at the Northwest Corner of Section 4, Township 2 South, Range 30 West of said Escambia County, Florida; thence North 52°36'16" East along the South line of Section 5, Township 2 South, Range 30 West for 1194.20 feet to the Easterly R/W line of the CSX Railroad (100 foot R/W); thence North 24°26'14" West along said Easterly R/W line for 295.98 feet to the Northerly R/W line of Fairfield Drive (SR #289-A); thence North 52°33'46" East along said Northerly R/W for 25.64 feet; thence North 24°26'14" West for 370.51 feet; thence North 14°47'54" West for 199.93 feet; thence North 52°39'08" East for 970.81 feet for the Point of Beginning; thence continue North 52°39'08" East for 416.63 feet to the Westerly R/W of Interstate I-110 (R/W varies); thence along said Westerly R/W North 16°22'22" West for 43.75 feet to the point of curvature of a curve concave to the Northeast having a radius of 2969.83 feet; thence along the arc of said curve through a central angle of 01°33'56" for an arc distance of 108.46 feet (Chord Bearing North 26°08'39" West, Chord Distance 108.46 feet); thence departing said Westerly R/W South 75°29'00" West for 62.02 feet; thence South 52°38'15" West for 356.65 feet; thence South 24°20'24" East for 175.71 feet to the Point of Beginning. [As recorded in OR Book 3758, Page 0952, Escambia County, Florida.]

PARCEL 4:

A portion of Section 5, Township 2 South, Range 30 West, Escambia County, Florida, being more particularly described as follows:

Commence at the Northwest corner of Section 4, Township 2 South, Range 30 West of said Escambia County, Florida; thence North 52°36'16" East along the South line Section 5, Township 2 South, Range 30 West for 1194.20 feet to the Easterly R/W line of the CSX Railroad (100' R/W); thence North 24°26'14" West along said Easterly R/W for 295.98 feet to the Northerly R/W line of Fairfield Drive (SR #289-A); thence North 52°33'46" East along said Northerly R/W for 25.64 feet; thence North 24°26'14" West for 370.51 feet; thence North 14°47'54" West for 199.93 feet; thence North 52°39'08" East for 970.81 feet; thence North 24°20'24" West for 175.71 feet to the Point of Beginning; thence continue North 24°20'24" West for 140.43; thence North 75°28'00" East for 259.23 feet to the Westerly R/W line of a Gulf Power Company Easement (100' R/W) as recorded to O.R. Book 298 at page 512 of the Public Records of said county; thence along said Westerly R/W line South 18°04'37" East for 38.40 feet; thence departing said Westerly R/W line South 52°38'15" West for 257.88 feet to the Point of Beginning, containing 0.519 acres more or less.

PARCEL 5:

A portion of Section 5, Township 2 South, Range 30 West, Escambia County, Florida, being more particularly described as follows:

Commence at the Northwest corner of Section 4, Township 2 South, Range 30 West of said Escambia County, Florida; thence North 52°36'16" East along the South line Section 5, Township 2 South, Range 30 West for 1194.20 feet to the Easterly R/W line of the CSX Railroad (100' R/W); thence North 24°26'14" West along said Easterly R/W line for 295.98 feet to the Northerly R/W line of Fairfield Drive (SR #289-A); thence North 52°33'46" East along said Northerly R/W for 25.64 feet; thence North 24°26'14" West for 370.51 feet; thence North 14°47'54" West for 199.93 feet; thence North 52°39'08" East for 118.25 feet for the Point of Beginning; thence continue North 52°39'08" East for 852.56 feet; thence North 24°20'24" West for 636.38 feet; thence South 65°39'36" West for 480.00 feet; thence South 24°20'24" East for 466.12 feet; thence South 52°38'43" West for 218.02 feet; thence South 2°28'32" West for 350.75 feet to the Point of Beginning; containing 9.1316 acres more or less.

Being more particularly shown on plat of survey dated March 19, 1995 prepared by Paul F. McCartney, Professional Land Surveyor Number 3140, Carlan Consulting Group, Inc., P.O. Box 2518, Pensacola, Florida 32513, incorporated herein by reference.

Being a portion of the property acquired by The Louisville and Nashville Railroad Company, a predecessor of Grantor, from Louis Boley, et ux, by deed dated November 17, 1896, recorded among the Public Land Records of Escambia County, Florida, in Book 17, Page 86.

On December 29, 1982 The Louisville and Nashville Railroad Company merged into Seaboard Coast Line Railroad Company, and the name of the surviving corporation changed to Seaboard System Railroad, Inc. On July 1, 1986, Seaboard System Railroad, Inc. changed its name to CSX Transportation, Inc.

PARCEL 6:

Commence at the Northwest corner of Section 4, Township 2 South, Range 30 West, Escambia County, Florida; thence North 52°36'16" East along the South line of Section 5, Township 2 South, Range 30 West, for a distance of 1194.20 feet to the easterly R/W line of the Louisville and Nashville Railroad (100' R/W); thence North 24°26'14" West along said easterly R/W line for a distance of 295.98 feet to the northerly R/W line of Fairfield Drive (SR #298-A); thence North 52°33'46" East along said northerly R/W for a distance of 25.64 feet to the Point of Beginning; then continue North 52°33'46" East along said R/W for a distance of 50.44 feet; thence South 37°26'14" East along said R/W for a distance of 90.00 feet; thence North 57°38'32" East along said R/W for a distance of 451.36 feet; thence North 50°39'13" East along said R/W for a distance of 150.08 feet; thence North 37°26'14" West for a distance of 490.00 feet; thence North 52°33'46" East for a distance of 200.00 feet; thence run North 37°26'14" West for a distance of 179.49 feet; thence South 52°39'08" West for a distance of 689.92 feet; thence South 14°47'54" East for a distance of 199.93 feet; thence South 24°26'14" East parallel to said Railroad R/W for a distance of 370.51 feet to the Point of Beginning. Containing 9.67 acres, more or less, and lying and being in Section 5, Township 3 South, Range 30 West, Escambia County, Florida.

RCD Aug 07, 1997 12:39 pm
Escambia County, Florida

Ernie Lee Magaha
Clerk of the Circuit Court
INSTRUMENT 97-407567

APPENDIX D

OU-1 Bi-Annual Inspection Report

**Agrico Chemical Site
Pensacola, Florida**

ROUTINE FACILITY INSPECTION CHECKLIST AGRICO CHEMICAL SITE, PENSACOLA FLORIDA	SATISFACTORY	UNSATISFACTORY	DATE CORRECTED	INITIALED	REMARKS
GENERAL FACILITY AREA					
Gates and Locks Secured	✓				
Perimeter Fencing	✓				
Signage	✓				
Roadway Conditions	✓				
COVER SYSTEM					
Surface Water Runoff Controlled	✓				
No Ponding Water On Cover	✓				
No Sideslope or Top Erosion or Gulying	✓				
Topsoil and Vegetation Intact	✓				
Settlement/Cracking Inspection	✓				
SURFACE WATER COLLECTION SYSTEM					
No Obstructions of Culverts or Inlets	✓				
Inlet Sediment Controls Intact	✓				
No Erosion of Drainage Ditches or Berms	✓				
Detention Ponds Draining Adequately	✓				
Side Slope Erosion of Detention Ponds	✓				
Leaks, Structural Damage to Inlets, Culverts, or Pipes	✓				

INSPECTION PERIOD: June 2014 Bi-Annual Inspection Report

INSPECTED BY: DeHilton
NAME:
SIGNATURE: DeHilton
DATE: 11.11.14
